

License Number: IH / 1133271 / 1 Name: DALE HOUSTON			
Order #: 6928	Label #: 127509	Manufacturer: <u>LIVE OAK</u>	(Check Size of Home)
Homeowner:		Year Model: <u>2026</u>	Single _____
Address:		Length & Width: <u>68x32</u>	Double <u>X</u>
City/State/Zip:		Type Longitudinal System:	Triple _____
Phone #:		Type Lateral Arm System:	HUD Label #:
Date Installed:		New Home: <u>X</u> Used Home: _____	Soil Bearing / PSF:
Installed Wind Zone:		Data Plate Wind Zone:	Torque Probe / in-lbs:
			Permit #:
Note: <u>S# 20256AB</u>			

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

127509

LABEL #	DATE OF INSTALLATION
DALE HOUSTON	
NAME	
IH / 1133271 / 1	6928
LICENSE #	ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS
PLEASE WRITE DATE OF INSTALLATION AND AFFIX LABEL NEXT TO HUD LABEL. USE PERMANENT INK PEN OR MARKER ONLY. COMPLETE INFORMATION ABOVE AND KEEP ON FILE FOR A MINIMUM OF 2 YEARS. YOU ARE REQUIRED TO PROVIDE COPIES WHEN REQUESTED.



Mobile Home Permit Worksheet

Installer: Dale Houston License # EH/1133271

Address of home being installed

Manufacturer Live Oak Length x width 285 SW Pines Place Fort Worth TX 76132


NOTE: If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home. I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials DH

Typical pier spacing



Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

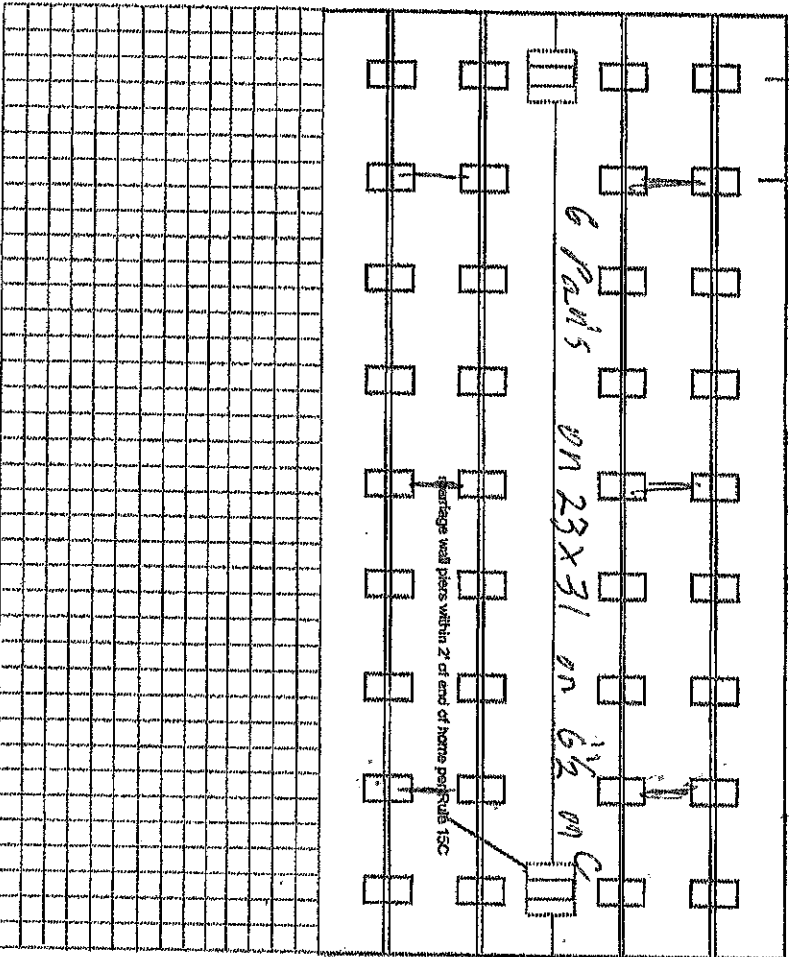

UNRA

Permit Number:

Date:

New Home ☐ Used Home ☒

Home installed to the Manufacturer's Installation Manual Home is installed in accordance with Rule 15-C

Single wide ☐

Wind Zone II ☒

Wind Zone III ☐

Double wide ☒

Installation Decal # 127509

Triple/Quad ☐

Serial # ADHGA1192025646

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	Footer size (256)	18 1/2" x 18 (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'	5'	6'	7'	8'	9'
2000 psf	5'	6'	7'	8'	9'	10'
2500 psf	6'	7'	8'	9'	10'	11'
3000 psf	7'	8'	9'	10'	11'	12'
3500 psf	8'	9'	10'	11'	12'	13'

*Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

23x31

Perimeter pier pad size

16x16

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

4 ft

5 ft

23x31

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer

OTHER TIES

Number

Slidewall

Longitudinal Marriage Wall

Shear Wall

ANCHORS

FRAME TIES

within 2' of end of home spaced at 5' 4" oc





Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil ✓ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5" anchors without testing. A test showing 275 inch pounds or less will require 5" anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5" anchors are required at all centerline the points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's Initials _____

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name DATE HONSTON

Date Tested 6/1/26

ELECTRICAL

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

PLUMBING

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Permit Number _____

Date: _____

Site Preparation

Debris and organic material removed _____ Swale _____ Pad ✓ Other _____

Fastening multi wide units

Floor- Type Fastener: 1/2" x 6" Length: 6" Spacing: 18"
Walls- Type Fastener: 1" Length: 1" Spacing: 1"
Roof- Type Fastener: 1" Length: 1" Spacing: 1"

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials DH

Type gasket FOAM
Pg. _____

Installed:
Between Floors _____ Yes ✓
Between Walls _____ Yes ✓
Bottom of ridge beam _____ Yes ✓

Weatherproofing

The bottom board will be repaired and/or taped. _____ Yes ✓ Pg. _____
Siding on units is installed to manufacturer's specifications. _____ Yes ✓
Fireplace chimney installed so as not to allow intrusion of rain water. _____ Yes ✓

Miscellaneous

Skirting to be installed.	Yes	No	N/A
Dryer vent installed outside of skirting.	Yes	No	N/A
Range downflow vent installed outside of skirting.	Yes	No	N/A
Drain lines supported at 4' intervals.	Yes	No	N/A
Electrical crossovers protected.	Yes	No	N/A
Other:			

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer's Signature DATE HONSTON Date _____
