



Mobile Home Permit Worksheet

Installer:

Kyle Johnson

License #

IH 1122657

Address of home
being installed

1800 Big Coast
Ft. White 32038

Manufacturer

Deer Valley

Length x width

32' x 86' Box

NOTE:

If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Typical pier spacing

2'

6.6


lateral

longitudinal

Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

Installer's initials

YJ

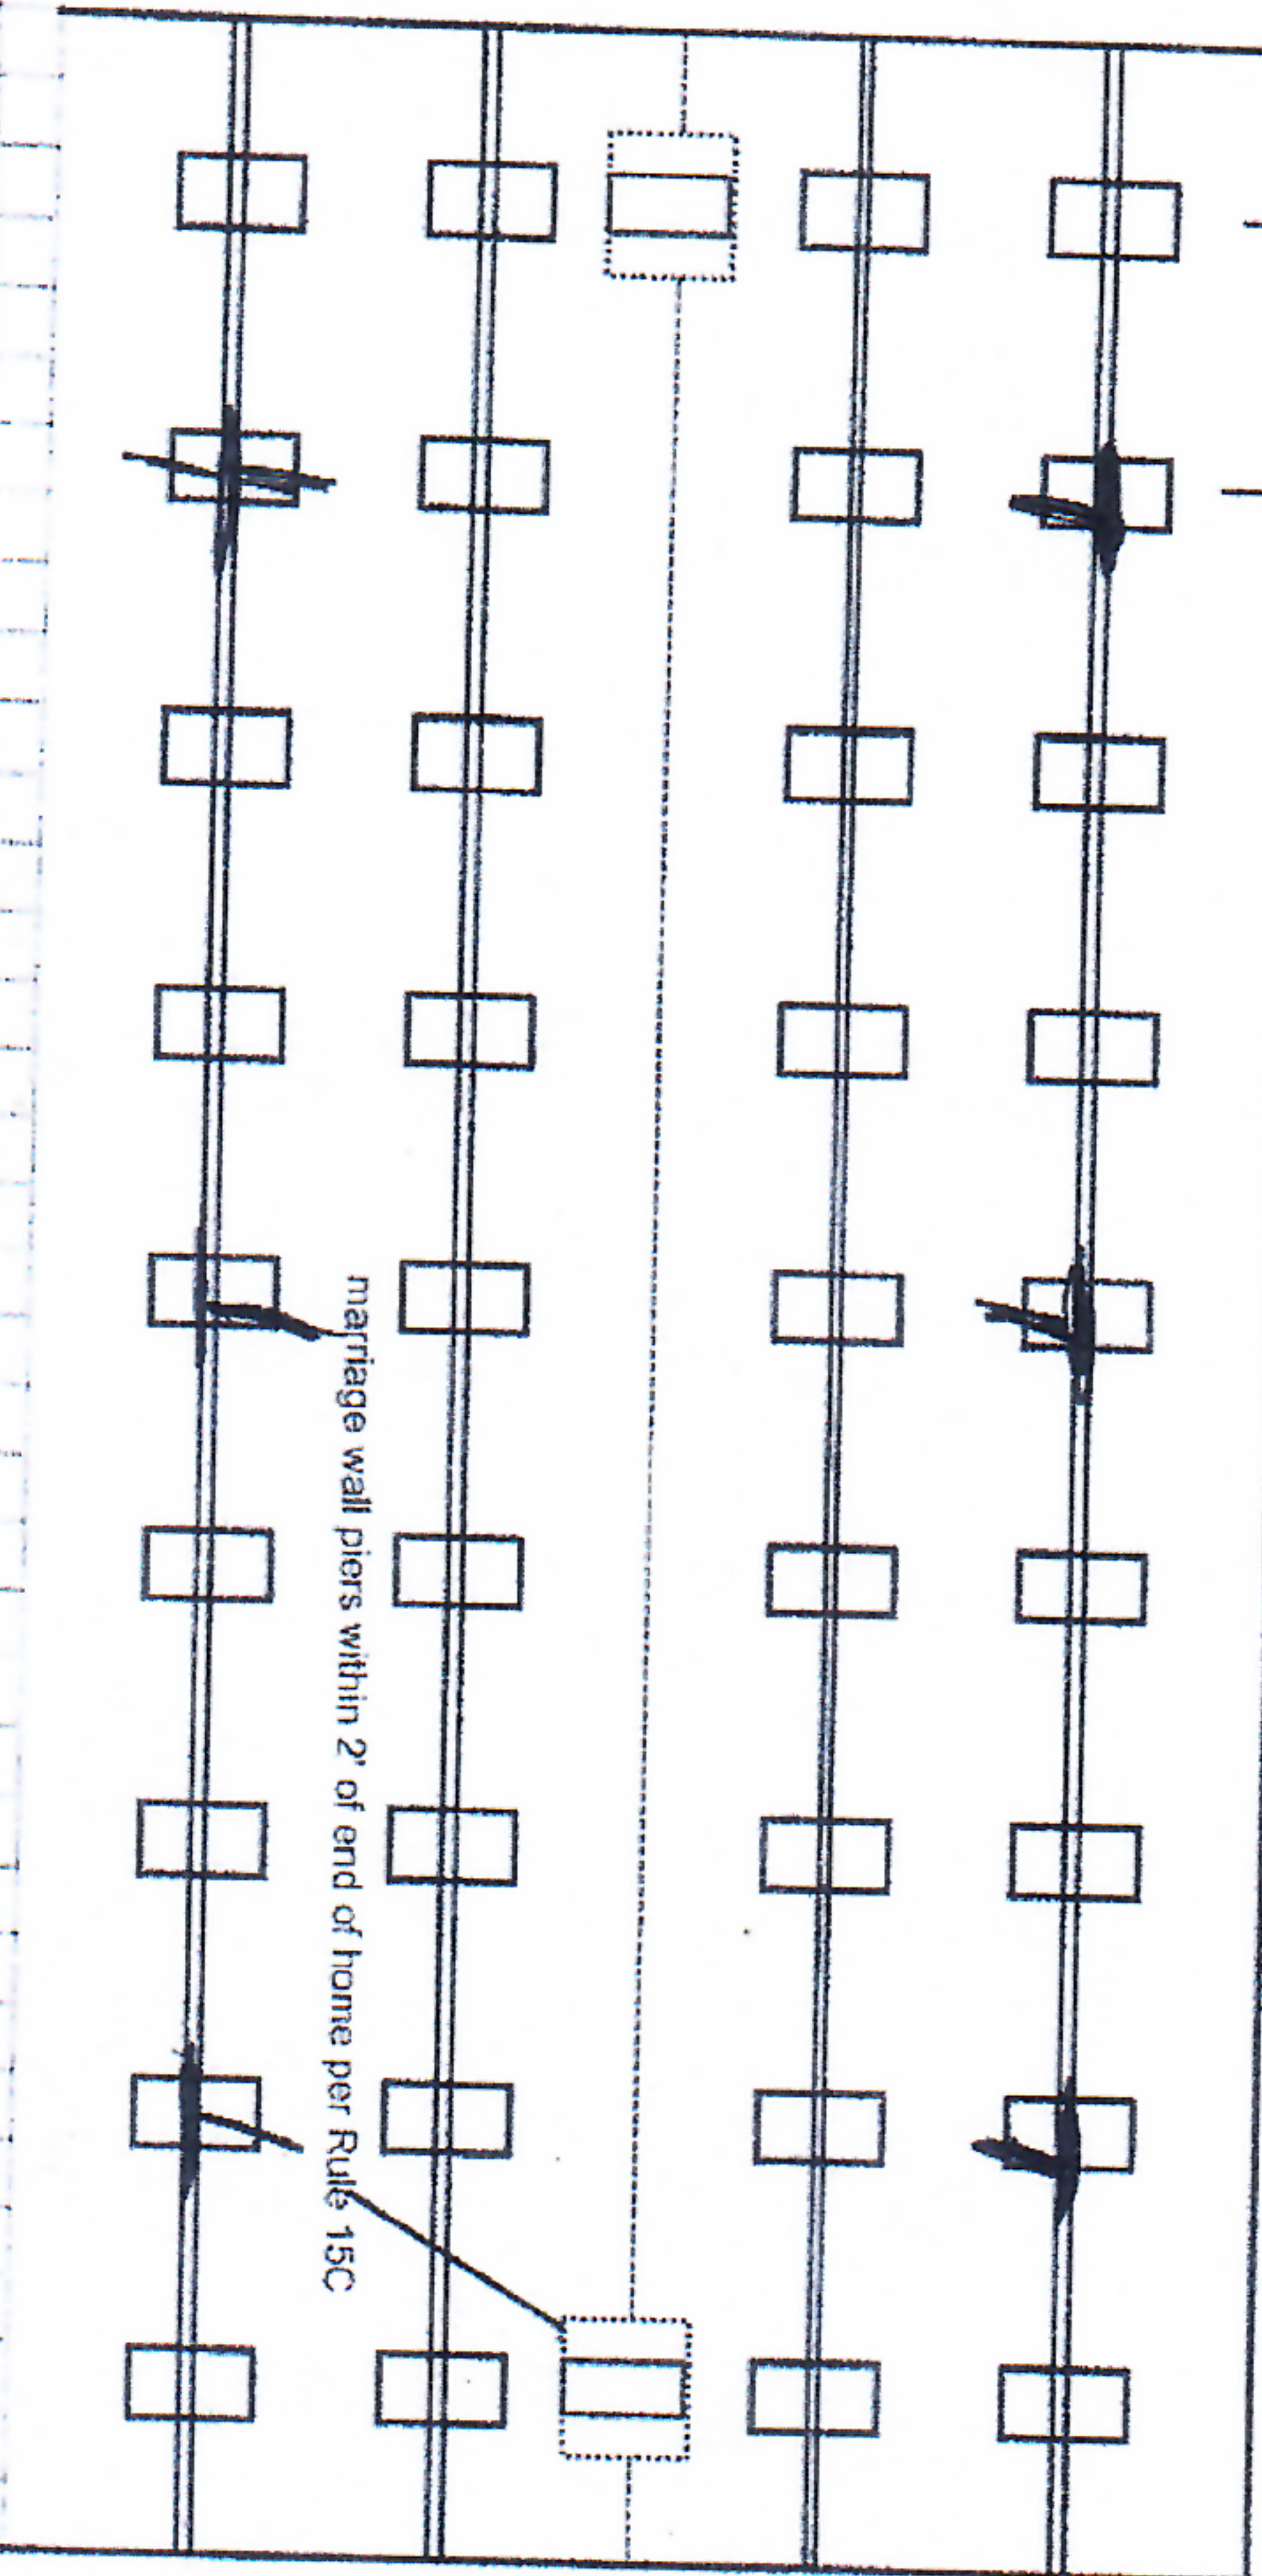

Permit Number:

Date:

New Home

☒

Used Home

☐

Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C

Single wide

☐

Wind Zone II

☐

Wind Zone III

☒

Double wide

☒

Installation Decal #

132343

Triple/Quad

☐

Serial #

DVA-12712749A/B

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4'	5'	6'	7'	8'	8'	8'
2000 psf	5'	6'	7'	8'	8'	8'	8'
2500 psf	6'	7'	8'	8'	8'	8'	8'
3000 psf	7'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

*Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

23.5 x 31.5

Perimeter pier pad size 17.5 x 25.5

OLIVER 1055-11 Outriggers Bars

Other pier pad sizes
(required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

4 ft

5 ft

See Factory Blocking Plan

ANCHORS

FRAME TIES

within 2' of end of home
spaced at 5' 4" oc

OTHER TIES

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer OLIVER 1101V

Sidewall
Longitudinal
Marriage Wall
Shear Wall

Number

40

8

2



Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing _____. A test showing 275 inch pounds or less will require 5' anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. 1 understand 5' anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name Kyle Johnson

Date Tested Assumed Oliverly v US 445' Anchors

ELECTRICAL

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

PLUMBING

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Permit Number: _____

Date: _____

Site Preparation

Debris and organic material removed ☒
Water drainage: Natural ☒ Swale ☐ Pad ☒ Other ☐

Fastening multi wide units

Floor- Type Fastener: 1465 Length: 7 Spacing: 20
Walls- Type Fastener: 1465 Length: 4 Spacing: 10
Roof- Type Fastener: 1465 Length: 7 Spacing: 20

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials KJ

Type gasket Phc Torgy
Pg. form

Installed:

Between Floors ☒ Yes ☐
Between Walls ☒ Yes ☐
Bottom of ridge beam ☒ Yes ☐

Weatherproofing

The bottom board will be repaired and/or taped. _____ Yes ☒ Pg. _____
Siding on units is installed to manufacturer's specifications. _____ Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. _____ Yes ☒

Miscellaneous

Skirting to be installed. _____ Yes ☒ No ☐ N/A
Dryer vent installed outside of skirting. _____ Yes ☒ No ☐ N/A
Range downflow vent installed outside of skirting. _____ Yes ☒ No ☐ N/A
Drain lines supported at 4' intervals. _____ Yes ☒ No ☐ N/A
Electrical crossovers protected. _____ Yes ☒ No ☐ N/A
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer's Signature

Date

ARRIAGE WALL AND PERIMETER BLOCKING REQUIRED 8'-0" ON CENTER

MARRIAGE LINE OPENING SUPPORT PIER/TYP. LOADING

 SUPPORT PIER/TYP. LOADING

FUNDATION NOTES:

ENGINE HOME INSULATION MANUAL FOR OPTIONAL PIER SPACING AND LOADING (I.E. FIREPLACES, ETC.)

1 DIMENSIONS ARE FROM FRONT OF UNIT UNLESS SPECIFIED OTHERWISE.
SINGLE STACK PIERS MAX. 36" HIGH; DOUBLE STACK PIERS MAX. 67" HIGH.

ALL DIMENSIONS ARE FROM FRONT OF HOME UNLESS OTHERWISE NOTED.

(A) MAIN ELECTRICAL
(B) ELECTRICAL CROSSOVER
(C) WATER INLET
(D) WATER CROSSOVER
(E) GAS INLET
(F) GAS CROSSOVER (IF ANY)
(G) PLENUM / DUCT CROSSOVER
(H) SEWER DROPS
(I) RETURN AIR (W/OPT. HEAT PUMP)
(J) SUPPLY AIR (W/OPT. HEAT PUMP / OH DUCT)
(K) DOWNDRAFT COOKTOP VENT

"NAME"
DEER VALLEY HOMEBUILDERS, IN
"SIGNATURE SERIES"
MODEL: DVHBS-9006
SERIAL: L1-12749
PAUL 530

DVHBS-9006C

FIELD

L1-12749

07/29/2026

NTS

STAFF

ALL

DEER VALLEY HOMEBUILDERS, INC.
SIGNATURE SERIES

六

License Number: IH / 1126657 / 1 Name: KYLE JOHNSON

Order #: 7128	Label #: 132343	Manufacturer:	(Check Size of Home)
Homeowner:		Year Model:	Single _____
Address:		Length & Width:	Double _____
City/State/Zip:		Type Longitudinal System:	Triple _____
Phone #:		Type Lateral Arm System:	HUD Label #:
Date Installed:		New Home: _____ Used Home: _____	Soil Bearing / PSF:
Installed Wind Zone:		Data Plate Wind Zone:	Torque Probe / in-lbs:
Note:			Permit #:

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

132343	
LABEL #	DATE OF INSTALLATION
KYLE JOHNSON	
NAME	
IH / 1126657 / 1	7128
LICENSE #	ORDER #
CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325 AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.	

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2
YEARS. YOU ARE REQUIRED
TO PROVIDE COPIES WHEN
REQUESTED.
