



Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psi or check here to declare 1000 lb. soil ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing _____. A test showing 275 inch pounds or less will require 5' anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. 1' understrand 5' anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's initials kg

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name Kyle Johnson

Date Tested Assumed Oliver 11/10/05 4' 5" anchors

ELECTRICAL

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

PLUMBING

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Permit Number: _____

Date: _____

Site Preparation

Debris and organic material removed ☒
Water drainage: Natural ☒ Swale ☐ Pad ☒ Other ☐

Fastening multi wide units

Floor- Type Fastener: lags Length: 7 Spacing: 20
Walls- Type Fastener: lags Length: 4 Spacing: 10
Roof- Type Fastener: lags Length: 7 Spacing: 20
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials kg

Type gasket: Factory Mem

Installed:
Between Floors: Yes
Between Walls: Yes
Bottom of ridge beam: Yes

Weatherproofing

The bottom board will be repaired and/or taped. Yes
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous

Skirting to be installed. Yes
Dryer vent installed outside of skirting. Yes
Range downflow vent installed outside of skirting. Yes
Drain lines supported at 4' intervals. Yes
Electrical crossovers protected. Yes
Other: No

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer's Signature Kyle Johnson

Date 3/3/06



Mobile Home Permit Worksheet



Installer: Kyle Johnson License # TH1126657

Address of home being installed 1304 SW 26th Dr, Lake City, FL 33804

Manufacturer CAPO/DeShing Length x width 32x76ft

NOTE: If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home where the sidewall ties exceed 5 ft 4 in.

Typical pier spacing 2' 6.6" Installer's initials KA

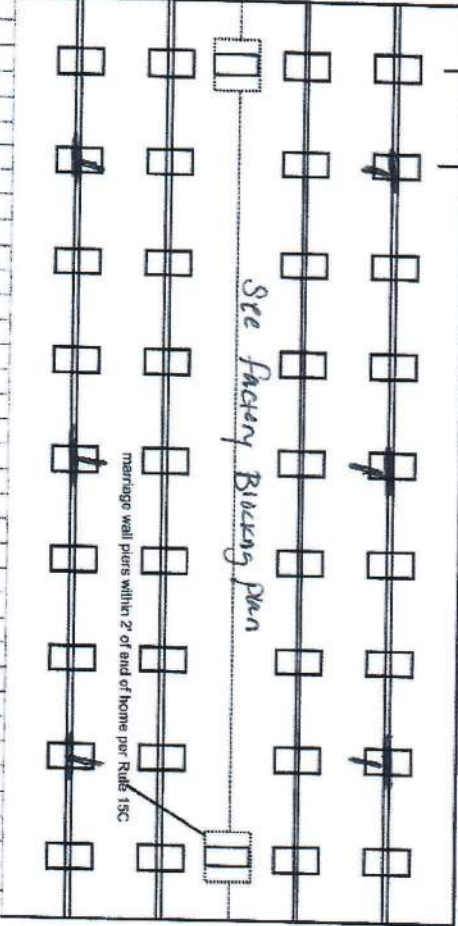

Permit Number: _____ Date: _____

New Home ☒ Used Home ☐

Home installed in the Manufacturer's Installation Manual Home is installed in accordance with Rule 15-C ☒

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Decal # 127276

Triple/Quad ☐ Serial # CA2306A22-15112A16

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)	26" x 26" (676)
1000 psf	3"	4"	5"	6"	7"	8"	8"
1500 psf	4 1/2"	6"	7"	8"	9"	10"	10"
2000 psf	6"	8"	9"	10"	11"	12"	12"
2500 psf	7 1/2"	9"	10"	11"	12"	13"	13"
3000 psf	8"	10"	11"	12"	13"	14"	14"
3500 psf	8"	10"	11"	12"	13"	14"	14"

*Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 23.5 x 31.5
Perimeter pier pad size or 17.5 x 25.5
Other pier pad sizes Oliver 1055-1100 trigger bars w/ doors + windows
(required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening _____ Pier pad size _____

See Blocking

factory plan

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer _____

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer Oliver 1101 V

OTHER TIES

Number _____

Longitudinal

Marriage Wall

Shear Wall

ANCHORS

FRAME TIES

within 2' of end of home - spaced at 5' 4" OC ☒

4 ft ☒ 5 ft ☒

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/2 x 26 1/2	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676
