



# Mobile Home Permit Worksheet

Installer: Jerome Jordan License # IH1129310

Address of home being installed 834 SW JOE MAYHAW DR.  
LAKE CITY FL 32024


Manufacturer NOBI Length x width 48 x 24

**NOTE:** If home is a single wide fill out one half of the blocking plan  
If home is a triple or quad wide sketch in remainder of home  
I understand Lateral Arm Systems cannot be used on any home (new or used)  
where the sidewall ties exceed 5 ft 4 in.

Typical pier spacing

Installer's initials jjd

2' 5' lateral longitudinal  
Show locations of Longitudinal and Lateral Systems  
(use dark lines to show these locations)

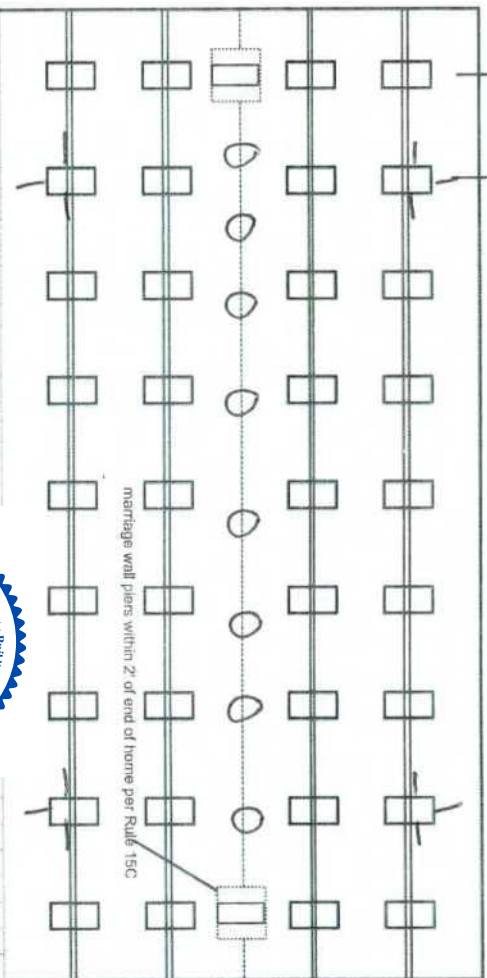

Permit Number: \_\_\_\_\_

Date: \_\_\_\_\_

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual  
Home is installed in accordance with Rule 15-C

Single wide

☐ Wind Zone II

☒ Wind Zone III

Double wide

☒ Installation Decal #

125192

Triple/Quad

☐ Serial #

N11SSCA1B

## PIER SPACING TABLE FOR USED HOMES

| Load bearing capacity (sq in) | 16" x 16" (256) | 18 1/2" x 18 (342) | 20" x 20" (400) | 22" x 22" (484)* | 24" x 24" (576)* | 26" x 26" (676) |
|-------------------------------|-----------------|--------------------|-----------------|------------------|------------------|-----------------|
| 1000 psf                      | 3'              | 4'                 | 5'              | 6'               | 7'               | 8'              |
| 1500 psf                      | 4'              | 6'                 | 7'              | 8'               | 8'               | 8'              |
| 2000 psf                      | 6'              | 8'                 | 8'              | 8'               | 8'               | 8'              |
| 2500 psf                      | 7'              | 8'                 | 8'              | 8'               | 8'               | 8'              |
| 3000 psf                      | 8'              | 8'                 | 8'              | 8'               | 8'               | 8'              |
| 3500 psf                      | 8'              | 8'                 | 8'              | 8'               | 8'               | 8'              |

\*Interpolated from Rule 15C-1 pier spacing table.

### PIER PAD SIZES

I-beam pier pad size

17 x 25

Perimeter pier pad size

10 x 10

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

17 x 25

ANCHORS

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Longitudinal Stabilizing Device (LSD)

Manufacturer OLIVEY TECHNOLOGY

Longitudinal Stabilizing Device w/ Lateral Arms  
Manufacturer OLIVEY TECHNOLOGY

Sidewall

Longitudinal

Marriage Wall  
Shear Wall

Number

20

10  
2+  
8



## Mobile Home Permit Worksheet

### POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to \_\_\_\_\_ psf or check here to declare 1000 lb. soil ☒ without testing.

X \_\_\_\_\_ X \_\_\_\_\_ X \_\_\_\_\_

#### POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X \_\_\_\_\_ X \_\_\_\_\_ X \_\_\_\_\_

#### TORQUE PROBE TEST

The results of the torque probe test is \_\_\_\_\_ inch pounds or check here if you are declaring 5' anchors without testing ☒. A test showing 275 inch pounds or less will require 5' anchors.

**Note:** A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5' anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's initials

### ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name \_\_\_\_\_

Date Tested \_\_\_\_\_

#### ELECTRICAL

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. \_\_\_\_\_

#### PLUMBING

Connect all sewer drains to an existing sewer tap or septic tank. Pg. \_\_\_\_\_

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. \_\_\_\_\_

Permit Number: \_\_\_\_\_

Date: \_\_\_\_\_

### Site Preparation

Debris and organic material removed YES  
Water drainage: Natural \_\_\_\_\_ Swale \_\_\_\_\_ Pad ☒ Other \_\_\_\_\_

#### Fastening multi wide units

Floor- Type Fastener: LAG Length: 0 Spacing: 24  
Walls- Type Fastener: LAG Length: 0 Spacing: 24  
Roof- Type Fastener: LAG Length: 0 Spacing: 24

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

#### Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

Type gasket: FOAM  
Pg. 98

Installed:  
Between Floors: Yes ☒  
Between Walls: Yes ☒  
Bottom of ridge beam: Yes ☒

#### Weatherproofing

The bottom board will be repaired and/or taped. \_\_\_\_\_ Yes \_\_\_\_\_ Pg. \_\_\_\_\_  
Siding on units is installed to manufacturer's specifications. \_\_\_\_\_ Yes \_\_\_\_\_  
Fireplace chimney installed so as not to allow intrusion of rain water. \_\_\_\_\_ Yes \_\_\_\_\_

#### Miscellaneous

Skirting to be installed. \_\_\_\_\_ Yes \_\_\_\_\_ No \_\_\_\_\_ N/A \_\_\_\_\_  
Dryer vent installed outside of skirting. \_\_\_\_\_ Yes \_\_\_\_\_ No \_\_\_\_\_ N/A \_\_\_\_\_  
Range downflow vent installed outside of skirting. \_\_\_\_\_ Yes \_\_\_\_\_ No \_\_\_\_\_ N/A \_\_\_\_\_  
Drain lines supported at 4' intervals. \_\_\_\_\_ Yes \_\_\_\_\_ No \_\_\_\_\_ N/A \_\_\_\_\_  
Electrical crossovers protected. \_\_\_\_\_ Yes \_\_\_\_\_ No \_\_\_\_\_ N/A \_\_\_\_\_  
Other: \_\_\_\_\_

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer's Signature

*Deanne Jones*

Date 4/26/20
