

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT

Order #: 5934	Label #: 103261	Manufacturer: LIVE OAK	(Check Size of Home)
Homeowner: VIDEON		Year Model: 2024	Single _____
Address: 233 SW MICANOPY GLN		Length & Width: 72 x 32	Double X
City/State/Zip: FT WHITE FL 32038		Type Longitudinal System: OTI (6)	Triple _____
Phone #:		Type Lateral Arm System: OTI (6)	HUD Label #:
Date Installed:		New Home: X Used Home: _____	Soil Bearing / PSF:
Installed Wind Zone: II		Data Plate Wind Zone: II	Torque Probe / in-lbs:
Note:			Permit #:

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

103261

LABEL #

DATE OF INSTALLATION

DAVID E ALBRIGHT

NAME

IH / 1129420 / 1

5934

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

Mobile Home Permit Worksheet

Dr

Application Number:

Date:

Installer: DAVID ALBRIGHT

License # 1H-1129420

Address of home being installed

233 SW Micanopy Gen Ft White Fl 32038

Manufacturer

Live Oak

Length x width

32x72/76

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual Home is installed in accordance with Rule 15-C

Single wide ☐

Wind Zone II ☒

Wind Zone III ☐

Double wide ☒

Installation Decal #

103261

Triple Quad ☐

Serial #

LOHGA20038990

Triplex Quad ☐

NOTE: If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home where the sidewall ties exceed 5 ft 4 in.


Typical pier spacing

2' 4" 6"

Installer's Initials

DAV

Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

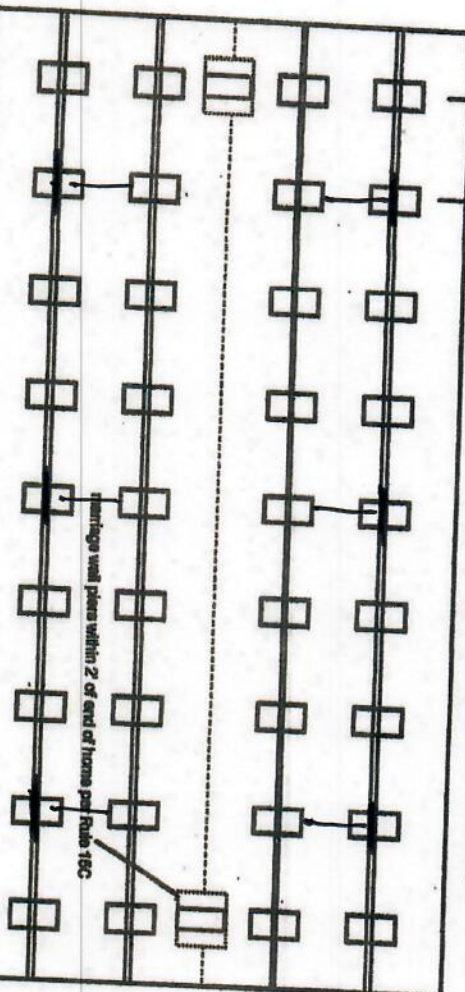

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	Footer size (253)	16" x 16" (253)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3	4	5	6	7	8	8
1500 psf	4	5	6	7	8	8	8
2000 psf	5	6	7	8	8	8	8
2500 psf	6	7	8	8	8	8	8
3000 psf	7	8	8	8	8	8	8
3500 psf	8	8	8	8	8	8	8

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

17" x 26"

Perimeter pier pad size

16" x 16"

Other pier pad sizes (required by the mfg.)

24" x 24"
35" x 25.5"

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Pad Size	Sq in
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

Opening

Pier pad size

FACTORY DIMENSION

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer Over Tech/Novelty
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer Over Tech/Novelty

OTHER TIES

Sidewall
Longitudinal
Marriage wall
Shearwall
Number 2
8-5-6-4
2

Mobile Home Permit Worksheet

Dw

Application Number

Date: 1

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to per
or check here to declare 1000 lb. soil ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 245 inch pounds or check here if you are declaring 5 anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all corners to the points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. bending capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

DAVID RIBBERT MOBILE HOME SVC

Date Tested

Electrical

Connect electrical conductors between multi-wire units, but not to the main power source. This includes the bonding wire between multi-wire units. Pg. 64-68

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 70

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 107

Site Preparation

Debris and organic material removed ☒ Pad ☒ Other

Water drainage: Natural Swale

Fastening multi-wire units

Floor: Type Fastener: 19G Length: 6" Spacing: 2'
WALL: Type Fastener: 19G Length: 4" Spacing: 16"
Roof: Type Fastener: 19G Length: 6" Spacing: 2'
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket (weatherstripping requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

Type gasket Pg. 36

Installed:
Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 119
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous

Siding to be installed. Yes ☒ No ☒
Dryer vent installed outside of siding. Yes ☒ N/A ☒
Range downflow vent installed outside of siding. Yes ☒ N/A ☒
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other:

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and/or Rule 15C-1 & 2


Installer Signature David Ribbert Date

Live Oak Homes
MODEL: L-3725B - 32 X 76
5-BEDROOM / 3-BATH

- (A) MAIN ELECTRICAL
 (B) ELECTRICAL CROSSOVER
 (C) WATER INLET
 (D) WATER CROSSOVER (IF ANY)
 (E) GAS INLET (IF ANY)
 (F) GAS CROSSOVER (IF ANY)
 (G) DUCT CROSSOVER
 (H) SEWER DROPS
 (I) RETURN AIR (W/OPT. HEAT PUMP OR DUCT)
 (J) SUPPLY AIR (W/OPT. HEAT PUMP OR DUCT)


MARRIAGE LINE OPENING SUPPORT PIER/TYP.
SUPPORT PIER/TYP.
FOUNDATION NOTES:
 - THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
 - FOOTINGS ARE SHOWN FOR EXAMPLE ONLY. QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
 - FOOTINGS ARE REQUIRED AT SUPPORT POSTS. SEE INSTALLATION MANUAL FOR REQUIREMENTS.

7-5-2016

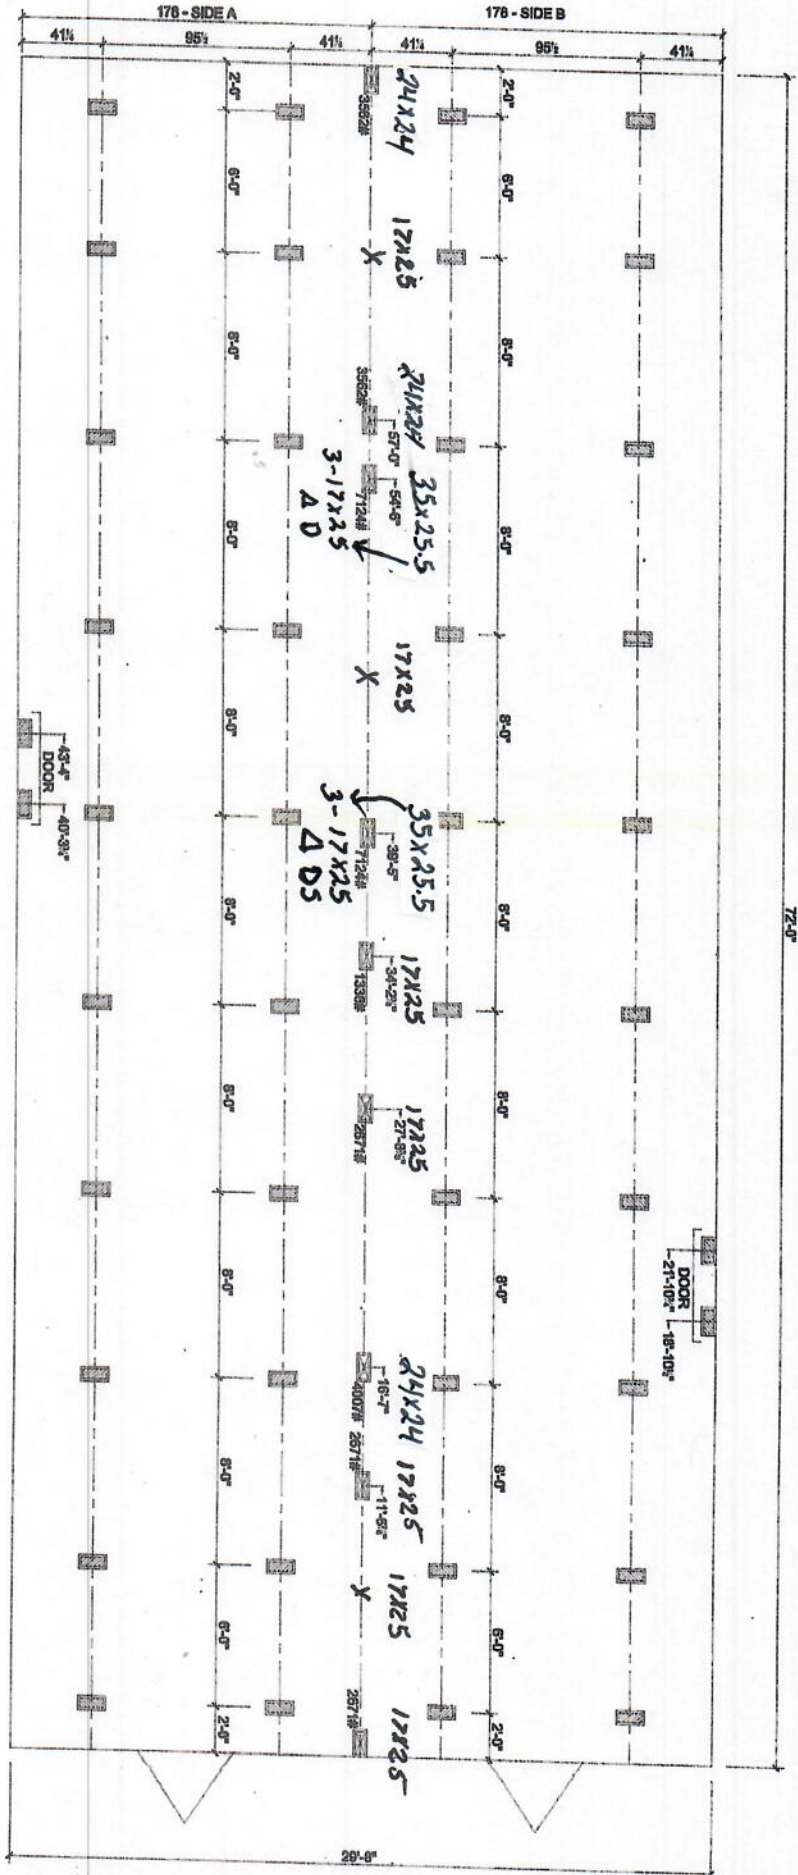

5K

5K

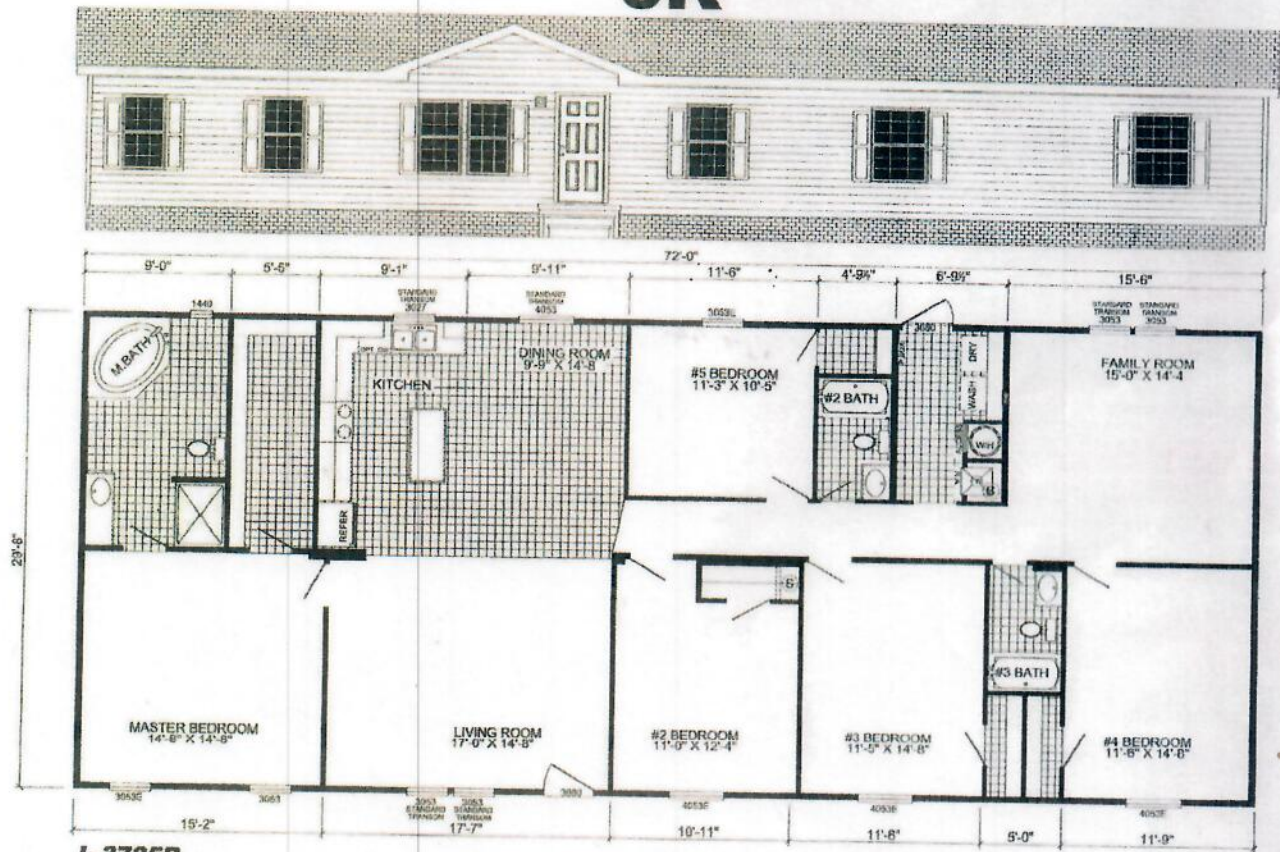

L-3725B

5-BEDROOM / 3-BATH

32 X 76 - Approx. 2136 Sq. Ft.

2-9-2018

- * All room dimensions include closets and square footage figures are approximate.
- * Transoms windows are available on optional 9'-0" side wall houses only.
- * Underpinning shown is optional.
