
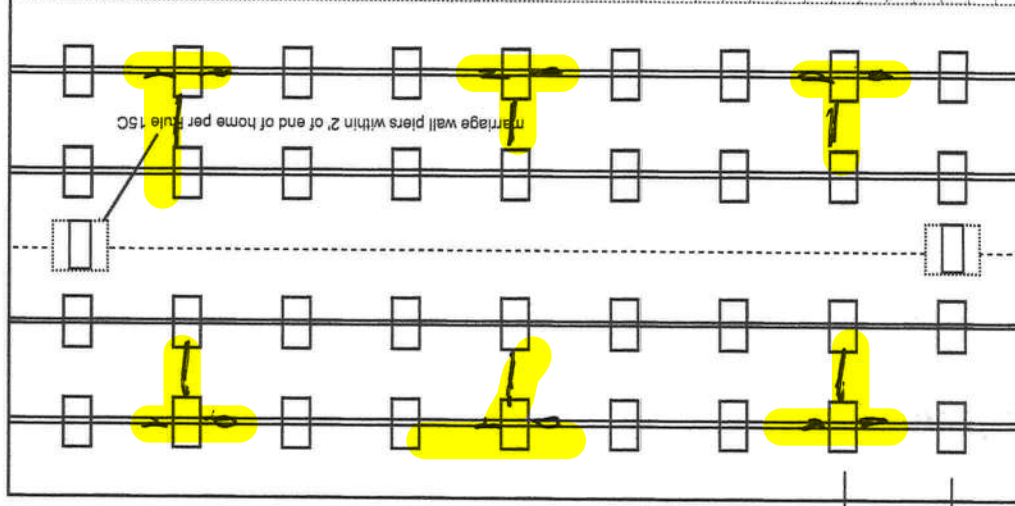


Mobile Home Permit Worksheet

Installer: Ronnie Norris License # TH10AS145
 Address of home being installed 387 Walnut Place
 Manufacturer Dayland Length x width 60' x 28'

NOTE: If home is a single wide fill out one half of the blocking plan
 If home is a triple or quad wide sketch in remainder of home
 I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.



Digitally signed by Laurie Hodson
 Date: 2021.01.27 11:57:41 -05'00'



Application Number: _____

Date: _____

☐ New Home
☒ Used Home
 Home is installed in accordance with Rule 15-C Manual
☐ Wind Zone II
☐ Wind Zone III

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	16" x 16"	18 1/2" x 18"	20" x 20"	22" x 22"	24" x 24"	26" x 26"
4000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'	6'	7'	8'	9'	10'
2000 psf	6'	8'	9'	10'	11'	12'
2500 psf	8'	10'	11'	12'	13'	14'
3000 psf	10'	12'	13'	14'	15'	16'
3500 psf	12'	14'	15'	16'	17'	18'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17.3/16 x 25.3/16	441
18 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

I-beam pier pad size 17x25
 Perimeter pier pad size NR
 Other pier pad sizes (required by the mfg.) 16x4
 Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.
 List all marriage wall openings greater than 4 foot and their pier pad sizes below.

TIEDOWN COMPONENTS

Opening	Pier pad size
8	16 x 16
4	16 x 16
4	16 x 16

OTHER TIES

Within 2' of end of home spaced at 5' 4" oc

FRAME TIES

4 ft
5 ft 9 in

ANCHORS

Sidewall
 Longitudinal
 Marriage wall
 Shearwall
 Number

Longitudinal Stabilizing Device (LSD)
 Manufacturer
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer
 Oliver Tech

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

Site Preparation

Debris and organic material removed _____
 Water drainage: Natural _____ Swale _____ Pad _____ Other _____

Fastening multi wide units

Floor: _____ Walls: _____ Roof: _____
 Type Fastener: _____ Type Fastener: _____ Type Fastener: _____
 Length: 6" Length: 6" Length: 6"
 Spacing: 16" Spacing: 16" Spacing: 16"
 For used homes within 30 gauge, 8" wide, galvanized metal strip
 will be centered over the peak of the roof and fastened with galv.
 roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used
 homes and that condensation, mold, mildew and buckled marriage walls are
 a result of a poorly installed or no gasket being installed. I understand a strip
 of tape will not serve as a gasket.

Installer's initials _____

Installed: _____

Between Floors Yes _____

Between Walls Yes _____

Bottom of ridgebeam Yes _____

Weatherproofing

The bottomboard will be repaired and/or taped. Yes _____ Pg. _____

Siding on units is installed to manufacturer's specifications. Yes _____

Fireplace chimney installed so as not to allow intrusion of rain water. Yes _____

Miscellaneous

Skirting to be installed. Yes _____ No _____

Dryer vent installed outside of skirting. Yes _____ N/A _____

Drain lines supported at 4 foot intervals. Yes _____

Electrical crossovers protected. Yes _____

Other: _____

Installer verifies all information given with this permit worksheet
 is accurate and true based on the
 manufacturer's installation instructions and or Rule 15C-1 & 2

Date _____

Installer Signature _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf
 or check here to declare 1000 lb. soil without testing.

_____ x 100 _____ x 100 _____ x 100

1. Test the perimeter of the home at 6 locations.

2. Take the reading at the depth of the footer.

3. Using 500 lb. increments, take the lowest
 reading and round down to that increment.

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check
 here if you are declaring 5' anchors without testing A test

showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft.

anchors are allowed at the sidewall locations. I understand 5 ft

reading is 275 or less and where the mobile home manufacturer may

requires anchors with 4000 lb holding capacity.

Installer's initials _____

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name _____

Date Tested _____

Electrical

Connect electrical conductors between multi-wide units, but not to the main power
 source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other
 independent water supply systems. Pg. _____

