

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

Installer: David Albright License # _____



Address of home being installed: 4687 SW US Hwy 27
Fort White, FL 32028

Manufacturer: Live Oak Homes Length x width: 32 x 28

NOTE: If home is a single wide fill out only half of the blocking plan. If home is a triple or quad wide sketch in remainder of home. Understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials: DA

Typical pier spacing

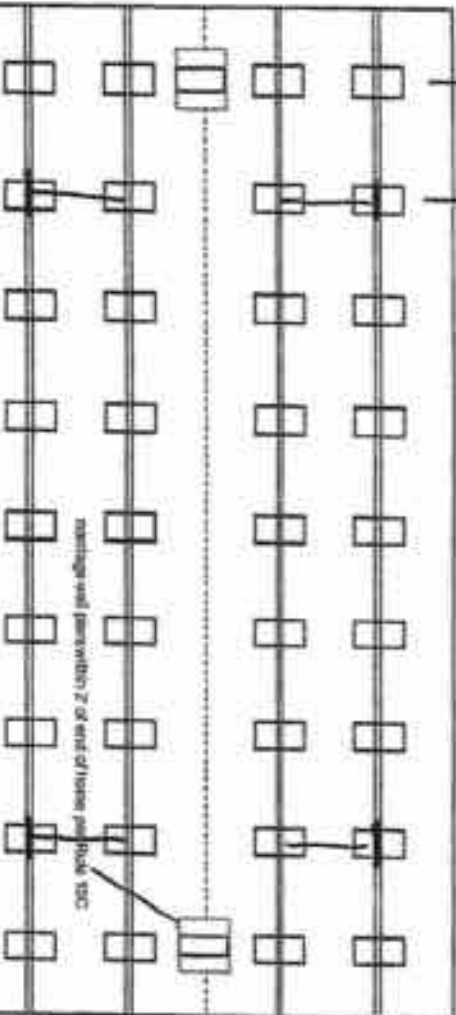

Row Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual Home is installed in accordance with Rule 15C ☒

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Detail # 120090

Triple/Quad ☐ Serial # LOH6A 300 34 50 47A

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	16' x 16' (256)	16 1/2' x 16 1/2' (262)	21' x 20' (420)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'6"	6'	7'	8'	9'	10'
2000 psf	6'	8'	9'	10'	11'	12'
2500 psf	7'6"	9'	10'	11'	12'	13'
3000 psf	8'	10'	11'	12'	13'	14'
3500 psf	8'	10'	11'	12'	13'	14'

* Interpolated from Rule 15C-1 pier spacing table

PIER PAD SIZES

I-beam pier pad size

17 x 25

Perimeter pier pad size

16 x 16

Other pier pad sizes (required by the mfg.)

24x24, 23x31

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

Trailer Dinner

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) Manufacturer OLIVER TECHNOLOGIES
Longitudinal Stabilizing Device w/ Lateral Arms Manufacturer OLIVER TECHNOLOGIES

OTHER TIES

Sidewall Longitudinal Marriage wall Shearwall
Number 20
4
6-3' 6-4'
8

POPULAR PAD SIZES

Pad Size	Sq ft
16 x 16	256
16 x 18	288
18.5 x 18.5	342
18 x 22.5	380
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 9/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psi or check here to declare 1000 lb. soil ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 250 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all corners. The points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

AW Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

DAVID MONTGOMERY MOBILE HOME INC

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 64-68

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 70

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply system. Pg. 109

Application Number: _____

Date: _____

Site Preparation

Debris and organic material removed ☒ Pad ☒ Other _____
Water drainage: Natural Swale

Footing (multi wide units)

Floor: Type Fastener: 2x6 Length: 6" Spacing: 2'
Walls: Type Fastener: 3x8 Length: 9" Spacing: 12"
Roof: Type Fastener: 1x6 Length: 6" Spacing: 2'
For used houses a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with gals. roofing nails at 2" on center on both sides of the ventline.

Gas/Vent fastening (optional)

I understand a properly installed gas/vent is a requirement of all new and used homes and that condensation, mold, mildew and buckled rafter/walls are a result of a poorly installed or no gas/vent being installed. I understand a strip of tape will not serve as a gas/vent.

Installer's initials

Type gas/vent
Pg. 36

Installed
Between Floors: Yes ☒
Between Walls: Yes ☒
Bottom of ridgebeam: Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 119
Sealing on units is installed to manufacturer's specifications. Yes
Flue/chimney installed so as not to show intrusion of rain water. Yes

Miscellaneous


Sterling to be installed: Yes _____ No ☒
Dryer vent installed outside of sterling. Yes _____ N/A ☒
Range downflow vent installed outside of sterling. Yes _____ N/A ☒
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and/or Rule 15C-1 & 2

Installer Signature

David Montgomery

Date

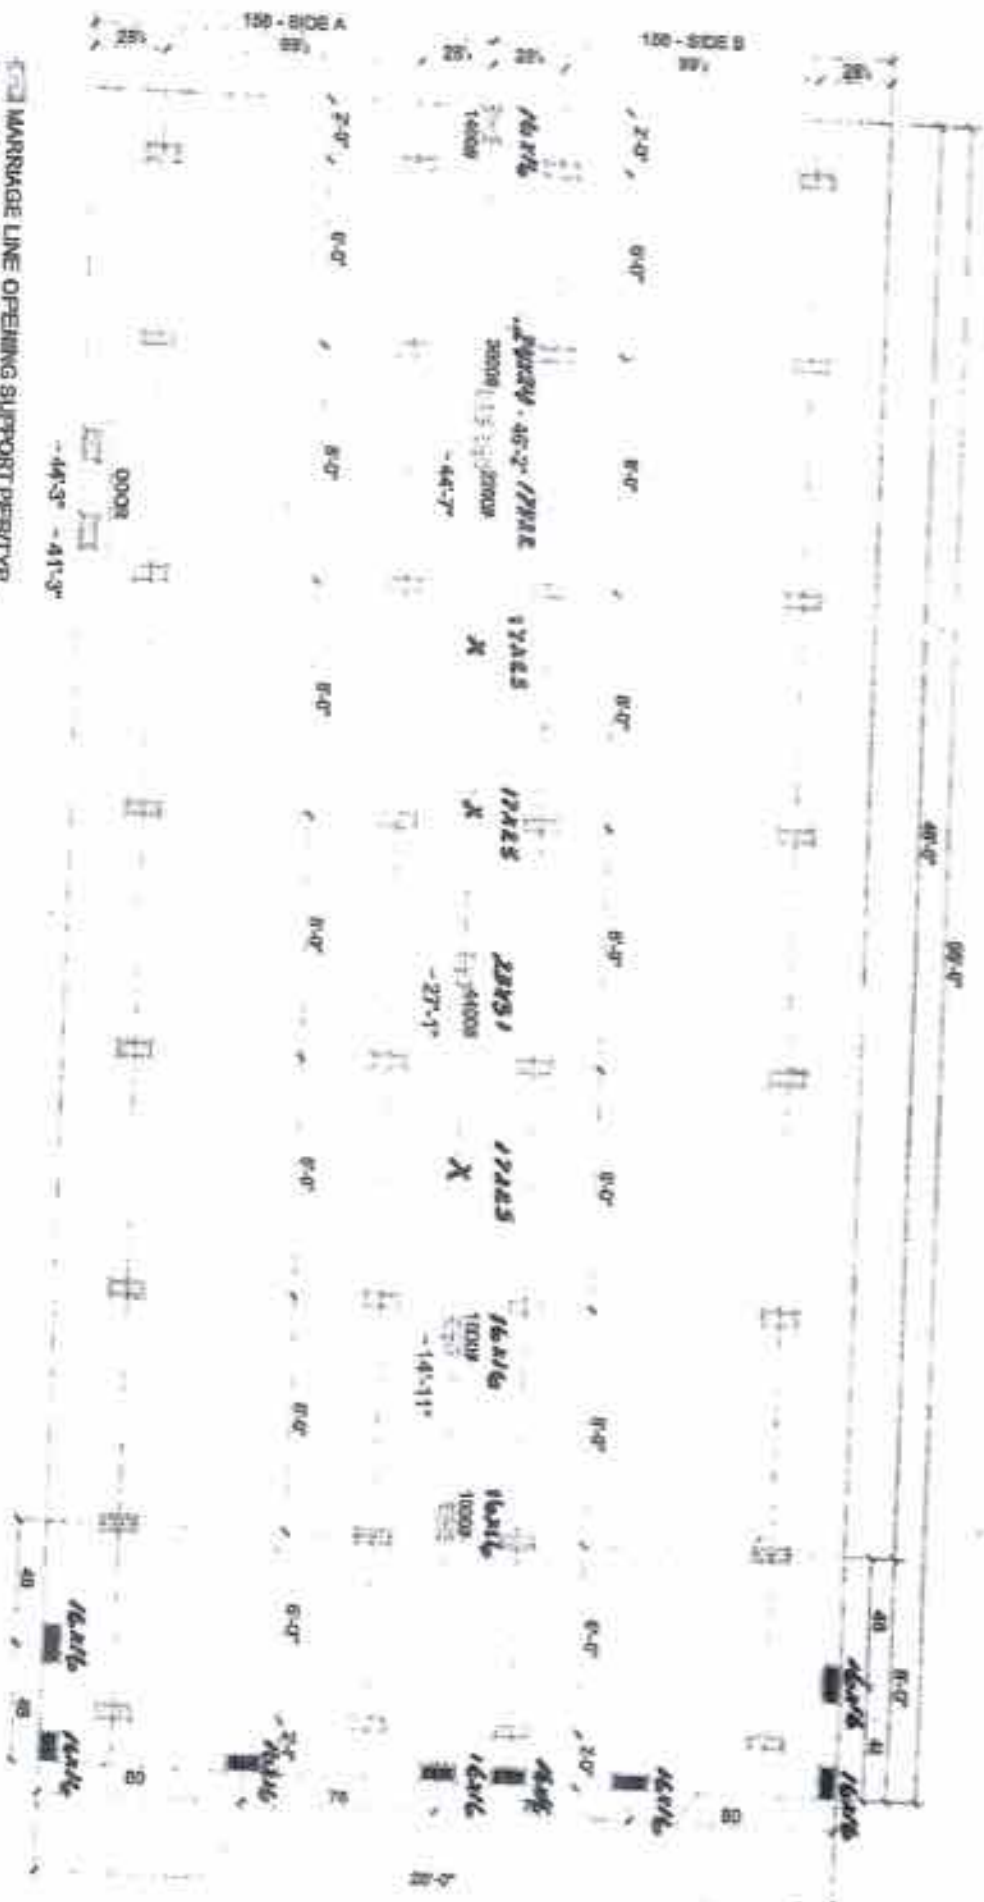

CH0023

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENT.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY. QUANTITY AND SIZING MAY VARY BASED ON PADS TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS. SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes

MODEL: H-2483N-PS - 28 X 56 (BOX)
3-BEDROOM / 2-BATH

(99-1/2" I-BEAM SPACING)

H-2483N-PS w/ FULL PORCH

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT

Order #: 6606

Label #: 120090

Homeowner:

SHEPHERD

Address:

4687 SW USHWY 27

City/State/Zip

FT WHITE FL 32038

Phone #:

Date Installed:

Installed Wind Zone:

4

Note:

Manufacturer:

LIVE OAK

Year Model:

Length & Width:

Type Longitudinal System:

OTI 4

Type Lateral Arm System:

OTI 4

New Home: ☒ Used Home: ☐

Data Plate Wind Zone:

7

(Check Size of Home)

Single ☐

Double ☒

Triple ☐

HUD Label #:

Soil Bearing / PSP:

Torque Probe / in-lbs:

Permit #:

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

120090

LABEL #

DATE OF INSTALLATION

DAVID E ALBRIGHT

NAME

IH / 1129420 / 1

6606

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
