

Contractor Changed

16

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only (Revised 7-1-15) Zoning Official _____ Building Official _____
AP# _____ Date Received _____ By _____ Permit # 40060
Flood Zone _____ Development Permit _____ Zoning _____ Land Use Plan Map Category _____
Comments _____
FEMA Map# _____ Elevation _____ Finished Floor _____ River _____ In Floodway _____
☐ Recorded Deed or ☐ Property Appraiser PO ☐ Site Plan ☐ EH # _____ ☐ Well letter OR
☐ Existing well ☐ Land Owner Affidavit ☐ Installer Authorization ☐ FW Comp. letter ☐ App Fee Paid
☐ DOT Approval ☐ Parent Parcel # 22A ☐ STUP-MH _____ ☐ 911 App
☐ Ellisville Water Sys ☐ Assessment _____ ☐ Out County ☐ In County ☐ Sub VF Form

Property ID # 20-45-16-03077.01 Subdivision N/A Lot# N/A
▪ New Mobile Home X Used Mobile Home _____ MH Size _____ Year _____
▪ Applicant Cameron Chase Phone # 407-529-6028
▪ Address 4984 SW Birley Ave Lake City FL 32024
▪ Name of Property Owner Cameron Chase Phone# 407-529-6028
▪ 911 Address _____
▪ Circle the correct power company - FL Power & Light - Clay Electric
(Circle One) - Suwannee Valley Electric - Duke Energy
▪ Name of Owner of Mobile Home Denise Orr Phone # 407-520-0561
Address 4984 S.W. Birley Ave.
▪ Relationship to Property Owner Mother
▪ Current Number of Dwellings on Property 1
▪ Lot Size _____ Total Acreage _____
▪ Do you : Have Existing Drive or Private Drive or need Culvert Permit or Culvert Waiver (Circle one)
(Currently using) (Blue Road Sign) (Putting in a Culvert) (Not existing but do not need a Culvert)
▪ Is this Mobile Home Replacing an Existing Mobile Home NO
▪ Driving Directions to the Property Head W. Hernandez @ NE Madison St
@ N Main Ave @ US 90 W/W Duval St @ FL 247 S
@ CR 242 @ SW Birley Ave
▪ Name of Licensed Dealer/Installer William R. Price Phone # 386-943-4298
▪ Installers Address 3360 152nd Place Lake City FL 32028
▪ License Number TH-1041934 Installation Decal # 72500

000040060

By pd

PERMIT WORKSHEET

PERMIT NUMBER

Installer

William Price

License #

14-104193L

Address of home being installed

4984 SW Parkway Ave
Lake City FL 32024

Manufacturer

Clayton

Length x width

28x50

NOTE:

If home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials


WPA

Typical pier spacing

2

Longitudinal

Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

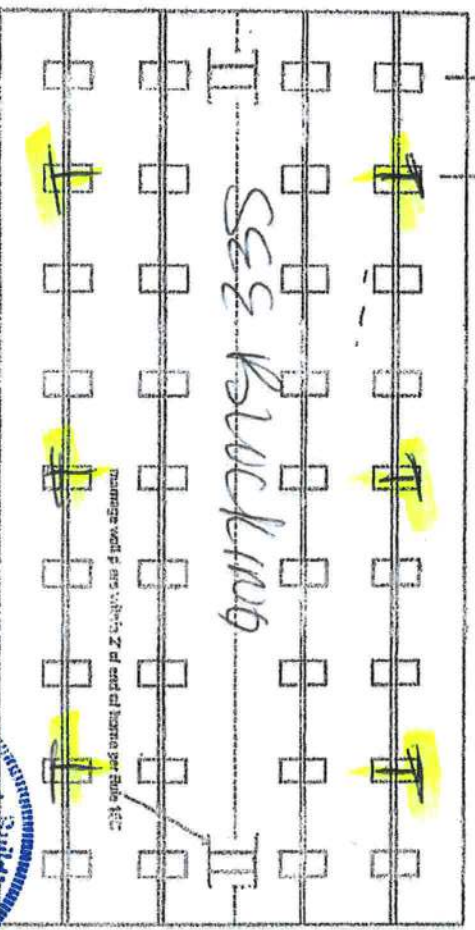

New Home

☒

Used Home

☐

Home installed to the Manufacturer's Installation Manual

☒

Home is installed in accordance with Rule 15-C

☐

Single wide

☐

Wind Zone II

☒

Wind Zone III

☐

Double wide

☒

Installation Detail #

7a507

Triple/Quad

☐

Serial #

#12891 AB

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	16' x 16" (256)	18 1/2" x 18 1/2" (342)	20' x 20" (400)	22' x 22" (484)	24' x 24" (576)	26' x 26" (676)
1000 psf	3'	4'	5'	5'	5'	5'
1500 psf	4'	5'	6'	7'	8'	8'
2000 psf	5'	6'	7'	8'	9'	9'
2500 psf	6'	7'	8'	9'	10'	10'
3000 psf	7'	8'	9'	10'	11'	11'
3500 psf	8'	9'	10'	11'	12'	12'

Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

17x25

Perimeter pier pad size

16x16

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of manhole wall openings 4 foot or greater. (Use this symbol to show the piers.)

List all manhole wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

large

23x31

MSpace

(TIEDOWN COMPONENTS)

Longitudinal Steepling Devices (LSD)
Manufacturer: Clayton
Model: CL-100
Serial: 12891

Shave Length: 12
Shave Width: 12
Shave Depth: 12

ANCHORS

within 1' of end of home spaced 4' 0" 4' 0" 4' 0"

OTHER TIES

Number

BY PERMIT NUMBER

PERMIT WORKSHEET

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 150 psi
or check here to declare 1000 lb. soil without testing.

X 150 X 100 X 100

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 3 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 150 X 100 X 100

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 4 foot anchors.

Notes: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewalk locations. Understand 5 ft anchors are required at all locations the footer where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

William R. Price

Date Tested

4/24/20

Electrical

Contract mechanical contractors, plumbers multi-wide units, not call to the main power source. This includes the bonding wire between multi-wide units. Pg. 1

Plumbing

Contract a sewer drains to an existing sewer line or septic tank. Pg. 1

Contract a potable water supply according to an existing water meter, water line, or other method of water supply system. Pg. 1



Site Preparation

Debris and organic material removed 90% 4/25
Water drainage: Natural Swale Pad OK Other

Fastening multi wide units

Floor Joist Fastener: 1/2" Length: 18" Spacing: 18"
Rivet Fastener: 1/2" Length: 18" Spacing: 18"
Used homes a min. 30 gauge, 8" wide, galvanized metal strip centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket location, sealing requirement

Understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled masonry walls are a result of a poorly installed or no gasket being installed. Understand a strip of tape will not serve as a gasket.

Installer's initials

WRA

Type gasket FOAM
Pg. 111

Installed:
Between Floors Yes
Between Walls Yes
Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes Pg.
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous


Skirting to be installed. Yes No
Dryer vent installed outside of skirting. Yes No
Range ductwork vent installed outside of skirting. Yes No
Drain lines supported at 4 foot intervals. Yes No
Electrical crossovers protected. Yes No
Other:

Installer verifies all information given with this permit worksheet is accurate and true based on the

manufacturer's installation instructions and or PUD 15C-1 & 2


Installer's Signature

William R. Price Date 6/30/20



D - THE WASHINGTON
Home Plan 657AT2009AH

2009 - 2 Bath - 1484 sq. ft. - 58' width - 28' depth
www.claytonhomes.com/home-plans/657AT2009AH

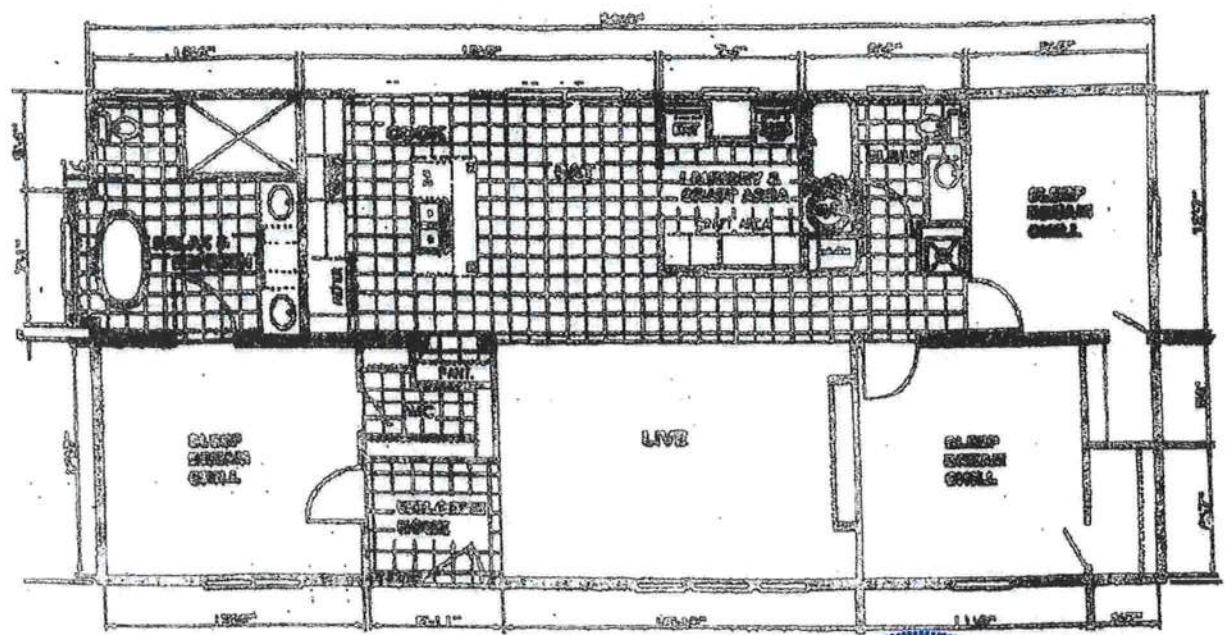

RECEIVED
JUN 30 2020
By *JK*



The home series and floor plans shown all have starting prices within the price range indicated. Your local Home Center can quote you specific prices and terms of purchase for specific homes. Clayton invests in continuous product and process improvement. All home series, floor plans, specifications, dimensions, features, materials, availability, and closing prices shown are artist's renderings or estimates and are subject to change without notice or obligation. Dimensions are nominal and length and width measurements are from exterior wall to exterior wall. Starting prices include the home only, plus typical delivery and installation. Starting prices do not include other costs such as taxes, title fees, insurance premiums, filing or recording fees, land or improvements to the land, optional home features, optional delivery or installation services, wheels and axles, community or homeowner association fees, or any other items not shown on your Retailer Closing Agreement and related documents (your RCA). Your RCA will show the details of your purchase. 2011 Clayton Homes. All rights reserved.


JUN 30 2020

MARRIAGEWALL COLUMN SUPPORT LOADS AND LOCATIONS

20 lb ROOF LOAD		SHEARL OPENING (FT) REQUIRED PIER LOAD (KSI)					
SHEARL OPENING PIER LOAD	28" BOX WIDTH	3	4	5	6	8	10
		1162	1315	1467	1620	1925	2230

*FOR 30 lb & 40 lb ROOF LOAD REFER TO TABLES 7b & 7c IN THE INSTALLATION MANUAL.

4. MUST BE ADDED (2" PER ENDWALL) TO OVERALL LENGTH WITH 2X6 WALLS.

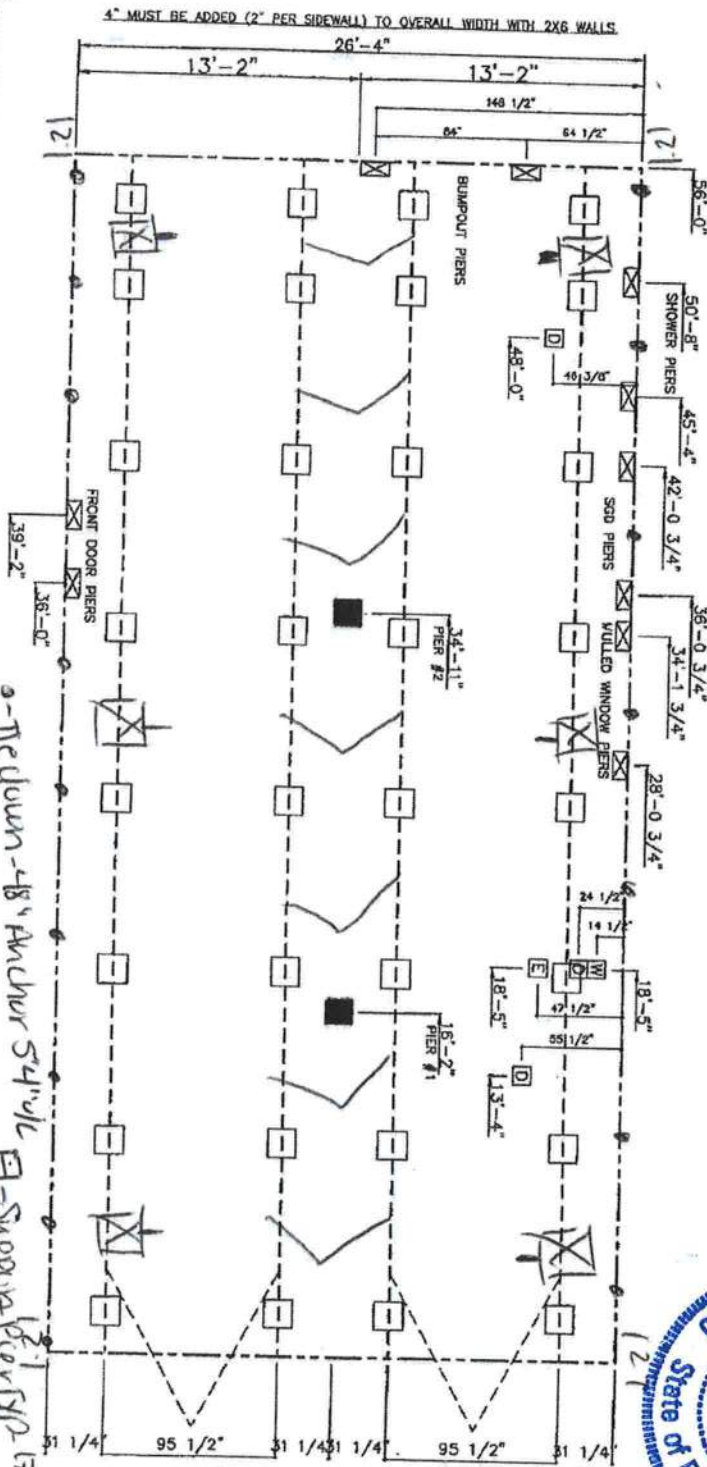

π -down - 48' Anchor 5'4" w/c
E-Supporter 16'7" 17x25 ft abs w/pax 8x10
9-0. TID 17x25

IX - Oliver System

1 - Double Frame Tie-48"
Anchor 5' from end then

* All center line anchors led
* All perimeter sd.f. (Std Plan "CONDITIONED")
N/A SQ.FT. (W/OPT. PORCH/RECESS "CONDITIONED")

Product Description: TAM-001	CMH MANUFACTURING	Model #: PAT20563A	Drawing #: 44-11M024
		Date: 7/25/15	

PIER LOADS

1. PIER LOADS SHOWN ARE TO BE USED TO SIZE THE FOOTINGS BELOW THE MARRIAGEWALL FOR COLUMN SUPPORT PIERS. REFER TO TABLES 6b AND 6c IN THE INSTALLATION MANUAL FOR LOAD ON FRAME PIER FOOTINGS FOR HOMES THAT DO NOT REQUIRE PERIMETER BLOCKING. REFER TO TABLES 7b AND 7c IN THE INSTALLATION MANUAL FOR LOAD ON FRAME PIER FOOTINGS THAT REQUIRE PERIMETER BLOCKING. REFER TO TABLES 10 AND 10c TO DETERMINE FOOTING SIZE FOR ALL PIERS.
2. REFER TO TABLE 9 FOR PIER CONFIGURATION AND MAXIMUM ALLOWABLE HEIGHTS. CROSS REFERENCE THE PIER HEIGHT WITH THE MAXIMUM ALLOWABLE FLOOR HEIGHT LISTED IN THE FRAME MEDIAN CHARTS (TABLE 18, 19, AND 20).
3. FLOOR WIDTH SHOWN IS FOR STANDARD PRODUCT ONLY. CONTACT THE MFG PLANT FOR SPECIFICATIONS OF OPTIONS ORDERED.
4. SERVICE DROP LOCATIONS IDENTIFIED ARE APPROXIMATE. THE MAXIMUM SPACING FOR 8" I-BEAMS IS 8 FEET, 10" & 12" I-BEAMS ARE TO FEET.

PIER LOAD 201b. ROOF LOAD	
COLUMN PIER #	COLUMN LOAD (LBS)
PIER #1	4103
PIER #2	4103

SERVICE DROP LEGEND

PIER LEGEND

☐ = SUPPORT UNDER WAITING OPENING

☒ = SUPPORT AT WAITING COLLUM

D = DWV PLUMBING DROP
G = GAS INLET

☐ = PER MAN BEAM
 PM = PER PRODUCT

Don

28x50

Columbia
Show Case

License Number: IH / 1041936 / 1 Name: WILLIAM R PRICE

Order #: 4494

Label #: 72500

Manufacturer:

Homeowner:

Year Model:

Address:

Length & Width:

City/State/Zip:

Type Longitudinal System:

Phone #:

Type Lateral Arm System:

Date Installed:

New Home: _____ Used Home: _____

Installed Wind Zone:

Data Plate Wind Zone:

(Check Size of Home)

Single _____

Double _____

Triple _____

HUD Label #:

Soil Bearing / PSF:

Torque Probe / in-lbs:

Permit #:

Note:



STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

72500

LABEL #

DATE OF INSTALLATION

WILLIAM R PRICE

NAME

IH / 1041936 / 1

4494

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.


July 1, 2020

Regarding: Denise Orr
Cameron Chase
4984 SW Birley Ave.
Lake City FL 32024

To Whom it May Concern at the Columbia County Building Department,


This letter is to inform you that we would like to change contractors on Permit # 000040060. The contractor we are changing from is Ernest Johnson IH-1025249, and the new contractor will be William Price IH-1041936.

Thank you for your time and consideration.



Property Owner

Cameron Chase
FLDL C200-112-77-443-3
exp 12/3/2022



John Davis
GG299936
exp 2/10/23
