

BRECHEN

CAMBRIDGE

P-3603J

page 1 of 2

These worksheets must be completed and signed by the installer.
Submit the originals with the packet.

Installer **DAVID ALBRIGHT** License # **IH/1129420**

911 Address where home is being installed. **238 BATTLEHILL LANE**

LAKE CITY, FL 32055

Manufacturer **LIVE OAK HOMES** Length x width **32x60/64**

NOTE: If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials **DA**


Typical pier spacing

2' 5'

folded

longitudinal

Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

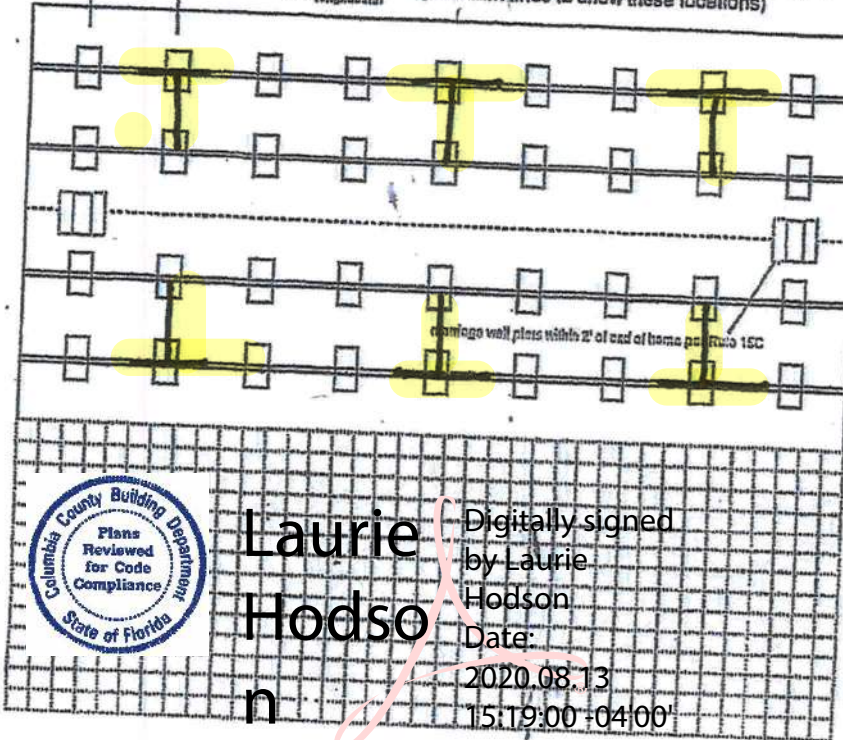

Laurie
Hodson
n

Digitally signed
by Laurie
Hodson
Date:
2020.08.13
15:19:00 -04:00

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual ☒

Home is installed in accordance with Rule 15-C ☐

Single wide ☐ Wind-Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Detail # **71624**

Triple/Quad ☐ Serial # **LOHGA 119 20558 A/B**

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	3'	4'	5'	6'	7'	8'
1500 psf	4' 6"	4' 6"	6'	7'	8'	9'	10'
2000 psf	6'	6'	8'	9'	10'	11'	12'
2500 psf	7' 6"	7' 6"	9'	10'	11'	12'	13'
3000 psf	8'	8'	10'	11'	12'	13'	14'
3500 psf	8'	8'	10'	11'	12'	13'	14'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size **17 x 25**

Perimeter pier pad size

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening **FACTORY** Pier pad size **DIAGRAM**

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) OTI
Manufacturer
Longitudinal Stabilizing Device w/ Lateral Arms OTI
Manufacturer

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 25 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft ☒

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Number
Sidewall **29**
Longitudinal **6**
Marriage wall **6-8 5-4**
Shearwall **3**

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb. soil _____ without testing.

x 1500x 1500x 1500

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1500x 1500x 1500

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5' anchors without testing _____. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 6 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

Installer's Initials _____

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

DAVID ALBRIGHT MOBILE HOME SVC

Date Tested _____



Site Preparation

Debris and organic material removed XWater drainage: Natural _____ Swale _____ Pad X Other _____

Fastening multi wide units

Floor: Type Fastener: LAGS Length: 6" Spacing: 2'
 Walls: Type Fastener: SCREWS Length: 3" Spacing: 18"
 Roof: Type Fastener: LAGS Length: 6" Spacing: 2'
 For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials DAType gasket FACTORY
Pg. 41 INSTALLED

Installed:

Between Floors Yes X
 Between Walls Yes X
 Bottom of ridgebeam Yes X

Weatherproofing

The bottomboard will be repaired and/or taped. Yes X Pg. 124
 Siding on units is installed to manufacturer's specifications. Yes X
 Fireplace chimney installed so as not to allow intrusion of rain water. Yes X

Miscellaneous

Skirting to be installed. Yes _____ No N/A
 Dryer vent installed outside of skirting. Yes _____ N/A X
 Range downflow vent installed outside of skirting. Yes _____ N/A X
 Drain lines supported at 4 foot intervals. Yes X
 Electrical crossovers protected. Yes X
 Other: _____

BONDING WIRE

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature David Albright

Date _____

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 73-77

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 79-80

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 78-110

60'-0"



FOUNDATION NOTES:

Live Oak Homes
MODEL: P-3603J - 32 X 60
3-BEDROOM / 2-BATH

- | | |
|------------------------------|---|
| (A) MAIN ELECTRICAL | (G) DUCT CROSSOVER |
| (B) ELECTRICAL CROSSOVER | (H) SEWER DROPS |
| (C) WATER INLET | (I) RETURN AIR (W/OPT. HEAT PUMP OH DUCT) |
| (D) WATER CROSSOVER (IF ANY) | (J) SUPPLY AIR (W/OPT. HEAT PUMP OH DUCT) |
| (E) GAS INLET (IF ANY) | |
| (F) GAS CROSSOVER (IF ANY) | |



P-3603J

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT		
Order #: 4444	Label #: 71624	Manufacturer: LIVE OAK
Homeowner: BRECHEN	Year Model: 2020	(Check Size of Home)
Address: 238 BATTLEHILL LN	Length & Width: 64x32	Single _____
City/State/Zip: LAKE CITY FL 32055	Type Longitudinal System: 6 OTI	Double ☒
Phone #:	Type Lateral Arm System: 6 OTI	Triple _____
Date Installed:	New Home: ☒ Used Home: _____	HUD Label #:
Installed Wind Zone: II	Data Plate Wind Zone: II	Soil Bearing / PSF:
Note:		Torque Probe / in-lbs:
		Permit #:

**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

71624

LABEL #	DATE OF INSTALLATION
DAVID E ALBRIGHT	
NAME	
IH / 1129420 / 1	4444
LICENSE #	ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS



PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.



CAMBRIDGE



FRONT ELEVATION

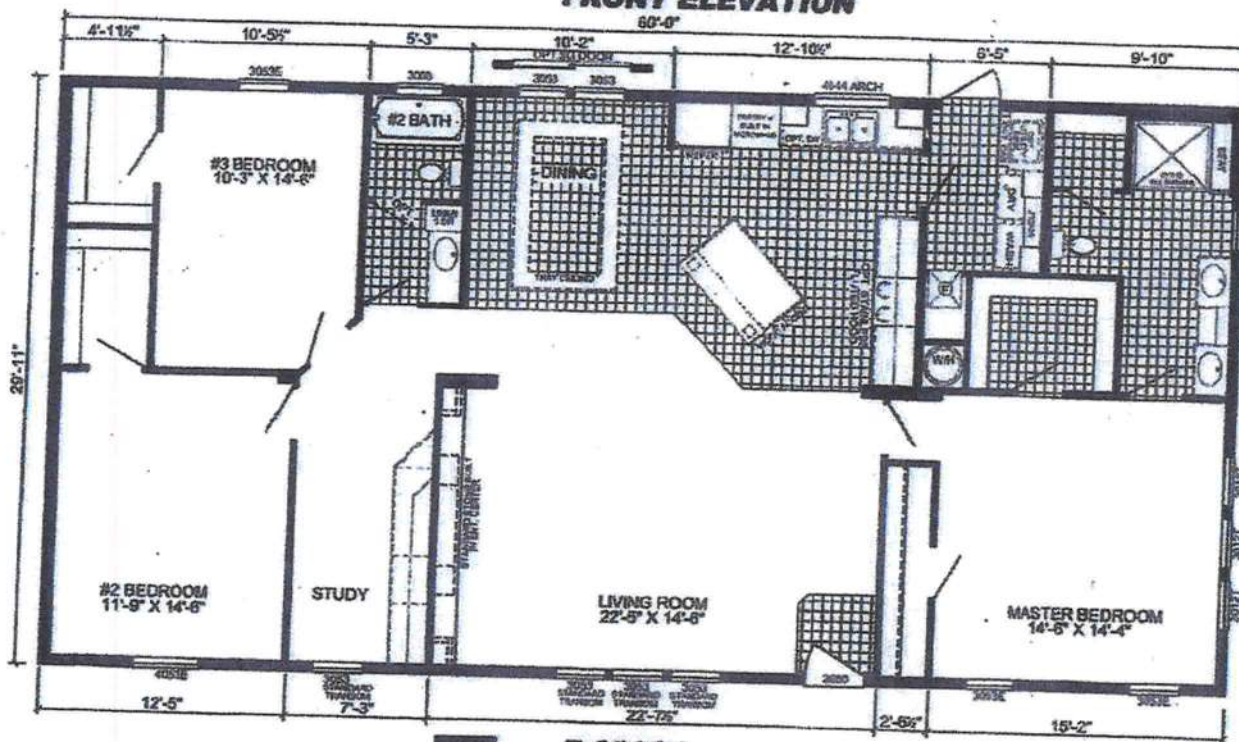

P-3603J
3-BEDROOM / 2-BATH
32 X 64 - Approx. 1795 Sq. Ft.
 Date: 1-15-2018

* All room dimensions include closets and square footage figures are approximate.
 * Transom windows are available on optional 9'-0" sidewalk houses only.



FREEDOM SERIES HOMES

- PINK SAFE AND TEXTURE RASH OVER 1" DIVISUAL
- INTERIOR FINISHES
- 3/4" GUTTERED VINYL CONSTRUCTION ON AVERAGE 30" CENTERS
- 20" COVERS ON ENGINEERED ROOF TRUSSES
- INTERIOR FINISHES CHANGES WITH FINISHES SHOWN AND SHOWN FINISHES ARE NOT
- FINISHES TO YOUR PERSONAL PREFERENCES
- YOU PICK THE COLOURS
- CONSTRUCTION THAT MEETS/BEATS SITE BUILT QUALITY AT A FRACTION OF THE COST!!
