

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT

Order #: 5763	Label #: 98734	Manufacturer: <u>LIVE OAK</u>	(Check Size of Home)
Homeowner: <u>JOHNSON</u>	Year Model: <u>2023</u>		Single _____
Address: <u>1198 SW BARON GLEN</u>	Length & Width: <u>72/76 x 32</u>		Double <u>X</u>
City/State/Zip: <u>FORT WHITE FL 32038</u>	Type Longitudinal System: <u>60TI</u>		Triple _____
Phone #:	Type Lateral Arm System: <u>60TI</u>		HUD Label #:
Date Installed:	New Home: <u>X</u> Used Home: _____		Soil Bearing / PSF:
Installed Wind Zone: <u>D</u>	Data Plate Wind Zone: <u>H</u>		Torque Probe / in-lbs:
Note:			Permit #:

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

98734

LABEL #

DATE OF INSTALLATION

DAVID E ALBRIGHT

NAME

IH / 1129420 / 1

5763

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

Mobile Home Permit Worksheet

OR

Application Number:

Date:

Installer: DAVID RIBRIGHT

License # 1H-1129420

Address of home being installed 1198 SW Baron Glen Fort White Fl 32038

Manufacturer Live Oak

Length x width 32X72/76

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual ☒

Home is installed in accordance with Rule 15-C ☒

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☐ Installation Decal # 98734



Title/Quad ☐ Serial # LOHGA20038339AB

NOTE:

If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home where the sidewall ties exceed 5 ft 4 in.

Typical pier spacing

Installer's initials DR

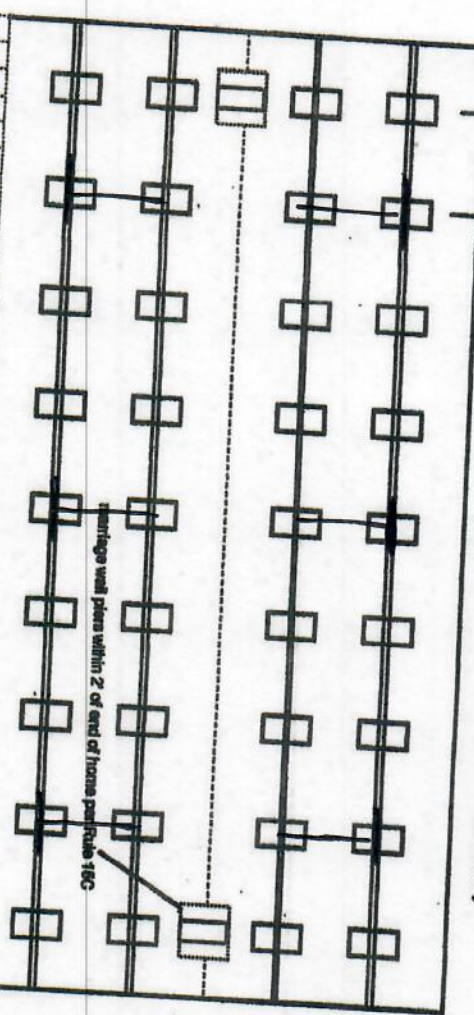

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	Footer size (sq ft)	16" x 16" (256)	18 1/2" x 16 (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4'	5'	6'	7'	8'	8'	8'
2000 psf	5'	6'	7'	8'	8'	8'	8'
2500 psf	6'	7'	8'	8'	8'	8'	8'
3000 psf	7'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17x26

Perimeter pier pad size 16x16

Other pier pad sizes (required by the mfg.) 23x31

POPULAR PAD SIZES

Pad Size	Sq ft
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening 16x26 Pier pad size 16x16

16x26 DIAGRAM

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) 2

Manufacturer Cliver Technologies

Longitudinal Stabilizing Device w/ Lateral Arms 2

Manufacturer Cliver Technologies

OTHER TIES

Sidewall Longitudinal Marriage wall 2

Number 2

Size 8-5'6-4'

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

Mobile Home Permit Worksheet

Dr

Application Number:

Date:

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psi or check here to declare 1000 lb. soil without testing.

X 2500

X 1500

X 1500

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 2500

X 2500

X 1500

TORQUE PROBE TEST

The results of the torque probe test is 250 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sideline locations. I understand 5 ft anchors are required at all centerline to points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 ft. locking capacity.

Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

DAVID ABERNETHY MOBILE HOME SVC

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 64-68

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 70

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply system. Pg. 107

Site Preparation

Debris and organic material removed

X

Swale

Pad

Other

Fastening multi wide units

Floor: Type Fastener: 1/2" Length: 6" Spacing: 2' 1/2" Type Fastener: 1/2" Length: 1" Spacing: 18"

Roof: Type Fastener: 1/2" Length: 6" Spacing: 18" For used homes a min. 30 gauge, 6" wide, galvanized metal strip will be centered over the peak of the roof and fastened with gals. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherstripping required)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials

Type gasket Pg. 36

Installed:

Between Floors Yes X

Between Walls Yes END UNITS

Bottom of ridgebeam Yes X

Weatherproofing

The backboard will be repaired and/or taped. Yes X Pg. 119
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous

Siding to be installed. Yes

No X

Dryer vent installed outside of siding. Yes

N/A

Range downflow vent installed outside of siding. Yes

N/A

Drain lines supported at 4 foot intervals. Yes

N/A


Other:

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 19C-4 & 2

Installer Signature

David Abernethy

Date

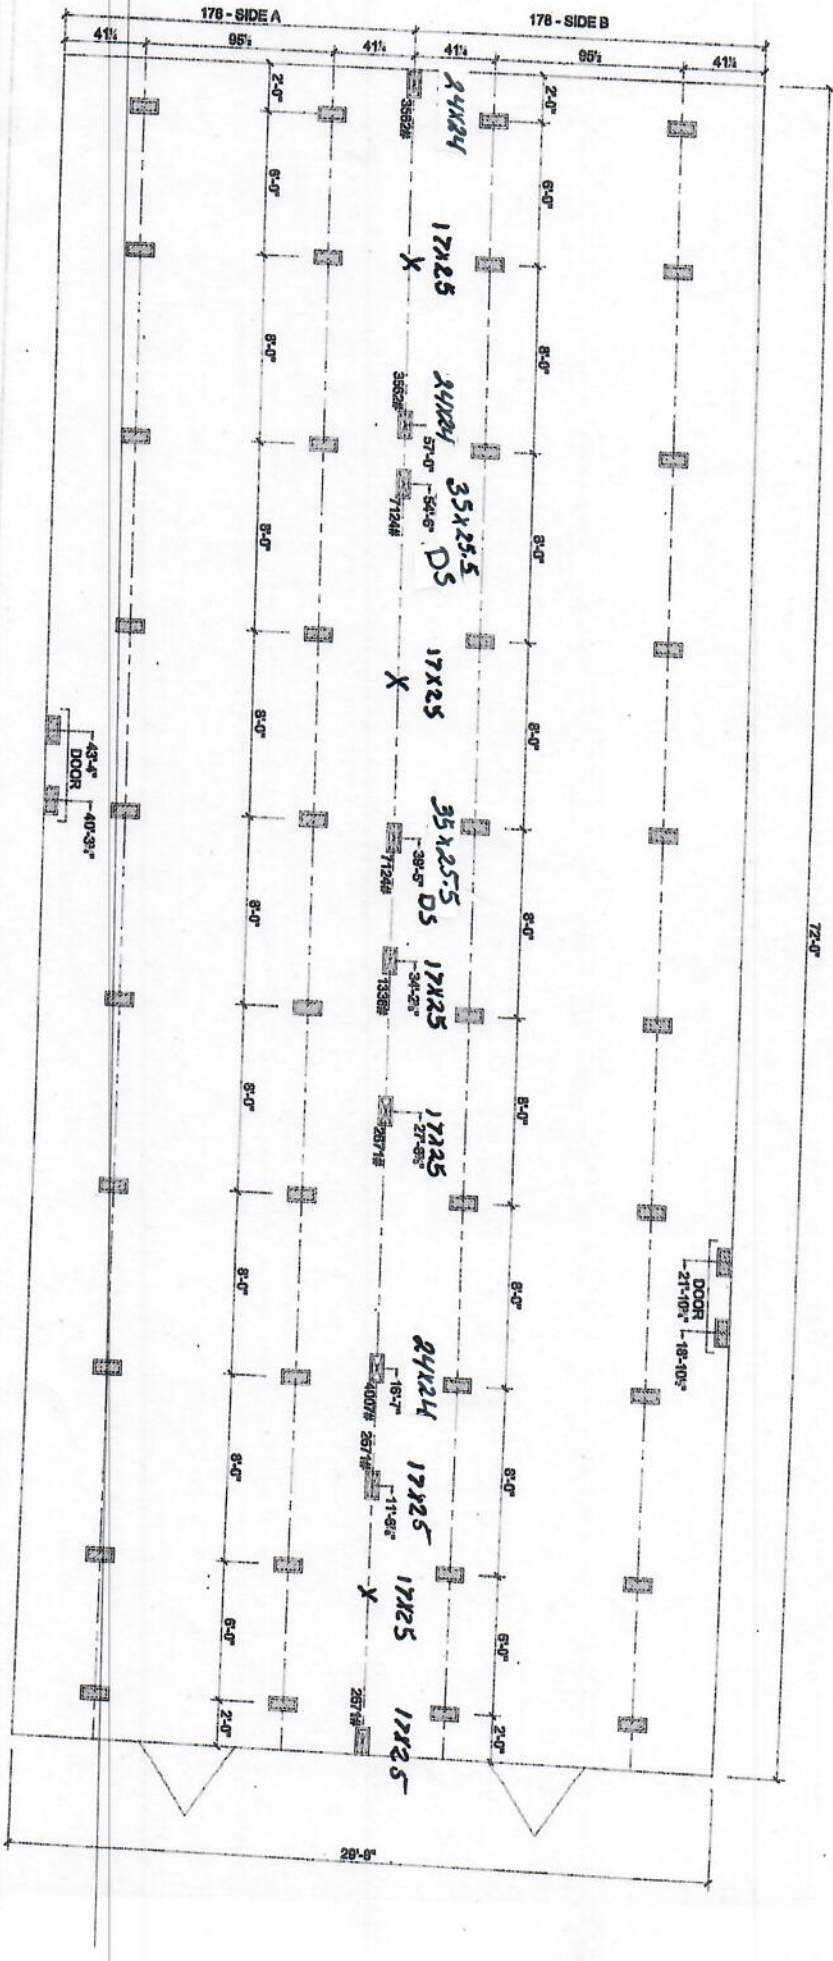

7-5-2016

MARRIAGE LINE OPENING SUPPORT PIERTYP.

SUPPORT PIERTYP

FOUNDATION NOTES:



- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON FND TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes
MODEL: L-3725B - 32 X 76
5-BEDROOM / 3-BATH

- (A) MAIN ELECTRICAL
- (B) ELECTRICAL CROSSOVER
- (C) WATER INLET
- (D) WATER CROSSOVER (IF ANY)
- (E) GAS INLET (IF ANY)
- (F) GAS CROSSOVER (IF ANY)
- (G) DUCT CROSSOVER
- (H) SEWER DROPS
- (I) RETURN AIR (W/OPT. HEAT PUMP OR DUCT)
- (J) SUPPLY AIR (W/OPT. HEAT PUMP OR DUCT)

5K

5K

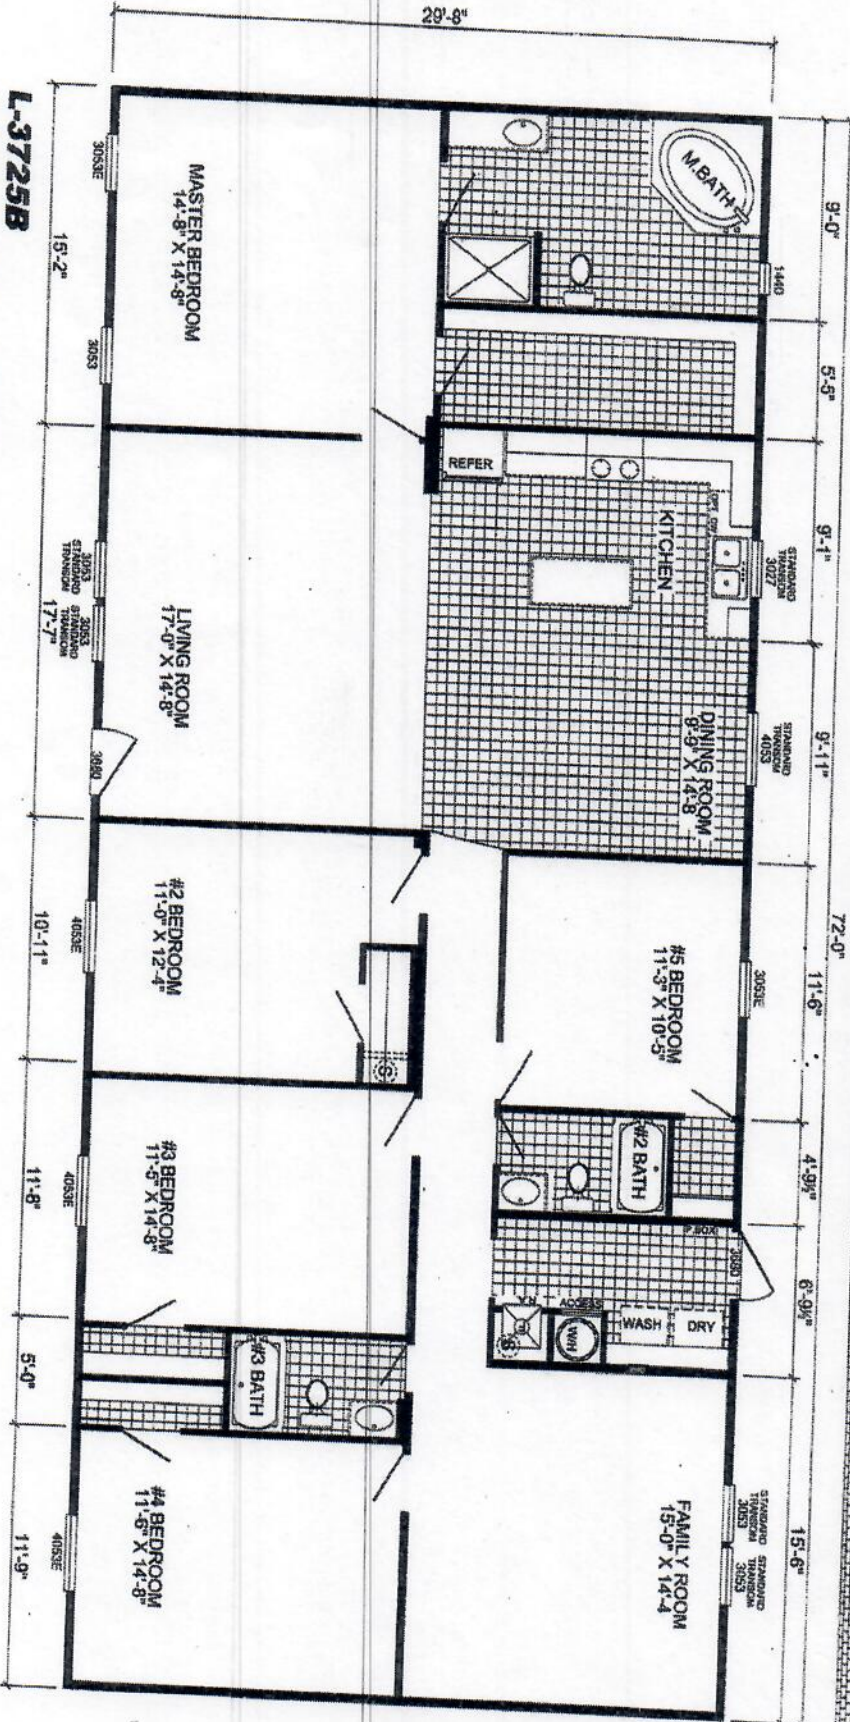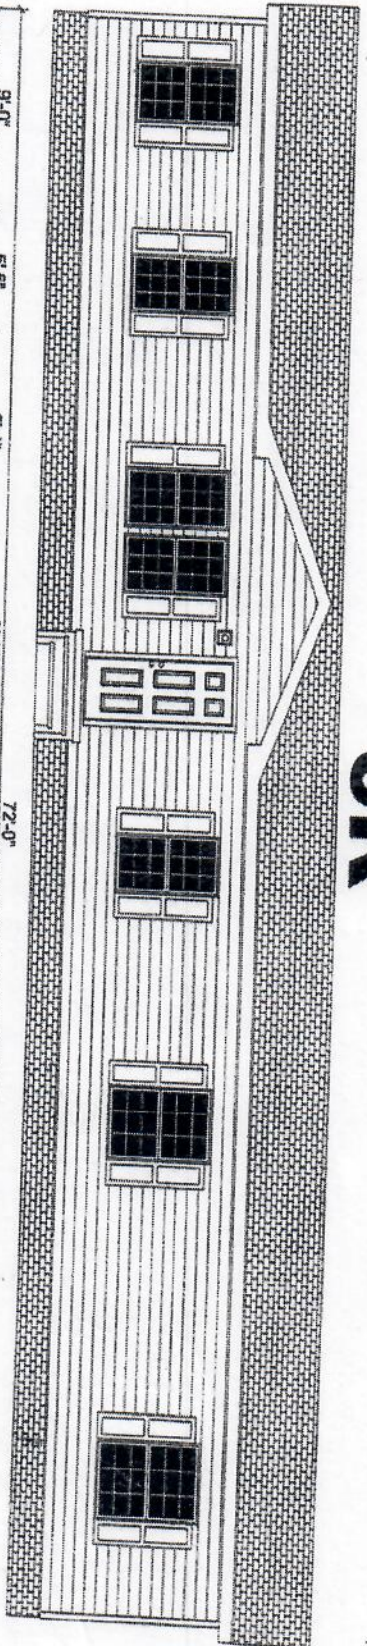

L-3725B

5-BEDROOM / 3-BATH

32 X 76 - Approx. 2136 Sq. Ft.

2-6-2016
 * All room dimensions include closets and square footage figures are approximate.
 * Transom windows are available on optional 9'-0" siderail houses only.
 * Underpinning shown is optional.

Date: 2-22-23

AGENT AUTHORIZATION

I / We DEANNA JOHNSON hereby authorize
James Warren to be my agent. Said agent has my
permission to make any necessary decisions on my behalf concerning the onsite sewage
treatment and disposal system located at

Property ID: 35-55-16-03752-423

Address: 1198 SW Baron Glen
Fort White FL 32038

Property Owner Signature:

[Signature]

Witness Signature:

[Signature]

Date:

2-22-23
