

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT

Order #: 6912	Label #: 127189	Manufacturer: LIVE OAK HOMES	(Check Size of Home)
Homeowner: CARMEN, WALTER		Year Model: 2026	Single _____
Address: 154 SW HARRINGTON ^{GLEW}		Length & Width: 60/64 X 28	Double X _____
City/State/Zip: LAKE CITY, FL 32024		Type Longitudinal System: DT1 6	Triple _____
Phone #:		Type Lateral Arm System: DT1 6	HUD Label #:
Date Installed:		New Home: X Used Home: _____	Soil Bearing / PSF:
Installed Wind Zone: II		Data Plate Wind Zone: II	Torque Probe / in-lbs:
Note:			Permit #:

**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

127189

LABEL #	DATE OF INSTALLATION
DAVID E ALBRIGHT	
NAME	
IH / 1129420 / 1	6912
LICENSE #	ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

Mobile Home Permit Worksheet DW



Application Number: _____ Date: _____

Installer: DAVID AIBRIGT License # 1H-1129420
 Address of home being installed: 154 SW Harrington Gln Lake City FL 32024

Manufacturer: Live Oak Length x width: 28X60/64

NOTE: *if home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home*
 I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials: DA

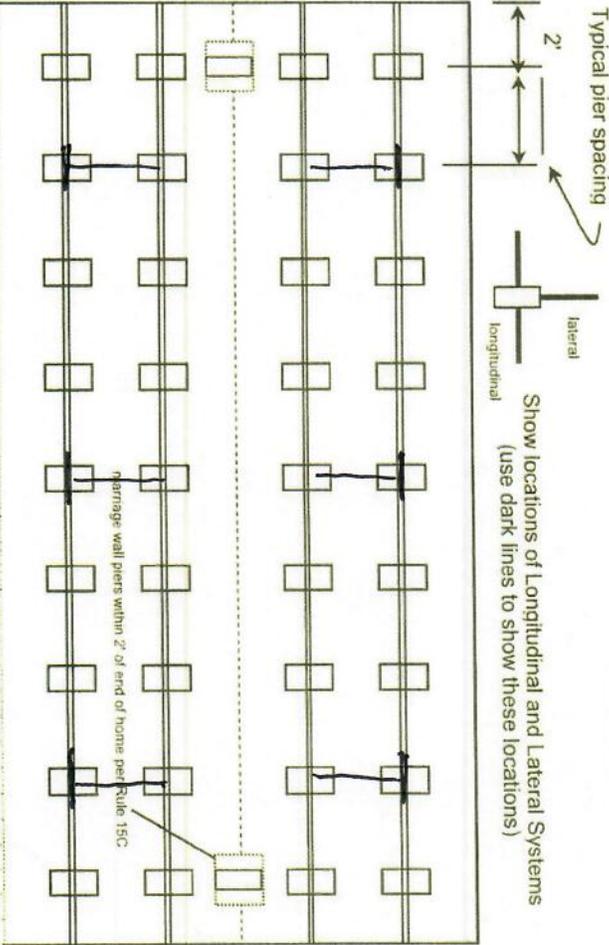

New Home Used Home

Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C

Single wide Wind Zone II Wind Zone III

Double wide Installation Decal # 127/89

Triple/Quad Serial # LOHGA20040996AB

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	Footer size (sq in)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4' 6"	6'	7'	8'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'
2500 psf	7' 6"	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size: 17X25
 Perimeter pier pad size: 16x16
 Other pier pad sizes (required by the mfg.): 17x22, 24x24

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening: _____ Pier pad size: _____
FACTORY DIAGRAM

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
 Manufacturer: OLIVER TECHNOLOGIES
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer: OLIVER TECHNOLOGIES

OTHER TIES

Sidewall Longitudinal Marriage wall Shearwall
 Number: 29
6
7-5' 6-4'
2

Mobile Home Permit Worksheet

Application Number: _____ Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 255 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline the points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.
 _____ Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name DAVID AIRBRIGHT MOBILE HOME SVC
 Date Tested _____

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 64-68

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 70

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 107

Site Preparation

Debris and organic material removed
 Water drainage: Natural Swale Pad Other _____

Fastening multi wide units

Floor:	Type Fastener: <u>LPG</u>	Length: <u>6"</u>	Spacing: <u>18"</u>
Walls:	Type Fastener: <u>SCREW</u>	Length: <u>4"</u>	Spacing: <u>18"</u>
Roof:	Type Fastener: <u>LPG</u>	Length: <u>6"</u>	Spacing: <u>24"</u>

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials _____

Type gasket Pg. 36

Installed: _____
 Between Floors Yes
 Between Walls Yes END UNITS
 Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes Pg. 119
 Siding on units is installed to manufacturer's specifications Yes
 Fireplace chimney installed so as not to allow intrusion of rain water. Yes



Miscellaneous

Skirting to be installed. Yes _____ No <input checked="" type="checkbox"/>	Yes _____ No <input checked="" type="checkbox"/>	N/A <input checked="" type="checkbox"/>	N/A <input checked="" type="checkbox"/>
Dryer vent installed outside of skirting. Yes _____	Yes _____	N/A <input checked="" type="checkbox"/>	N/A <input checked="" type="checkbox"/>
Range downflow vent installed outside of skirting. Yes <input checked="" type="checkbox"/>	Yes _____	N/A <input checked="" type="checkbox"/>	N/A <input checked="" type="checkbox"/>
Drain lines supported at 4 foot intervals. Yes <input checked="" type="checkbox"/>	Yes _____	N/A <input checked="" type="checkbox"/>	N/A <input checked="" type="checkbox"/>
Electrical crossovers protected. Yes <input checked="" type="checkbox"/>	Yes _____	N/A <input checked="" type="checkbox"/>	N/A <input checked="" type="checkbox"/>

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature David Airbright Date _____

THE EARNHARDT

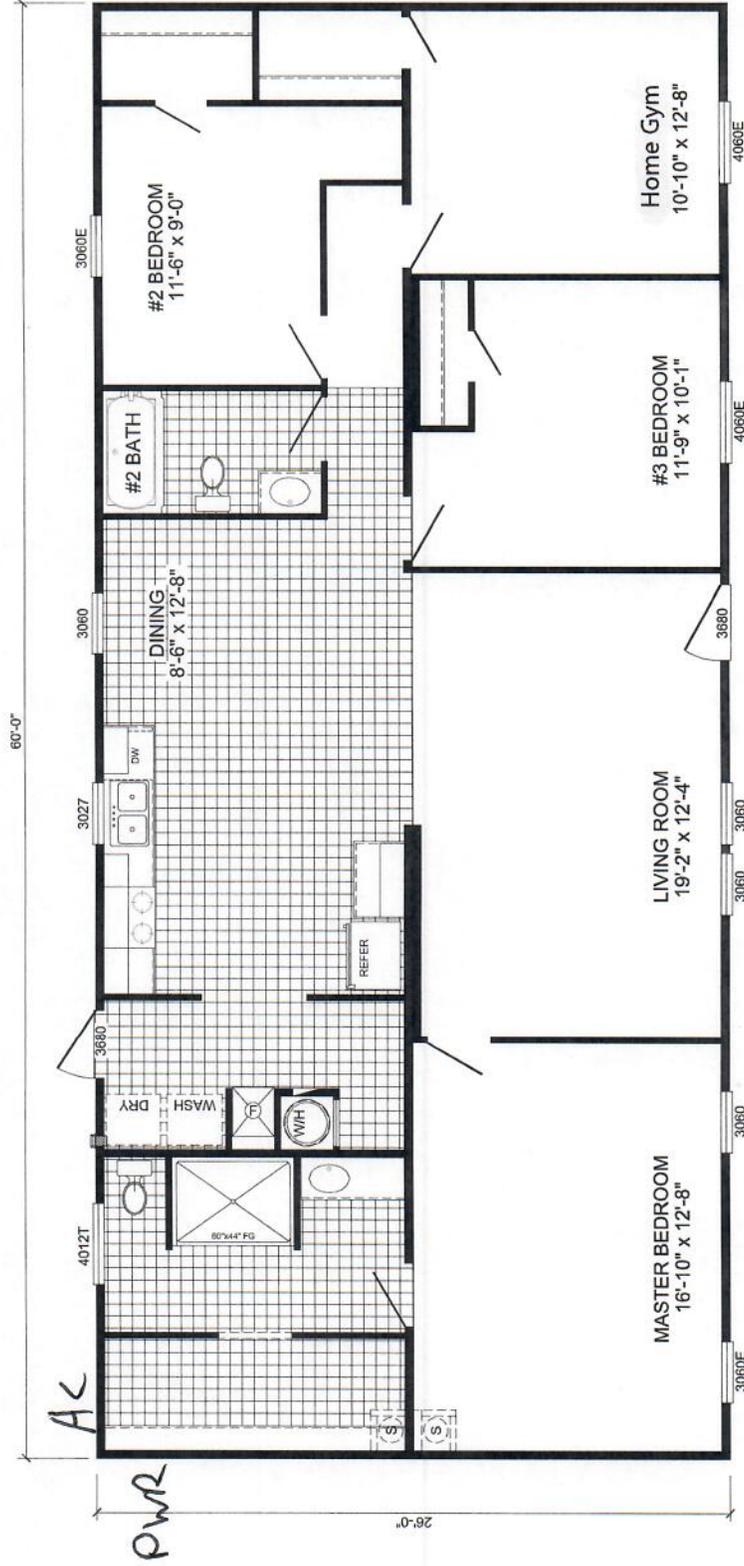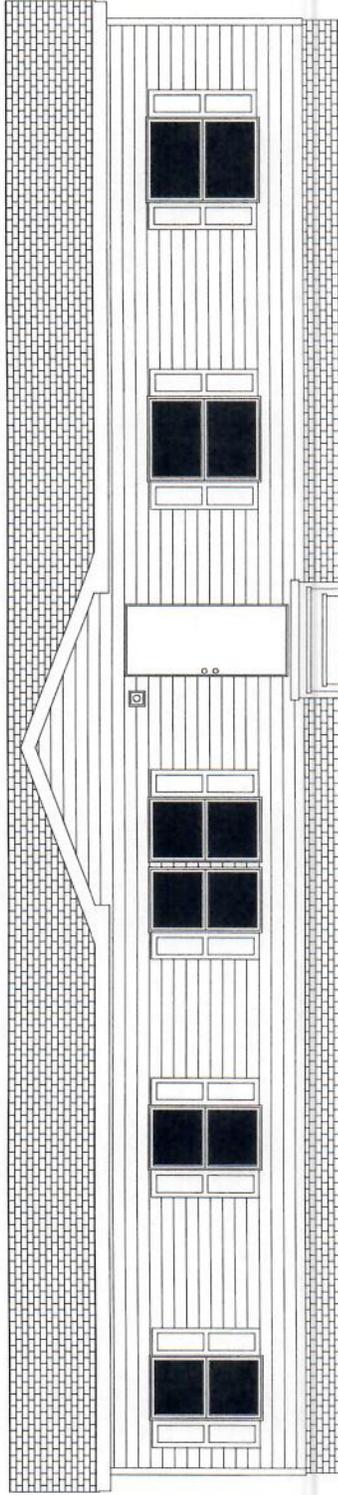


Runner SS

L-2604F - RUNNER SS
3-BEDROOM / 2-BATH
28 x 64 - Approx. 1560 Sq. Ft.

Date: 03/21/24
 * All room dimensions include closets and square footage figures are approximate.
 * Live Oak Homes reserves the right to change product offering at any time.

SW SPARROW TER

**EXISTING DRIVEWAY/
START OF
HARRINGTON GLN**

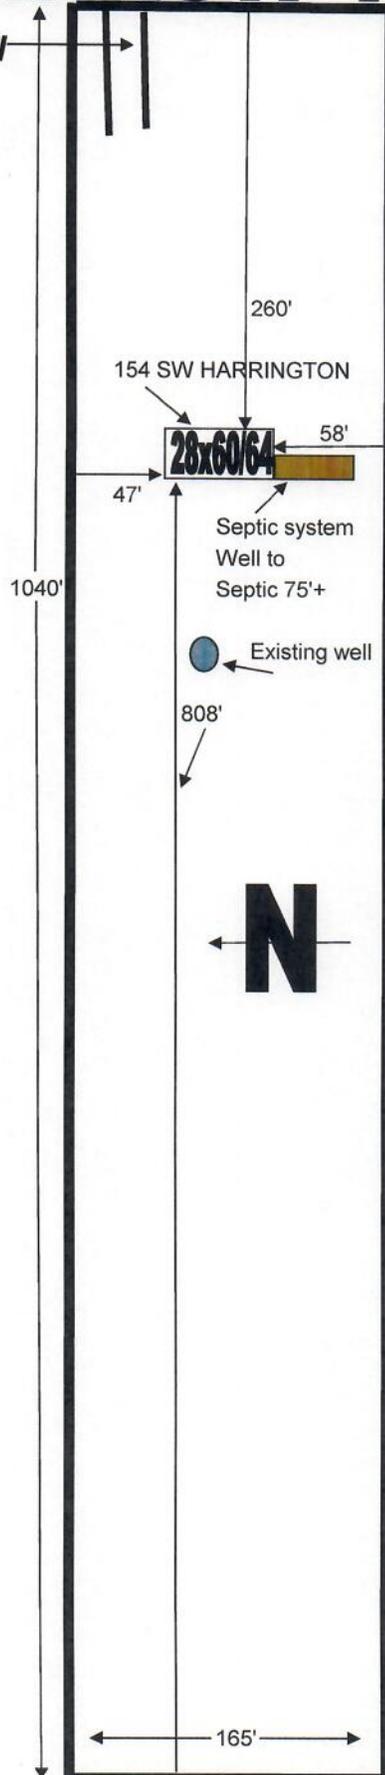

BUYER CARMAN,WALTER
ACREAGE 4

PARCEL ID# 15-4S-16-03023-001
DEALER:STARS & STRIPES 386-365-8549

DATE DRAWN 2/19/2026
