

DATE 07/20/2005

Columbia County Building Permit**PERMIT**

This Permit Expires One Year From the Date of Issue

000023396

APPLICANT KELLY FORD

PHONE 497-2311

ADDRESS P.O. BOX 39

FT. WHITE

FL 32038

OWNER ANNETTE JOHNSON

PHONE 719-6576

ADDRESS 298 NW ROWE COURT

LAKE CITY

FL 32055

CONTRACTOR RONNIE NORRIS

PHONE 752-3871

LOCATION OF PROPERTY

LAKE JEFFREY RD, TL ON NASH, TR ON WOODLAND TERR, TL ON

MACK MARY, TR ROWE CT, LAST SITE ON RIGHT

TYPE DEVELOPMENT MH, UTILITY

ESTIMATED COST OF CONSTRUCTION

.00

HEATED FLOOR AREA

TOTAL AREA

HEIGHT .00

STORIES

FOUNDATION

WALLS

ROOF PITCH

FLOOR

LAND USE & ZONING

A-3

MAX. HEIGHT

Minimum Set Back Requirements:

STREET-FRONT

30.00

REAR

25.00

SIDE

25.00

NO. EX.D.U.

1

FLOOD ZONE

X

DEVELOPMENT PERMIT NO.

PARCEL ID 07-3S-16-02031-001

SUBDIVISION

LOT

BLOCK

PHASE

UNIT

TOTAL ACRES

IH0000049

Culvert Permit No.

Culvert Waiver

Contractor's License Number

Applicant/Owner/Contractor

EXISTING

05-0719-N

BK

N

Driveway Connection

Septic Tank Number

LU & Zoning checked by

Approved for Issuance

New Resident

COMMENTS: ONE FOOT ABOVE THE ROAD

Check # or Cash 11406

FOR BUILDING & ZONING DEPARTMENT ONLY

(footer/Slab)

Temporary Power

Foundation

Monolithic

date/app. by

date/app. by

date/app. by

Under slab rough-in plumbing

Slab

Sheathing/Nailing

date/app. by

date/app. by

date/app. by

Framing

Rough-in plumbing above slab and below wood floor

date/app. by

date/app. by

Electrical rough-in

Heat & Air Duct

Peri. beam (Lintel)

date/app. by

date/app. by

date/app. by

Permanent power

C.O. Final

Culvert

date/app. by

date/app. by

date/app. by

M/H tie downs, blocking, electricity and plumbing

date/app. by

Pool

date/app. by

Reconnection

Pump pole

Utility Pole

date/app. by

date/app. by

date/app. by

M/H Pole

Travel Trailer

Re-roof

date/app. by

date/app. by

date/app. by

BUILDING PERMIT FEE \$

.00

CERTIFICATION FEE \$

.00

SURCHARGE FEE \$

.00

MISC. FEES \$

200.00

ZONING CERT. FEE \$

50.00

FIRE FEE \$

WASTE FEE \$

FLOOD ZONE DEVELOPMENT FEE \$

CULVERT FEE \$

TOTAL FEE 250.00

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only

Zoning Official BK 19.07.05Building Official OK JTH 7-18-05AP# 0507-08Date Received 7/5/05By GPermit # 23396Flood Zone XDevelopment Permit N/AZoning A-3Land Use Plan Map Category A-3

Comments _____

FEMA Map # _____ Elevation _____ Finished Floor _____ River _____ In Floodway _____

☒ Site Plan with Setbacks shown ☒ Environmental Health Signed Site Plan ☐ Env. Health Release☐ Well letter provided ☒ Existing Well see address

Revised 9-23-04

▪ Property ID 7-3-16-02031-001 Must have a copy of the property deed▪ New Mobile Home ☒ Used Mobile Home _____ Year 2005▪ Subdivision Information N/A▪ Applicant DALE BURD Phone # 997-2311▪ Address 296 NW ROWIE CT, L.C., FL 32055▪ Name of Property Owner Annette Johnson Phone# 719-6576▪ 911 Address Applied for 298 NW Rowe Ct. L.C. 32055▪ Circle the correct power company - FL Power & Light - Clay Electric per DALE
(Circle One) - Suwannee Valley Electric - Progressive Energy▪ Name of Owner of Mobile Home SAME Phone # _____


▪ Address _____

▪ Relationship to Property Owner SAME▪ Current Number of Dwellings on Property 1▪ Lot Size 618 x 1200 Total Acreage 15▪ Do you : Have an Existing Drive or need a Private Culvert Permit or a Culvert Waiver Permit▪ Driving Directions LAKE JEFFERY, Left on NASH, Right on
WOODLAND TERR, Left on MACK MARY, Rt on ROWIE CT
Follow SITE on Right
1st▪ Is this Mobile Home Replacing an Existing Mobile Home YES▪ Name of Licensed Dealer/Installer Rowanie Norris Phone # 752 3871▪ Installers Address 1004 SW Chard Ter▪ License Number IH 0000049 Installation Decal # 285848

Following Bladderman

harts

TOTAL

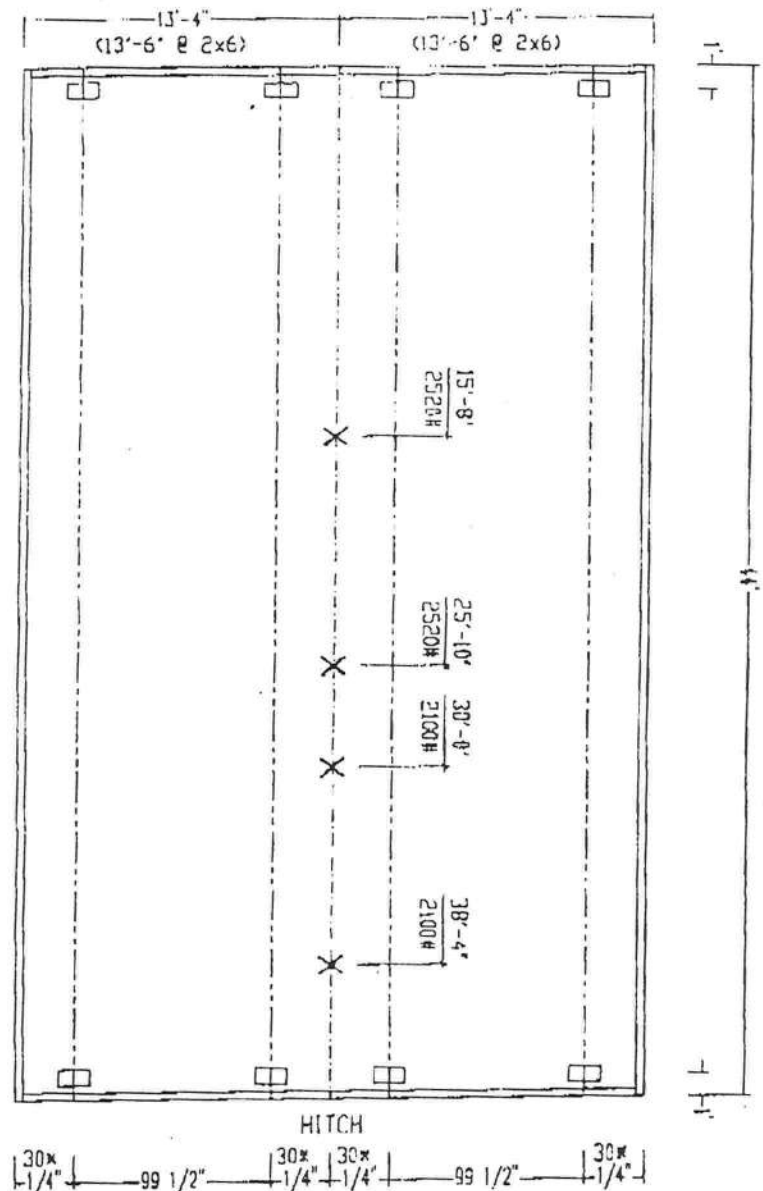

FLORIDA ONLY PIER POINT LAYOUT (PIERS & I-BEAM & CENTERLINE WITHOUT PERIMETER FOUNDATION)

20 PSF ROOF ZONE

X OCCUPY SUPPORTS - SEE ABOVE DIAGRAM FOR LOCATIONS & LOAD REQUIREMENTS & 2014 ROOF ZONE. SEE TABLE 4 OF INSTALLATION MANUAL FOR FOOTING SIZES.
 I-BEAM PIER SUPPORTS - 8' MAX SPACING - SEE INSTALLATION MANUAL TABLE 2 FOR SPACING AND TABLE 4 FOR FOOTING SIZES.
 NOTE: CONTACT MANUFACTURING DIVISION FOR LOCATION OF OPTIONAL PANE DOORS OR OTHER LARGE OPENINGS.

DIVISIONS			REVISIONS			BOX LENGTH			DESCRIPTION			DRAWING NUMBER		
111	344	552												
112	344	553												
115	345	571												
125	355	591												
131	528	812												
143	531													
163	X 535													
171	536													
181	538													
						44'-0"			4428-30K-1 3/48-CATH			7270-CT		

SKYLINE

DRAWN BY: VM
 DATE: 06/20/2012
 SHEET: 1 OF 1

DRAWING NUMBER: 7270-CT

These worksheets must be completed and signed by the installer.
Submit the originals with the packet.

COLUMBIA COUNTY PERMIT WORKSHEET

Page 1 of 2

Installer

Korie Norris

License #

TH000099

911 Address where home is being installed

296 NW RIVER CT
LE FL 32055

Manufacturer

SKYLINE

Length x width

44x26

NOTE:

If home is a single wide fill out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Installer's initials

SW

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'6"	6'	7'	8'	9'	10'
2000 psf	6'	8'	9'	10'	11'	12'
2500 psf	7'6"	9'	10'	11'	12'	13'
3000 psf	8'	10'	11'	12'	13'	14'
3500 psf	8'	10'	11'	12'	13'	14'

Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

17X22

Perimeter pier pad size

16X16

Other pier pad sizes (required by the mfg.)

16X16

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

820X20617X22416X16

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer

ANCHORS

4 ft5 ft


FRAME TIES

within 2' of end of home
spaced at 5' 4" oc

OTHER TIES

Sidewall
Longitudinal
Marriage wall
Shearwall

Number

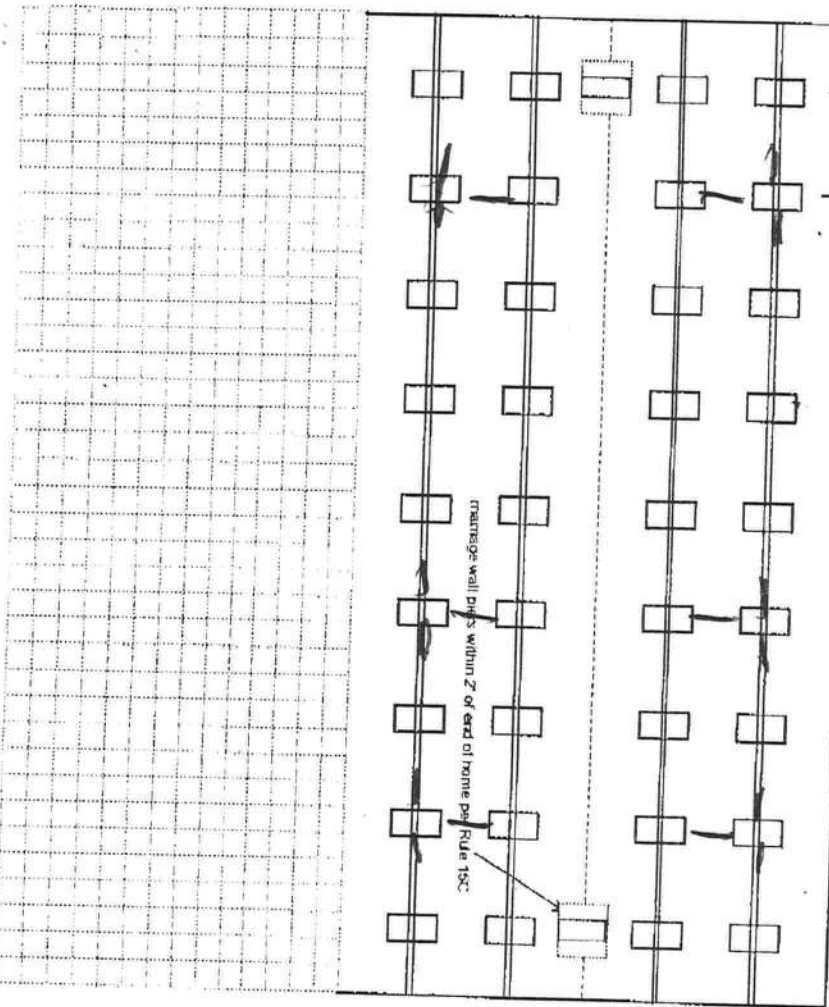8244

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 500 psf or check here to declare 1000 lb. soil without testing.

x 500x 500x 500

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 500x 500x 500

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5" anchors without testing 4. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewall locations. 1 underground 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's Initials MM

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Kevin Adams

Date Tested

7-1-05

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg.

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg.

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg.

Site Preparation

Debris and organic material removed ✓
Water drainage: Natural ✓ Swale ✓ Pad ✓ Other ✓

Fastening multi wide units

Floor: Type Fastener: LP Length: 6 Spacing: 24" on center
Walls: Type Fastener: LP Length: 6 Spacing: 24" on center
Roof: Type Fastener: LP Length: 6 Spacing: 24" on center
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials MMType gasket Pg. MM

Installed: ✓
Between Floors: Yes ✓
Between Walls: Yes ✓
Bottom of ridgebeam: Yes ✓

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ✓ Pg.
Siding on units is installed to manufacturer's specifications. Yes ✓
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ✓

Miscellaneous

Skirting to be installed. Yes ✓ No ✓
Dryer vent installed outside of skirting. Yes ✓ N/A ✓
Range downflow vent installed outside of skirting. Yes ✓ N/A ✓
Drain lines supported at 4 foot intervals. Yes ✓ N/A ✓
Electrical crossovers protected. Yes ✓ Other: ✓

Installer verifies all information given with this permit worksheet is accurate and true based on the

manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature Kevin AdamsDate 7-1-05

SET-UP PROCEDURES (Continued)

DOUBLE-WIDE INTERCONNECTION

The procedure for connecting the homes is as follows.

Remove the temporary closure materials (polyethylene and batten strips) and position the halves as close together as possible in the final desired location. Do not remove temporary beam supports until step 7 has been completed.

Move the first section of home into its desired position. Jack and level it in the same manner as described for a single section home. Skyline Corp. recommends, if possible, the heavy half be blocked and leveled first as it is easier to lift and roll the light half and fit into place.

Install sill sealer insulating material (provided) around the home (to the ridge beam at the ceiling panel line), endwalls and floor mating line. Fasten sill sealer with staples or nails. See figure 5-8A.

Slide the two halves together with rolling and jacking equipment. Care must be taken during rolling and jacking operations to avoid overstressing structural members. With the halves together at the floor, align the floors at the ends of the home. It is better to have a minor misalignment under the eave where it cannot be seen and will not cause a problem, than a small misalignment that will be observed in the interior of the home.

With the home aligned at the floor and supported by its foundation, join the floors using $3/8" \times 3"$ (4-1/2" lags with double perimeter joist) lag screws 2 to 3 feet on center. The centerline gap at the floor should be a maximum of $3/16"$. See the procedures outlined on page 19 to level the home and check supports and footings with tables 2 and 3.

To obtain access into the ceiling cavity to bolt or alternatively lag screw the ridge beam sections together, fold back the underlayment paper and remove the 16" wide sheathing panel(s) at the peak. Note that the shingles may not have been installed on one or both halves, at the 16" wide area at

the peak. If one side is shingled, it is intended that the beam be lag screwed together. If neither side is shingled, the beam may be lag screwed or bolted together. Bolts to be $3/8" \times 4-1/2"$ at 48" o.c. with 3 additional bolts at 3" o.c. over interior beam supports. Lag screws to be $3/8" \times 5"$ at 24" o.c. with 6 additional lag screws at 3" o.c. over interior beam supports. (If marriage walls and ridge beam halves have been plated with $3/8"$ sheathing, then the bolts/lags must be increased in length by $3/4"$ to $5-3/4"$.) Pre-drill $1/4"$ pilot holes for the lag screws at 1-1/2" down from the top of the beam and with a maximum offset from the horizontal of 45 degrees. A gap between beam halves up to 1" is allowable. Gaps larger than $1/2"$ must be filled with plywood or lumber shims. For $1/2"$ max gaps, increase fastener length $1/2"$. For 1" max. gaps increase fastener length $1-1/4"$. See Fig. 5-7.

7. Prior to interconnecting the ridge beam halves, examine the ridge beam ends. Should there be a slight misalignment, it can be eliminated by placing a jack under the low side of the main beam on one half and use the jack to raise the beam. The alignment can be held by properly bolting or lag screwing the beam halves together. See Fig. 5-8.

8. Place additional pier supports at the centerline at the interior column locations marked on the floor with indicator straps or paint (see Figure 5-3 and 5-4 and Table 3). Skyline Corp. provides pier location diagrams for all multiwide models. These diagrams show the required locations of piers and are very useful in determining pier placement prior to taking receipt of home. Additional piers are required each side of exterior doors and sidewall openings greater than 4' in width. See Table 3A for these pier load requirements.

9. Toe-nail endwall centerline studs together using 16d nail: 10" o.c.

10. If home has double mating walls, then fasten the mating wall columns together with #8 x 4" screws 16" o.c. See Figure 5-7A.

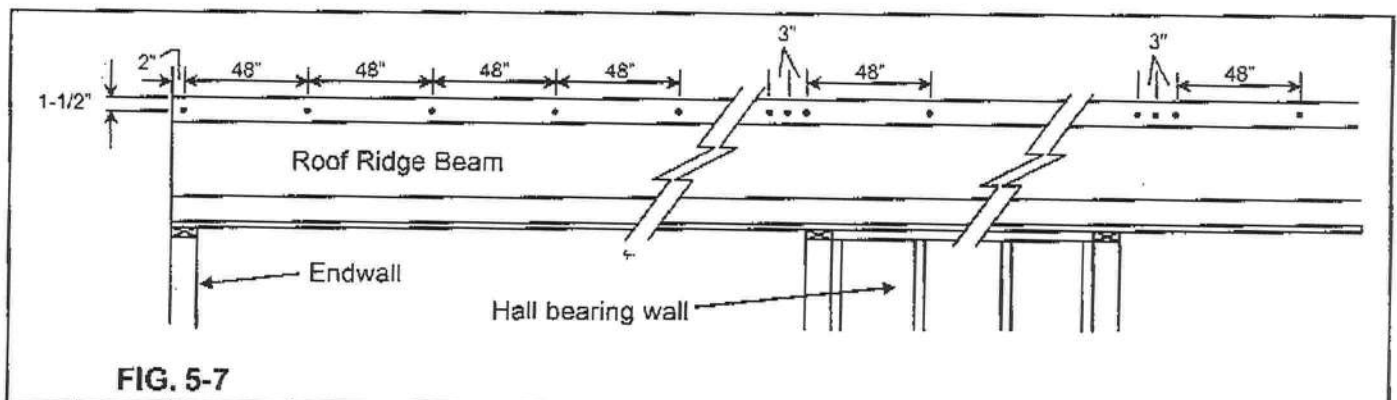


FIG. 5-7

APPROVED
PFS Corporation
Madison WI
01/31/05
HUD Manufactured
Home
Construction &
Safety Standard

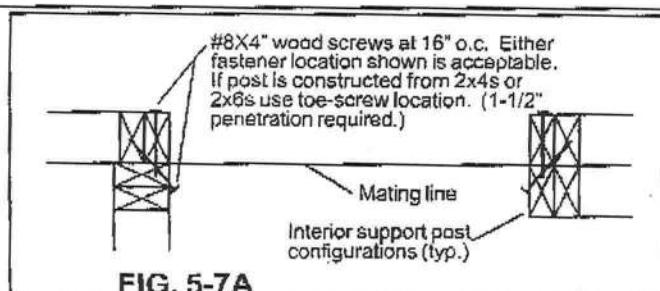


FIG. 5-7A

SET-UP PROCEDURES (Continued)

DOUBLE-WIDE INTERCONNECTION (Continued)

NOTE: IT IS IMPORTANT TO HAVE ROOF/CEILING SECTIONS FLUSH AT MATING LINE PRIOR TO FASTENING OF RIDGE BEAM HALVES. IF THEY ARE NOT FLUSH, THEN THE LOW SIDE SHOULD BE RAISED BY JACKING WITH A WOOD POST OR STEEL PIPE WITH A WOOD OR METAL PAD AT THE CEILING. PLACE THE BASE OF THE JACK ACROSS THE FLOOR MATING LINE SO THAT IT RESTS ON BOTH HALVES. JACK AGAINST CEILING ONLY IN AREAS WHERE THERE IS NO MARRIAGE WALL.

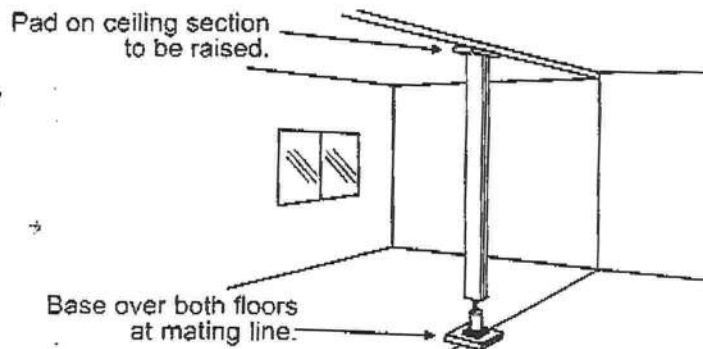


FIG. 5-8


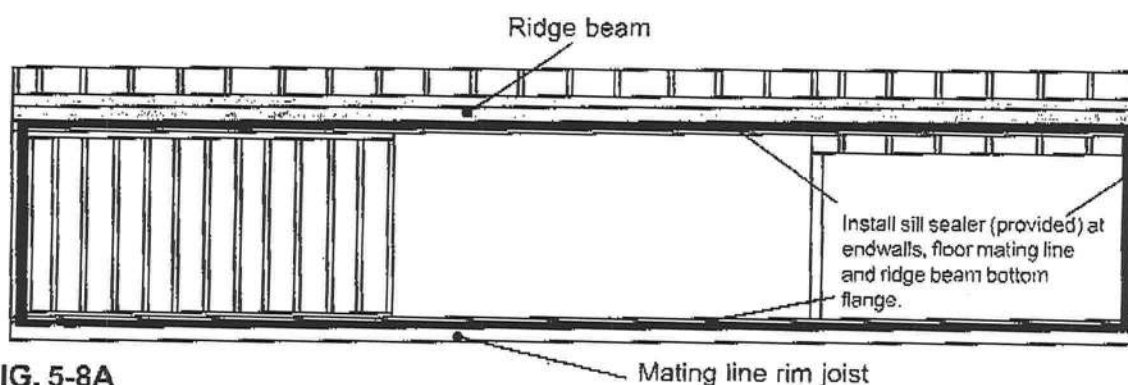


FIG. 5-8A

ATTACHMENT OF GYPSUM PANELS AT DOUBLE-WIDE CENTERLINE

Some multiple-wide units will have a gypsum panel left off at the centerline for field attachment. Fasten the factory supplied gypsum wallboard panel(s) at the center of the endwalls after the units have been attached. Fasten the panel(s) to wall framing as described in figure 5-8B below.

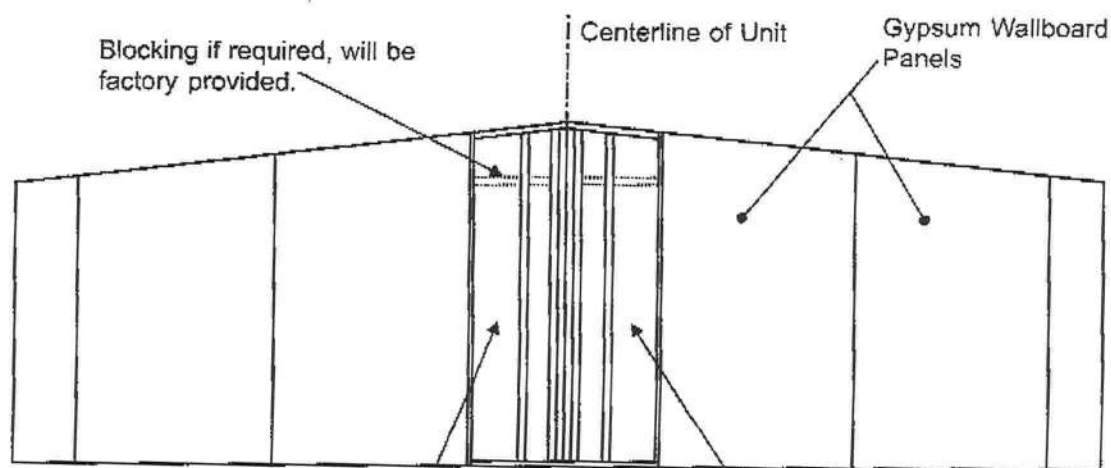

Fasten 5/16" gypsum panels to framing with 3/16"x1" staples or 1" washer head screws 6" o.c. around perimeter & 12" o.c. in the field. Fasten 1/2" gypsum w/1-5/8" x 0.099" gypsum nails 8" o.c. or 1-1/4" type 'w' drywall screws 12" o.c. If gypsum is overlaying 3.6mm luan, then increase fastener lengths 1/4". Gypsum may be glued to framing (optional) in combination w/ mechanical fastening above. Use an approved glue.

4' for field installed gyp. Panel.

INTERIOR VIEW

Center gypsum panel is field installed. All required gypsum panels, fasteners and adhesives are supplied by the factory.

FIG. 5-8B

AFFIDAVIT

I Certify that the following described mobile home being placed on the referenced parcel is not a Wind Zone 1 mobile home.

Customer Name: ANNETTE JOHNSON

Property ID: Sec: 7 Twp: 3 Rge: 16 Tax Parcel No: 02031-601


Lot: NA Block NA Subdivision: NA

Moible Home Year/Make: 2005 Size: 26'8" x 44

Ronnie Norris
Signature of Mobile Home Installer

Sworn to and subscribed before me this 5th day of July, 2005

By Ronnie Norris



Notary's name printed/typed

Rebecca L. Gallina
Notary Public, State of Florida
Commission No. DD 253343
Personally Known: ✓
Id Produced (type) _____

MOBILE HOME INSTALLER AFFIDAVIT

As per Florida Statutes Section 320.8249 Mobile Home Installers License:

Any person who engages in mobile home installation shall obtain a mobile home Installer's license from the Bureau of Mobile Home and Recreational Vehicle Construction of the Department of Highway Safety and Motor Vehicles pursuant to this section. Said license shall be renewed annually, and each licensee shall pay a fee of \$150.00.

I, RONNIE NORRIS, license number IH 0000049
Please Print

Do hereby state that the installation of the manufactured home for Mr. Bradon R. Ford
1004 SW 2nd St. Ft. Rd at 296 NW Rowlett Ct, Lc, Fl, 32055
Applicant
911 Address


will be done under my supervision.

Ronnie Norris
Signature

Sworn to and subscribed before me this 5th day of July,
2005.

Notary Public: Rebecca L. Gallina
Signature

My Commission Expires:




LETTER OF AUTHORIZATION TO PULL PERMITS

I, Ronnie Works, DO HEREBY GRANT
Alfredson Rocky Ford, AUTHORIZATION TO PULL THE NECESSARY
PERMITS REQUIRED FOR THE DELIVERY AND SET OF A MANUFACTURED
HOME IN Columbia COUNTY, FLORIDA.


THIS FOREGOING INSTRUMENT WAS ACKNOWLEDGED BEFORE ME THIS
5 DAY OF July, 2005 BY _____
Ronnie Norris, WHO IS PERSONALLY KNOWN TO ME.

STATE OF FLORIDA
COUNTY OF Columbia

Rebecca L. Hallina
NOTARY PUBLIC



Permit Application Number 03-01191

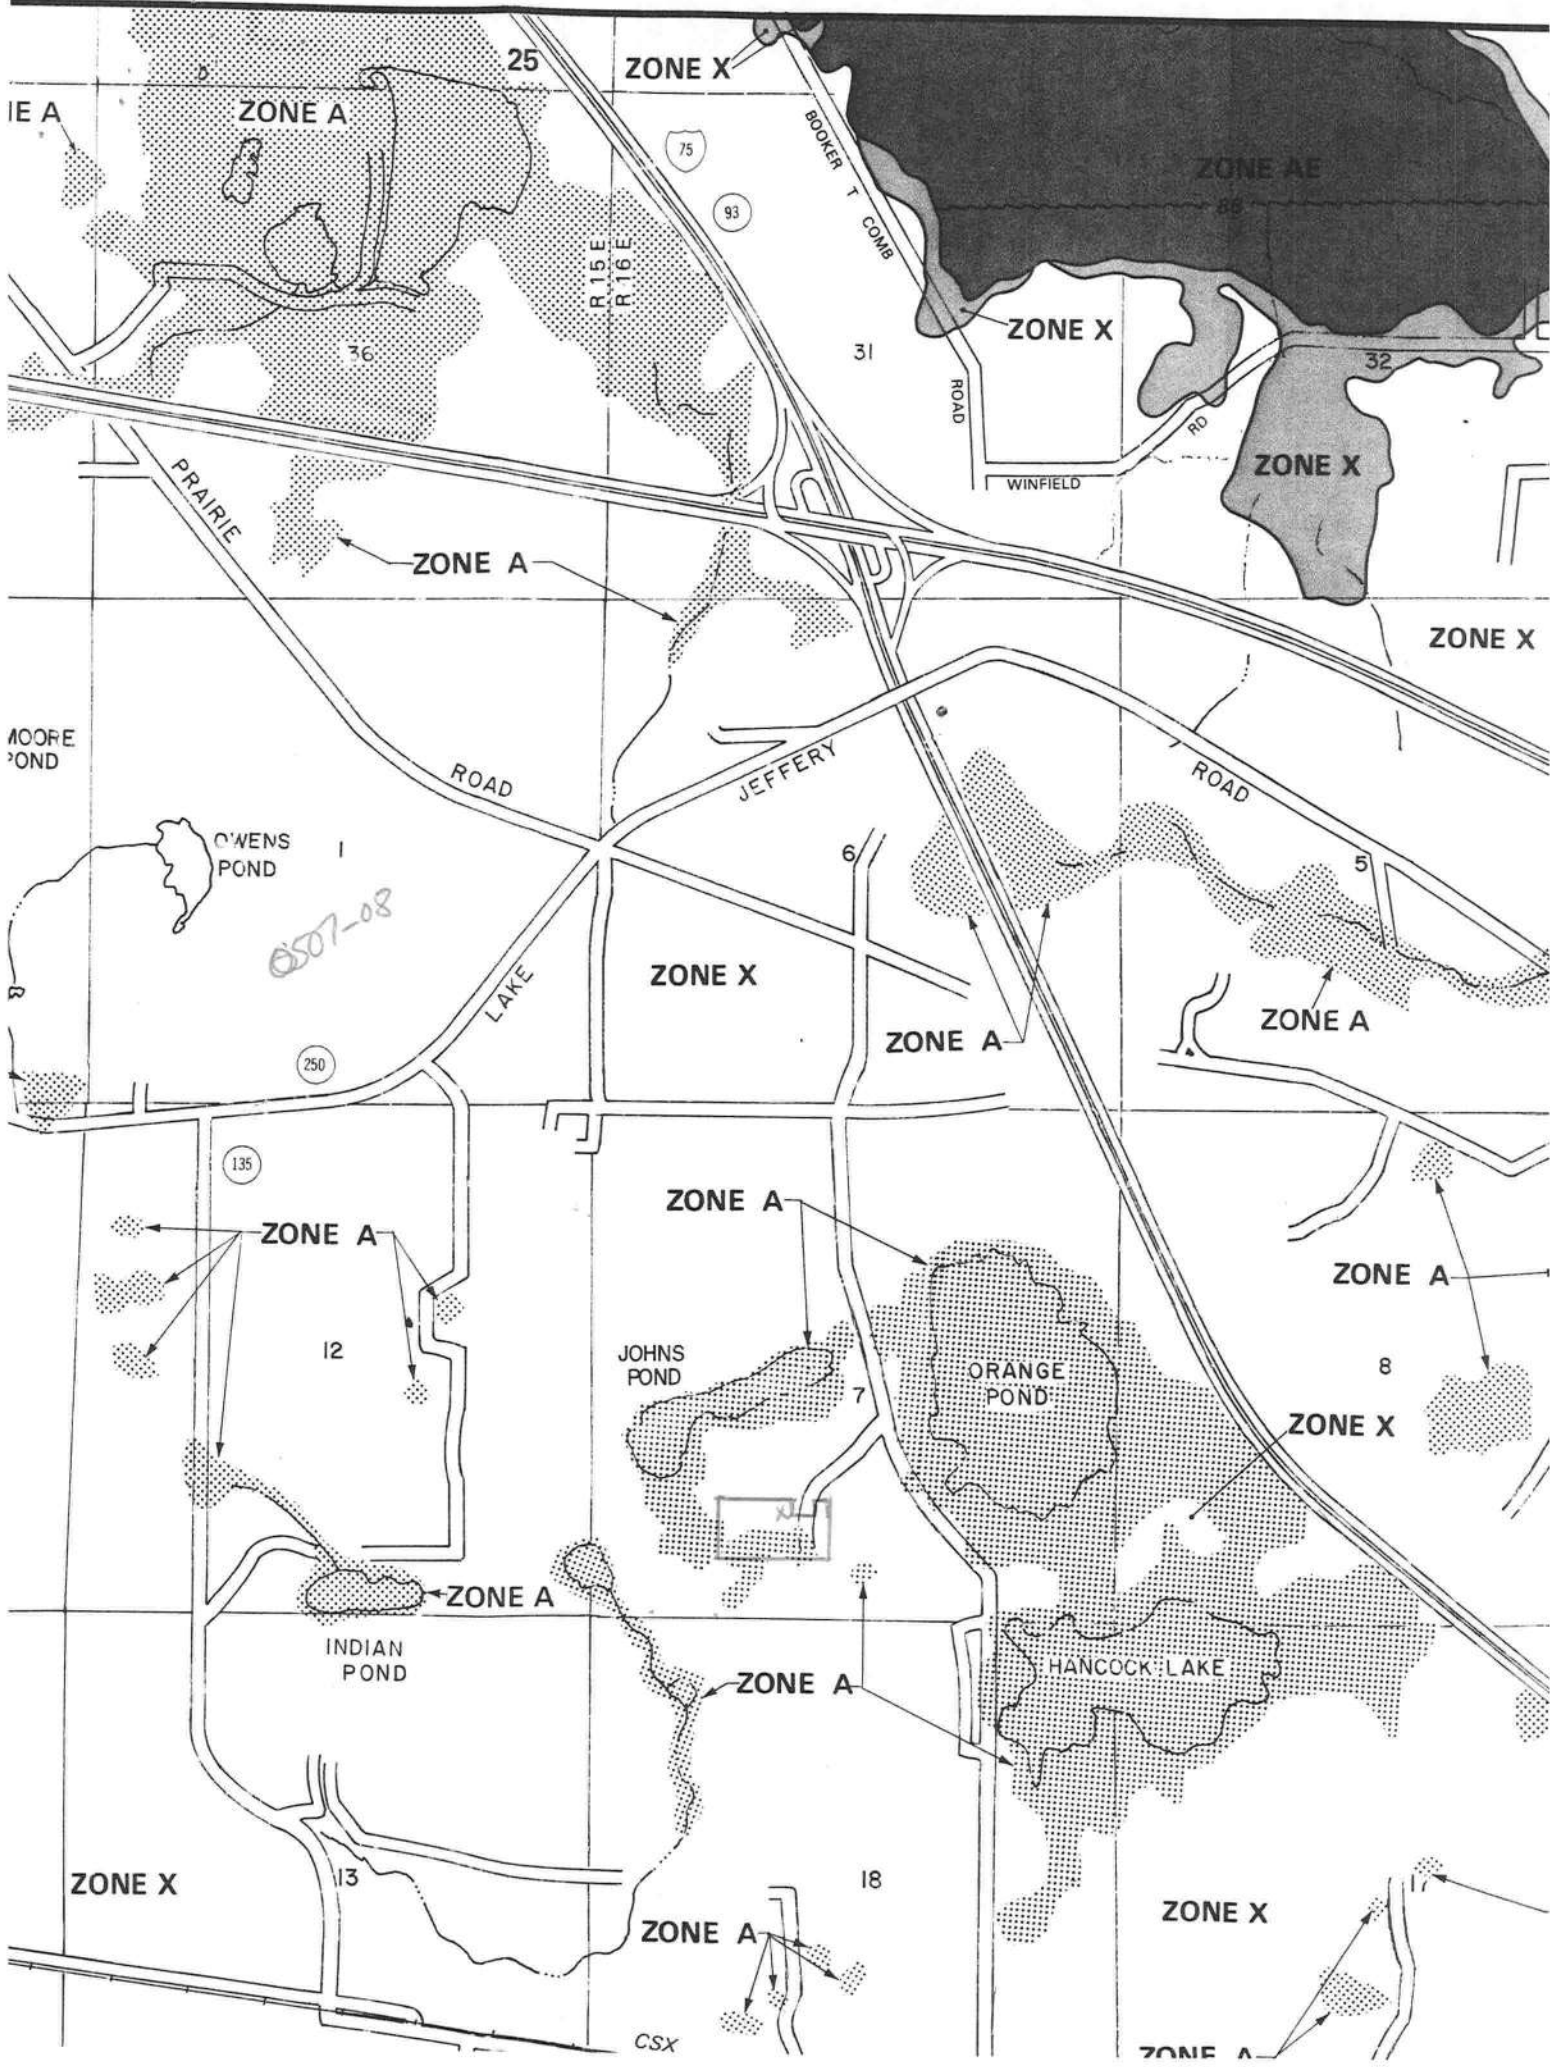

PURCHASE AGREEMENT

SHOWCASE HOMES

DIRECT

DATE OF BIRTH

HIM:

HER:

P. O. Box 2736 • Hwy. 252 S. - Pinemount Road
Lake City, FL 32056
386-758-9538 Office • 386-758-6889 Fax
Toll Free: 1-888-313-2899

DRIVER'S LICENSE

HIM:

HER:

Locally Owned and Operated

SOLD TO: <u>Jerry G. & Annette R. Johnson</u>		PHONE: <u>386-719-6576</u>		DATE	
ADDRESS: <u>296 NW Rowe Ct, LK. City, FL 32055</u>		COUNTY: <u>Columbia</u>		SALESMAN: <u>Kent G.</u>	
Subject to the Terms and Conditions Stated on Both Sides of this Agreement Seller Agrees to Sell and the Purchaser Agrees to Purchase the Following Described Property:					
MAKE: <u>Skyline</u>	MODEL: <u>Key Largo</u>	B. ROOMS: <u>3</u>	FLOOR SIZE: <u>L. 44 W. 26</u>	HITCH SIZE: <u>L. 48 W. 26</u>	STOCK NUMBERS
SERIAL NUMBER: <u>05-61-0430 TA/B</u>	<input checked="" type="checkbox"/> NEW <input type="checkbox"/> USED	COLOR	PROPOSED DELIVERY DATE	KEY NUMBERS	HUD label number
OPTIONAL EQUIPMENT, LABOR AND ACCESSORIES			PRICE OF UNIT \$ <u>46,995.00</u>		
<u>Set up</u> <u>3 ton heat pump</u> <u>Standard vinyl skirting</u> <u>2 code steps</u> <u>nothing else follows</u>			OPTIONAL EQUIPMENT		
			COST OF SET-UP PARTS		
			SUB-TOTAL <u>46,995.00</u>		
			SALES TAX <u>2870.00</u>		
			TAG & Fees NON-TAXABLE ITEMS <u>275.15</u>		
VARIOUS FEES AND INSURANCE			1. CASH PRICE \$ <u>50,140.15</u>		
			TRADE-IN ALLOWANCE \$		
			LESS BAL. DUE ON ABOVE \$		
			NET ALLOWANCE \$ <u>10,028.00</u>		
			CASH DOWN PAYMENT \$		
			CASH AS AGREED SEE "REMARKS"		
			2. LESS TOTAL CREDITS		
			3. UNPAID BALANCE OF CASH SALE PRICE \$ <u>40,112.15</u>		
<p>Title to said equipment shall remain in the Seller until the agreed purchase price therefor is paid in full <input type="checkbox"/> in cash or by the execution of a <input type="checkbox"/> Retail Installment Contract, or a Security Agreement and its acceptance by a financing agency; thereupon title to the within described unit passes to the buyer as of the date of either full cash payment or on the signing of said credit instruments even though the actual physical delivery may not be made until a later date.</p> <p>IT IS MUTUALLY UNDERSTOOD THAT THIS AGREEMENT IS SUBJECT TO NECESSARY CORRECTIONS, AND ADJUSTMENTS CONCERNING CHANGES IN NET PAYOFF ON TRADE-IN TO BE MADE AT THE TIME OF SETTLEMENT.</p> <p>S.S.# <u>24117019654</u> Name <u>Jerry G. Johnson</u></p> <p>S.S.# <u>26313217542</u> Name <u>Annette R. Johnson</u></p> <p>There is no assurance a mobile home can remain level when placed, upon any surface other than of blacktop or concrete.</p> <p>Purchasers certify that the matter printed on the back hereof has been read and agreed to as a part of this agreement the same as though it were printed above the signatures; that buyers are of statutory age or older; or have been legally emancipated; that the within described merchandise, the optional equipment and accessories thereon and, insurance if included, has been voluntarily purchased. The property being traded in is free from all encumbrances whatsoever, except as noted above. Purchaser agrees each paragraph and provision of this contract on both front and back is severable; if one portion thereof is invalid the remaining portion shall, nevertheless, remain in full force and effect.</p>					
BALANCE CARRIED TO OPTIONAL EQUIPMENT \$					
DESCRIPTION OF TRADE-IN		YEAR			
MAKE	MODEL	BEDROOMS	SIZE		
		X			
TITLE NO	SERIAL NO	COLOR			
AMOUNT OWING TO WHOM					
TRADE-IN DEBT TO BE PAID BY <input type="checkbox"/> DEALER <input type="checkbox"/> CUSTOMER					

SHOWCASE HOMES

DEALER

Not Valid Unless Signed and Accepted by an Officer of the Company

I, OR WE, HEREBY ACKNOWLEDGE RECEIPT OF A COPY OF THIS ORDER

SIGNED X

PURCHASER


7216CT/4428 (1,119 SQ. FT.) 2BEDROOM - 2BATHS - CATHEDRAL THRU-OUT



ANNE K. THOMPSON

Red 77-0

JUL 05 2005

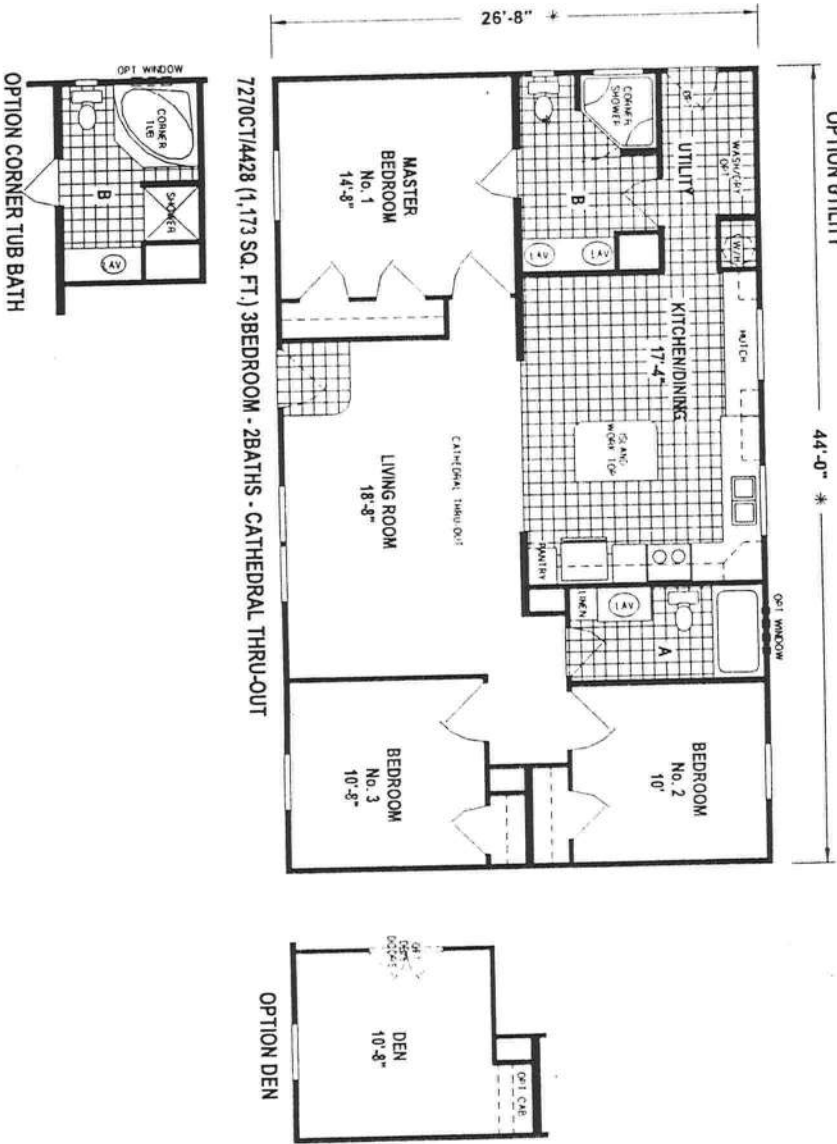

7270CT/4428 (1,173 SQ. FT.) 3BEDROOM - 2BATHS - CATHEDRAL THRU-OUT

**COLUMBIA COUNTY
OFFICE**

M/H OCCUPANCY

COLUMBIA COUNTY, FLORIDA

Department of Building and Zoning Inspection

This Certificate of Occupancy is issued to the below named permit holder for the building and premises at the below named location, and certifies that the work has been completed in accordance with the Columbia County Building Code.

Parcel Number 07-3S-16-02031-001

Building permit No. 000023396

Permit Holder RONNIE NORRIS

Owner of Building ANNETTE JOHNSON

Location: 298 NW ROWE COURT, LAKE CITY, FL 32055

Date: 08/09/2005



Tony Dick

Building Inspector

**POST IN A CONSPICUOUS PLACE
(Business Places Only)**
