

DATE 06/05/2009

Columbia County Building Permit

PERMIT

This Permit Must Be Prominently Posted on Premises During Construction

000027857

APPLICANT CINDY MOBLEY PHONE 850.510.9857
ADDRESS 122 SWEETBAY COURT LAKE CITY FL 32024
OWNER TIMBERLANE MHP -(CINDY MOBLEY -MH) PHONE 850.510.9857
ADDRESS 122 SW SWEETBAY COURT LAKE CITY FL 32024
CONTRACTOR ANDREW HALL PHONE 352.493.0705
LOCATION OF PROPERTY SR. 247-S TO TROY RD,TR 1 1/2 MILES ON THE R.
TYPE DEVELOPMENT M/H/UTILITY ESTIMATED COST OF CONSTRUCTION 0.00
HEATED FLOOR AREA TOTAL AREA HEIGHT STORIES
FOUNDATION WALLS ROOF PITCH FLOOR
LAND USE & ZONING RR MAX. HEIGHT
Minimum Set Back Requirments: STREET-FRONT 25.00 REAR 15.00 SIDE 10.00
NO. EX.D.U. 68 FLOOD ZONE X DEVELOPMENT PERMIT NO.

PARCEL ID 09-4S-16-02824-001 SUBDIVISION TIMBERLANE MH COMMUNITY,LLC
LOT 14 BLOCK PHASE 2 UNIT TOTAL ACRES 5.00

IH0000195
Culvert Permit No. Culvert Waiver Contractor's License Number Applicant/Owner/Contractor
EXISTING 09-0304-E CFS HD N
Driveway Connection Septic Tank Number LU & Zoning checked by Approved for Issuance New Resident

COMMENTS: LEGAL NON-CONFORMING MH PARK. PERMITTED FOR A TOTAL OF 68 UNITS.
1 FOOT ABOVE ROAD.

Check # or Cash 3154

FOR BUILDING & ZONING DEPARTMENT ONLY

(footer/Slab)

Temporary Power Foundation Monolithic
date/app. by date/app. by date/app. by
Under slab rough-in plumbing Slab Sheathing/Nailing
date/app. by date/app. by date/app. by
Framing Insulation
date/app. by date/app. by
Rough-in plumbing above slab and below wood floor Electrical rough-in
date/app. by date/app. by
Heat & Air Duct Peri. beam (Lintel) Pool
date/app. by date/app. by date/app. by
Permanent power C.O. Final Culvert
date/app. by date/app. by date/app. by
Pump pole Utility Pole M/H tie downs, blocking, electricity and plumbing
date/app. by date/app. by date/app. by
Reconnection RV Re-roof
date/app. by date/app. by date/app. by

BUILDING PERMIT FEE \$ 0.00 CERTIFICATION FEE \$ 0.00 SURCHARGE FEE \$ 0.00
MISC. FEES \$ 250.00 ZONING CERT. FEE \$ 50.00 FIRE FEE \$ 0.00 WASTE FEE \$
FLOOD DEVELOPMENT FEE \$ FLOOD ZONE FEE \$ 25.00 CULVERT FEE \$ TOTAL FEE 325.00
INSPECTORS OFFICE CLERKS OFFICE

NOTICE: IN ADDITION TO THE REQUIREMENTS OF THIS PERMIT, THERE MAY BE ADDITIONAL RESTRICTIONS APPLICABLE TO THIS PROPERTY THAT MAY BE FOUND IN THE PUBLIC RECORDS OF THIS COUNTY. AND THERE MAY BE ADDITIONAL PERMITS REQUIRED FROM OTHER GOVERNMENTAL ENTITIES SUCH AS WATER MANAGEMENT DISTRICTS, STATE AGENCIES, OR FEDERAL AGENCIES.

"WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY RESULT IN YOUR PAYING TWICE FOR IMPROVEMENTS TO YOUR PROPERTY. IF YOU INTEND TO OBTAIN FINANCING, CONSULT WITH YOUR LENDER OR AN ATTORNEY BEFORE RECORDING YOUR NOTICE OF COMMENCEMENT."

EVERY PERMIT ISSUED SHALL BECOME INVALID UNLESS THE WORK AUTHORIZED BY SUCH PERMIT IS COMMENCED WITHIN 180 DAYS AFTER ITS ISSUANCE, OR IF THE WORK AUTHORIZED BY SUCH PERMIT IS SUSPENDED OR ABANDONED FOR A PERIOD OF 180 DAYS AFTER THE TIME THE WORK IS COMMENCED. A VALID PERMIT RECIEVES AN APPROVED INSPECTION EVERY 180 DAYS. WORK SHALL BE CONSIDERED NOT SUSPENDED, ABANDONED OR INVALID WHEN THE PERMIT HAS RECIEVED AN APPROVED INSPECTION WITHIN 180 DAYS OT THE PREVIOUS INSPECTION.

The Issuance of this Permit Does Not Waive Compliance by Permittee with Deed Restrictions.

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only (Revised 1-10-08) Zoning Official aps 5/14/09 Building Official HO 5-14-09

AP# 0905-20 Date Received 5/13 By JW Permit # 27857

Flood Zone X Development Permit PP Zoning PP Land Use Plan Map Category RVL

Comments legal non-conf. MH Park - permitted for a total of 68 units

FEMA Map# _____ Elevation _____ Finished Floor _____ River _____ In Floodway _____

☐ Site Plan with Setbacks Shown ☒ H # 09-304 ☐ EH Release ☒ Well letter water system ☒ Existing well

☒ Recorded Deed or Affidavit from land owner ☒ Letter of Auth. from installer ☐ State Road Access

☐ Parent Parcel # _____ ☐ STUP-MH _____ ☐ F W Comp. letter

IMPACT FEES: EMS _____ Fire _____ Corr _____ Road/Code _____

School _____ = TOTAL 0 ☒ Authorization Letter for owner

for said MH to be in MHP

09-45-16

Property ID # R02824-001 Subdivision MOBILE HOME PARK LOT 15 PHASE 2

• New Mobile Home ☒ Used Mobile Home _____ MH Size 11x76 Year 2009

• Applicant Cindy Mobley Phone # 850-510-9857

• Address 122 SW SWEETBAY CT LAKE CITY, FL 32024

• Name of Property Owner Timberlane Mobile Home Community, LLC Phone # 386-755-6795

• 911 Address 122 SW SWEETBAY CT, LAKE CITY, FL 32024

• Circle the correct power company - FL Power & Light - Clay Electric

(Circle One) - Suwannee Valley Electric - Progress Energy

• Name of Owner of Mobile Home CINDY Mobley Phone # 850-510-9857

• Address 122 SW SWEETBAY CT, LAKE CITY, FL 32024

• Relationship to Property Owner renter

• Current Number of Dwellings on Property 68

• Lot Size 75 X 150 Total Acreage 20 5

• Do you : Have Existing Drive or Private Drive or need Culvert Permit or Culvert Waiver (Circle one)

(Currently using) (Blue Road Sign) (Putting in a Culvert) (Not existing but do not need a Culvert)

• Is this Mobile Home Replacing an Existing Mobile Home YES (pd)

• Driving Directions to the Property Hwy 247 to Troy St. Turn Right 1 1/2 miles on Right. IS MH.

• Name of Licensed Dealer/Installer Andrew J Hall Phone # 352-443-0705

• Installers Address 13610 NW Hwy 19 Chiefland FL 32626

• License Number TH0000195 Installation Decal # 303281

PERMIT WORKSHEET


Installer Andrew J. Hall License # 140000195
 Manufacturer Live Oak Length x Width 16 x 80
 Name of Owner of this Mobile Home Cindy Mobley
 Phone _____
 Address _____

New Home ☒ Used Home ☐ Year 2009
 Home installed to the Manufacturer's Installation Manual ☒
 Home is installed in accordance with Rule 15-C ☐
 Single wide ☒ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☐ Installation Decal # 303284
 Triple/Quad ☐ Series # ORLEED

NOTE: If home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials

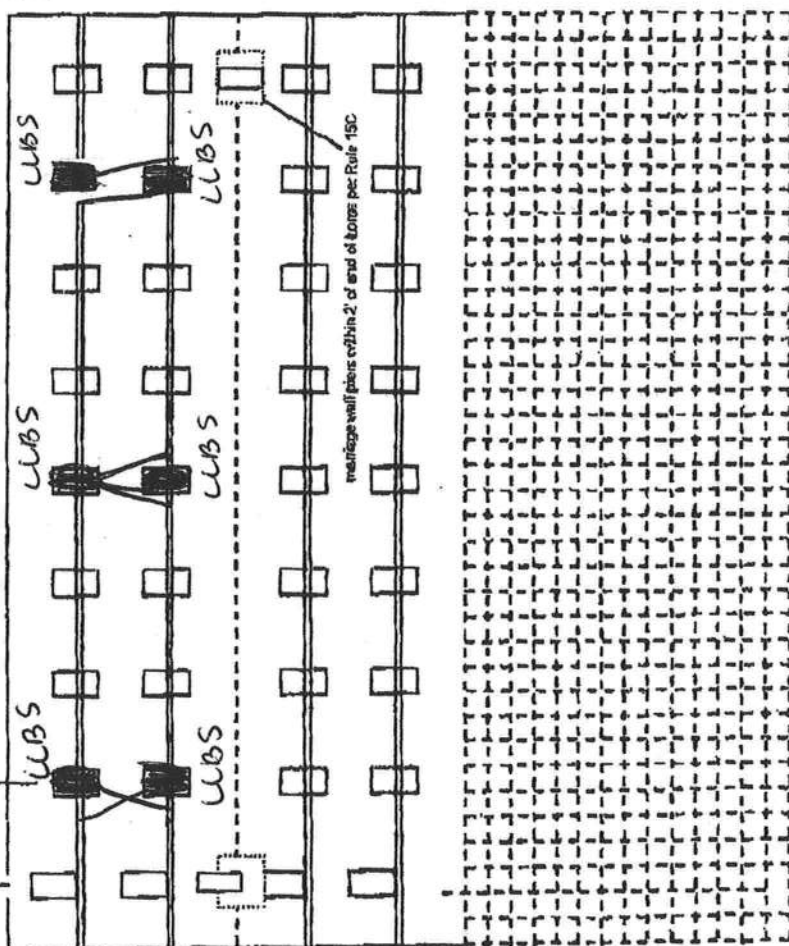

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16' x 16' (256)	18 1/2' x 18 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	4'	5'	6'	7'	8'
1500 psf	4'	6'	6'	7'	8'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'	8'
2500 psf	7' 6"	8'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17.5 x 25.5
 Perimeter pier pad size 16 x 16
 Other pier pad sizes (required by the mfg.) SLA

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
18 x 18	324
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening Pier pad size

SEE PIER LOAD DIAGRAM

ANCHORS

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
 Manufacturer _____
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer _____

OTHER TIES

Number 36
 Sidewall 6
 Longitudinal 6
 Marriage wall 6
 Shearwall 6

PERMIT WORKSHEET

PERMIT NUMBER

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to or check here to declare 1000 lb. soil without testing.

X X X

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X X X

TORQUE PROBE TEST

The results of the torque probe test is 276 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 4 foot anchors.

Note: A slate approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Andrew J. Hall

Date Tested

5-6-09

Electrical

connected electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg.

Plumbing

connect all sewer drains to an existing sewer tap or septic tank. Pg.

connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg.

Site Preparation

Debris and organic material removed
Water drainage: Natural Swale Pad Other

Fastening multi wide units

Floor: Type Fastener: Length: Spacing: N/A N/A N/A
Walls: Type Fastener: Length: Spacing: N/A N/A N/A
Roof: Type Fastener: Length: Spacing: N/A N/A N/A
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirements)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

N/A

Installed:

Between Floors. Yes
Between Walls. Yes
Bottom of ridgebeam Yes

N/A

Weatherproofing

The bottomboard will be repaired and/or taped. Yes Pg.
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes


Miscellaneous

Skirting to be installed: Yes No
Dryer vent installed outside of skirting. Yes N/A
Range downflow vent installed outside of skirting. Yes
Drain lines supported at 4 foot intervals. Yes
Electrical crossovers protected. Yes N/A
Other:

Installer verifies all information given with this permit worksheet is accurate and was based on the

Installer Signature

Date 5-6-09

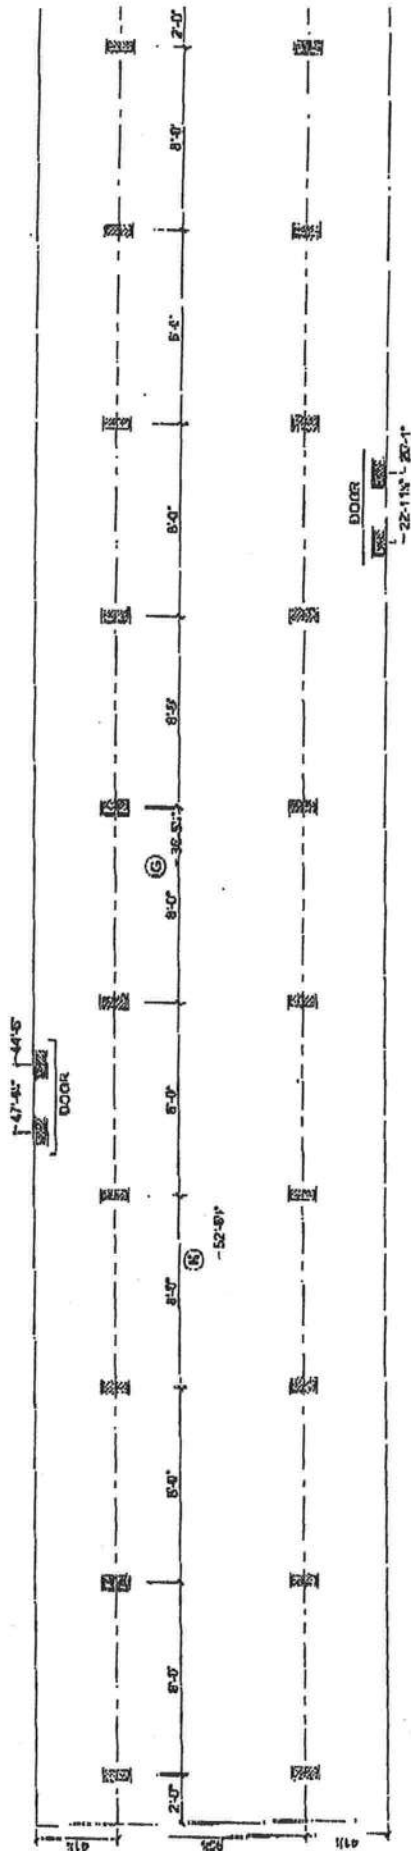

SUPPORT PIER/TYP

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes
MODEL: S-5763D - 16 X 80
3-BEDROOM / 2-BATH

- ① MAIN ELECTRICAL
- ② ELECTRICAL CROSSOVER
- ③ WATER INLET
- ④ WATER CROSSOVER (IF ANY)
- ⑤ GAS INLET (IF ANY)
- ⑥ GAS CROSSOVER (IF ANY)
- ⑦ DUCT CROSSOVER
- ⑧ SEWER DROPS
- ⑨ RETURN AIR (W/OPT. HEAT PUMP OR DUCT)
- ⑩ SUPPLY AIR (W/OPT. HEAT PUMP OR DUCT)

03/20/2002 15:40 4075231154

LMV



State of Florida
DEPARTMENT OF
HIGHWAY SAFETY AND MOTOR VEHICLES

TALLAHASSEE, FLORIDA 32399-0500

FRED Q. DICKINSON, III
Executive Director

March 20, 2002

Mr. Bert A. Moore, Financial Manager
Manufactured Housing Foundation Systems
Oliver Technologies, Inc.
Post Office Box 9 (467 Swan Avenue)
Hohenwald, Tennessee 38462

Dear Mr. Moore:

We wish to acknowledge receipt of your specifications and test results certifying that your Longitudinal Stabilizing and Lateral Bracing System, 1101 V, listed below complies with the specifications and regulations set by the Department of Highway Safety and Motor Vehicles, Rules 15C-1.0105, 15C-1.0107 and 15C-1.0108, Florida Administrative Code.

Installation instructions must be available at the installation site.

MODEL #DESCRIPTION

1101 V

Longitudinal Stabilizing and Lateral Bracing System

NOTE: This system is for replacement of longitudinal anchors. This system can only be used with sidewall anchor spacing of 5'4". Maximum strut angle 45°.

If you have any questions, please advise at (407) 623-1340.

Sincerely,

Phil Bergelt, Program Manager
Bureau of Mobile Home and
Recreational Vehicle Construction
Division of Motor Vehicles

PRB:srb

OLIVER TECHNOLOGIES, INC.
FLORIDA INSTALLATION INSTRUCTIONS FOR THE
MODEL 1101 "V" SERIES ALL STEEL FOUNDATION SYSTEM
MODEL 1101 "V" (STEPS 1-15)
MODEL 1101-L "V" LONGITUDINAL ONLY:
FOLLOW STEPS 1-9
FOR ADDING LATERAL ARM:
Follow Steps 10-15

ENGINEERS STAMP

ENGINEERS STAMP

1. SPECIAL CIRCUMSTANCES: If the following conditions occur - STOP! Contact Oliver Technologies at 1-800-284-7437:
a) Pier height exceeds 48" b) Length of home exceeds 76' c) Roof eaves exceed 18" d) Sidewall height exceed 96"
e) Location is within 1500 feet of coast

INSTALLATION OF GROUND PAN

2. Remove weeds and debris in an approximate two foot square to expose firm soil for each ground pan (C).
3. Place ground pan (C) directly below chassis I-beam. Press or drive pan firmly into soil until flush with or below soil.
SPECIAL NOTE: The longitudinal "V" brace system serves as a pier under the home and should be loaded as any other pier. It is recommended that after leveling piers, and one-half inch (1/2") before home is lowered completely on to piers, complete steps 4 through 9 below.

INSTALLATION OF LONGITUDINAL "V" BRACE SYSTEM

NOTE: WHEN INSTALLING THE MODEL # 1101-L "V" LONGITUDINAL SYSTEM ONLY, A MINIMUM OF 2 SYSTEMS PER FLOOR SECTION IS REQUIRED. SOIL TEST PROBE SHOULD BE USED TO DETERMINE CORRECT TYPE OF ANCHOR PER SOIL CLASSIFICATION. IF PROBE TEST READINGS ARE BETWEEN 175 & 275 A 5 FOOT ANCHOR MUST BE USED. IF PROBE TEST READINGS ARE BETWEEN 276 & 350 A 4 FOOT ANCHOR MAY BE USED. USE GROUND ANCHORS WITH DIAGONAL TIES AND STABILIZER PLATES EVERY 5'4". VERTICAL TIES ARE ALSO REQUIRED ON HOMES SUPPLIED WITH VERTICAL TIE CONNECTION POINTS (PER FLORIDA REG.).

4. Select the correct square tube brace (E) length for set-up (pier) height at support location. (The 18" tube is always used as the bottom part of the longitudinal arm). Note: Either tube can be used by itself, cut and drilled to length as long as a 40 to 45 degree angle is maintained.

PIER HEIGHT (Approx. 45 degrees Max.)	1.25" ADJUSTABLE Tube Length	1.50" ADJUSTABLE Tube Length
7 3/4" to 25"	22"	18"
24 3/4" to 32 1/4"	32"	18"
33" to 41"	44"	18"
40" to 48"	54"	18"

5. Install (2) of the 1.50" square tubes (E {18" tube}) into the "U" bracket (J), insert carriage bolt and leave nut loose for final adjustment.
6. Place I-beam connector (F) loosely on the bottom flange of the I-beam.
7. Slide the selected 1.25" tube (E) into a 1.50" tube (E) and attach to I-beam connectors (F) and fasten loosely with bolt and nut.
8. Repeat steps 6 through 7 to create the "V" pattern of the square tubes loosely in place. The angle is not to exceed 45 degree and not below 40 degrees.
9. After all bolts are tightened, secure 1.25" and 1.50" tubes using four(4) 1/4"-14 x 3/4" self-tapping screws in pre-drilled holes.

INSTALLATION OF LATERAL TELESCOPING TRANSVERSE ARM SYSTEM

THE MODEL 1101 "V" (LONGITUDINAL & LATERAL PROTECTION) ELIMINATES THE NEED FOR MOST STABILIZER PLATES & FRAME TIES.
NOTE: THE USE OF THIS SYSTEM REQUIRES VERTICAL TIES SPACED AT 5'4".
FOUR FOOT (4') GROUND ANCHOR MAY BE USED EXCEPT WHERE THE HOME MANUFACTURER SPECIFIES DIFFERENT.


10. Install remaining vertical tie-down straps and 4' ground anchors per home manufacturer's instructions. **NOTE:** Centerline anchors to be sized according to soil torque condition. Any manufacturer's specifications for sidewall anchor loads in excess of 4,000 lbs. require a 5" anchor.
11. **NOTE:** Each system is required to have a frame tie and stabilizer attached at each lateral arm stabilizing location. This frame tie & stabilizer plate needs to be located within 18" from of center ground pan.
12. Select the correct square tube brace (H) length for set-up lateral transverse at support location. The lengths come in either 60" or 72" lengths. (With the 1.50" tube as the bottom tube, and the 1.25" tube as the inserted tube.)
13. Install the 1.50 transverse brace (H) to the ground pan connector (D) with bolt and nut.
14. Slide 1.25" transverse brace into the 1.50" brace and attach to adjacent I-beam connector (I) with bolt and nut.
15. Secure 1.50" transverse arm to 1.25" transverse arm using four (4) 1/4" - 14 x 3/4" self-tapping screws in pre-drilled holes.

MANUFACTURED HOUSING FOUNDATION SYSTEMS
A DIVISION OF OLIVER TECHNOLOGIES, INC.
1-800-284-7437


Telephone: 931-796-4555
Fax: 931-796-8811
www.olivertechnologies.com

REQUIRED NUMBER AND LOCATION OF MODEL 1101 "V" BRACES FOR UP TO 4/12 ROOF PITCH

ALL WIDTHS; AND LENGTHS UP TO 52'

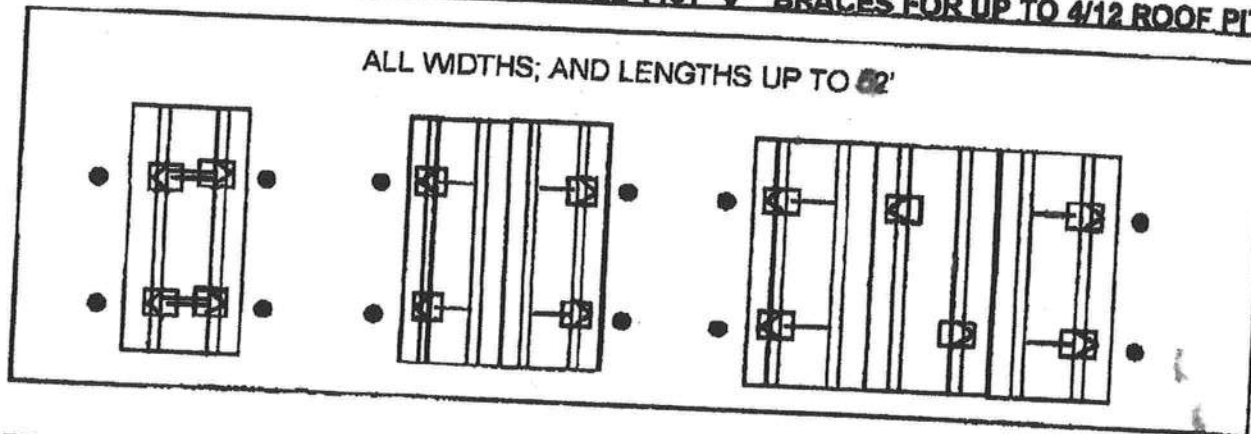


ALL WIDTHS; AND LENGTHS OVER 52' TO 80'

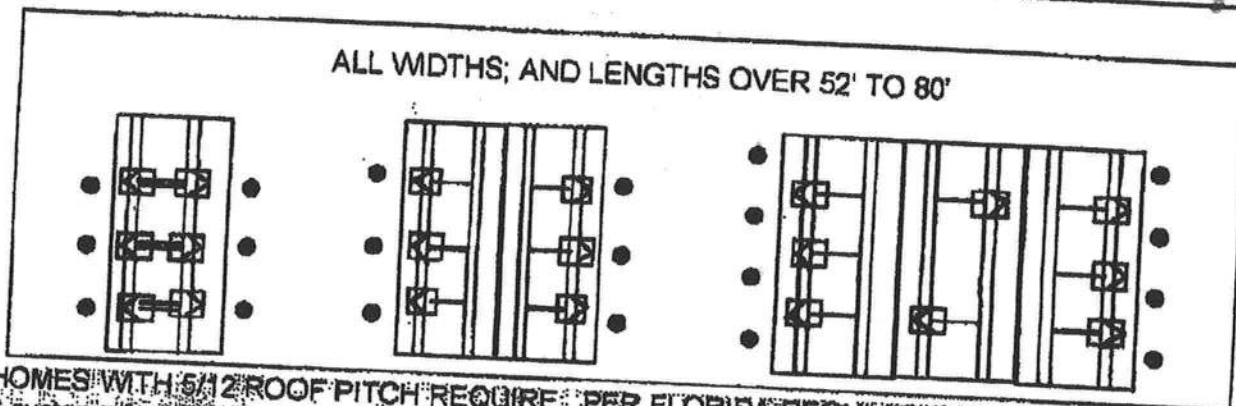

HOMES WITH 5/12 ROOF PITCH REQUIRE PER FLORIDA REGULATIONS 6 systems for home lengths up to 52' and 8 systems for homes over 52' and up to 80'. One stabilizer plate and frame tie required at each lateral bracing system.

Florida approved 4" ground anchors may be used in all locations except where home manufacturer specifications for sidewall straps are in excess of 4,000 lbs. These locations require a 5" anchor.

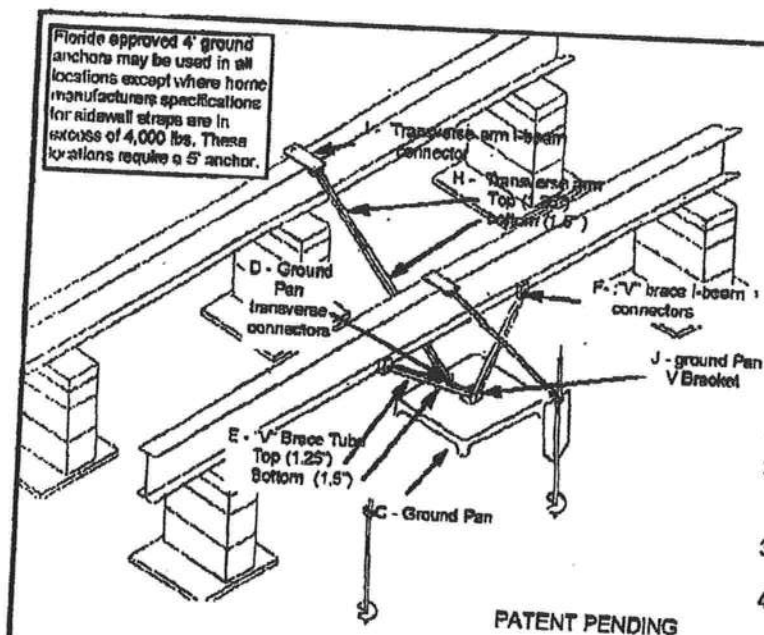

- C = GROUND PAN
- D = GROUND PAN CONNECTOR
- U BRACKETS
- E = TELESCOPING V BRACE TUBE ASSEMBLY W/ 1.5 BOT. TUB. AND 1.25 TUBE INSERT
- F = "V" BRACE I-BEAM CONNECTORS ASSEMBLY
- H = TELESCOPING TRANSVERSE ARM ASSEMBLY
- I = TRANSVERSE ARM I-BEAM CONNECTOR
- J = V PAN BRACKET

REVISED INSTRUCTIONS 4/23/03

NOTES:


1. LENGTH OF HOUSE IS THE ACTUAL BOX SIZE
2. • = STABILIZER PLATE AND FRAME TIE LOCATION (needs to be located within 18" from center of ground pan)
3. [Square with 'V'] = LOCATION OF ASF MODEL 1101 "V" (LATERAL & LONGITUDINAL BRACING).
4. [Square with 'L'] = LOCATION OF MODEL 1101 "L" (LONGITUDINAL BRACING ONLY).

PATENT PENDING


MANUFACTURED HOUSING FOUNDATION SYSTEMS
A DIVISION OF OLIVER TECHNOLOGIES, INC.
1-800-284-7437

Telephone: 831-798-4555
Fax: 831-798-8811
www.olivertechnologies.com


OLIVER TECHNOLOGIES, INC.
ALL STEEL FOUNDATION SYSTEM
MODEL# 1101 "V"

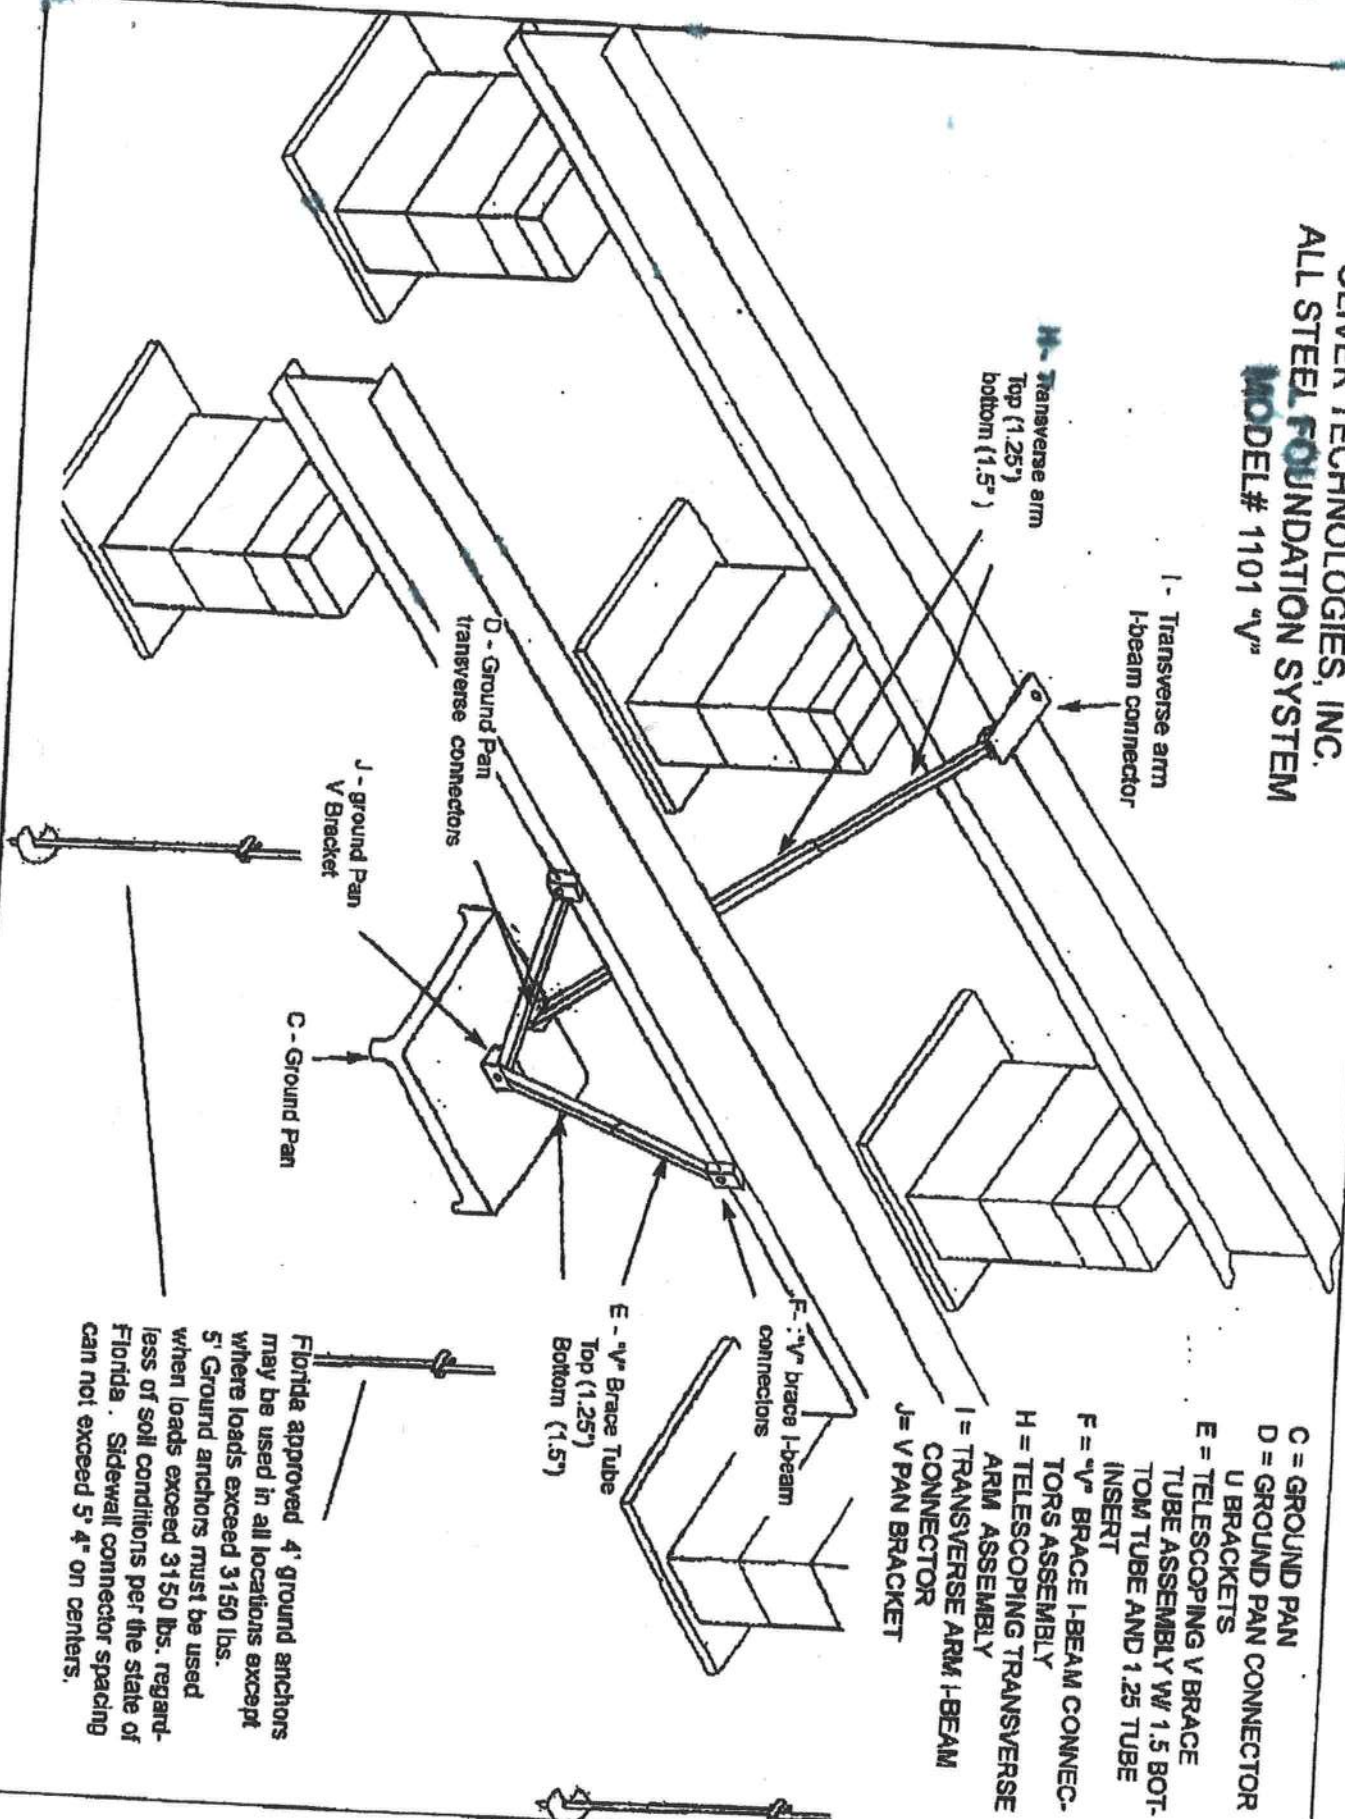

SITE PLAN EXAMPLE / WORKSHEET

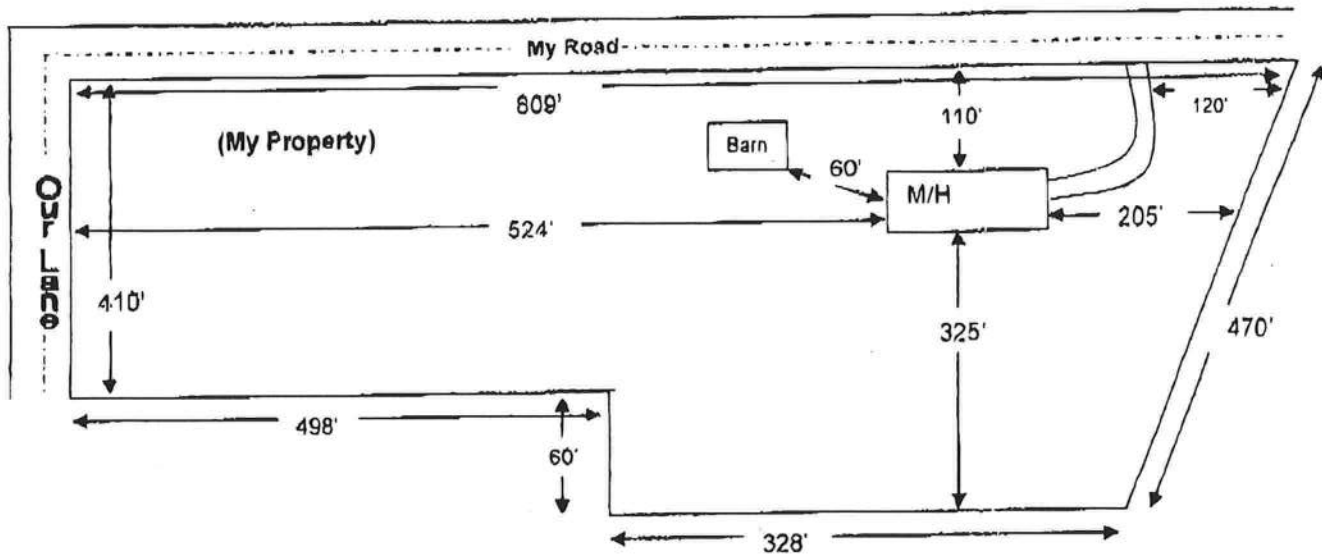

Use this example to draw your own site plan. Show all existing buildings and any other homes on this property and show the distances between them. Also show where the roads or roads are around the property. This site plan can also be used for the 911 Addressing department if you include the distance from the driveway to the nearest property line.

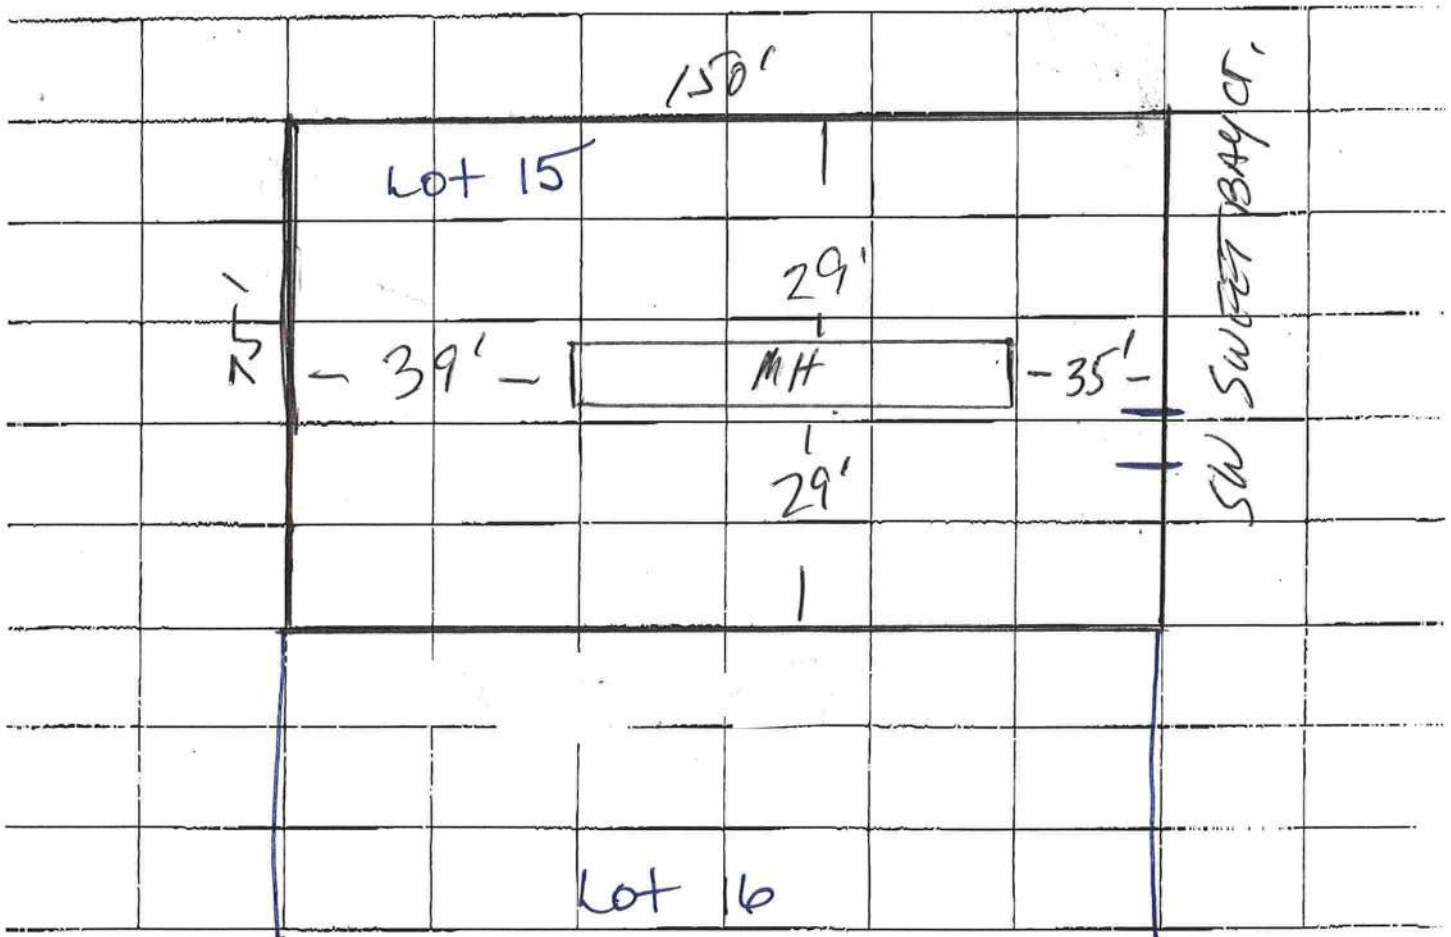

Columbia County Property Appraiser

DB Last Updated: 4/27/2009

2009 Preliminary Values

Tax Record

Property Card

Interactive GIS Map

Print

Parcel: 09-4S-16-02824-001

Owner & Property Info

Search Result: 1 of 1

Owner's Name	TIMBERLANE MOBILE HOME		
Site Address	SWEETBAY		
Mailing Address	COMMUNITY LLC 337 SW TOMPKINS ST LAKE CITY, FL 32024		
Use Desc. (code)	MH PARK (002802)		
Neighborhood	009416.00	Tax District	3
UD Codes	MKTA06	Market Area	06
Total Land Area	5.000 ACRES		
Description	E1/2 OF SE1/4 OF SW1/4 OF NE 1/4. (TIMBERLANE MH PARK) WD 1070-47.		

GIS Aerial



Property & Assessment Values

Mkt Land Value	cnt: (1)	\$41,040.00
Ag Land Value	cnt: (0)	\$0.00
Building Value	cnt: (0)	\$0.00
XFOB Value	cnt: (3)	\$58,160.00
Total Appraised Value		\$99,200.00

Just Value	\$99,200.00
Class Value	\$0.00
Assessed Value	\$99,200.00
Exemptions	\$0.00
Total Taxable Value	County: \$99,200.00 City: \$99,200.00 Other: \$99,200.00 School: \$99,200.00

Sales History

Sale Date	Book/Page	Inst. Type	Sale VImp	Sale Qual	Sale RCode	Sale Price
12/30/2005	1070/47	WD	V	Q		\$173,800.00
9/1/1986	601/481	WD	I	Q		\$40,000.00
1/1/1984	528/249	WD	V	Q		\$13,000.00

Building Characteristics

Bldg Item	Bldg Desc	Year Blt	Ext. Walls	Heated S.F.	Actual S.F.	Bldg Value
NONE						

Extra Features & Out Buildings

Code	Desc	Year Blt	Value	Units	Dims	Condition (% Good)
0259	MHP HOOKUP	0	\$38,400.00	0000016.000	0 x 0 x 0	AP (050.00)
0166	CONC,PAVMT	0	\$6,800.00	0000001.000	20 x 20 x 0	(000.00)
0260	PAVEMENT-A	0	\$12,960.00	0000001.000	0 x 0 x 0	(000.00)

Land Breakdown

Lnd Code	Desc	Units	Adjustments	Eff Rate	Lnd Value
000210	TRLR PARK (MKT)	0000005.000 AC	1.00/1.00/1.00/1.00	\$8,208.00	\$41,040.00



Date 11-5-08

All room dimensions include closets and square footage figures are approximate.

Hall Brothers Mobile Home Towing
13610 N.W. Hwy 19
Chiefland, Fl. 32626
(352)493-0705 Phone
(352)493-1997Fax

Power Of Attorney

Date: 5/6/09

I hereby name and appoint Cindy Mobley to be my lawful attorney.

In fact to act for me and apply to the Columbia County Building Department for a mobile home permit, for work to be performed on his property.

Mark Anderson Timberlane Mobile Home Community
(Owner of Property & Address) 122 SW Sweet Bay CT

And have my permission to sign my name and do all things necessary to this appointment. Levy County FL

Andrew J. Hall
Type or Print Name of Registered or Certified Contractor and License Number

[Signature]
Signature of Registered or Certified Contractor

The foregoing instrument was acknowledged before me this 6th day of May, 2009. By

Andrew J. Hall, who is personally known to me and who did take Oath.

State Of Florida

County of Levy

Connie Mamagone
Notary Public



Seal

TIMBERLANE MOBILE HOME COMMUNITY

337 SW Tompkins Street

Lake City, Florida 32024

H 386.755.6795

C 386.303.2222

F 386.752.7204

pgoodson@comcast.net

May 13, 2009

To Whom It May Concern:

Timberlane Mobile Home Community has granted permission to Westgate Mobile Home Sales to place a mobile home belonging to Cyndy Mobley in the park. It will be located in Phase II, Lot 15 with the 911 address of 122 SW Sweetbay Court, Lake City, Florida 32024.

Sincerely,

A handwritten signature in cursive script, appearing to read "Patti H. Goodson". The signature is written in dark ink and is positioned above the printed name.

Patti H. Goodson




STATE OF FLORIDA
DEPARTMENT OF HEALTH

APPLICATION FOR ONSITE SEWAGE DISPOSAL SYSTEM CONSTRUCTION PERMIT

Permit Application Number 09-0304E

PART II - SITE PLAN

Scale: Each block represents 5 feet and 1 inch = 50 feet.

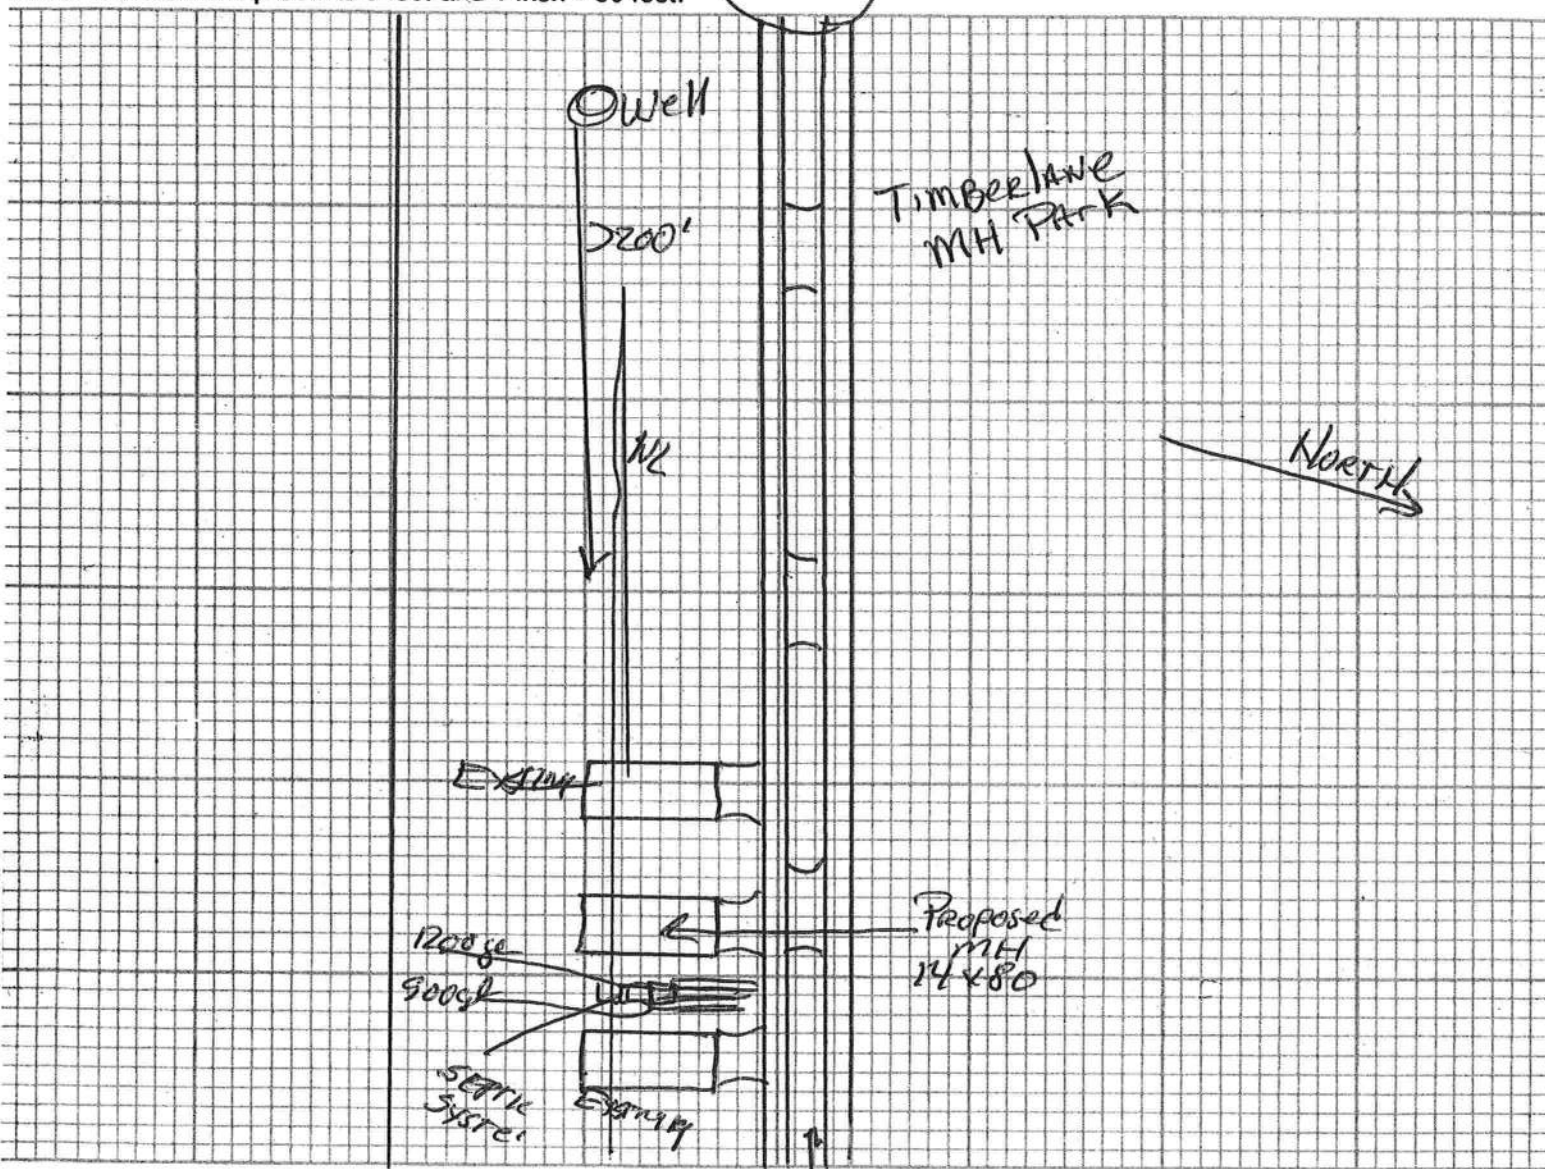

Notes: _____

Site Plan submitted by: Robert W. Jell Signature _____
Plan Approved [Signature] Not Approved _____
By [Signature] Date 6/4/9 Title _____
County Health Department

ALL CHANGES MUST BE APPROVED BY THE COUNTY HEALTH DEPARTMENT

**COLUMBIA COUNTY
FLORIDA
DEPARTMENT OF BUILDING AND ZONING**

M/H OCCUPANCY

COLUMBIA COUNTY, FLORIDA

Department of Building and Zoning Inspection

This Certificate of Occupancy is issued to the below named permit holder for the building and premises at the below named location, and certifies that the work has been completed in accordance with the Columbia County Building Code.

Parcel Number 09-4S-16-02824-001

Building permit No. 000027857

Permit Holder ANDREW HALL

Owner of Building TIMBERLANE MHP -(CINDY MOBLEY -MH)

Location: 122 SW SWEETBAY CT., LAKE CITY, FL

Date: 06/10/2009



[Signature]

Building Inspector

**POST IN A CONSPICUOUS PLACE
(Business Places Only)**
