

DATE 09/20/2004

Columbia County Building Permit

PERMIT

This Permit Expires One Year From the Date of Issue

000022322

APPLICANT ROBERT SHEPPARD PHONE 623-2203

ADDRESS 2355 SE CR 245 LAKE CITY FL 32055

OWNER NICOLE HARRISON PHONE 623-2905

ADDRESS 914 SW LAMBOY CIRCLE LAKE CITY FL 32055

CONTRACTOR MELVIN SHEPPARD PHONE 623-2203

LOCATION OF PROPERTY SISTERS WELCOME, TURN ON TUNSIL, TL ON SPARROW, TR ON LAMBOY CIRCLE, FIRST ROAD TO LEFT, 2ND PROPERTY ON RIGHT

TYPE DEVELOPMENT MH, UTILITY ESTIMATED COST OF CONSTRUCTION .00

HEATED FLOOR AREA TOTAL AREA HEIGHT .00 STORIES

FOUNDATION WALLS ROOF PITCH FLOOR

LAND USE & ZONING RR MAX. HEIGHT

Minimum Set Back Requirments: STREET-FRONT 25.00 REAR 15.00 SIDE 10.00

NO. EX.D.U. 0 FLOOD ZONE X DEVELOPMENT PERMIT NO.

PARCEL ID 22-4S-16-03086-124 SUBDIVISION LOBLOLLY

LOT 4 BLOCK B PHASE UNIT TOTAL ACRES 4.29

IH0000035

Culvert Permit No. Culvert Waiver Contractor's License Number Applicant/Owner/Contractor Robert Sheppard

EXISTING 04-0890-E BK RK Y

Driveway Connection Septic Tank Number LU & Zoning checked by Approved for Issuance New Resident

COMMENTS: ONE FOOT ABOVE THE ROAD

Check # or Cash 1109

FOR BUILDING & ZONING DEPARTMENT ONLY

(footer/Slab)

Temporary Power Foundation Monolithic

 date/app. by date/app. by date/app. by

Under slab rough-in plumbing Slab Sheathing/Nailing

 date/app. by date/app. by date/app. by

Framing Rough-in plumbing above slab and below wood floor

 date/app. by date/app. by date/app. by

Electrical rough-in Heat & Air Duct Peri. beam (Lintel)

 date/app. by date/app. by date/app. by

Permanent power C.O. Final Culvert

 date/app. by date/app. by date/app. by

M/H tie downs, blocking, electricity and plumbing Pool

 date/app. by date/app. by date/app. by

Reconnection Pump pole Utility Pole

 date/app. by date/app. by date/app. by

M/H Pole Travel Trailer Re-roof

 date/app. by date/app. by date/app. by

BUILDING PERMIT FEE \$.00 CERTIFICATION FEE \$.00 SURCHARGE FEE \$.00

MISC. FEES \$ 200.00 ZONING CERT. FEE \$ 50.00 FIRE FEE \$ 5.67 WASTE FEE \$ 12.25

FLOOD ZONE DEVELOPMENT FEE \$ CULVERT FEE \$ TOTAL FEE 267.92

INSPECTORS OFFICE CLERKS OFFICE CH

NOTICE: IN ADDITION TO THE REQUIREMENTS OF THIS PERMIT, THERE MAY BE ADDITIONAL RESTRICTIONS APPLICABLE TO THIS PROPERTY THAT MAY BE FOUND IN THE PUBLIC RECORDS OF THIS COUNTY. AND THERE MAY BE ADDITIONAL PERMITS REQUIRED FROM OTHER GOVERNMENTAL ENTITIES SUCH AS WATER MANAGEMENT DISTRICTS, STATE AGENCIES, OR FEDERAL AGENCIES.

"WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY RESULT IN YOUR PAYING TWICE FOR IMPROVEMENTS TO YOUR PROPERTY. IF YOU INTEND TO OBTAIN FINANCING, CONSULT WITH YOUR LENDER OR AN ATTORNEY BEFORE RECORDING YOUR NOTICE OF COMMENCEMENT."

This Permit Must Be Prominently Posted on Premises During Construction

PLEASE NOTIFY THE COLUMBIA COUNTY BUILDING DEPARTMENT AT LEAST 24 HOURS IN ADVANCE OF EACH INSPECTION, IN ORDER THAT IT MAY BE MADE WITHOUT DELAY OR INCONVIENCE, PHONE 758-1008. THIS PERMIT IS NOT VALID UNLESS THE WORK AUTHORIZED BY IT IS COMMENCED WITHIN 6 MONTHS AFTER ISSUANCE.

The Issuance of this Permit Does Not Waive Compliance by Permittee with Deed Restrictions.

left mess 2006 9/13/04 G

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only

Zoning Official

BLK 08.07.04

Building Official

PK 9-13-04

AP# 0408-97

Date Received

By

CH

Permit #

22322

Flood Zone

X

Development Permit

N/A

Zoning

RR

Land Use Plan Map Category

RES.U.2.DOU.

Comments

- ☒ Site Plan with Setbacks shown ☒ Environmental Health Signed Site Plan ☐ Env. Health Release
☒ Need a Culvert Permit ☒ Need a Waiver Permit ☒ Well letter provided ☒ Existing Well

* Need a preliminary inspection

Property ID R03086-124 (22-45-16) Must have a copy of the property deed

New Mobile Home _____ Used Mobile Home 97 Year 97

Subdivision Information Lobolly Subdivision

Applicant Melvin Sheppard
Nicole Harrison Phone # 386 623-2905

Address 2520 122nd Terr.

Name of Property Owner Nicole Harrison Phone# 386-623-2905

911 Address 914 SW Lambay Cr. Wake City Fl. 32055

Name of Owner of Mobile Home Same Phone # _____

Address _____

Relationship to Property Owner Same

Current Number of Dwellings on Property 0 (owe Assessments)

Lot Size 4.29 Total Acreage Same

Explain the current driveway Existing

Driving Directions Sisters Welcome to Dirt Rd Right Beside Rusty Acres (Tursil Rd.) go to Sparrow take a Left take a Right on Lambay Cr. go to First Rd to Left second property to Right

Is this Mobile Home Replacing an Existing Mobile Home No

Name of Licensed Dealer/Installer Melvin Sheppard Phone # 623-2203

Installers Address 2355 SE CR 245

License Number IH 0000035 Installation Decal # 27848

PERMIT NUMBER

Installer Melvin Sheppard License # TH0000035

Address of home being installed 9145w Lamboy Cr. Lakecity FL

Manufacturer Fleetwood Length x width 14x70


NOTE: if home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials MS



marriage wall piers within 2' of end of home per Rule 15C

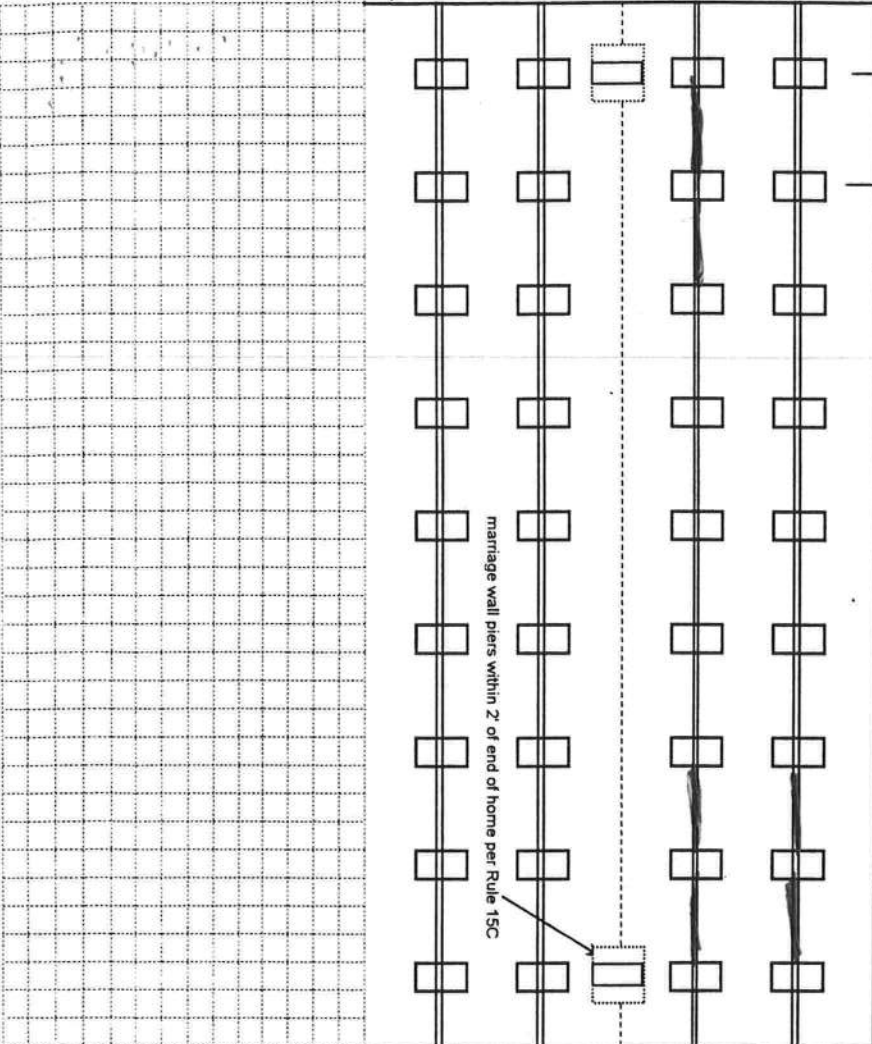

New Home ☐ Used Home ☒

Home installed to the Manufacturer's Installation Manual ☒

Home is installed in accordance with Rule 15-C ☐

Single wide ☒ Wind Zone II ☒ Wind Zone III ☐

Double wide ☐ Installation Decal # 27848

Triple/Quad ☐ Serial # 64L6389

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4'6"	6'	7'	8'	8'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'	8'
2500 psf	7'6"	8'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

Perimeter pier pad size

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening Pier pad size

POPULAR PAD SIZES

Pad Size	Sq in
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

OTHER TIES

Longitudinal Stabilizing Device (LSD)
Manufacturer Oliver
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer

Sidewall Longitudinal Marriage wall Shearwall
Number 30
3
0
2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb. soil without testing.

X 1500 X 1500 X 1500

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 1500 X 1500 X 1500

TORQUE PROBE TEST

The results of the torque probe test is 290 inch pounds or check here if you are declaring 5" anchors without testing _____. A test showing 275 inch pounds or less will require 4 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. 1 understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

MS Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Melvin Shepard

Date Tested

8-27-09

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 29

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 28

Site Preparation

Debris and organic material removed ✓
Water drainage: Natural ✓ Swale _____ Pad _____ Other _____

Fastening multi wide units

Floor: Type Fastener: _____ Length: _____ Spacing: _____
Walls: Type Fastener: _____ Length: _____ Spacing: _____
Roof: Type Fastener: _____ Length: _____ Spacing: _____
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials MS

Type gasket _____

Installed:

Between Floors Yes _____
Between Walls Yes _____
Bottom of ridgebeam Yes _____

Weatherproofing

The bottomboard will be repaired and/or taped. Yes _____ Pg. _____
Siding on units is installed to manufacturer's specifications. Yes _____
Fireplace chimney installed so as not to allow intrusion of rain water. Yes _____

Miscellaneous

Skirting to be installed. Yes _____ No ✓
Dryer vent installed outside of skirting. Yes _____ N/A ✓
Range downflow vent installed outside of skirting. Yes _____ N/A ✓
Drain lines supported at 4 foot intervals. Yes _____
Electrical crossovers protected. Yes _____
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the

manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature Melvin Shepard Date 8-30-09




DEPARTMENT OF HEALTH

APPLICATION FOR ONSITE SEWAGE DISPOSAL SYSTEM CONSTRUCTION PERMIT

Permit Application Number 04-0890-E

PART II - SITE PLAN


Scale: Each block represents 5 feet and 1 inch = 50 feet.

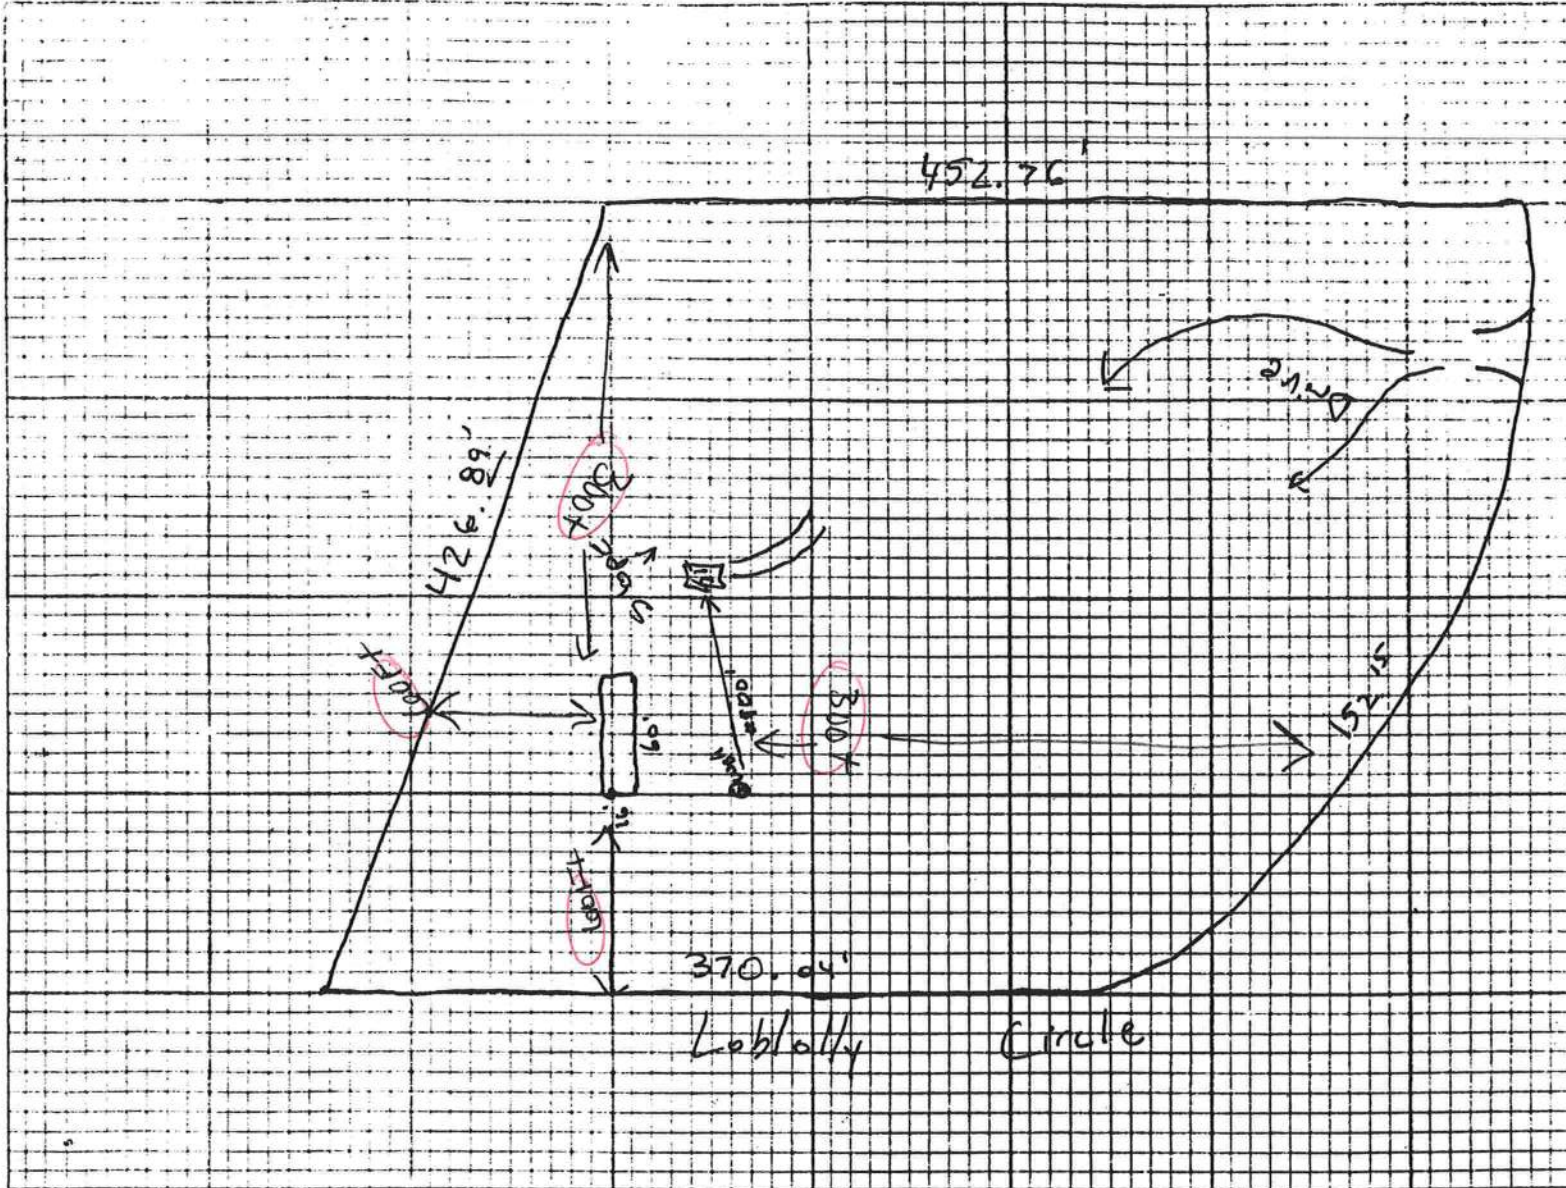

Notes: _____

Site Plan submitted by: Nick Harrison Signature
Plan Approved ☒ Not Approved _____
By Mr. S. S. Columbia County Health Department
Owner _____
Date 8/25/04 Title _____

ALL CHANGES MUST BE APPROVED BY THE COUNTY HEALTH DEPARTMENT

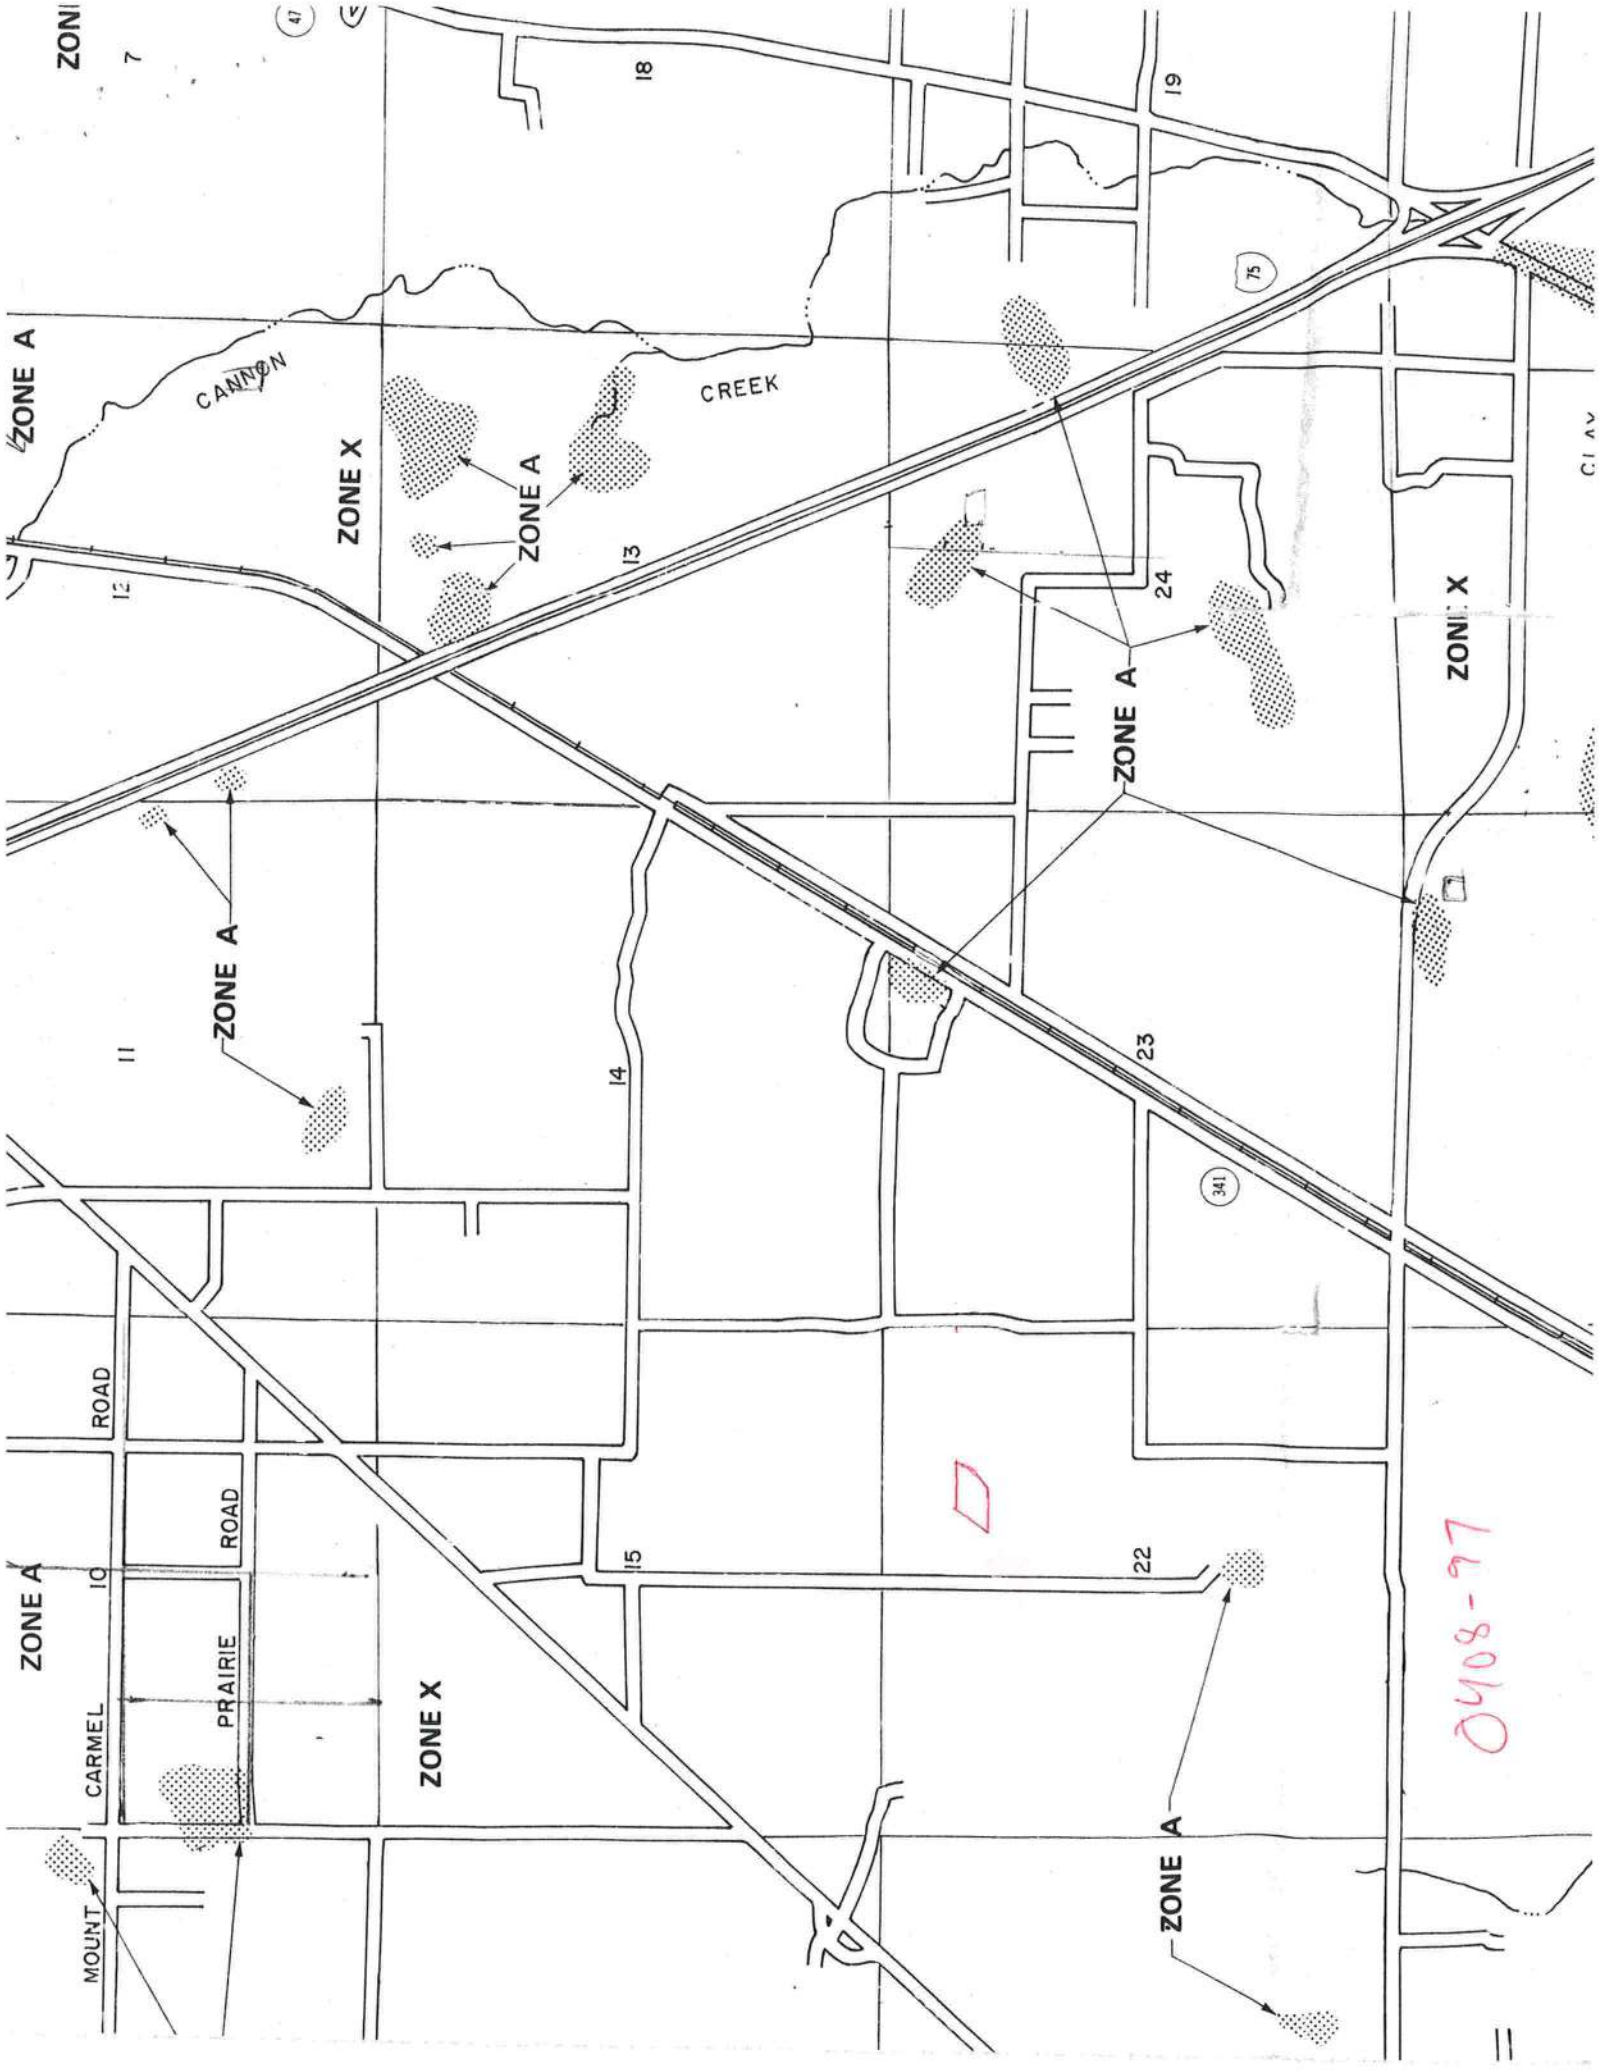

DEPARTMENT OF
CODE ENFORCEMENT
COLUMBIA COUNTY, FLORIDA

*Inspection is
needed on
Tuesday*

PRELIMINARY MOBILE HOME INSPECTION REPORT

DATE RECEIVED 8-25-04 BY LH

IS THE M/H ON THE PROPERTY WHERE THE PERMIT WILL BE ISSUED? Yes

OWNERS NAME Nicole Harrison PHONE _____ CELL 623-2905

911 ADDRESS 914 SW Lamboy Cr. Lakeland FL 32055

MOBILE HOME PARK NO SUBDIVISION Loblolly Lot 4 BLKB

DRIVING DIRECTIONS TO MOBILE HOME 341, (R) Tunsil, (L) Sparrow, (R) Loblolly
take 1st Dirt Rd to (L) then 2nd property on (R)

CONTRACTOR Melvin Sheppard PHONE _____ CELL _____

MOBILE HOME INFORMATION

MAKE ? YEAR 97 SIZE 16 X 60

COLOR Tan/Burgandy SERIAL No. _____

WIND ZONE II SMOKE DETECTOR yes

INTERIOR:

FLOORS ✓

DOORS ✓

WALLS ✓

CABINETS ✓

ELECTRICAL (FIXTURES/OUTLETS) ✓

EXTERIOR:

WALLS / SIDING ✓

WINDOWS ✓

DOORS ✓

STATUS:

APPROVED ✓ WITH CONDITIONS: None

NOT APPROVED _____ NEED REINSPECTION _____

INSPECTOR SIGNATURE Billy Dubois NUMBER 307

CODE ENFORCEMENT I
PRELIMINARY MOBILE HOME INSPECTION REPORT

22322

DATE RECEIVED 2-16-06 BY GT IS THE M/H ON THE PROPERTY WHERE THE PERMIT WILL BE ISSUED? No
OWNERS NAME Nicole Harrison PHONE 752-1034 CELL 984-7343
ADDRESS 914 SW Lambog Circle, Lake City
MOBILE HOME PARK N/A SUBDIVISION Loblobby, Lot B
DRIVING DIRECTIONS TO MOBILE HOME Sisters Welcome, TR Tunsil, TL on
Sparrow, TR on Lambog, 1st road on left,
2nd drive on right
MOBILE HOME INSTALLER Robert Sheppard PHONE 623-2203 CELL

MOBILE HOME INFORMATION

MAKE Horton YEAR 1996 ~~1997~~ SIZE 16 X 66 ~~60~~ COLOR White, Burgundy
SERIAL No. H202744G
WIND ZONE II Must be wind zone II or higher NO WIND ZONE I ALLOWED

INTERIOR:

INSPECTION STANDARDS

(P or F) - P= PASS F= FAILED

☒ SMOKE DETECTOR () OPERATIONAL () MISSING
☒ FLOORS () SOLID () WEAK () HOLES DAMAGED LOCATION _____
☒ DOORS () OPERABLE () DAMAGED
☒ WALLS () SOLID () STRUCTURALLY UNSOUND
☒ WINDOWS () OPERABLE () INOPERABLE
☒ PLUMBING FIXTURES () OPERABLE () INOPERABLE () MISSING
☒ CEILING () SOLID () HOLES () LEAKS APPARENT
☒ ELECTRICAL (FIXTURES/OUTLETS) () OPERABLE () EXPOSED WIRING () OUTLET COVERS MISSING () LIGHT FIXTURES MISSING

EXTERIOR:

☒ WALLS / SIDING () LOOSE SIDING () STRUCTURALLY UNSOUND () NOT WEATHERTIGHT () NEEDS CLEANING
☒ WINDOWS () CRACKED/ BROKEN GLASS () SCREENS MISSING () WEATHERTIGHT
☒ ROOF () APPEARS SOLID () DAMAGED

STATUS:

APPROVED ☒ WITH CONDITIONS: _____

NOT APPROVED _____ NEED REINSPECTION FOR FOLLOWING CONDITIONS _____

SIGNATURE Dary ID NUMBER 306 DATE 2-22-06

EMERALD LAKE ALLEY

OCCUPANCY

COLUMBIA COUNTY, FLORIDA

Department of Building and Zoning Inspection

This Certificate of Occupancy is issued to the below named permit holder for the building and premises at the below named location, and certifies that the work has been completed in accordance with the Columbia County Building Code.

Parcel Number 28-3S-16-02372-604

Building permit No. 000022328

Use Classification SFD, UTILITY

Fire: 22.68

Permit Holder ISAAC CONSTRUCTION

Waste: 49.00

Owner of Building CHRIS CURRY

Total: 71.68

Location: 725 NW ZACK DR (ARBOR GREEN @ EMERALD LAKES, LOT 4)

Date: 05/17/2005



Tony Dick

Building Inspector

POST IN A CONSPICUOUS PLACE
(Business Places Only)
