

# COLUMBIA COUNTY PERMIT WORKSHEET

page 1 of 2

These worksheets must be completed and signed by the installer.  
Submit the originals with the packet.

Installer Manuel Sanchez License # 1025396

911 Address where home is being installed. 314 SW Billowing Cir. Lake City, FL 32024


Manufacturer S.F. Length x width 32 x 62

NOTE: if home is a single wide fill out one half of the blocking plan  
if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)  
where the sidewall ties exceed 5 ft 4 in.

Installer's initials MS

Typical pier spacing 2'  
Show locations of Longitudinal and Lateral Systems  
(use dark lines to show these locations)

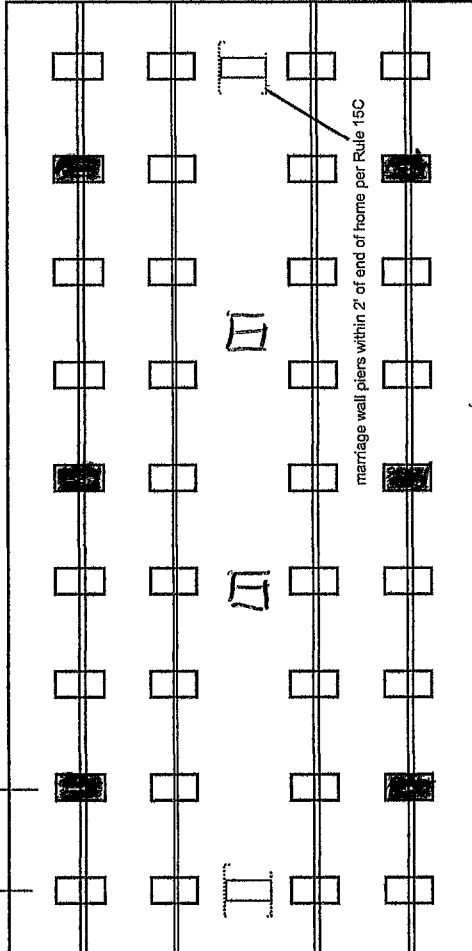

61101V all steel

17x25 ABS 5'6c I Beam

23x31 opening

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual ☒

Home is installed in accordance with Rule 15-C ☐

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Decal # 20947

Triple/Quad ☐ Serial # 007065

## PIER SPACING TABLE FOR USED HOMES

| Load bearing capacity | Footer size (sq in) | 16" x 16" (256) | 18 1/2" x 18 1/2" (342) | 20" x 20" (400) | 22" x 22" (484)* | 24" x 24" (576)* | 26" x 26" (676) |
|-----------------------|---------------------|-----------------|-------------------------|-----------------|------------------|------------------|-----------------|
| 1000 dsf              | 3'                  | 4'              | 4'                      | 5'              | 6'               | 7'               | 8'              |
| 1500 dsf              | 4'                  | 6'              | 6'                      | 7'              | 8'               | 8'               | 8'              |
| 2000 dsf              | 6'                  | 8'              | 8'                      | 8'              | 8'               | 8'               | 8'              |
| 2500 dsf              | 7'                  | 8'              | 8'                      | 8'              | 8'               | 8'               | 8'              |
| 3000 dsf              | 8'                  | 8'              | 8'                      | 8'              | 8'               | 8'               | 8'              |
| 3500 dsf              | 8'                  | 8'              | 8'                      | 8'              | 8'               | 8'               | 8'              |

\* interpolated from Rule 15C-1 pier spacing table.

## PIER PAD SIZES

I-beam pier pad size 17x25

Perimeter pier pad size 16x16

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening 18'

Pier pad size 23x31

4ft

5 ft

## ANCHORS

within 2' of end of home spaced at 5' 4" oc

## TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer

O.T.

## OTHER TIES

Number

Sidewall

Longitudinal

Marriage wall

Shearwall

# COLUMBIA COUNTY PERMIT WORKSHEET

page 2 of 2

## POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to  
or check here to declare 1000 lb. soil 1500 without testing.

X 1.5 X 1.5 X 1.5

## POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 1.5 X 1.5 X 1.5

## TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

**Note:** A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

MB Installer's initials

## ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Manuel Branan

Date Tested

3-12-14

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 152

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. \_\_\_\_\_

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. \_\_\_\_\_

## Site Preparation

Debris and organic material removed

Water drainage: Natural

Swale

Yes

Other

## Fastening multi wide units

Floor: Type Fastener: 1995 Length: 6" Spacing: 18"  
Walls: Type Fastener: Staples Length: 2 1/4" Spacing: 24"  
Roof: Type Fastener: 1995 Length: 6" Spacing: 24"  
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

## Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

MB

Type gasket

Factory

Installed.

Between Floors Yes

Between Walls Yes

Bottom of ridgebeam Yes

## Weatherproofing

The bottomboard will be repaired and/or taped. Yes

Siding on units is installed to manufacturer's specifications. Yes

Fireplace chimney installed so as not to allow intrusion of rain water. Yes

## Miscellaneous

Skirting to be installed. Yes

No

Dryer vent installed outside of skirting. Yes

Range downflow vent installed outside of skirting. Yes N/A

Drain lines supported at 4 foot intervals. Yes

Electrical crossovers protected. Yes

Other.

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature

Manuel Branan

Date

3-12-14
