

PERMIT WORKSHEET

page 1 of 2

PERMIT NUMBER

Installer Rusty Knowles License # IH 1038219

Installer Mobile Phone # 386-397-0886



Address of home being installed 268 SW Kinnard Court
Fort White FL 32038

Manufacturer Jacobson Length x width 32x52

NOTE: If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Installer's initials RL

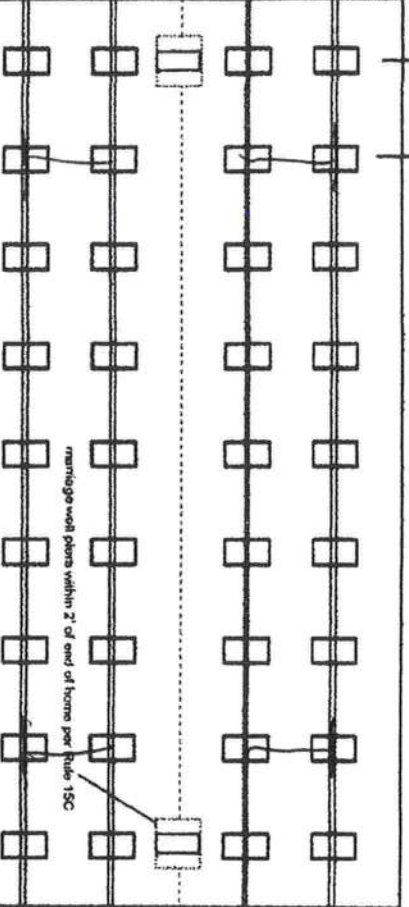

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual

Home is installed in accordance with Rule 15-C

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Decal # 82068

Triple/Quad ☐ Serial # 000000 JACFL 3765AB

Roof System: ☒ Typical ☐ Hinged

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	Footer size (sq ft)	16' x 16' (256)	18' 1/2' x 18' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4'	5'	6'	7'	8'	9'	10'
2000 psf	5'	6'	7'	8'	9'	10'	11'
2500 psf	6'	7'	8'	9'	10'	11'	12'
3000 psf	7'	8'	9'	10'	11'	12'	13'
3500 psf	8'	9'	10'	11'	12'	13'	14'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 24x24

Perimeter pier pad size 16x16

Other pier pad sizes (required by the mfg.) 16x16

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening 18'9" Pier pad size 24x24

21'5x22'5"

21'5x22'5"

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer Cloutier Technologies

Side wall Longitudinal Marriage wall Shearwall
Number 2

FRAME TIES

within 2' of end of home spaced at 5' 4" oc ☒

OTHER TIES

24x24

#43230

PERMIT NUMBER

PERMIT WORKSHEET

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil _____ without testing.

X 15 X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 12.8 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Bushy to K. K. K. K. K.

Date Tested

12-8-21

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 15C-1

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 15C-1

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 15C-1

Site Preparation

Debris and organic material removed _____

Water drainage: Natural _____ Swale _____ Pad _____ Other _____

Fastening multi wide units

Floor: Type Fastener: W45 Length: 6" Spacing: 18"
Walls: Type Fastener: 5/8" Length: 4" Spacing: 18"
Roof: Type Fastener: W45 Length: 6" Spacing: 18"

For used homes a r/n, 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket Installation/Sealing

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials RLC

Type gasket Pg. 15C-1

Installed:

Between Floors Yes ✓
Between Walls Yes ✓
Bottom of ridgebeam Yes ✓

Weatherproofing

Plans Reviewed for Code Compliance _____
Flapjacks/skimmy installed so as not to allow intrusion of rain water. Yes ✓ Pg. 15C-1

Miscellaneous

Skirting to be installed. Yes ✓ NO _____
Dryer vent installed outside of skirting. Yes _____ N/A _____
Range downflow vent installed outside of skirting. Yes _____ N/A _____
Drain lines supported at 4 foot intervals. Yes ✓
Electrical crossovers protected. Yes ✓
Other: _____


Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Date 12-8-21







JACOBSEN HOMES
PO BOX 3888, 6000 PAVILION CT.
SAFETY HARBOR, FLORIDA 34685
(727) 786-1198
www.jacobsonhomes.com

COLUMN INFO. TABLE			COLUMN PAD - MIN. SIZES (sq. in.)									
COL. NUM.	SPAN	LOAD	1000	1500	2000	2500	3000	3500	4000	4500	5000	5500

1	18'-0"	5.215	751	501	375	300	300	300	300	300	300	300
2	18'-0"	5.215	751	501	375	300	300	300	300	300	300	300
3	18'-0"	5.215	751	501	375	300	300	300	300	300	300	300
4	0"	0	0	0	0	0	0	0	0	0	0	0
5	0"	0	0	0	0	0	0	0	0	0	0	0
6	0"	0	0	0	0	0	0	0	0	0	0	0
7	0"	0	0	0	0	0	0	0	0	0	0	0
8	0"	0	0	0	0	0	0	0	0	0	0	0
9	0"	0	0	0	0	0	0	0	0	0	0	0
10	0"	0	0	0	0	0	0	0	0	0	0	0

MINIMUM PIER PAD SIZE (sq. in.)			I-BEAM PIER SPACING										MATING LINE PIER SPACING										PERIMETER PIER SPACING									
			1000	1500	2000	2500	3000	3500	4000	4500	5000	5500	1000	1500	2000	2500	3000	3500	4000	4500	5000	5500	1000	1500	2000	2500	3000	3500	4000	4500	5000	5500
A	256 sq. in.	256	400	400	400	400	400	400	400	400	400	400	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96
B	342.25 sq. in.	400	400	400	400	400	400	400	400	400	400	400	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96
C	396 sq. in.	400	400	400	400	400	400	400	400	400	400	400	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96
D	400 sq. in.	400	400	400	400	400	400	400	400	400	400	400	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96
E	432.875 sq. in.	400	400	400	400	400	400	400	400	400	400	400	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96
F	576 sq. in.	751	501	375	300	300	300	300	300	300	300	300	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96
G	676 sq. in.	751	501	375	300	300	300	300	300	300	300	300	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96	96

REFER TO SU-01-0020, SU-01-0021, AND OTHER DETAILS IN THE SET-UP MANUAL FOR MAXIMUM HEIGHT (THIS IS NOT DESIGNED, NOR INTENDED, TO BE A STILT FOUNDATION)

THIS BLOCKING DIAGRAM IS PROVIDED AS A COURTESY ONLY. THE LICENSED SET-UP CONTRACTOR SHALL REVIEW THIS DETAIL AND VERIFY COMPLIANCE. THE LICENSED SET-UP CONTRACTOR IS RESPONSIBLE AND LIABLE FOR ALL INSTALLATION.

PAGE 2 OF 2



OPTIMUM
WINDOW -

NOTE:
CHECK WITH YOUR SUPERVISOR
TO DETERMINE IF YOU
WILL HAVE TO SIGN THIS



© 10-12-14



600 Parkside Court, S.W., Harbor, Florida 34695 ■ Telephone (727) 726-1138
www.golfhomes.com/Floor-Plans
