

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT

Order #: 5934	Label #: 103270	Manufacturer: <u>LIVE OAK</u>	(Check Size of Home)
Homeowner: <u>KARI / HESTER</u>	Year Model: <u>2022</u>	Single _____	Double <u>X</u>
Address: <u>319 NW STARLING TER.</u>	Length & Width: <u>58/62 x 28</u>	Triple _____	HUD Label #: _____
City/State/Zip: <u>LAKE CITY FL 32055</u>	Type Longitudinal System: <u>6 OTI</u>	Soil Bearing / PSF: _____	Torque Probe / in-lbs: _____
Phone #: _____	Type Lateral Arm System: <u>6 OTI</u>	Permit #: _____	
Date Installed: _____	New Home: <u>X</u> Used Home: _____		
Installed Wind Zone: <u>II</u>	Data Plate Wind Zone: <u>II</u>		
Note: _____			

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

103270

LABEL #

DATE OF INSTALLATION

DAVID E ALBRIGHT

NAME

IH / 1129420 / 1

5934

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

Mobile Home Permit Worksheet

DN

Application Number: _____

Date: _____

Installer: DAVID ALBRIGHT License # 1H-1129420

Address of home being installed

319 NW Staring Ter Lake City


Manufacturer Live Oak Length x width 28x56/62

NOTE: If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home. Understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Typical pier spacing

Installer's initials ALB

Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

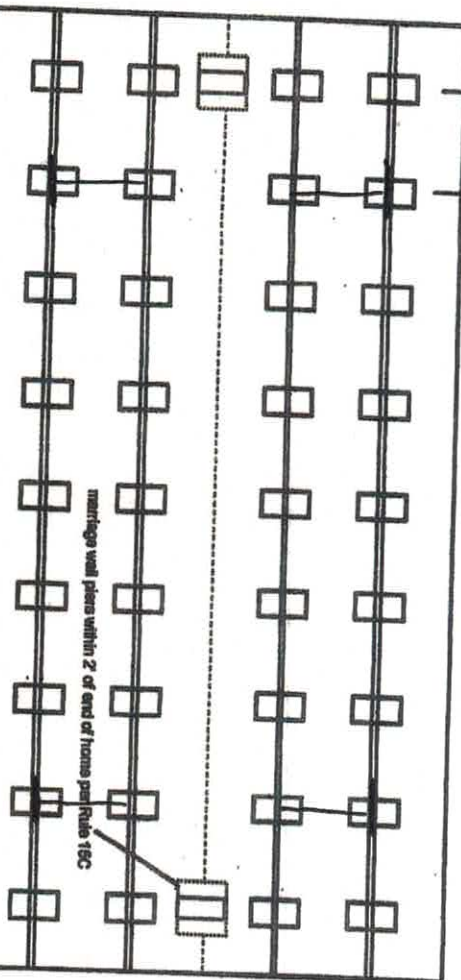

New Home ☒ Used Home ☐
 Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C ☒
 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Decal # _____
 Triple/Quad ☐ Serial # LOHGA30073179

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	Footer size (250)	16' x 16' (250)	18 1/2' x 18 (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4'	5'	6'	7'	8'	8'	8'
2000 psf	5'	6'	7'	8'	8'	8'	8'
2500 psf	6'	7'	8'	8'	8'	8'	8'
3000 psf	7'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17x26
 Perimeter pier pad size 16x16
 Other pier pad sizes (required by the mfg.) 24x24

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
18 x 18	324
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	448
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening FACTORY Pier pad size DIAGRAM

FACTORY DIAGRAM

ANCHORS

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

OTHER TIES

Longitudinal Stabilizing Device (LSD)
 Manufacturer Oliver Technology
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer Oliver Technology

Skewwell
 Longitudinal Marriage wall
 Shearwell
 Number 23
5-5 5-4
3

Mobile Home Permit Worksheet

Dr

Application Number: _____

Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ per or check here to declare 1000 lb. soil ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 260 inch pounds or check here if you are declaring 5 anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewalk locations. 1 undersized 5 ft. anchors are required at all centerline points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 400 lb. folding capacity.

NY Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER.

Installer Name DAVID ALBERT MOBILE HOME SVC

Date Tested _____

Electrical

Connect electrical conductors between multi-wire units, but not to the main power source. This includes the bonding wire between multi-wire units. Pg. 64-68

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 70

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 107

Site Preparation

Debris and organic material removed ☒ Pad ☒ Other _____

Feathering multi-wire units

Floor: Type Fastener: LAGS Length: 6" Spacing: 2'

Walls: Type Fastener: LAGS Length: 1 1/2" Spacing: 16"

Roof: Type Fastener: LAGS Length: 6" Spacing: 2'
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket (weatherstripping) requirements

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials

Type gasket
Pg. 36

Installed:
Between Floors Yes ☒
Between Walls Yes END UNITS
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 119
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous


Siding to be installed. Yes _____ No ☒
Dryer vent installed outside of siding. Yes _____ N/A ☒
Range downflow vent installed outside of siding. Yes _____ N/A ☒
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and a Rule 19C-1 & 2

Installer Signature David Albert Date _____

DAKOTA

58'-0"

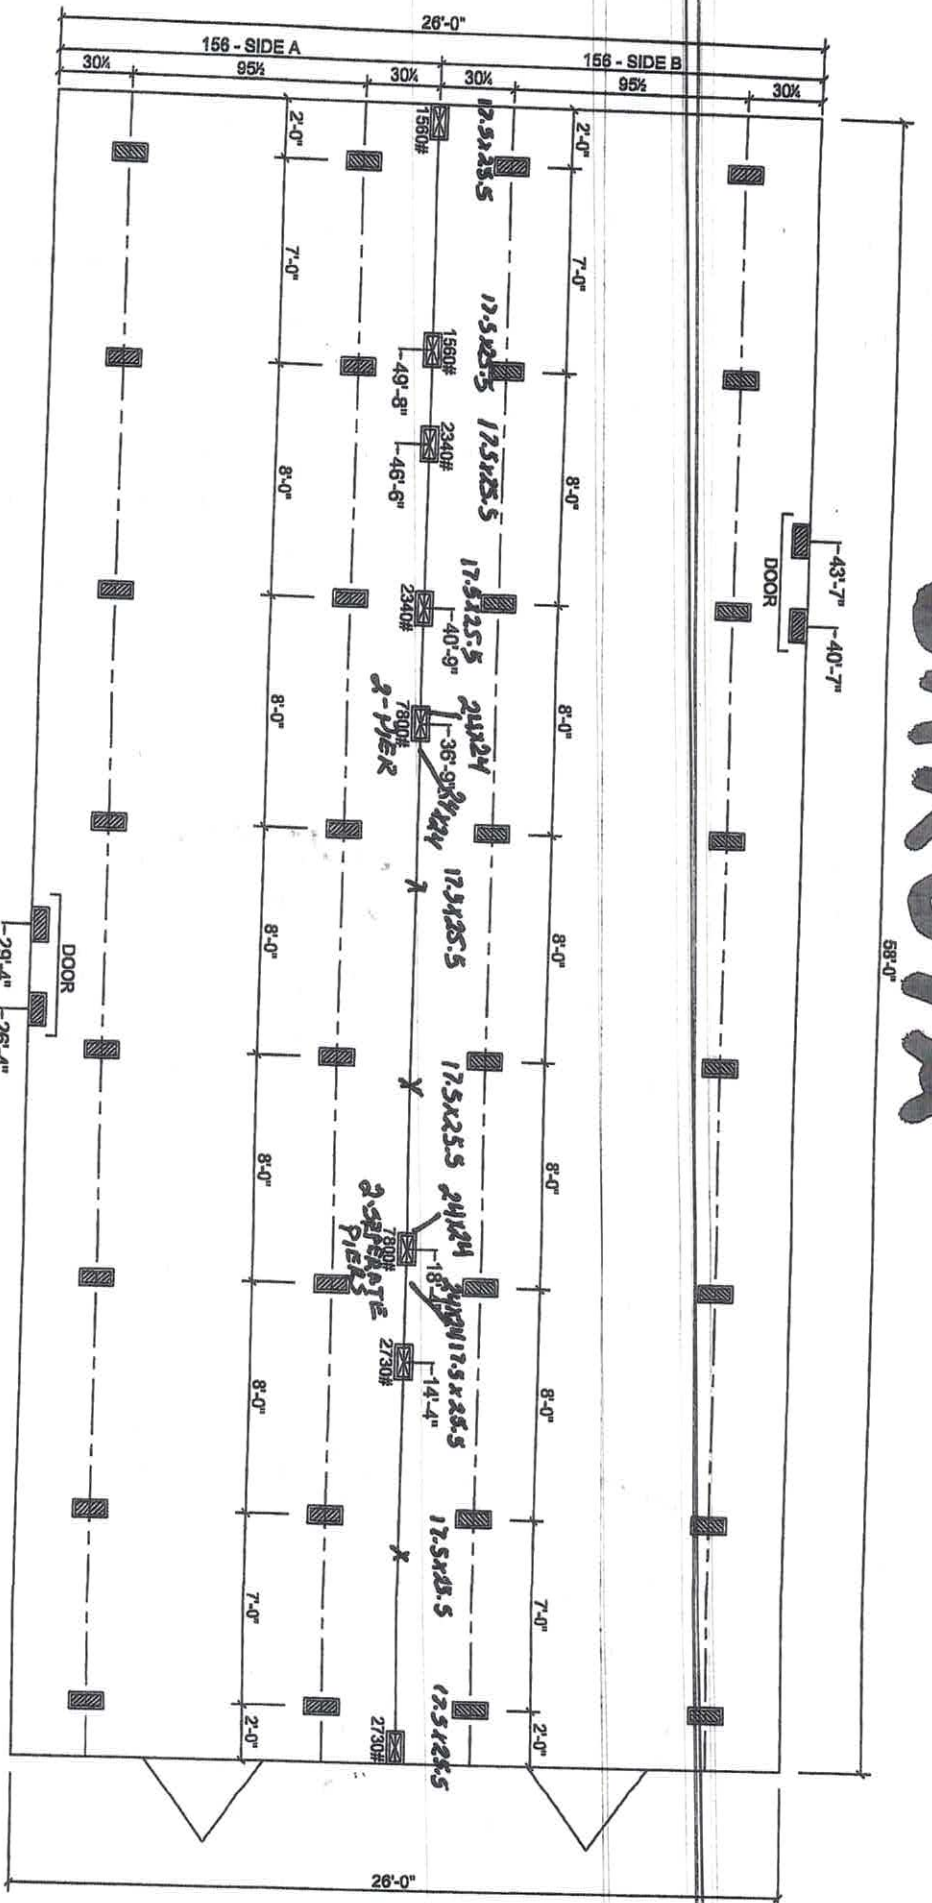

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.

- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.

- FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.


Live Oak Homes

MODEL: H-2583C-PS - 28 X 60

3-BEDROOM / 2-BATH

REV: 04/09/21

H-2583C-PS

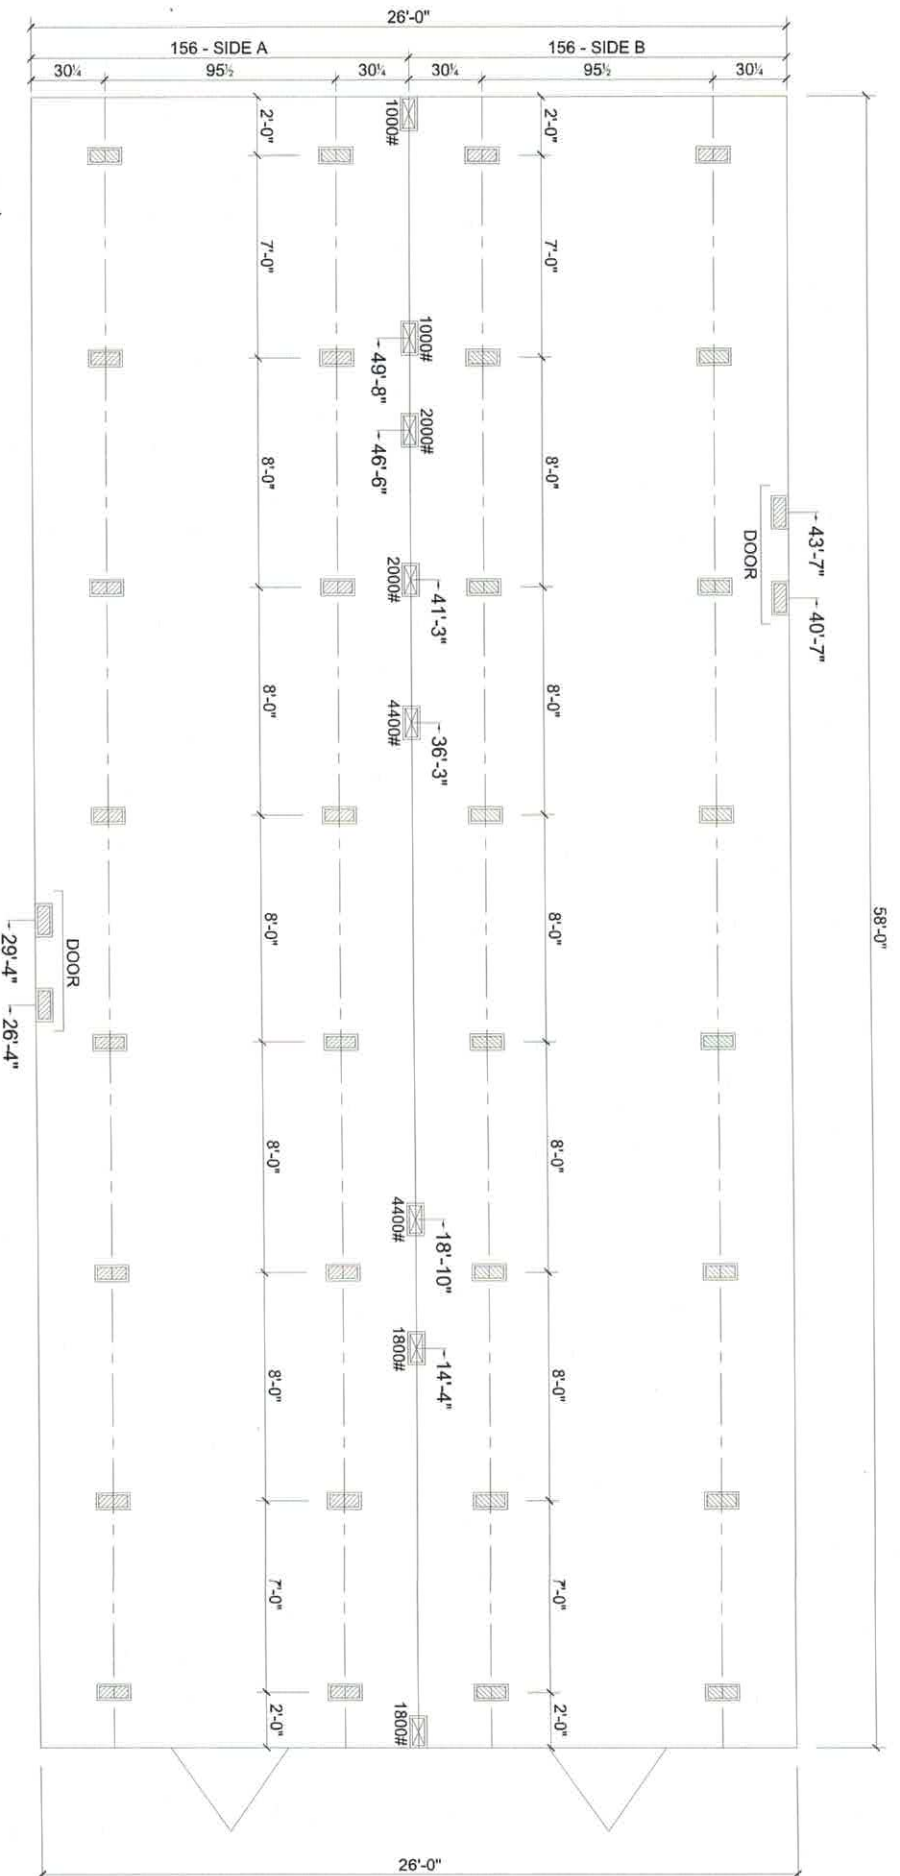

MARRIAGE LINE OPENING SUPPORT PIERTYP.
 SUPPORT PIERTYP

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes
MODEL: H-2583C-PS - 28 X 60
3-BEDROOM / 2-BATH

REV: 04/25/22

H-2583C-PS

