

Mobile Home Permit Worksheet

Application Number: _____ Date: _____

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual ☒
 Home is installed in accordance with Rule 15-C

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Detail # order 2

Triple/Quad ☐ Serial # ordered 74897

Installer: Fordy L. Brundley License # 41038249

Address of home being installed: _____

Manufacturer LINCOLN Length x width 26 x 50

NOTE: If home is a single wide fill out one half of the blocking plan.


If home is a triple or quad wide sketch in remainder of home. Understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials RB

Typical pier spacing



Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

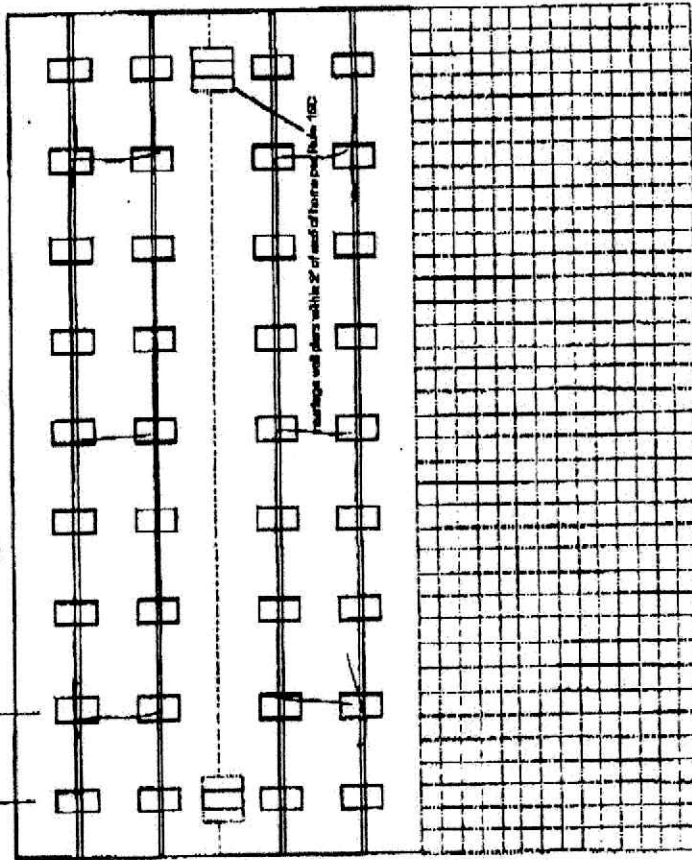

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16' x 16' (256)	18' 1/2' x 18' (332)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	3'	4'	5'	6'	7'	8'
1500 psf	4'	4'	5'	6'	7'	8'	9'
2000 psf	5'	5'	6'	7'	8'	9'	10'
2500 psf	6'	6'	7'	8'	9'	10'	11'
3000 psf	7'	7'	8'	9'	10'	11'	12'
3500 psf	8'	8'	9'	10'	11'	12'	13'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 11' x 22.5'

Perimeter pier pad size N/A

Other pier pad sizes (required by the mfg.) 12' x 16'

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the plans.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening 19' Pier pad size 12' x 16'

ANCHORS

4 ft ☒ 5 ft ☒

FRAME TIES

Within 2' of end of home spaced at 5' 4" OC ☒

OTHER TIES

Number

Sidewall 16
 Longitudinal 16
 Marriage wall 2
 Shearwall 2

TIEDOWN COMPONENTS

Longitudinal Seating Device (LSD) _____
 Manufacturer _____
 Longitudinal Seating Device w/ Lateral Arms _____
 Manufacturer Overton

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 100 psi or check here to declare 1000 lb. soil without testing.

X 100 X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 8 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is N/A (no) lbs. pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewalk locations. I understand 5 ft anchors are required at all cantilevered locations where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 11C-1


Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 11C-1

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 11C-1

Page 2 of 2

Debris and organic material removed		Shingle		Pad		Other	
Water drainage: Natural							
Fastening nails into studs							
Floor:	Type Fastener:	Length:	Spacing:				
Walls:	Type Fastener:	Length:	Spacing:				
Roof:	Type Fastener:	Length:	Spacing:				
For used homes: 30 gauge, 6" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.							
I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and budged marriages walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.							
Installer's Initials: <u>RUC</u>							
Type gasket:	FA 4007	Installed:	Between Floors:	Yes	✓		
Pg. <u>152</u>		Between Walls:	Yes	✓			
		Bottom of Ridgebeam:	Yes	✓			
Weatherstripping							
The bottomboard will be repaired and/or taped. Yes <u>✓</u> Pg. 11C-1							
Siding on units is installed to manufacturer's specifications. Yes <u>✓</u>							
Fireplace chimney installed so as not to allow invasion of rain water. Yes <u>✓</u>							
Siding to be installed. Yes <u>✓</u> No <u>✓</u>							
Dryer vent installed outside of skirting. Yes <u>✓</u> N/A <u>✓</u>							
Range downflow vent installed outside of skirting. Yes <u>✓</u>							
Drain lines supported at 4 foot intervals. Yes <u>✓</u>							
Electrical crossovers protected. Yes <u>✓</u>							
Other: _____							
Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2							
Installer Signature: <u>[Signature]</u>						Date: <u>1-7-25</u>	

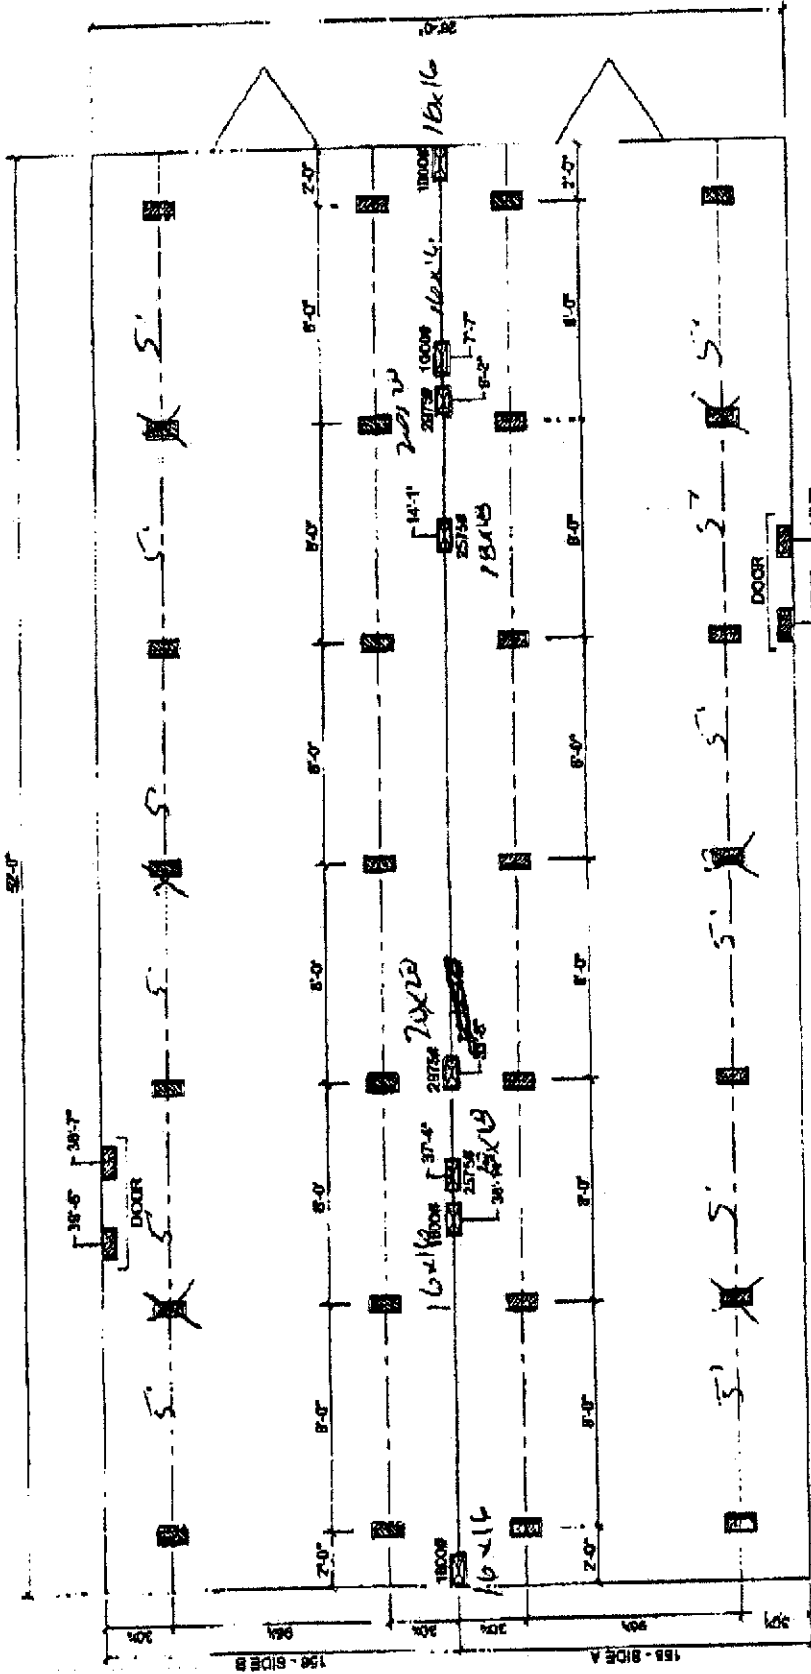

REV: 05/16/22

MARRIAGE LINE OPENING SUPPORT PIERTYP.

SUPPORT PIERTYP

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY. QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS. SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes
MODEL: D-2523H - 28 X 56
3-BEDROOM / 2-BATH

D-2523H

2025/JAN/07/TUE 11:32

PROPERTY IDealer's Name: Wayne Frier Home CentsCustomer's Name DAVID MORRELLPhone # Work # Physical Address 601 NW TURNER AVELAKE CITY, FL 32055

Description of Manufactured Home:

Year 2025 Make LIVE OAK MSize 20x8 / 56 Serial #

Specific Driving Instructions to Property I

AMPlease draw map from sales lot to home site**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

119092

LABEL #

DATE OF INSTALLATION

RUSTY L. KNOWLES

NAME

IH / 1038219 / 1

6566

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.**INSTRUCTIONS**

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
