

Mobile Home Permit Worksheet

Application Number:

Date:

New Home

Used Home

☐

Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C

Single wide

☐

Wind Zone II

☐

Wind Zone III

☒

Double wide

☒

Installation Decal #

72782

Triple/Quad

☐

Serial #

1210871614B

Installer: Forest Johnson License # TH 1025249

Address of home: 3276 Wilson Springs Rd
being installed: FT. White, FL 32038

Manufacturer: Deer Valley Length x width: 66' x 32'

NOTE: If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home
Understand Lateral Arm-Strengtheners cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.


Typical pier spacing

2' 5'

Installer's Initials

[Signature]

Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

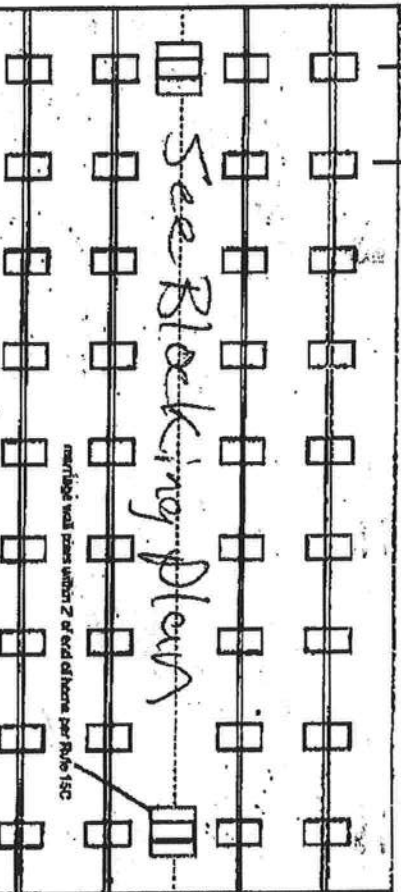

TH 1025249

PIERSPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	16' x 16' (256)	18' 1/2' x 18' (324)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'	5'	6'	7'	8'	9'
2000 psf	5'	6'	7'	8'	9'	10'
2500 psf	6'	7'	8'	9'	10'	11'
3000 psf	7'	8'	9'	10'	11'	12'
3500 psf	8'	9'	10'	11'	12'	13'

Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size: 23x31
Perimeter pier pad size: 17.5x25.5
Other pier pad sizes (required by the mfg.):

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening Pier pad size

See Blocking Plan

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer: Oliver 1101 V
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer: Oliver 1101 V

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Sidewall Longitudinal Marriage wall Shearwall

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to psi or check here to declare 1000 lb. soil without testing.

x 1000 x 1000 x 1000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1000 x 1000 x 1000

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5 anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Ernest S Johnson

Date Tested

Assumed Oliver 11/01/17

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Site Preparation

Debris and organic material removed

Water drainage: Natural Swale

Fastening multi-wide units

Floor: Type Fastener: 1/4" x 3" Length: 7" Spacing: 20"

Walls: Type Fastener: 1/4" x 3" Length: 7" Spacing: 20"

Roof: For used homes - 3/4" x 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherstripping, requirement) _____

Installer's initials

Type gasket

Pg. 11

Installed: Between Floors Yes Between Walls Yes Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or tapered. Yes

Skirting to be installed. Yes No

Dryer vent installed outside or skirting. Yes

Range downflow vent installed outside of skirting. Yes

Drain lines supported at 4 foot intervals. Yes

Electrical crossovers protected. Yes

Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature


Ernest S Johnson Date

Shell



- 1

Zone III

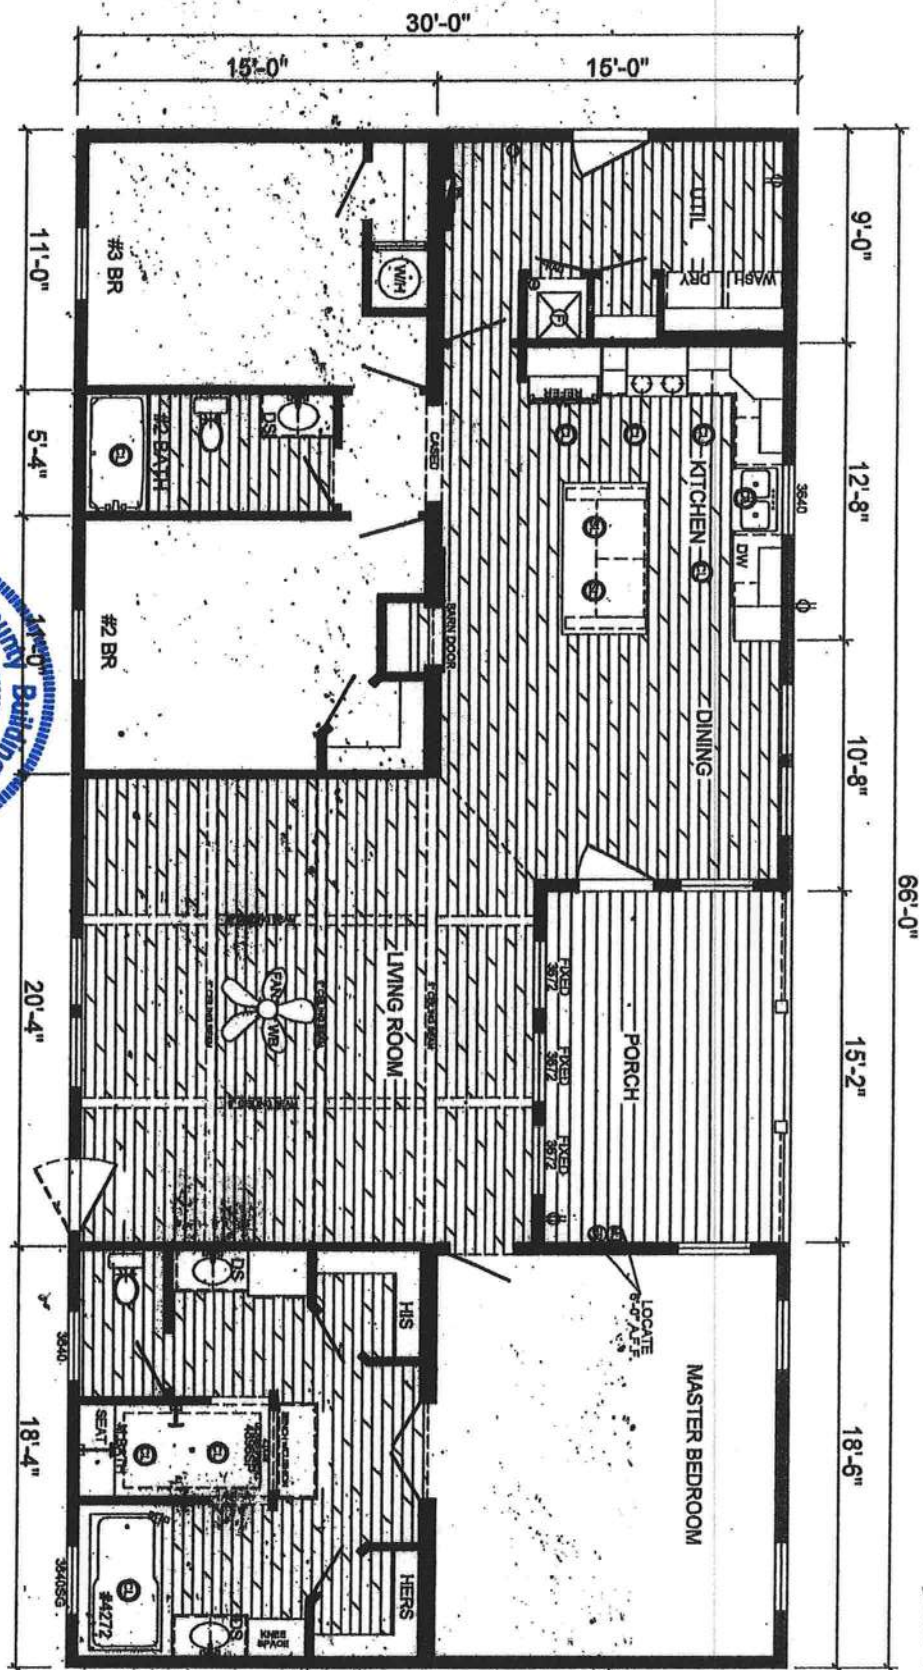

SERIAL: ELVIS692
MODEL: WL-7012B
3-BEDROOM / 2-BATH
32 x 70 - Approx. 1980 Sq. Ft.



DEER VALLEY HOMEBUILDERS, INC.
Woodland Homes Series

**For more information visit us at
www.deeralleyvib.com**

"STOCK"

DATE:
08/05/2019

***All rooms dimensions include closets and square footage are approximate.**

Drawn by:
JM
