

COLUMBIA COUNTY PERMIT WORKSHEET

These worksheets must be completed and signed by the installer.
Submit the originals with the packet.

Installer Rusty L. Knocks License # EH-1038219

911 Address where home is being installed SW Buck Court
14 White FL 32038

Manufacturer Fleetwood Length x width 14x70

NOTE: If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Installer's initials AK

New Home ☐ Used Home ☒
Home installed to the Manufacturer's Installation Manual ☐
Home is installed in accordance with Rule 15-C ☐
Single wide ☒ Wind Zone II ☒ Wind Zone III ☐
Double wide ☐ Installation Decal # 10196
Triple/Quad ☐ Serial # 6AFLP75A185130E
(726)

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	Footer size (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 dsf	3'	4'	5'	6'	7'	8'
1500 dsf	4' 6"	6'	7'	8'	9'	10'
2000 dsf	6'	8'	9'	10'	11'	12'
2500 dsf	7' 6"	9'	10'	11'	12'	13'
3000 dsf	8'	10'	11'	12'	13'	14'
3500 dsf	8'	10'	11'	12'	13'	14'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 23 1/4 x 31 1/4
Perimeter pier pad size NA
Other pier pad sizes 16x16
(required by the rule.)

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
18 x 18	324
20 x 20	400
22 x 22	484
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening NA Pier pad size

ANCHORS


4 ft ☒ 5 ft ☒

FRAME TIES

Longitudinal Stabilizing Device (LSD)
Manufacturer DL Systems
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer DL Systems

OTHER TIES

Number
Sidewall 24
Longitudinal 24
Marriage wall NA
Shearwall 24

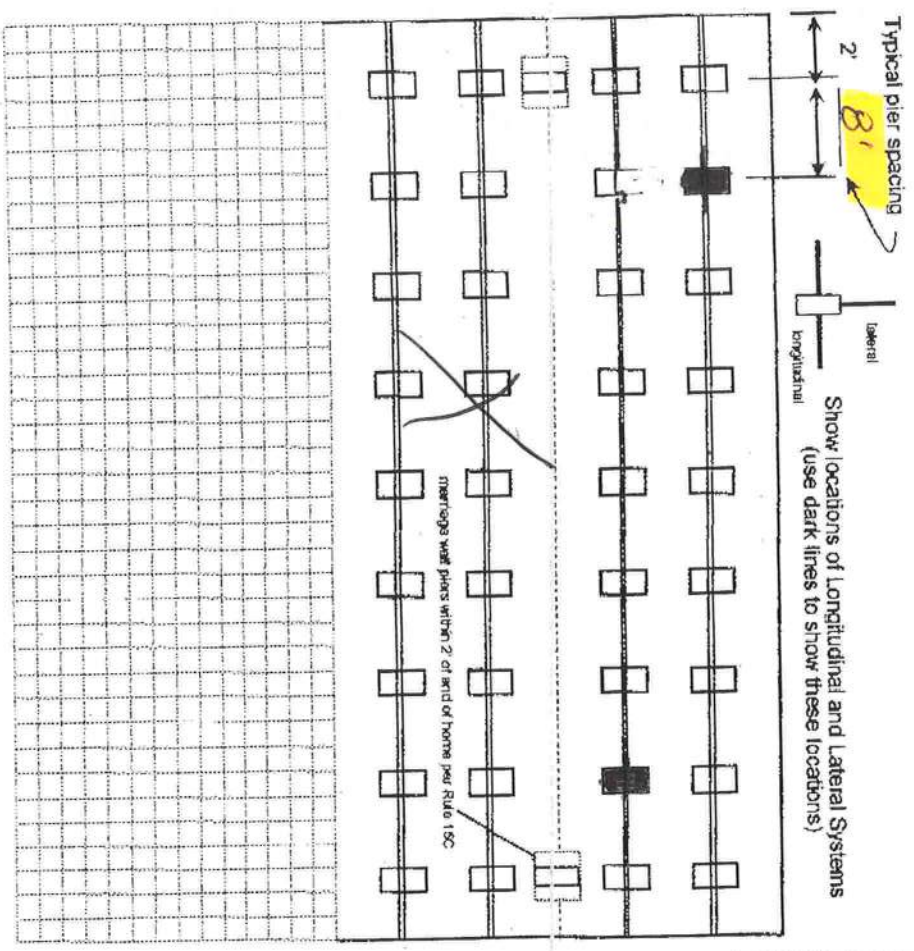

COLUMBIA COUNTY PERMIT WORKSHEET

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf
or check here to declare 1000 lb. soil ☒ without testing.

x 1.0

x 1.0

x 1.0

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1.0

x 1.0

x 1.0

TORQUE PROBE TEST

The results of the torque probe test is N/A 4518/11014 inch pounds or check here if you are declaring 5' anchors without testing _____ A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewall locations. 1 understand 5 ft anchors are required at all centerline the points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

RLK Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Rushy L. Knodes

Date Tested

7-27-12

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 15C-1

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 15C-1

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 15C-1

Site Preparation

Debris and organic material removed ☒
Water drainage: Natural ☒ Swale ☐ Pad ☒ Other ☐

Fastening multi wide units

Floor: Type Fastener: N/A Length: _____ Spacing: _____
Walls: Type Fastener: N/A Length: _____ Spacing: _____
Roof: Type Fastener: N/A Length: _____ Spacing: _____
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

RLKType gasket N/APg. _____

Installed:

Between Floors Yes ☐
Between Walls Yes ☐
Bottom of ridgebeam Yes ☐

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 15C-1
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes N/A

Miscellaneous

Skirting to be installed. Yes ☒ No ☐
Dryer vent installed outside of skirting. Yes ☐ N/A ☒
Range downflow vent installed outside of skirting. Yes ☐ N/A ☒
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes N/A
Other: 15C-1 may or may not have page #


NO PLUMBING

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature

Date 7-27-12

14X70

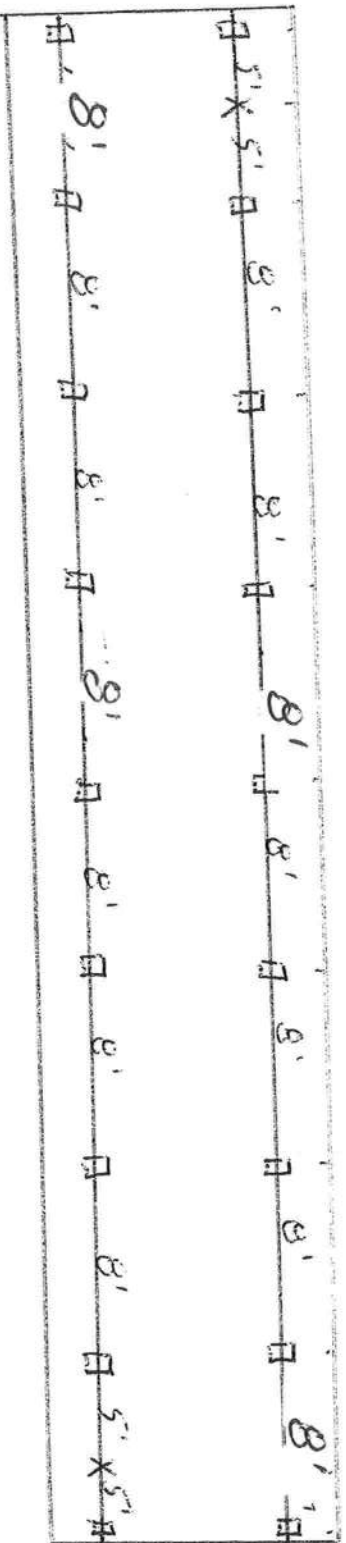

X-2 1101V All steel foundations from other technology

□ - I Beam piers 8' o.c. using 23 1/4 x 31 1/4 Abs pnd.s

Rocky 7-0

North



Columbia County Property Appraiser

J. Doyle Crews - Lake City, Florida 32055 | 386-758-1083

NOTES:

PARCEL: 20-7S-17-10027-122 - MOBILE HOM (000200)
COMM SW COR, RUN E 85 FT, N 144.2 FT TO POB, CONT N 361.80 FT, E 1235.48 FT, S 361.80 FT, W 1235.48 FT TO POB, AKALOT 22 COX SURVEY OFF US-27, ORB

2011 Certified Values

Land	\$49,962.00
Bldg	\$21,662.00
Aspd	\$59,317.00
Exmpl	\$34,317.00
Taxbl	Chrg: \$25,000
	Other: \$25,000 Schl: \$34,317

Name: LOMAS DAVID B
Site: 429 SW BUCK CT
Mail: 429 SW BUCK CT
Info: 3/1/1987



This information, updated 6/7/2012, was derived from data which was compiled by the Columbia County Property Appraiser's Office solely for the governmental purpose of property assessment. This information should not be relied upon by anyone as a determination of the ownership of property or market value. No warranties, expressed or implied, are provided for the accuracy of the data herein, its use, or its interpretation. Although it is periodically updated, this information may not reflect the data currently on file in the Property Appraiser's office. The assessed values are NOT certified values and therefore are subject to change before being finalized for ad valorem assessment purposes.

powered by
gizzylogic.com
