

Aliguyen

PERMIT WORKSHEET

page 1 of 2

PERMIT NUMBER

Installer Ernest Scott Johnson License # 147

Owner Name & Address of home being installed
5014 SW Ichetucknee Ave
Alt White Fl 32033


Manufacturer Clayton Length x width 29x48

NOTE: If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home


I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall has exceed 5 ft 4 ft.

Installer's initials [Signature]

Typical pier spacing



Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

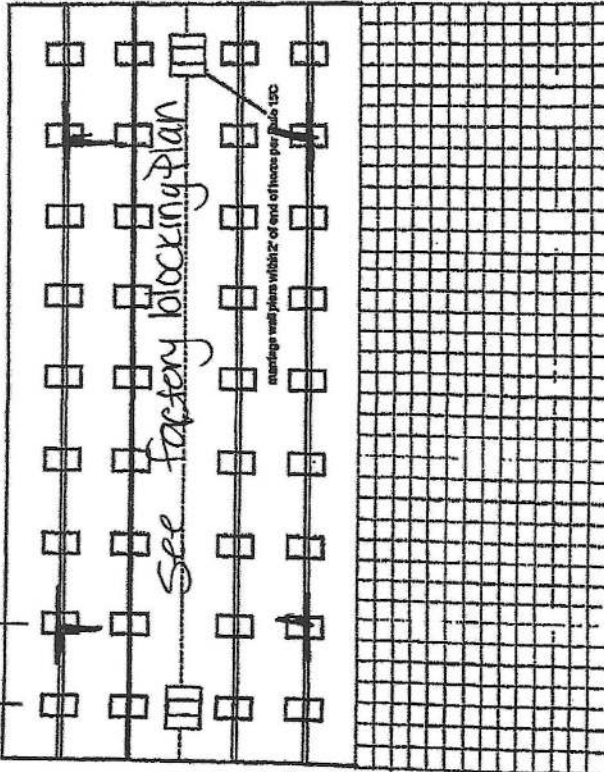

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16' x 16' (256)	18' x 12' x 18' 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4'	5'	6'	7'	8'	8'	8'
2000 psf	5'	6'	7'	8'	8'	8'	8'
2500 psf	6'	7'	8'	8'	8'	8'	8'
3000 psf	7'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table

POPULAR PAD SIZES

Pad Size	Sq in
16' x 16'	256
18' x 18'	324
18' x 18.5'	342
16' x 22.5'	360
17' x 22'	374
13' 1/4' x 26' 1/4'	348
20' x 20'	400
17' 1/2' x 22' 1/2'	432
17' 3/16' x 25' 3/16'	441
24' x 24'	576
26' x 26'	676

PIER PAD SIZES

I-beam pier pad size 23x31
Perimeter pier pad size or 17.5x15.5

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.



List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening 3'-2" Pier pad size factory

Opening blocking plan

ANCHORS
4 ft 5 ft

FRAME TIES
within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer Longitudinal
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer Longitudinal

Oliver 1101V

PERMIT WORKSHEET

page 2 of 2

PERMIT NUMBER

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to
or check here to declare 1000 lb. soil without testing.

$\times 1000$ $\times 1000$ $\times 1000$

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

$\times 1000$ $\times 1000$ $\times 1000$

TORQUE PROBE TEST

The results of the torque probe test is
here if you are declaring 5' anchors without testing
showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewalk locations. Undersound 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb. holding capacity.

Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Ernest Scott Johnson

Date Tested

Assumed Oliver 11/11/17
UGS 4:51 Anchors

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg.

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg.

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg.

Site Preparation

Debris and organic material removed Swale (Pad) Other

Fastening multi wide units

Floor: Type Fastener: 1995 Length: 7 Spacing: 20
Walls: Type Fastener: 1995 Length: 10 Spacing: 10
Roof: Type Fastener: 1995 Length: 20 Spacing: 20
For use homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials

Type gasket

Pg. R11

Installed:

Between Floors Yes

Between Walls Yes

Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous

Skirting to be installed. Yes No

Dryer vent installed outside of skirting. Yes No

Range downflow vent installed outside of skirting. Yes N/A

Drain lines supported at 4 foot intervals. Yes

Electrical crossovers protected. Yes

Other:

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature Ernest Scott Johnson Date

All information on this worksheet must be filled out completely to be accepted.
