

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT		
Order #: 6912	Label #: 127181	Manufacturer: <u>LIVE OAK</u>
Homeowner: <u>HANCOCK / HERMESMAN</u>	Year Model: <u>2016</u>	(Check Size of Home) Single <u> </u> Double <u>X</u> Triple <u> </u>
Address: <u>SW LEGION DR</u>	Length & Width: <u>56/60 X 28</u>	HUD Label #: <u> </u>
City/State/Zip: <u>LAKE CITY FL 32024</u>	Type Longitudinal System: <u>OTI (6)</u>	Soil Bearing / PSF: <u> </u>
Phone #: <u> </u>	Type Lateral Arm System: <u>OTI (6)</u>	Torque Probe / in-lbs: <u> </u>
Date Installed: <u> </u>	New Home: <u>X</u> Used Home: <u> </u>	Permit #: <u> </u>
Installed Wind Zone: <u>II</u>	Data Plate Wind Zone: <u>II</u>	
Note: <u> </u>		

**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

127181

LABEL #	DATE OF INSTALLATION
DAVID E ALBRIGHT	
NAME	
IH / 1129420 / 1	6912
LICENSE #	ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325 AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS
<p>PLEASE WRITE DATE OF INSTALLATION AND AFFIX LABEL NEXT TO HUD LABEL. USE PERMANENT INK PEN OR MARKER ONLY. COMPLETE INFORMATION ABOVE AND KEEP ON FILE FOR A MINIMUM OF 2 YEARS. YOU ARE REQUIRED TO PROVIDE COPIES WHEN REQUESTED.</p>

Mobile Home Permit Worksheet DW

Application Number: _____

Date: _____

New Home Used Home

Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C

Single wide Wind Zone II Wind Zone III


Double wide Installation Decal # 127181

Triple/Quad Serial # LOHGA30076314AB


Installer: DAVID AIRBRIGHT License # 14-LL29420
Address of home being installed: TBD SW Legion Dr Lake City FL 32024

Manufacturer Live Oak Length x width 28x56/60

NOTE: If home is a single wide fill out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in. Installer's Initials [Signature]



Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

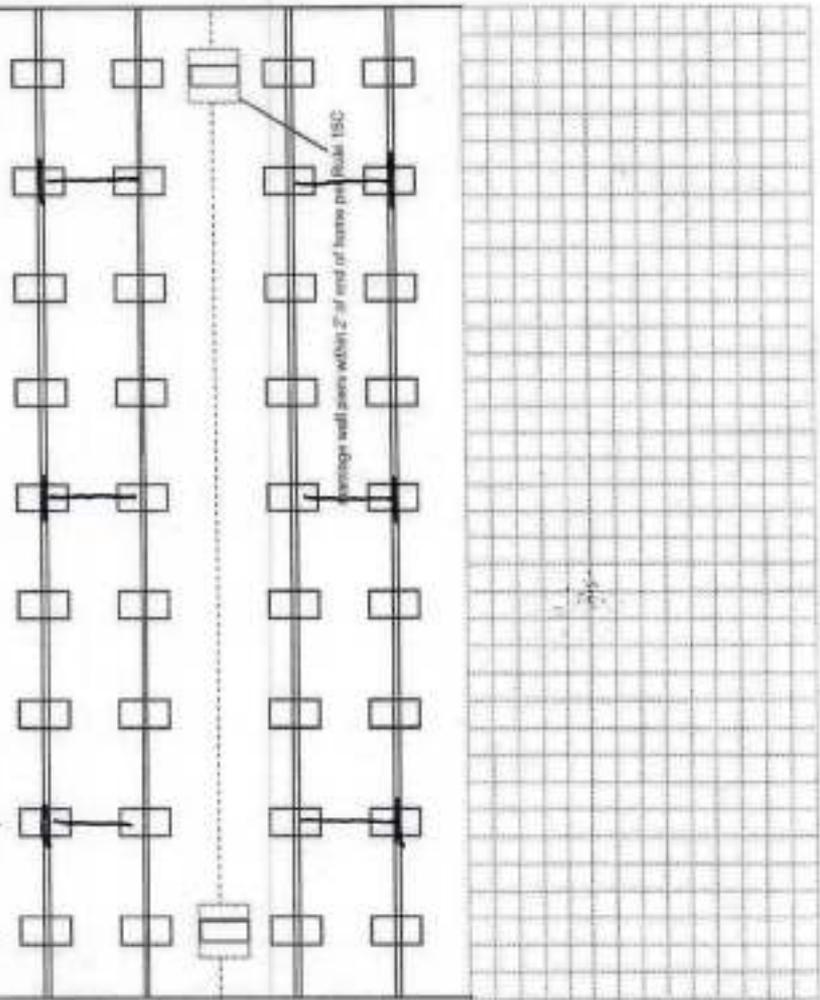

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq ft)	16' x 16' (256)	18 1/2' x 18 1/2' (342)	20' x 20' (400)	22' x 22' (484)*	24' x 24' (576)*	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4'-6"	6'	7'	8'	8'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'	8'
2500 psf	7'-6"	8'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17 x 25

Perimeter pier pad size 16 x 16

Other pier pad sizes (required by the mfg.) _____

POPULAR PAD SIZES

Pad Size	Sq. In.
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening FACTORY Pier pad size DIAGRAM

ANCHORS

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" OC

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer CHIVER TECHNOLOGIES

Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer CHIVER TECHNOLOGIES

OTHER TIES

Number 6

Sidewall 6

Longitudinal 1-3-5-4

Marriage wall 4

Shearwall 4

Mobile Home Permit Worksheet

Application Number: _____ Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ pcf or check here to declare 1000 lb. soil without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 150 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lbs. holding capacity.

Installer Name DAVID AUBRIGHT MOBILE HOME SVC

Date Tested _____

Electrical

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 70

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 101

Site Preparation

Debris and organic material removed Pad Other _____
Water drainage: Natural Swale

Fastening multi wide units

Floor: Type Fastener: LAG Length: 6" Spacing: 2'
Walls: Type Fastener: SCREW Length: 4" Spacing: 18"
Roof: Type Fastener: LAG Length: 6" Spacing: 2'
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirements)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled rafter walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials _____

Type gasket Pg. 36

Installed:
Between Floors Yes Pg. 119
Between Walls Yes END WALLS
Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes Pg. 119
Sliding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes


Miscellaneous

Skirting to be installed. Yes _____ No
Dryer vent installed outside of skirting. Yes _____ N/A
Range downflow vent installed outside of skirting. Yes _____
Drain lines supported at 4 foot intervals. Yes N/A
Electrical crossovers protected. Yes
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature David Aubright Date _____

SW Legion Dr

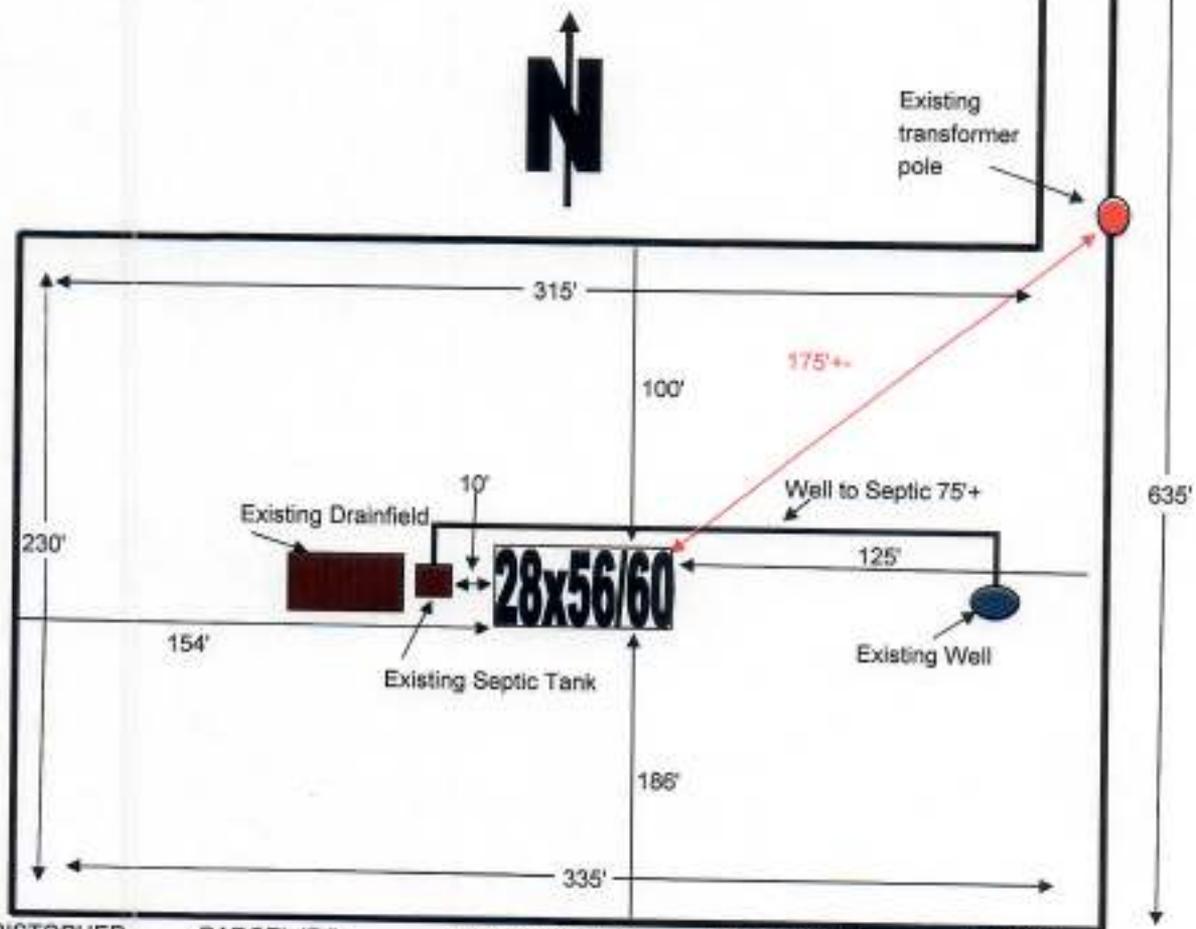

BUYER
ACREAGE

HANCOCK, CHRISTOPHER
1.98

PARCEL ID# 16-4S-16-03041-030
DEALER: STARS & STRIPES 396-365-8549

DATE DRAWN 1/7/2025
