

COLUMBIA COUNTY PERMIT WORKSHEET

Permit Number _____



Date **7/17/2023**Installer **ROY M. HARVEY** License # **IH1122397**Address of home
being installed _____Manufacturer **NOBILITY** Length x width **28' X 56'**

NOTE: If home is a single wide fill out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall has exceed 5 ft 4 in.

Installer's initials **RMH**

Typ. Lateral pier spacing

7'

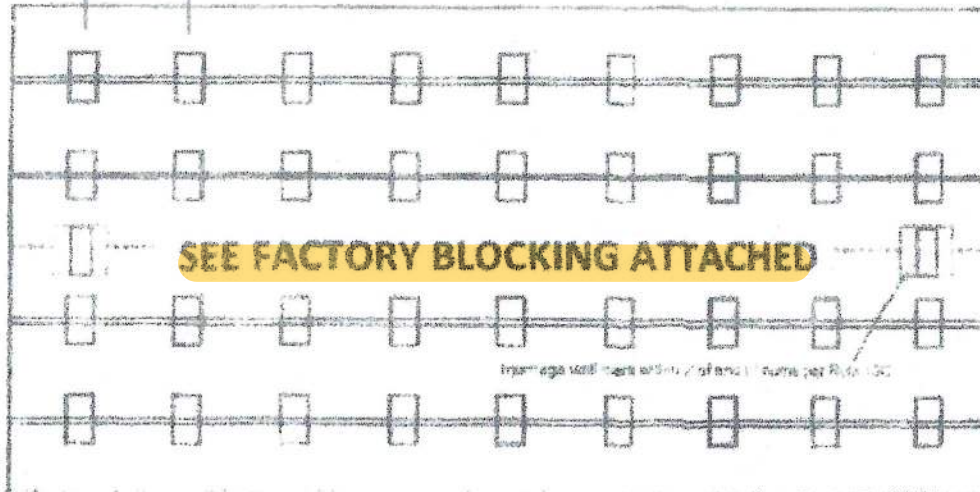Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

Marrage wall must extend 2' of end of home per Rule 15C



Anthony Islam
08-10-2023

New Home ☒ Used Home ☐Home installed to the Manufacturer's Installation Manual ☒
Home is installed in accordance with Rule 15-C ☐Single wide ☐ Wind Zone II ☒ Wind Zone III ☐Double wide ☒ Installation Detail # _____Triple/Quad ☐ Serial # _____

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Pier size (sq. ft.)	16' x 16' (256)	18 1/2" x 18 1/2" (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	3'	4'	5'	5'	7'	8'
1500 psf	4'	4'	5'	6'	6'	8'	9'
2000 psf	5'	5'	6'	7'	7'	9'	10'
2500 psf	6'	6'	7'	8'	8'	10'	11'
3000 psf	7'	7'	8'	9'	9'	11'	12'
3500 psf	8'	8'	9'	10'	10'	12'	13'

* Interpolated from Rule 15C-1 pier spacing table.

PIERPAD SIZES

I-beam pier pad size

17" X 25"

Perimeter pier pad size

NA

Other pier pad sizes (required by the mfg.)

21" X 29"

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening
"A"Pier pad size
21" X 29"

POPULAR PAD SIZES

Pad Size	Sq. ft.
16 x 16	256
18 x 18	324
18.5 x 18.5	342
18 x 22.5	405
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/8 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft ☐

FRAME TIES

within 2' of end of home
spaced at 5' 4" oc

OTHER TIES

Number

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer **OLIVER TECH**

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer **OLIVER TECH**

Sidewall

Longitudinal

Marriage wall

Shearwall

COLUMBIA COUNTY PERMIT WORKSHEET

Permit Number: _____

Date: 7/17/2023

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb. soil without testing.

X 1700

X 1700

X 1700

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 1700

X 1700

X 1700

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 40% holding capacity.

Installer's initials RMH

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

ROY M. HARVEY

Installer Name

Date Tested

7/14/2023

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg 43

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 45

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg 44

Department of Growth Management
Building Division

Page 2 of 2

Site Preparation

Debris and organic material removed **YES**
Water drainage: Natural Swale Pad ☒ Other

Fastening multi wide units

Floor: Type Fastener LAGS Length: 6" Spacing: 16" o/c
Walls: Type Fastener NAILS Length: 3" Spacing: 8" o/c
Roof: Type Fastener Length: Spacing: **FULL ROOF CAP**
For used homes a min. 30 gauge, 8" wide galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials RMH

Type gasket: **FOAM**
Pg **FACTORY INSTALLED**

Installed:
Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg **SU.58**
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous

Skirting to be installed. Yes ☒ No
Dryer vent installed outside of skirting. Yes ☒ N/A
Range downflow vent installed outside of skirting. Yes ☒ N/A
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other


Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature RMH

Date 7/17/2023

BF 27 MH Permit Worksheet
Revised September 28, 2010

1500 LB SOIL.....28' X 56'
 I BEAM PADS.....17" X 25".....7'o/c
 MARRIAGE WALL "A" PADS...29" X 21"
 OLIVER TECH STABILIZING SYSTEM
 4' ANCHORS@ 5'4" OR LESS

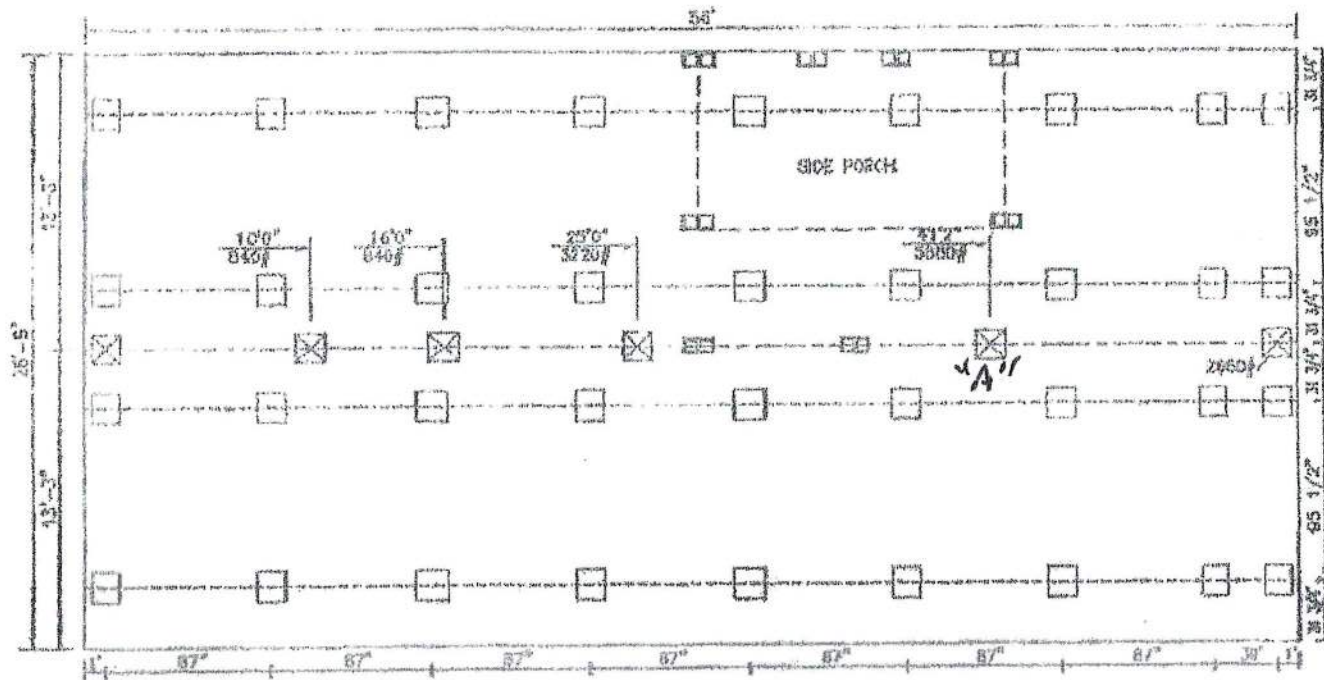

- NOTES: (1) COLUMN SUPPORT PIERS MAY BE WITHIN 8" OF OPENINGS GREATER THAN 48"
 (2) ADDITIONAL PIERS ARE REQUIRED AT EACH SIDE OF EXTERIOR DOOR OPENINGS.
 (3) THIS IS A TYPICAL DRAWING FOR THIS MODEL. SPACING MAY BE DIFFERENT IF MAX. SPACING IS NOT EXCEEDED.


- ☒ COLUMN SUPPORT PIERS
☐ 17" X 25" X 25 1/2" BASE PAD

SPACING FOR 1500 PSF SOIL WITH 17 1/2" X 25 1/2" BASE PAD
 MAXIMUM SPACING FOR THE I-BEAM PIERS IS 67"

	REVISIONS	6-17-28p66
	DATE 7-14-30	50E3D(25)
	SCALE	

Prestige Home Centers

ELI

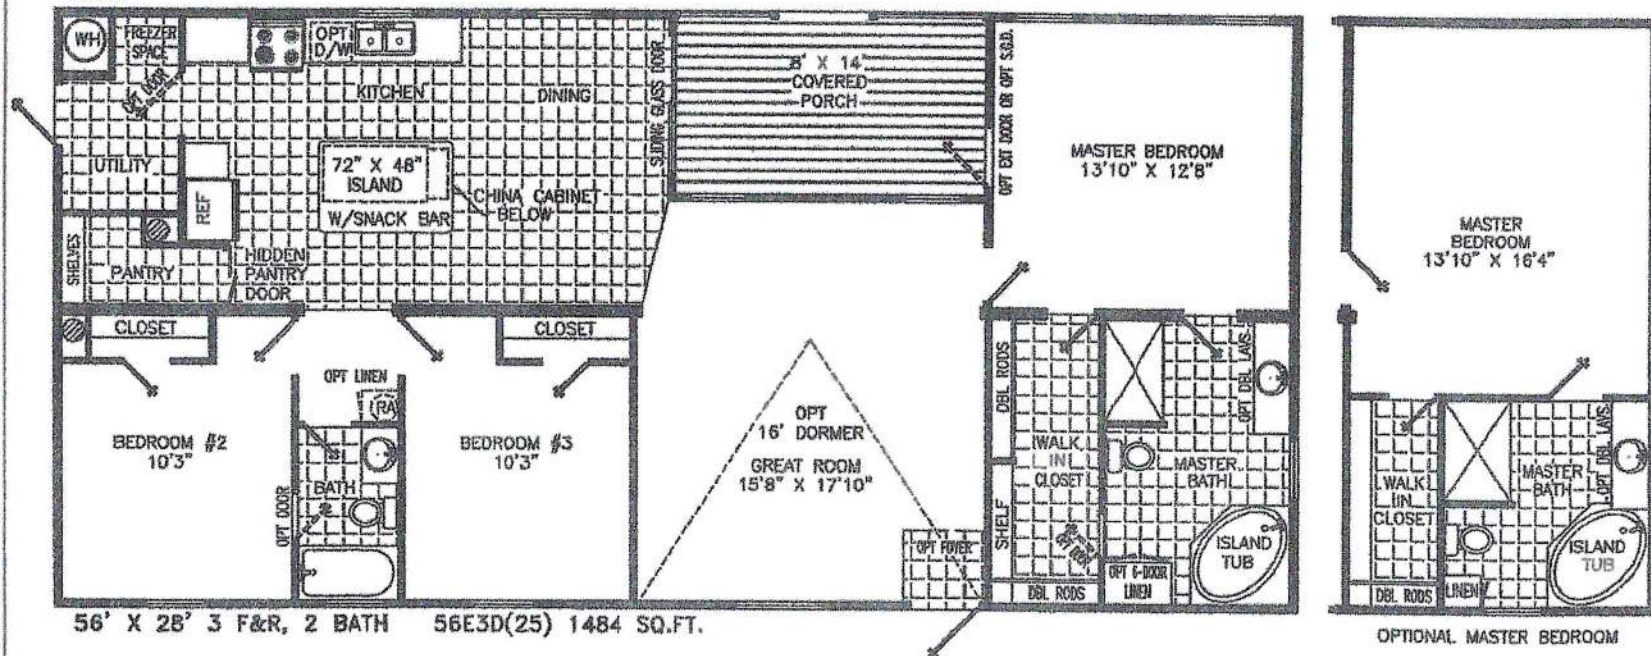

*Homes Designed, Built & Serviced
By NOBILITY HOMES*

MANUFACTURED IN ACCORDANCE WITH STANDARDS DEVELOPED AND ENFORCED BY HUD. DUE TO OUR CONTINUING PROGRAM OF PRODUCT IMPROVEMENT, PRICES AND SPECIFICATIONS ARE SUBJECT TO CHANGE WITHOUT NOTICE. SOME ITEMS SUCH AS TIRES, RIMS, AXLES AND HITCHES MAY HAVE BEEN RECYCLED AFTER INSPECTION FOR SAFETY AND APPEARANCE. ALL DIMENSIONS ARE NOMINAL.
