Installer: Tyler Brown License #IH1142500 325 NW Walter Mayo Glen Lake City Address of home being installed Manufacturer Live Oak Length x width 56X14 NOTE: if home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in. Installer's initials TB Typical pier spacing lateral Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations) Reviewed for Code Compliance / 07-17-2024 ate of Florid


Mobile Home Permit Worksheet

bl	olication	Numb	er:			Date	e:			
	New H	ome	X	Used Home						
	Home Home	installed is instal	to the Ma led in acco	anufacturer's Ins ordance with Ru	stallation M ile 15-C	Manual	Х			
Single wide			X	Wind Zone II	X	Wind Zon	ind Zone III			
Double wide				Installation De	06060	6060				
Triple/Quad Serial # LOHGA20038249										
			PIER SE	PACING TABLE	FOR US	ED HOME	S			
	Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" X 24" (576)*	26" x 26" (676)		
1	1000	psf	3'	4'	5'	6'	7'	8'		
	1500	psf	4' 6"	6'	7'	8'	8'	8,		
	2000	psf	6'	8'	8'	8'	8'	8'		
	2500	psf	7' 6"	8'	8'	8'	8,	8'		
L	3000		8'	8'	8'	8'	8'	8'		
Ļ	3500	psf	8'	8'	8'	8'	8'	8'		
	interpola	ated from	Rule 15C-	1 pier spacing tab	ole.	500				
			PIER PA	D SIZES		POPI	JLAR PAI	SIZES		
	l-heam	pier pa	d eizo	174	-25	D.	Pad Size Sq In			
	Dodin	pici pa	u 5126	1/1	-		16 x 16 256			
	Perime	ter pier	pad size	16 X		16 x 18 288				
Perimeter pier pad size Other pier pad sizes						18.5 x 18.5 342 16 x 22.5 360				
					16					
	(require	ed by th	e mfg.)		1	17 x 22 374 13 1/4 x 26 1/4 348				
					13 1/					
		Draw th	ne approxi	mate locations	of marriag	e 2	20 x 20 400			
				oot or greater.	Use this					
	horselessed and	symbol	to show t	he piers.		17 1/	17 1/2 x 25 1/2 446			
	Liet all	morrios	a	-1		2	24 x 24 576			
	and the	marnag	ad sizes t	nings greater th	nan 4 root		26 x 26 676			
	and the	all biet h	ad sizes t	below.			ANCHOR	2		
	0	pening		Pier pad siz	•		ANOTION			
		Permis		r let pau siz	G	4 ft /	5 ft			
						710	5 10			
within 2' of end of home spaced at 5' 4" oc										
Longitudinal Stabilizing Device (LSD) Sidewall Number										
	Manuf	acturer	OLV	Sidewa						
	Manufacturer Column TCCh Longitudinal Stabilizing Device w/ Lateral Arms						Longitudinal			
	Manuf	acturer	OL'L							
Manufacturer Oliver Tich Shearwall								_6		

Mobile Home Permit Worksheet

The Workshield	Application Number:Date:
POCKET PENETROMETER TEST	Site Preparation
The pocket penetrometer tests are rounded down to or check here to declare 1000 lb. soil without testing.	Debris and organic material removed Water drainage: Natural Swale Pad Other
x x x	Fastening multi wide units
POCKET PENETROMETER TESTING METHOD 1. Test the perimeter of the home at 6 locations. 2. Take the reading at the depth of the footer. Plans Reviewed for Code Compliance	Floor: Type Fastener: Length: Spacing: Walls: Type Fastener: Length: Spacing: Roof: Type Fastener: Length: Spacing: For used homes a min. 30 gauge, 8 wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.
	Gasket (weatherproofing requirement)
3. Using 500 lb. increments, take the lowest reading and round down to that increment. X X X	I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, meldew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.
TORQUE PROBE TEST	Towards
The results of the torque probe test is tinch pounds or check here if you are declaring 5' anchors without testing A test showing 275 inch pounds or less will require 5 foot anchors.	Type gasket Instacted: Pg Between Walls Yes Bottom of ridgebeam Yes
Note: A state approved lateral arm system is being used and 4 ft.	Weatherproofing
anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.	The bottomboard will be repaired and/or taped. Yes A. Pg. Siding on units is installed to manufacturer's specifications. Yes Fireplace chimney installed so as not to allow intrusion of rain water. Yes
Installer's initials	Miscellaneous
Installer Name Date Tested ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER 1-7-24	Skirting to be installed. Yes AA No Dryer vent installed outside of skirting. Yes N/A Range downflow vent installed outside of skirting. Yes N/A Drain lines supported at 4 foot intervals. Yes Electrical crossovers protected. Yes AA Other:
Electrical	
Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg.	Installer verifies all information given with this permit worksheet
Plumbing	is accurate and true based on the
Connect all sewer drains to an existing sewer tap or septic tank. Pg	manufacturer's installation instructions and or Rule 15C-1 & 2
Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg	Installer Signature Ugu Date /- 7-29





SUPPORT PIER/TYP

1-31-2014

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND IT'S SUPPLEMENTS.
 FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.

Live Oak Homes MODEL: L-4562A - 14 X 60 2-BEDROOM / 2-BATH

Order #: 6038 Label #: 106060	Manufacturer:	(Check Size of Home)	
Homeowner: Mago	Year Model.	Single Double Triple	
Address:	Length & Width:		
City/State/Zip:	Type Longitudinal System	HUD Label #:	
Phone #:	Type Lateral Arm System:	Soil Bearing / PSF	
Date Installed:	New Home: Used Home:	Torque Probe / in-lbs:	
Installed Wind Zone:	Data Plate Wind Zone:	Permit #:	



STATE OF FLORIDA INSTALLATION CERTIFICATION LABEL

106060

LABEL#

DATE OF INSTALLATION

TYLER M BROWN

NAME

IH / 1142500 / 1

6038

LICENSE # ORDER #
CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320 8249, 320 8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF INSTALLATION AND AFFIX LABEL NEXT TO HUD LABEL. USE PERMANENT INK PEN OR MARKER ONLY. COMPLETE INFORMATION ABOVE AND KEEP ON FILE FOR A MINIMUM OF 2 YEARS. YOU ARE REQUIRED TO PROVIDE COPIES WHEN REQUESTED.



. 107

467 Swan Ave ● Hohenwald, TN 38462 ● (800) 284-7437 ● www.olivertechnologies.com ● Fax (931) 796-8811

OLIVER TECHNOLOGIES, INC. INSTALLATION INSTRUCTIONS FOR FLORIDA MODEL 1101 "V" SERIES ALL STEEL FOUNDATION SYSTEM PAN & CONCRETE (revision 5/18)

PATENT# 6634150 & OTHER PATENT PENDING





467 Swan Ave ● Hohenwald, TN 38462 ● (800) 284-7437 ● www.olivertechnologies.com ● Fax (931) 796-8811

OLIVER TECHNOLOGIES, INC. FLORIDA INSTALLATION INSTRUCTIONS FOR THE MODEL 1101 "V" SERIES ALL STEEL FOUNDATION SYSTEM

MODEL 1101"V" (Steps 1-14) **LONGITUDINAL ONLY: Follow Steps 1-9** LATERAL ONLY: Follow Steps 1-3 and Steps 10-14 FOR CONCRETE APPLICATIONS: Follow Steps 15-18

ENGINEERS STAMP

ENGINEERS STAMP

1.50"

SPECIAL CIRCUMSTANCES: If the following conditions occur - STOP! Contact Oliver Technologies at 1-800-284-7437:

a) Pier height exceeds 48"

PIER HEIGHT

- c) Roof eaves exceed 16"
- e) Location is within 1500 feet of coast

- b) length of home exceeds 76'
- d) Sidewall height exceed 96"

INSTALLATION OF GROUND PAN

2. Remove weeds and debris in an approximate two foot square to expose firm soil for each ground pan (C).

1.50"

3. Place ground pan (C) directly below chassis I-beam. Press or drive pan firmly into soil until flush or below soil then install pier per manufacturer's instructions or per Florida Regs.

SPECIAL NOTE: The longitudinal "V" brace system may also serve as a pier under the home and should be loaded as any other pier. It is recommended that after leveling piers, and one-third inch (1/3") before home is lowered completely on to piers, complete steps 4 through 9 below then remove jacks.

INSTALLATION OF LONGITUDINAL "V" BRACE SYSTEM (Model 1101 L "V")


NOTE: WHEN INSTALLING THE LONGITUDINAL SYSTEM ONLY, A MINIMUM OF 2 SYSTEMS PER FLOOR SECTION IS REQUIRED. SOIL TEST PROBE SHOULD BE USED TO DETERMINE CORRECT TYPE OF ANCHOR PER SOIL CLASSIFICATION. IF PROBE TEST READINGS ARE BETWEEN 175 & 275 A 5 FOOT ANCHOR MUST BE USED. IF PROBE TEST READINGS ARE BETWEEN 276 & 350 A 4 FOOT ANCHOR MAY BE USED. USE GROUND ANCHORS WITH DIAGONAL TIES AND STABILIZER PLATES EVERY 5'4". VERTICAL TIES ARE ALSO REQUIRED ON HOMES SUPPLIED WITH VERTICAL TIE CONNECTION POINTS (PER FLORIDA REG.).

4. Choose one of the approved longitudinal tube installations; either Diagram A or B. Then select the correct square tube (E) length from the diagram for appropriate pier height at support location or cut and drill 1.5" square tube to achieve appropriate length.

(40° Min 45° Max.)	Tube Length	Tube Length	
7 3/4" to 25"	22"	18"	
24 3/4" to 32 1 /4"	32"	18"	
33" to 41"	44"	18"	
40" to 48"	54"	18"	

1.25"

Diagram A



(40° Min 60° Max.)	Tube Length
14" to 18"	20"
18" to 25"	28"
24" to 35"	39"
30" to 40"	44"
36" to 48"	54"

Diagram B

- 5. Install (2) of the 1.50" square tubes (E) into the "U" bracket (J), insert carriage bolt and leave nut loose for final adjustment.
- 6. Place I-beam connector (F) loosely on the bottom flange of the I-beam.
- 7. (For Diagram A installation) Slide the selected 1.25" tube (E) into a 1.50" tube (E) and attach to I-beam connectors (F) and fasten loosely with bolt and nut. (For Diagram B installation) Attach the selected 1.5" tubes (E) to the I-beam connectors (F) and fasten loosely with bolts and nuts.
- 8. Repeat steps 6 through 7 to create the "V" pattern of the square tubes loosely in place.
- 9. Using standard hand tools tighten all nuts and bolts. (For Diagram A installation only, secure 1.25" and 1.50" tubes using four(4) 1 /4"-14 x 3/4" self-tapping screws in pre-drilled holes.)

INSTALLATION OF LATERAL TELESCOPING TRANSVERSE ARM SYSTEM (Model 1101 T "V")

THE MODEL 1101 "V" (LONGITUDINAL & LATERAL PROTECTION) ELIMINATES THE NEED FOR STABILIZER PLATES & FRAME TIES. NOTE: THE USE OF THIS SYSTEM REQUIRES VERTICAL TIES SPACED AT 5'4".

FOUR FOOT (4') GROUND ANCHOR MAY BE USED EXCEPT WHERE THE HOME MANUFACTURER SPECIFIES DIFFERENT.

- 10. Install remaining vertical tie-down straps and 4' ground anchors per home manufacturer's instructions. NOTE: Centerline anchors to be sized according to soil torque condition. Any manufacturer's specifications for sidewall anchor loads in excess of 4,000 lbs. require a 5' anchor per Florida Code.
- 11. Select the correct square tube brace (H) length for set-up lateral transverse at support location. The lengths come in either 60" or 72" lengths. (With the 1.50" tube as the bottom tube, and the 1.25" tube as the inserted tube.)
- 12. Install the 1.50 transverse brace (H) to the ground pan connector (D) with bolt and nut.
- 13. Slide 1.25" transverse brace into the 1.50" brace and attach to adjacent I-beam connector (I) with bolt and nut.
- 14. Secure 1.50" transverse arm to 1.25" transverse arm using four (4) 1 /4" 14 x 3/4" self-tapping screws in pre-drilled holes.

Page

DUNIER Technologies, Inc.



467 Swan Ave ● Hohenwald, TN 38462 ● (800) 284-7437 ● www.olivertechnologies.com ● Fax (931) 796-8811

INSTALLATION USING CONCRETE RUNNER/ FOOTER

- 15. A concrete runner, footer or slab may be used in place of the steel ground pan.
 - a) The concrete shall be minimum 2500 psi mix
 - b) A concrete runner may be either longitudinal or transverse, and must be a minimum of 8" deep with a minimum width of 16 inches longitudinally or 18 inches transverse to allow proper distance between the concrete bolt and the edge of the concrete (see below).
 - c) Footers must have minimum surface area of 441 sq. in. (I.e. 21" square), and must be a minimum of 8" deep.
 - d) If a full slab is used, the depth must be a 4" minimum . Special inspection of the system bracket installation is not required. Footers must allow for at least 4" from the concrete bolt to the edge of the concrete.

NOTE: The bottom of all footings, pads, slabs and runners must be per local jurisdiction.

LONGITUDINAL: (Model 1101 LC "V")

16. When using Part# 1101-W-CPCA (wetset) simply install the bracket in runner/footer OR When installing in cured concrete use Part# 101-D-CPCA (dryset). The 1101 (dryset) CA bracket is attached to the concrete using (2) 5/8"x3" concrete wedge bolts (Simpson part # S162300H 5/8" X 3" or Powers equivalent). Place the CA bracket in desired location. Mark bolt hole locations, then using a 5/8" diameter masonry bit, drill a hole to a minimum depth of 3". Make sure all dust and concrete is blown out of the holes. Place wedge bolts into drille holes, then place 1101 (dry set) CA bracket onto wedge bolts and start wedge bolt nuts. Take a hammer and lightly drive the wedge bolts down by hitting the nut (making sure not to hit the top of threads on bolt). The sleeve of concrete wedge bolt needs to be at or below th top of concrete. Complete by tightening nuts.


LATERAL: (Model 1101 TC "V")


- 17. For wet set (part # 1101-W-TACA) installation simply install the anchor bolt into runner/footer. For dry set installation (part # 1101-D-TACA) mark bolt hole locations, then using a 5/8" diam. masonry bit. drill a hole to a minimum depth of 3". Make sure all dust and concrete is blown out of the hole. Place wedge bolts (Simpson part #S162300H 5/8" X 3" or Powers equivalent) into (D) concrete dry transverse connector and into drilled hole. If needed, take a hammer and lightly drive the wedge bolts down by hitting the nut (making sure not to hit the top of threads on bolt), then remove the nut. The sleeve of concrete wedge bolt needs to be at or below the top of concrete.
- 18. When using part# 1101 CVW (wetset) or 1101 CVD (dryset), install per steps 17 & 18.


Notes:

- 1. LENGTH OF HOUSE IS THE ACTUAL BOX SIZE
- 2. —= LOCATION OF TRANSVERSE BRACING ONLY
- 3 🛛 = LOCATION OF LONGITUDINAL BRACING ONLY
- 4. F- = TRANSVERSE AND LONGITUDINAL LOCATIONS


ALL WIDTHS AND LENGTHS UP TO 52'









ALL WIDTHS AND LENGTHS OVER 52' TO 80"








HOMES WITH 5/12 ROOF PITCH REQUIRE: PER FLORIDA REGULATIONS 6 systems for home lengths up to 52' and 8 systems for homes over 52' and up 80'.

PATENT# 6634150 & OTHER PATENT PENDING

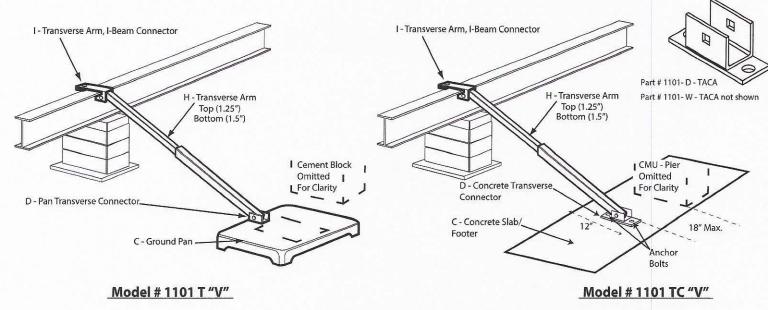

Florida approved 4' ground anchors may be used in all locations except where home manufacturers specifications for sidewall straps are in excess of 4,000 lbs. These locations require a 5' anchor. Per Florida code.

C = GROUND PAN / CONCRETE FOOTER OR RUNNER

D = GROUND PAN / CONCRETE U BRACKETS TRANSVERSE CONNECTOR (connects with grade 5 - 1/2" x 2" 1/2" carriage bolt and nut)


E = TELESCOPING V BRACE TUBE ASSEMBLY (1.5" TUBE BOTTOM AND 1.25" TUBE INSERT) OR 1.5" TUBE

F = "V" BRACE I-BEAM CONNECTOR ASSEMBLY

H = TELESCOPING TRANSVERSE ARM ASSEMBLY

I = TRANSVERSE ARM I-BEAM CONNECTOR (connects with grade 5 - 1/2" x 2" 1/2" carriage bolt and nut)

J = V PAN BRACKET (connects with grade 5 - 1/2" x 2" 1/2" carriage bolt and nut)

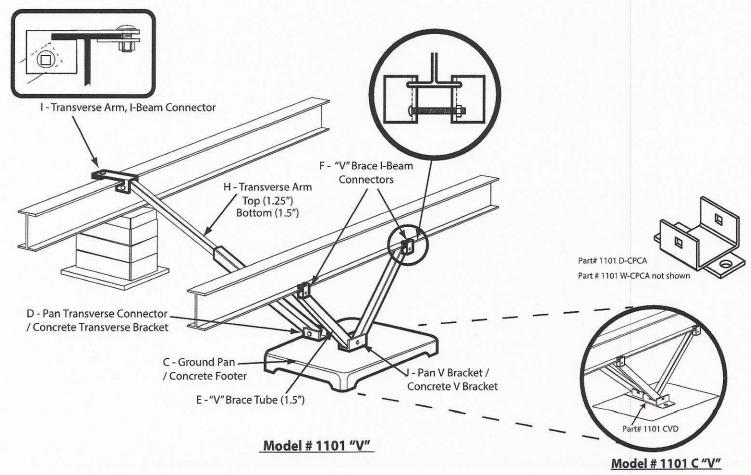



State of Florida DEPARTMENT OF HIGHWAY SAFETY AND MOTOR VEHICLES

TALLAHASSEE, FLORIDA 32399-0500

FRED O. DICKINSON, III

October 27, 1999

Mr. Lon Larson, General Manager
Manufactured Housing Foundation Systems
A Division of Oliver Technologies
562 Glenheather Drive
San Marcos, California 92069

Dear Mr. Larson:

We wish to acknowledge receipt of your print specifications and test results certifying your Adjustable Outrigger listed below complies with the Federal Manufactured Construction and Safety Standards, § 3280.305 and § 3280.401 and with the rules and regulations set forth by the Department of Highway Safety and Motor Vehicles, Florida Administrative Rule Code 15C-1.01105.

Based on the information submitted to the bureau, the following product is listed for use in Florida when the installation instructions showing the way the outrigger was tested, are provided.

MODEL#	INDENTIFICATION	DESCRIPTION		
1055-11	Adjustable Outrigger	Bracket, Pipe, & Screw Adjustment		

NOTE: The outrigger was tested on September 19, 1999, for an allowable load of 1700 pounds.

If you have any questions, please advise at (850) 413-7600.

Sincerely,

Phil Bergelt, Program Manager
Bureau of Mobile Home and

Recreational Vehicle Construction


Division of Motor Vehicles

PB:bsc

OLIVER TECHNOLOGIES, INC.

Adjustable Outrigger Installation Instructions MODEL # 1055-11

- 1. Locate the floor joist that requires support.
- 2. Mark the I-Beam directly under the floor joist to align the outrigger.
- 3. Adjust the nut on the threaded rod so it clears the frame flange for easy adjustment.
- 4. Set the threaded rod in the pipe and against the frame.
- 5. Set the notched end of the thrust bracket into the end of the pipe and secure it with 5 # 12 x 2" screws to the floor joist. The thrust bracket should be approximately 6" from the outside rim joist.
- 6. Bottom board and insulation should be between the bracket and the joist.
- 7. For minor adjustments align the door and window openings by tightening or loosening the adjustment nut. For all other adjustments use a hydraulic jack to raise the floor joist before installation of the outrigger.



NOTES:

*REMOVE OUTRIGGER WHEN HOME IS BEING TRANSPORTED

*SPECIFY WIDTH OF HOME WHEN ORDERING OUTRIGGER. PIPE MAY BE CUT TO FIT

*THE ADJUSTABLE OUTRIGGERS SHALL ONLY BE USED ON HOMES FOR OPENINGS UP TO:

Listing # 1055-11 Patent # 6.334.279

6' ON 20 LB ROOF LOAD


4' ON 30 LB ROOF LOAD

3' ON 40 LB ROOF LOAD

*WHEN ADJUSTABLE OUTRIGGERS ARE USED FOR DOOR AND WINDOW SUPPORTS, THEY MUST BE INSTALLED ON THE CLOSEST FLOOR JOIST UP TO 16" FROM THE OUTSIDE EDGE OF THE OPENING

*DO NOT INSTALL ADJUSTABLE OUTRIGGER AT LOCATIONS WHERE THE HOME MANUFACTURER INDICATES A LOAD IN EXCESS OF 1,700 LBS.
*THE ADJUSTABLE OUTRIGGER MUST BE USED ON A MINIMUM 10" I-BEAM AND BE PLACED WITHIN 4' OF A MAIN FRAME SUPPORT PIER OR FRAME CROSSMEMBER.

DOUBLE WIDE ON-SITE FASTENING

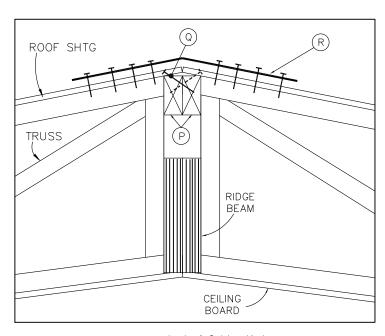

ROOF FASTENING

FLOOR DECKING S RIM **FLOOR** JOIST JOIST


FLOOR FASTENING

WIND ZONE 1

- CONTINUOUS WOOD BLOCKING EACH HALF (MAY BE FULL HEIGHT RIDGE BEAM-NOT SHOWN)
- #10 x 4" WOOD SCREWS 8" O.C. STAGGERED FROM SIDE TO SIDE AT 30 DEG ANGLE FROM HORIZONTAL*
- 26GA. x 1-1/2" STEEL STRAP LOCATED ABOVE TRUSSES SPACED AT MAXIMUM OF 96" O.C. FASTENED AT EACH END WITH: (10) 15GA. \times 1-1/2" STAPLES OR

 - (6) 8D COMMON NAILS OR
 - (5) #10 x 1-1/2" WOOD SCREWS
 - IN LIEU OF (R) AND (Q) ABOVE MAY INSTALL A CONTINUOUS 30 GA. \times 6" MINIMUM STEEL ROOF CAP OVER 15# FELT WITH: (2) #10 \times 1-1/2" SCREWS EACH TRUSS AT 16" O.C. (3) #10 \times 1-1/2" SCREWS EACH TRUSS AT 24" O.C.

 - OR (6) .082" X 1-1/2" NAILS EACH TRUSS AT 16" O.C. OR
 - (9) .082" X 1-1/2" NAILS EACH TRUSS AT 24" O.C.
 - OR
 - (5) 16 GA X 1" STAPLES EACH TRUSS AT 16" O.C. OR (7) 16 GA X 1" STAPLES EACH TRUSS AT 24" O.C.




- #10 X 4" WOOD SCREWS 10" O.C. STAGGERED FROM SIDE TO SIDE AT 30 DEG ANGLE FROM HORIZONTAL OR 3/8" X 4" LAG SCREWS 16" O.C. STAGGERED FROM SIDE TO SIDE AT 30 DEG ANGLE FROM HORIZONTAL*
- 26 GA. \times 1-1/2" STEEL STRAP SPACED 32" O.C. WITH (5) 8D COM NAILS EACH END OR (4) #10 \times 1-1/2" WOOD SCREWS EACH END OR (7) .120"X 1-1/4" NAILS EACH END OR
 - 26 GA. x 2-1/2" STEEL STRAP SPACED 48" O.C. WITH
 (8) 8D COM NAILS EACH END OR (6) #10 x 1-1/2" WOOD
 SCREWS EACH END OR (11) .120"X 1-1/4" NAILS EACH END
 (ALL FASTENERS MUST PENETRATE INTO FLOOR JOISTS)

NOTE: BOTTOM BOARD NOT SHOWN FOR CLARITY. HOLES IN BOTTOM BOARD MUST BE PATCHED WITH A VINYL TAPE DESIGNED FOR REPAIRING TEARS AND HOLES.

*NOTE: ADJUST FASTENER LENGTHS FOR ANY GAPS BETWEEN THE MODULES TO OBTAIN THE SAME PENETRATION AND FILL ALL THE GAPS WITH SPF LUMBER OR PLYWOOD BEFORE INSTALLING THE FASTENERS — LAG SCREWS MUST PENE— TRATE THE BACK SIDE OF THE RIM JOIST BY A MINIMUM OF 1/4 INCH.

P.E. SEAL	THIRD PARTY		EVIS	IONS	LIVE OAK HOMES	
RTIFICADE			BY:	DATE:		OAK HOMES
No 0033841					DOUBLE WIDE ON-SITE FASTENING FIELD INSTALLED DRAWN BY: TC DAPIA NO.:	
STATE OF A THE STATE OF THE STA						
10/17/22	0/17/22					SC: N.T.S.

DOUBLE WIDE ON-SITE FASTENING

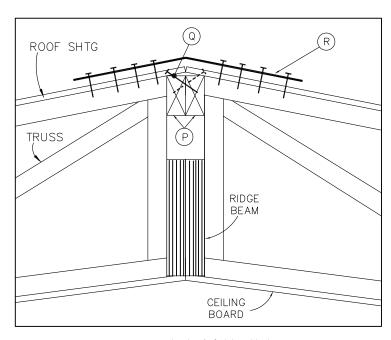


ROOF FASTENING

- CONTINUOUS WOOD BLOCKING EACH HALF (MAY BE FULL HEIGHT RIDGE BEAM-NOT SHOWN)
- #10 x 4" WOOD SCREWS 8" O.C. STAGGERED FROM "SIDE TO SIDE AT 30 DEG ANGLE FROM HORIZONTAL*
- 26GA. \times 1-1/2" STEEL STRAP LOCATED ABOVE TRUSSES SPACED AT MAXIMUM OF 96" O.C. IN ZONE 2 AND 80" O.C. IN ZONE 3 FASTENED AT EACH END WITH: (10) 15GA. \times 1–1/2" STAPLES OR
 - (6) 8D COMMON NAILS OR
 - (5) #10 x 1-1/2" WOOD SCREWS

IN LIEU OF \circledR AND \circledR ABOVE MAY INSTALL A CONTINUOUS 30 GA. \times 6" MINIMUM STEEL ROOF CAP OVER 15# FELT WITH: (2) #10 \times 1-1/2" SCREWS EACH TRUSS AT 16" O.C. (3) #10 \times 1-1/2" SCREWS EACH TRUSS AT 24" O.C.

- OR
- (6) .082" X 1-1/2" NAILS EACH TRUSS AT 16" O.C. OR (9) .082" X 1-1/2" NAILS EACH TRUSS AT 24" O.C OR
- (5) 16 GA X 1" STAPLES EACH TRUSS AT 16" O.C. OR (7) 16 GA X 1" STAPLES EACH TRUSS AT 24" O.C.




- #10 X 4" WOOD SCREWS 10" O.C. STAGGERED FROM SIDE TO SIDE AT 30 DEG ANGLE FROM HORIZONTAL OR 3/8" X 4" LAG SCREWS 16" O.C. STAGGERED FROM SIDE TO SIDE AT 30 DEG ANGLE FROM HORIZONTAL*
- 26 GA. x 1-1/2" STEEL STRAP SPACED 32" O.C. WITH (6) 8D COM NAILS EACH END OR (4) #10 x 1-1/2" WOOD SCREWS EACH END OR (7) .120"X 1-1/4" NAILS EACH END OR

26 GA. x 2-1/2" STEEL STRAP SPACED 48" O.C. WITH (9) 8D COM NAILS EACH END OR (8) #10 x 1-1/2" WOOD SCREWS EACH END OR (11) .120"X 1-1/4" NAILS EACH END (ALL FASTENERS MUST PENETRATE INTO FLOOR JOISTS)

NOTE: BOTTOM BOARD NOT SHOWN FOR CLARITY. HOLES IN BOTTOM BOARD MUST BE PATCHED WITH A VINYL TAPE DESIGNED FOR REPAIRING TEARS AND HOLES.

*NOTE: ADJUST FASTENER LENGTHS FOR ANY GAPS BETWEEN THE MODULES TO OBTAIN THE SAME PENETRATION AND FILL ALL THE GAPS WITH SPF LUMBER OR PLYWOOD BEFORE INSTALLING THE FASTENERS — LAG SCREWS MUST PENE— TRATE THE BACK SIDE OF THE RIM JOIST BY A MINIMUM OF 1/4 INCH.



FLOOR FASTENING

WIND ZONES 2 \$ 3

P.E. SEAL	THIRD PARTY	RE	EVIS	IONS		
NIM J. KALKER		LTR:	BY:	DATE:	LIVE	OAK HOMES
No 0033841 / * #					DOUBLE WIDE ON-SITE FASTENING	
STATE OF CONTROL OF CO					DRAWN BY: TC	FIELD INSTALLED DAPIA NO.:
10/17/22					DATE: 10/17/22	SC: N.T.S.

Horsia Building Code

Residential Section

R311 and R312

SINRETAINS

R311.7.2 Headroom

R311.7.5.1 Riser Height

R311.7.5.2 Tread Depth

R3117.8 Handralls


R311_7.B.2 Continuity

R311.7.8.3 Handrail Grip Size

R312.1.2 Guards

R312.1.3 Guard Opening Limits

Nenciscalar Handreii



bourgipulli final de part cheurine remut Levre de graffinalise of 4 ML Film and c. 25 ML film white a comme reasique cheumalise of 2.20 Mathew

