



HITCH-END

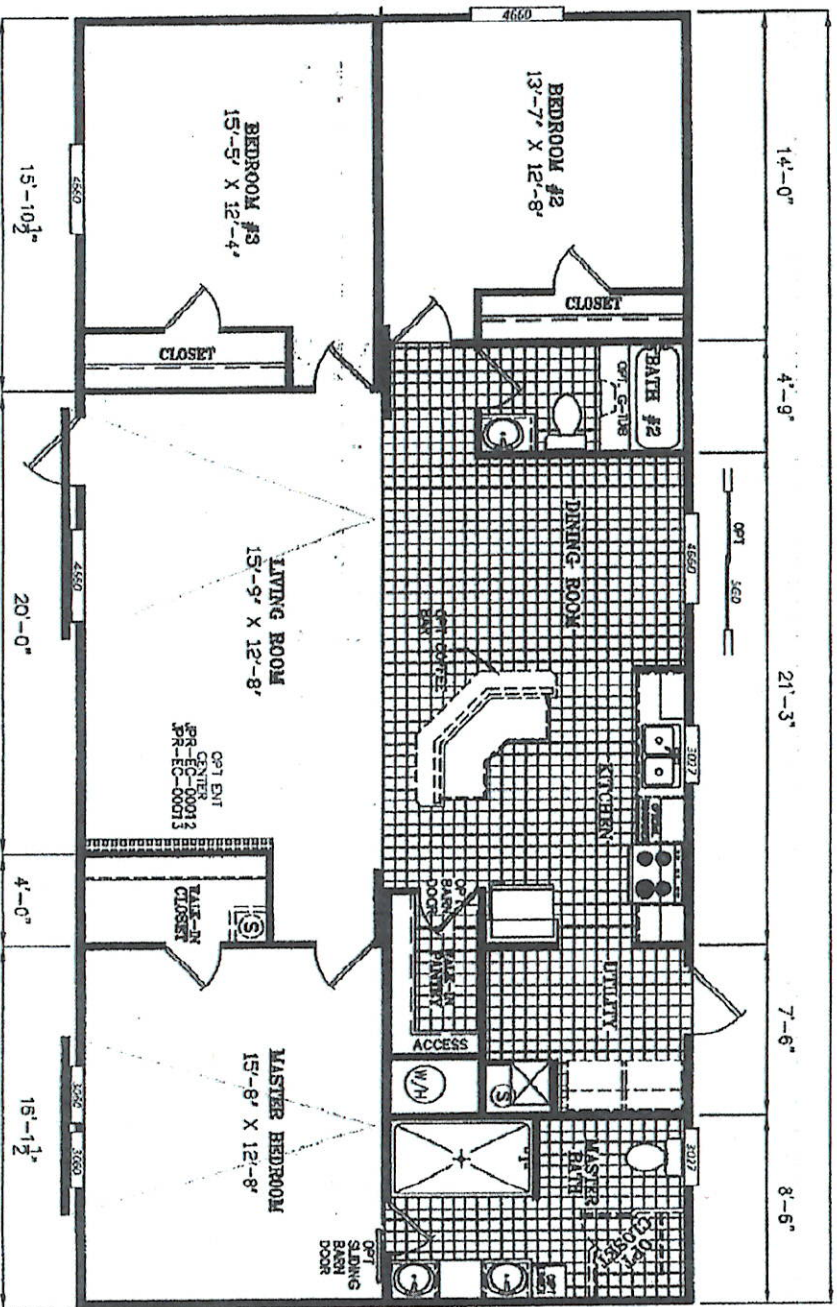

DATE:	02/02/2017	UNIT SPECIFICATIONS:	DRAWING/MODEL NUMBER:
VERSION	A	TOTAL: 1,456 sq ft	2856256GSM
REFERENCE: M256		LIVING SPACE: 1,456 sq ft	
		PORCH: 0 sq ft	
		GRAND SLAM	
		28' X 80'	
		3 BEDROOM / 2 BATH	

ScotBilt
 HOMES, INC.



T.	1,456 SQ. FT.
	0 SQ. FT.

PERMIT NUMBER

Installer

Ernest S. Johnson

License #

IH-1025429

Address of home being installed

Manufacturer

Scotbitt

Length x width

56' x 28'

NOTE:

If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.


Installer's initials

Typical pier spacing

Lateral

Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

Typical wall pier within 2' of end of home per Rule 15C

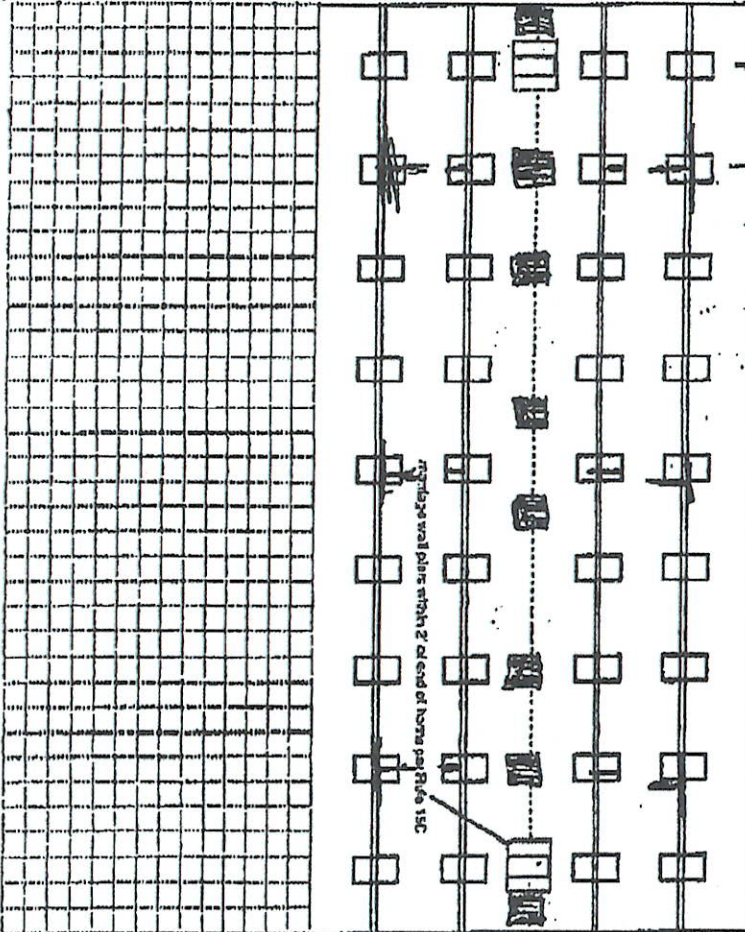

WORKSHEET

page 1 of 2

New Home



Used Home



Home installed to the Manufacturer's Installation Manual

Home is installed in accordance with Rule 15-C

Single wide



Wind Zone II



Wind Zone III



Double wide



Installation Decal #

074447

Triple/Quad



Serial #

Roof System: X Typical

Hinged

PIER SPACING TABLE FOR USED HOMES

Load Bearing Capacity (sq ft)	16' x 16' (256)	18' 1/2" x 18' 1/2" (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 PSI	3'	4'	5'	6'	7'	8'
1500 PSI	4' 6"	6'	7'	8'	9'	10'
2000 PSI	6'	8'	9'	10'	11'	12'
2500 PSI	7' 6"	9'	10'	11'	12'	13'
3000 PSI	8'	10'	11'	12'	13'	14'
3500 PSI	8'	10'	11'	12'	13'	14'

Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

7'0" 23'x31'

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

12'15"

17'5" x 25'5"

TEEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer
Longitudinal Stabilizing Device with Lateral Arms
Manufacturer

OTHER TIES

Sidewall
Longitudinal
Marriage wall
Shearwall

Number

30

10

2

Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil _____ without testing.

X 1000 X 1000 X 1000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 1000

X 1000

X 1000

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing _____ A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral anchoring system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. readings are required at all ceiling line the points where the torque test requires anchors with 1000 lb. locking capacity.

1. _____ Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Ernest S Johnson

Date Tested

Assured Oliver 11/01/19

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____
Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Application Number: _____

Date: _____

Site Preparation

Debris and organic material removed Yes
Water drainage: Natural Swale Pad X Other _____

Fastening multi wide units

Floor: Type Fastener: lag Length: 4" Spacing: 20"
Walls: Type Fastener: lag Length: 4" Spacing: 10"
Roof: Type Fastener: lag Length: 4" Spacing: 10"

For used homes - 8 min.-30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

Type gasket R-11

Pg. _____

Installed:

Between Floors Yes X
Between Walls Yes X
Bottom of ridgebeam Yes X

Weatherproofing

The bottomboard will be repaired and/or taped. Yes X Pg. _____
Siding on units is installed to manufacturer's specifications. Yes X
Fireplace chimney installed so as not to allow intrusion of rain water. Yes X

Miscellaneous

Skirting to be installed. Yes X No _____
Dryer vent installed outside of skirting. Yes X N/A _____
Range downflow vent installed outside of skirting. Yes _____ N/A X
Drain lines supported at 4 foot intervals. Yes X N/A _____
Electrical crossovers protected. Yes X Other _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Ernest S Johnson Date _____
