



Mobile Home Permit Worksheet

Application Number: _____ Date: _____

☒ New Home ☐ Used Home
 Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C ☒
 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Decal # order 2
 Triple/Quad ☐ Serial # order 74897

Installer: Fordy L. Brandy License # 41038249


Address of home being installed: _____

Manufacturer LINCOLN Length x width 26 x 50


NOTE: If home is a single wide fill out one half of the blocking plan.
 If home is a double or quad wide sketch in remainder of home.
 I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Installer's initials RB

Typical pier spacing



Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

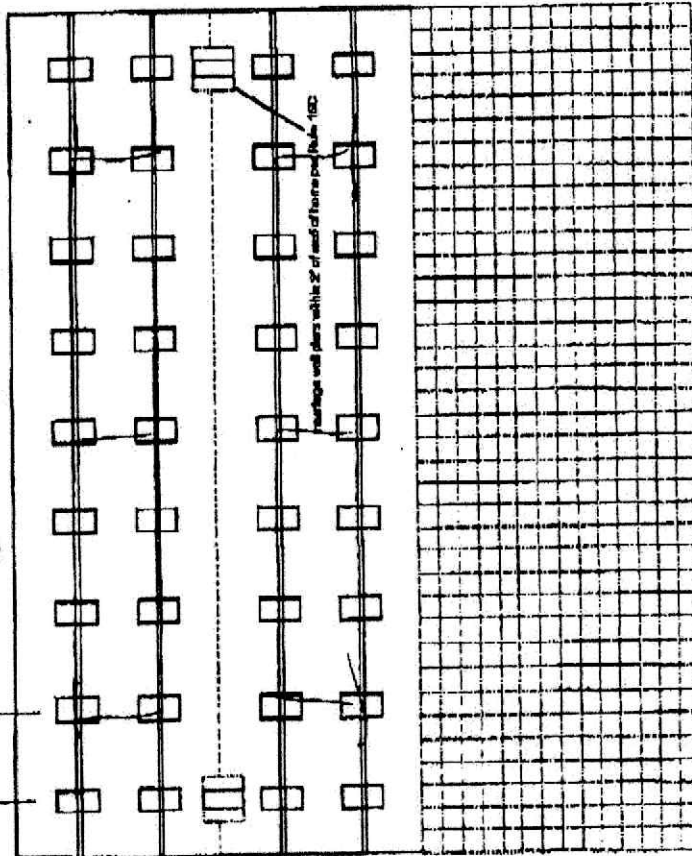

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footprint (sq ft)	16' x 16' (256)	10 1/2' x 18 1/2' (342)	20' x 20' (400)	22' x 22' (484)	14' x 24' (576)	25' x 26' (650)
1000 psf	3'	3'	4'	5'	6'	7'	8'
1500 psf	4'	4'	5'	6'	7'	8'	8'
2000 psf	5'	5'	6'	7'	8'	8'	8'
2500 psf	6'	6'	7'	8'	8'	8'	8'
3000 psf	7'	7'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 11 x 22.5
 Prefabricated pier pad size N/A
 Other pier pad sizes (required by the mfg.) 12 x 16

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the plans.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

ANCHORS

Opening 19' Pier pad size 12 x 16

FRAME TIES

Within 2' of end of home spaced at 5' 4" OC

OTHER TIES

Number 18

Longitudinal Stabilizing Device (LSD)
 Manufacturer _____
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer Overhead

TEDOWN COMPONENTS

Sidewall _____
 Longitudinal _____
 Marriage wall _____
 Shearwall _____

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 100 psi or check here to declare 1000 lb. soil without testing.

X 100 X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 8 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is NA 1000 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all cantilevered locations where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 11C-1


Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 11C-1

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 11C-1

Page 2 of 2

Debris and organic material removed		Seals		Pad		Other	
Water drainage: Natural							
Fastening nails/wide nails							
Floor:	Type Fastener:	Length:	Spacing:	Floor:	Type Fastener:	Length:	Spacing:
Walls:	Type Fastener:	Length:	Spacing:	Walls:	Type Fastener:	Length:	Spacing:
Roof:	Type Fastener:	Length:	Spacing:	Roof:	Type Fastener:	Length:	Spacing:
For used homes a min. 30 gauge, 6" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.							
I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and budged marlings walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.							
Installer's Initials							
Type gasket:	FA 4017	Installed:	Between Floors	Yes	Between Walls	Yes	Bottom of Ridgebeam
Weatherstripping							
The bottomboard will be retained and/or taped. Yes ☒ Pg. 11C-1							
Siding on units is installed to manufacturer's specifications. Yes ☒							
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒							
Siding to be installed. Yes ☒ No ☐							
Dryer vent installed outside of siding. Yes ☒ No ☐ N/A							
Range downflow vent installed outside of siding. Yes ☒ No ☐							
Drain lines supported at 4 foot intervals. Yes ☒ No ☐							
Electrical crossovers protected. Yes ☒ No ☐							
Other:							
Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2							
Installer Signature							
Date 1-7-25							

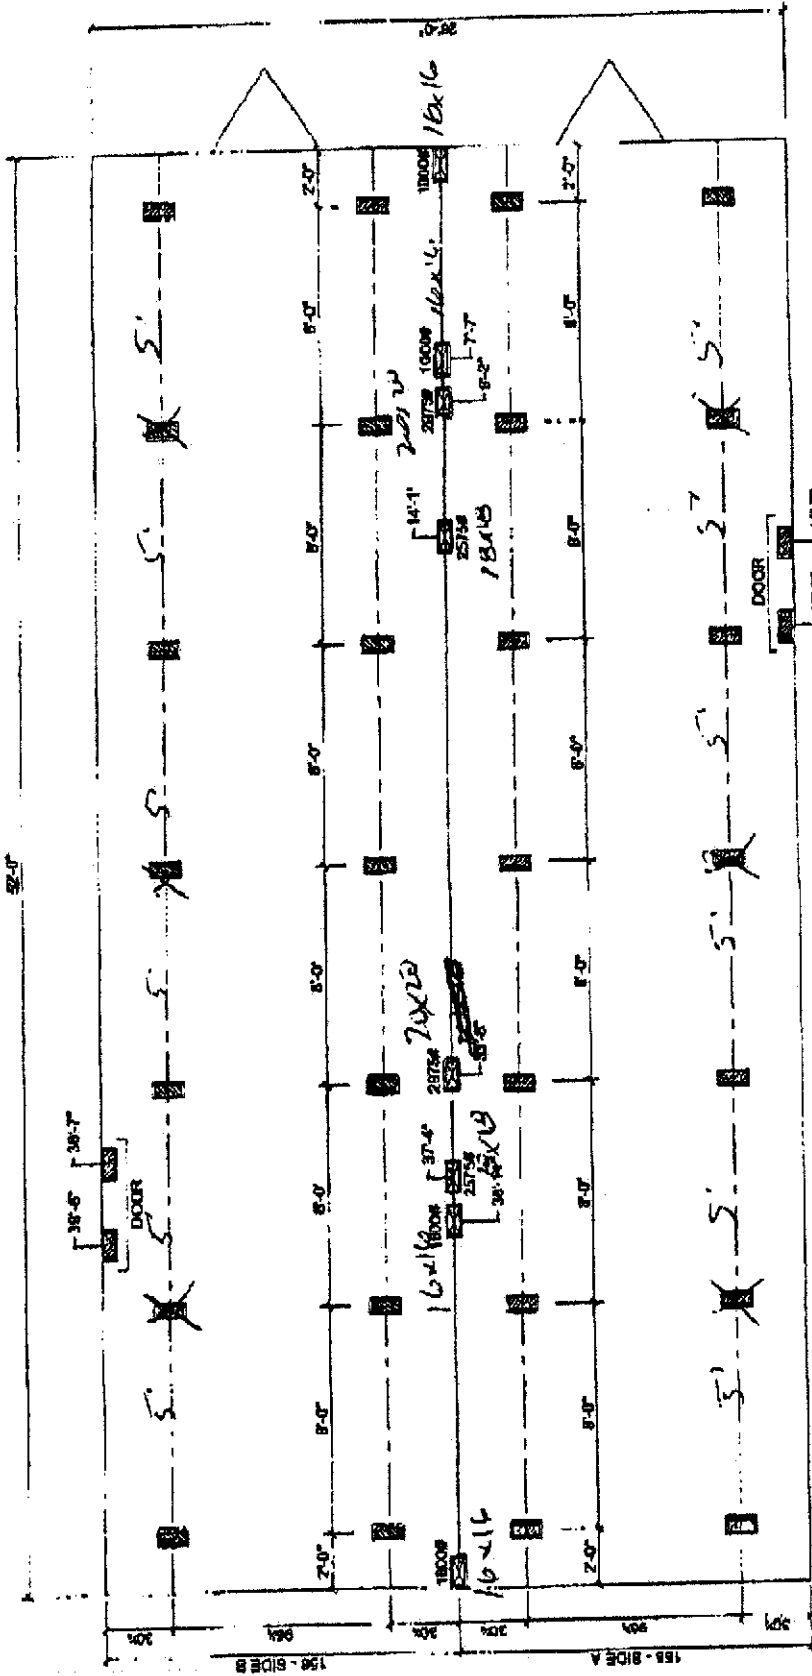

REV: 05/16/22

23 MARRIAGE LINE OPENING SUPPORT PIERTYP.
23 SUPPORT PIERTYP

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY. QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS. SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes
MODEL: D-2523H - 28 X 56
3-BEDROOM / 2-BATH

D-2523H

2025/JAN/07/TUE 11:32

PROPERTY I

Dealer's Name: Wayne Frier Home Cent

Customer's Name DAVID MORRELL

Phone # _____ Work # _____

Physical Address 601 NW TURNER AVE

LAKE CITY, FL 32055

Description of Manufactured Home:

Year 2025 Make LIVE OAK M

Size 20x56 Serial # _____

Specific Driving Instructions to Property I

AM

Please draw map from sales lot to home site

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

119092

LABEL #

DATE OF INSTALLATION

RUSTY L. KNOWLES

NAME

IH / 1038219 / 1

6566

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
