


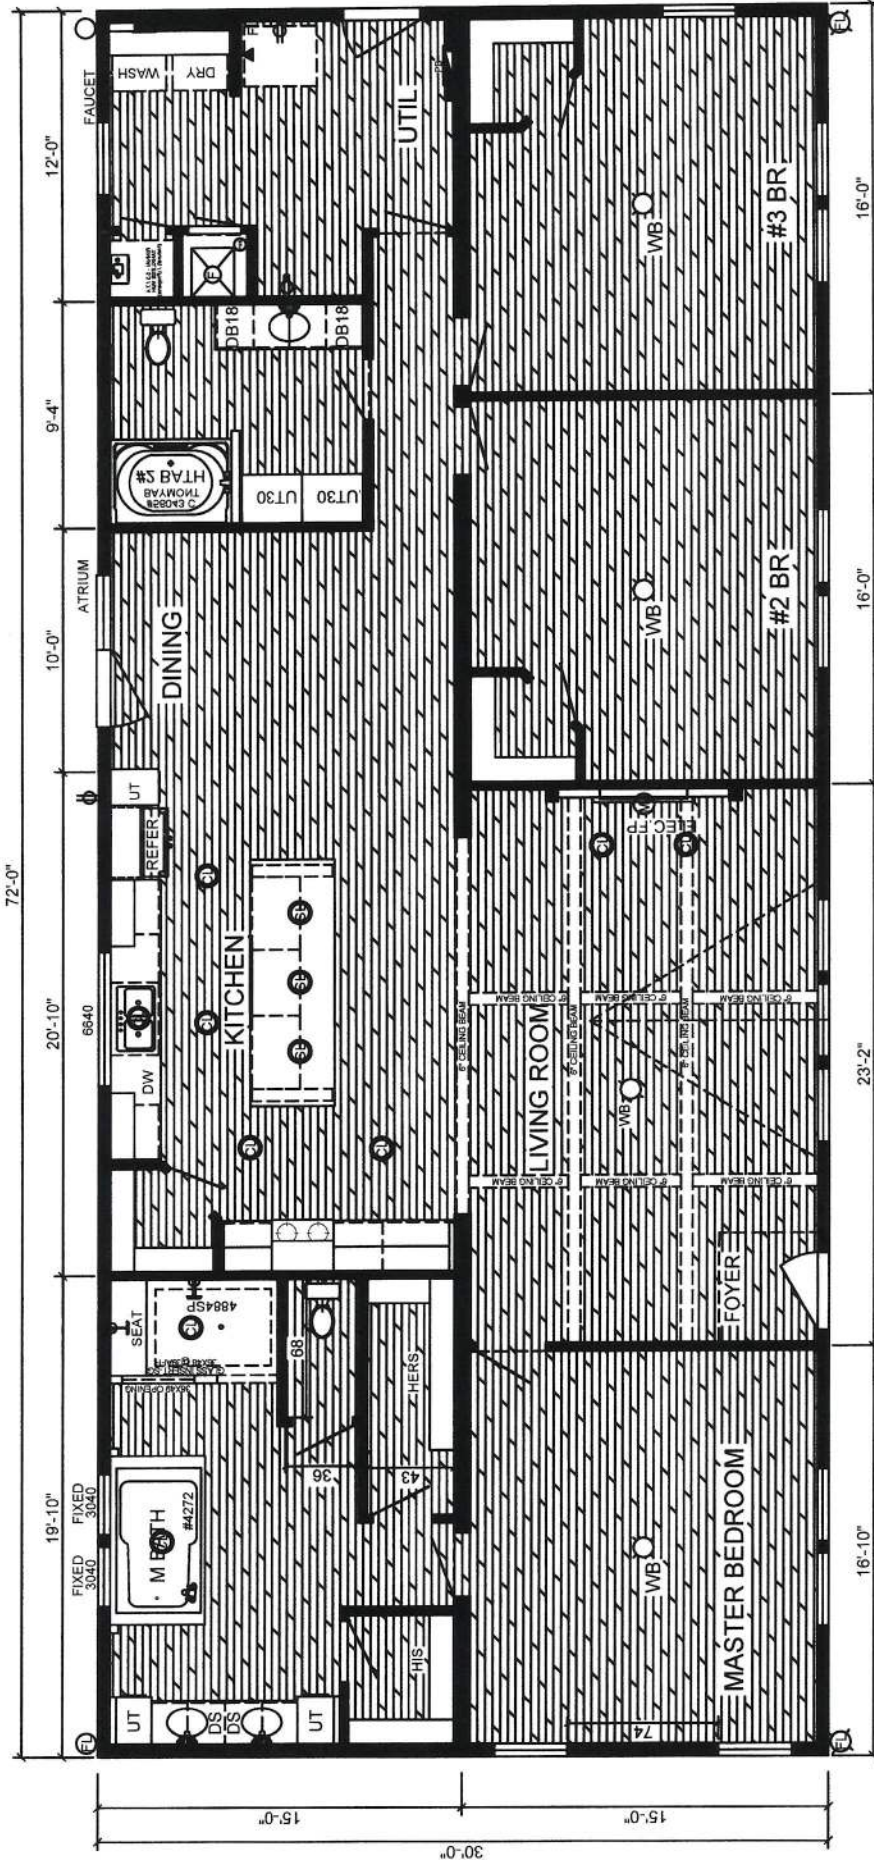

Deer Valley Builders

*All rooms dimensions include closets and square footage are approximate.
 *Drawing layout subject to change if required by engineering review.

DEER VALLEY HOMEBUILDERS, INC.
 Woodland Homes Series

MODEL: PAUL229(WL-6808)
3-BEDROOM / 2-BATH
 32 x 76 - Approx. 2160 Sq. Ft.
CUSTOMER: STEEDLEY



"ZEMIRA"
 For more information visit us at
www.deervalleyhb.com

DATE: 08-11-22 08-15-22BC
 Drawn By: BCROW

Legend:

- (A) MAIN ELECTRICAL
- (B) ELECTRICAL CROSSOVER
- (C) WATER INLET
- (D) WATER CROSSOVER
- (E) GAS INLET
- (F) GAS CROSSOVER (IF ANY)
- (G) PLENUM / DUCT CROSSOVER
- (H) SEWER DROPS
- (I) RETURN AIR (W/OPT. HEAT PUMP)
- (J) SUPPLY AIR (W/OPT. HEAT PUMP / OH DUCT)
- (K) DOWNDRAFT COOKTOP VENT

Room Dimensions:

- Overall Dimensions: 10' x 10'
- Wall Thickness: 8" (except where noted)
- Door Opening: 3'-2" x 6'-6"
- Window Opening: 6'-6" x 6'-6"
- Staircase: 6'-6" x 6'-6"
- Support Pier: 8" x 8" (except where noted)
- Support Pier Spacing: 8'-0" (except where noted)
- Support Pier Loading: 1000 LBS (except where noted)


Room Details:

- Room Name: L1-0000
- Room Type: LIVING ROOM
- Room Area: 100 SQ. FT.
- Room Volume: 1000 CU. FT.
- Room Notes: ALL DIMENSIONS ARE FROM FRONT OF HOME UNLESS OTHERWISE NOTED.

Mobile Home Permit Worksheet



Installer: Ernest S. Johnson License # IF1025249
 Address of home being installed: SW Howell St
Lake City #1 32056
 Manufacturer: Deer Valley Length x width: 72 X 30

NOTE: if home is a single wide fill out one half of the blocking plan
 if home is a triple or quad wide sketch in remainder of home
 I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.



Show locations of Longitudinal and Lateral Systems
 (use dark lines to show these locations)

Installer's initials: ES

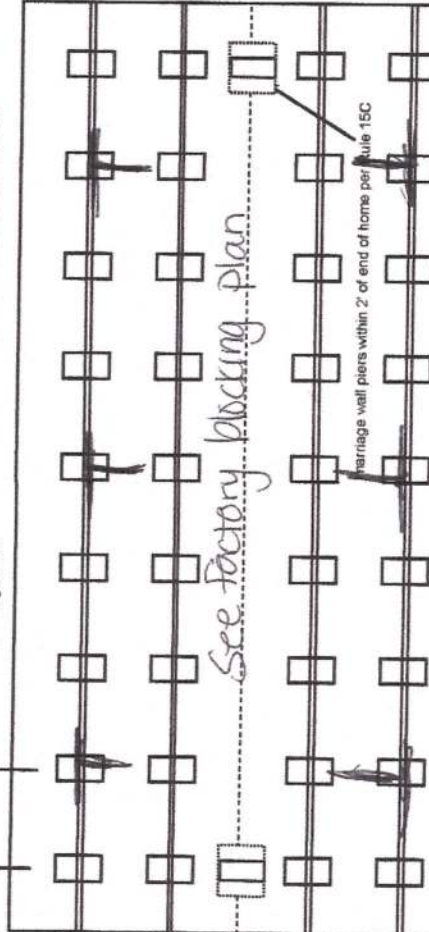

Application Number: _____

Date: _____

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C ☒

Single wide ☐ Wind Zone II ☐ Wind Zone III ☒

Double wide ☒ Installation Decal # 94268

Triple/Quad ☐ Serial # DNAL2310694AB

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3'	3'	4'	5'	6'	7'	8'
1500 psf	4'	4'	5'	6'	7'	8'	8'
2000 psf	6'	6'	8'	8'	8'	8'	8'
2500 psf	7'	7'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size: 23X31 6.6 oc
 Perimeter pier pad size: 17.5X25.5
 Other pier pad sizes (required by the mfg.): _____

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.



List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening: See Pier pad size: factory blocking plan

ANCHORS

4 ft ☒ 5 ft ☒

FRAME TIES

within 2' of end of home spaced at 5' 4" oc ☒

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
 Manufacturer: _____
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer: Oliver 1101V

OTHER TIES

Number	38
Sidewall	0
Longitudinal	10
Marriage wall	2
Shearwall	

PERMIT WORKSHEET

page 2 of 2

PERMIT NUMBER

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil ☒ without testing.

x 1000 x x x

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x x x x 1000

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb. holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Ernest S Johnson

Date Tested

Assumed Oliver 11/1/11
uses 485 foot Anchors Both

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Site Preparation

Debris and organic material removed Swale ☒ Pad ☐ Other ☐

Fastening multi wide units

Floor: Type Fastener: 1995 Length: 7 Spacing: 20
Walls: Type Fastener: 1995 Length: 7 Spacing: 10
Roof: Type Fastener: 1995 Length: 7 Spacing: 20
For used homes a min 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

EG

Type gasket

factory
OK 11

Installed:

Between Floors Yes

Between Walls Yes

Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes Pg. _____
Siding on units is installed to manufacturer's specifications. Yes Pg. _____
Fireplace chimney installed so as not to allow intrusion of rain water. Yes Pg. _____

Miscellaneous

Skirting to be installed Yes No

Dryer vent installed outside of skirting. Yes N/A

Range downflow vent installed outside of skirting. Yes N/A

Drain lines supported at 4 foot intervals. Yes

Electrical crossovers protected. Yes

Other: Yes

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature Ernest S Johnson Date

District No. 1 - Ronald Williams
District No. 2 - Rocky Ford
District No. 3 - Robby Hollingsworth
District No. 4 - Toby Witt
District No. 5 - Tim Murphy

**BUILDING AND ZONING
DEPARTMENT**



BOARD OF COUNTY COMMISSIONERS • COLUMBIA COUNTY

**MOBILE HOME INSTALLER
OBLIGATION LETTER**

I, Ernest S. Johnson, of Dependable M.H.S., license number
(Print Name) (Company Name)

I, 1025249, do hereby agree to affix the installation decal onto this manufactured home as required by law and provide a copy of this decal to the permitting authority.

I further understand that once these decals become available I must provide them to obtain any further permits in Columbia County, Florida.

Ernest S. Johnson 10.10.22
Signature - Licensed Mobile Home Installer Date

Job Information

Job Name: Speedway

Location: TBD Howell St. Lake City FL 32055

Application or Permit #: _____

BOARD MEETS FIRST AND THIRD THURSDAY AT 5:30 P.M.

P.O. BOX 1529

LAKE CITY, FLORIDA 32056-1529

PHONE (386) 755-4100
