

Mobile Home Permit Worksheet

Installer: David Albright License # IT/1129420/1


Address of home being installed 2654 SW Ichetucknee Ave
Lake City, FL, 32024

Manufacturer Lawn Homes Length x width 54' x 26'8"

NOTE: if home is a single wide fill out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in

Installer's initials DA

Typical pier spacing 4'6"
2' 4'6"
lateral
longitudinal
Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

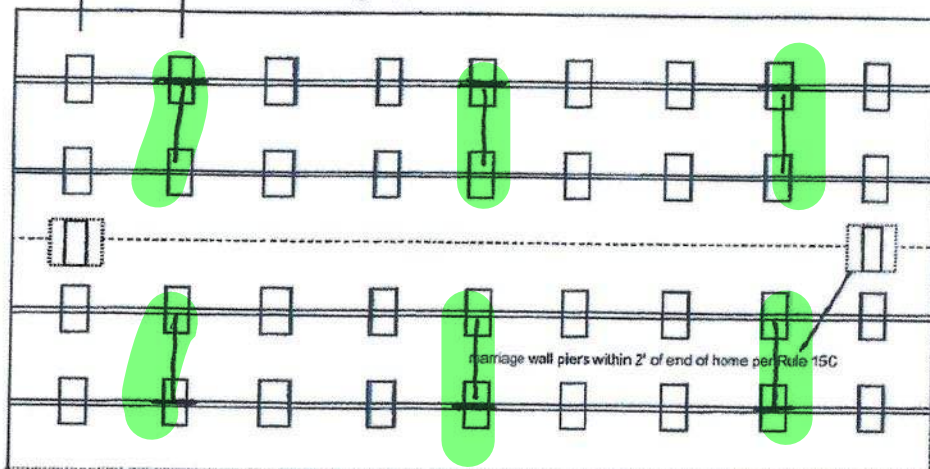

Application Number: _____ Date: 11-12-24

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C ☐

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Decal # 114488

Triple/Quad ☐ Serial # FLTHLCT28396-4734AB

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf		3'	4'	5'	6'	7'	8'
1500 psf		4'6"	6'	7'	8'	8'	8'
2000 psf		6'	8'	8'	8'	8'	8'
2500 psf		7'6"	8'	8'	8'	8'	8'
3000 psf		8'	8'	8'	8'	8'	8'
3500 psf		8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17.5 x 25.5
Perimeter pier pad size 16 x 16
Other pier pad sizes 23 x 31
(required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening Pier pad size

FACTORY DIAGRAM

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc ☒

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer OLIVER TECHNOLOGIES 6
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer OLIVER TECHNOLOGIES 6

OTHER TIES

Number
Sidewall 24
Longitudinal 6
Marriage wall 43'54"
Shearwall 2

Mobile Home Permit Worksheet

Application Number: _____

Date: 11-12-24

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 250 inch pounds or check here if you are declaring 5" anchors without testing _____. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's initials DA

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name DAVID AIBRIGHT MOBILE HOME SVC

Date Tested _____

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 5V-34

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 5U-36.2

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 5U-36.2



Site Preparation

Debris and organic material removed ☒ Pad ☒ Other _____
Water drainage: Natural _____ Swale _____

Fastening multi-wide units

Floor: Type Fastener: LAG Length: 6" Spacing: 2' OC
Walls: Type Fastener: SCREW Length: 4" Spacing: 18" OC
Roof: Type Fastener: LAG Length: 6" Spacing: 2' OC
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials DA

Type gasket 3/4" FOAM TAPE
Pg. 5U-13

Installed:
Between Floors Yes ☒
Between Walls Yes ENDS
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 5V-39 5U-A-4
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes _____


Miscellaneous

Skirting to be installed. Yes _____ No ☒
Dryer vent installed outside of skirting. Yes _____ N/A ☒
Range downflow vent installed outside of skirting. Yes _____ N/A ☒
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature David Albright

Date 11-12-24

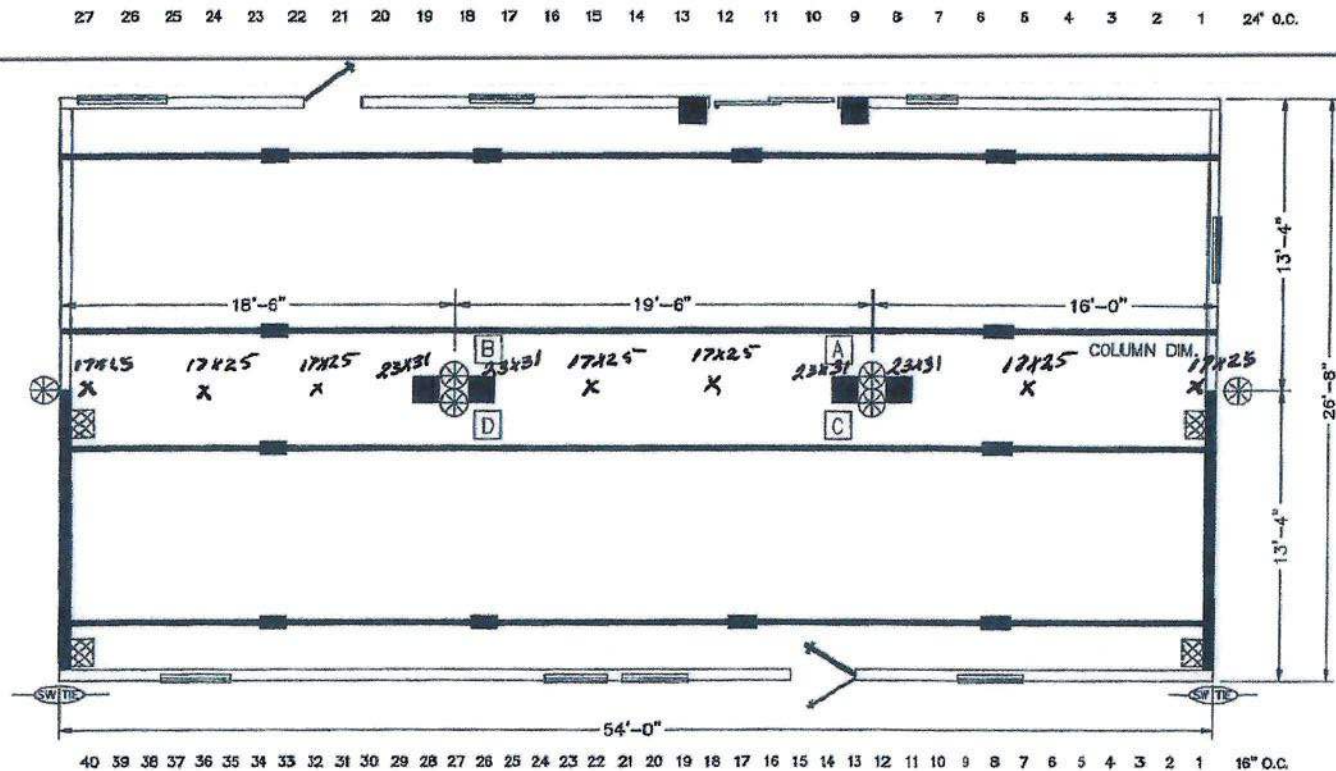


I-BEAM BLOCKING SEE SOIL BEARING CAPACITY CHARTS FOR SPACING	SHEARWALL TIE	BLOCKING LEGEND: FLORIDA
COLUMN BLOCKING SEE SOIL BEARING CAPACITY CHARTS FOR PAD SIZE		
SHEARWALL BLOCKING	1) ALL EXTERIOR DOORS, BAY WINDOWS, RECESSED SIDEWALLS AND EXTERIOR WALL OPENINGS 48" OR GREATER, WILL REQUIRE BLOCKING ON EACH SIDE. 2) 32" WIDE HOMES REQUIRED TO BE BLOCKED MIN 8'-0" ON CENTER BETWEEN COLUMNS.	
SHEARWALL FRAME TIE		
CENTER LINE TIES	VERTICAL TIE MAX. SPACING 5'-4" CENTER TO CENTER	
LONGITUDINAL TIES		

TownHomes LLC VISION - QUALITY - INTEGRITY - BUILDING YOUR FUTURE		TownHomes P.O. BOX 1059 LAKE CITY, FLORIDA 32056	
Date: 5-1-17	Revisions	Cad#: 2839A1	
Des: ROB/SIM	11-14-17 hb	12-2-23 hb	
Parent: 2839A	2-8-22 hb		
Code: T (22)	ALT# 15 - MASTER BATH SHWR/LINEN		
2008 2	Model: 2839-216	Print: FLORIDA BLOCKING PLAN	

25'-8" WIDE HOME
SIDEWALL HEIGHT 8'-0"

FRONT

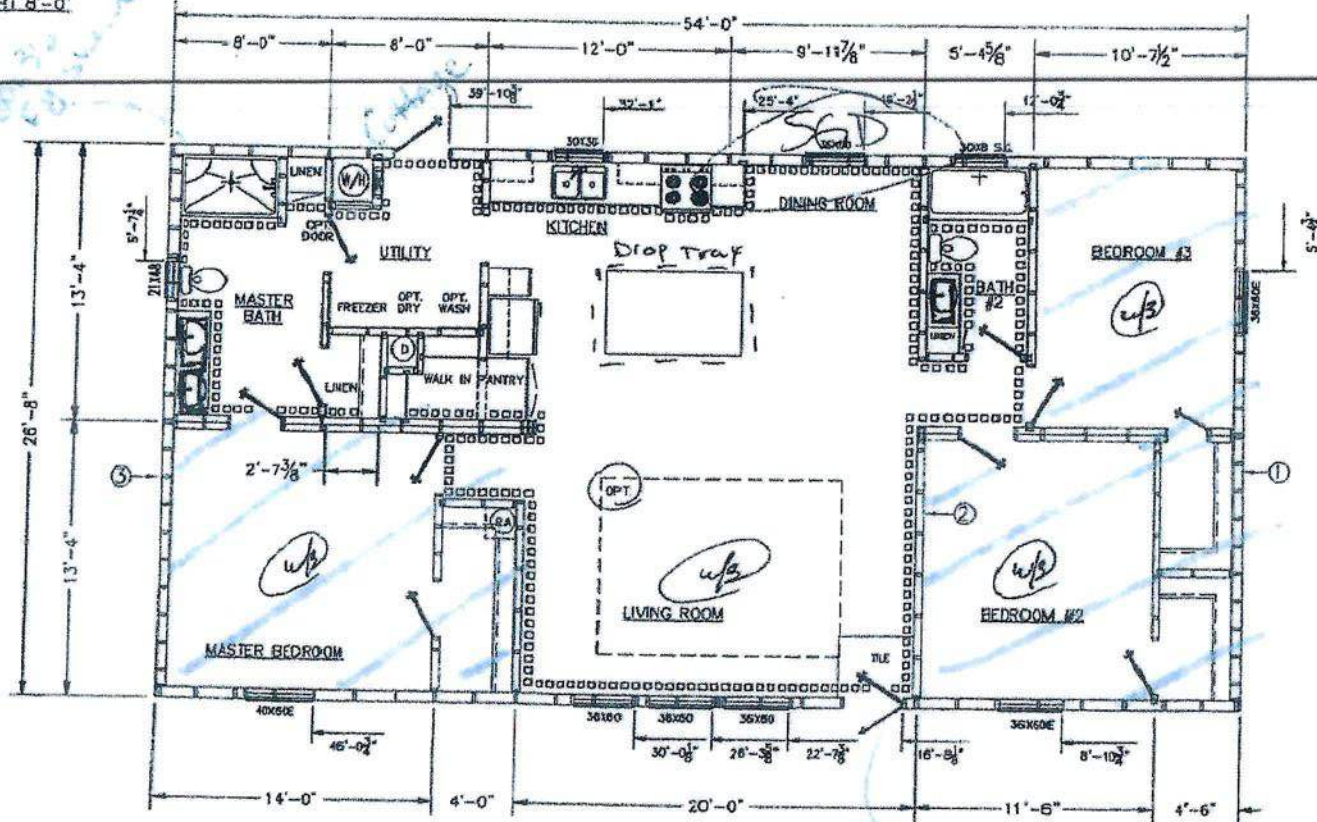

General
w/line
STORM



TownHomes
P.O. BOX 1059
LAKE CITY, FLORIDA
32056

Date: 5-1-17	Revisions	Code: 2839A.1
Dr'n: ROB/SLM	11-14-17 kb	
Parent: 2839A	2-8-22 kb	
Code: T (17)	ALT# 15 - MASTER BATH SHWR/LINEN	
2	Model: 2839-216	Print: 1440 SQ.FT. SALES

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT

Order #: 6367

Label #: 114488

Manufacturer:

JOLEY HOMIE

(Check Size of Home)

Homeowner

MIKE MORRISON
KENT

Year Model:

Single

Address:

2664 SW 104TH AVENUE

Length & Width:

54' x 26'8"

Double ☒

Triple

HUD Label #:

City/State/Zip:

LAKE CITY FL 32024

Type Longitudinal System:

OTI 6

Type Lateral Arm System:

OTI 6

Soil Bearing / PSF:

Phone #:

Torque Probe / in-lbs:

Date Installed:

New Home: ☒

Used Home: ☐

Permit #:

Installed Wind Zone:

II

Data Plate Wind Zone:

12

Note:



STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

114488

LABEL #

DATE OF INSTALLATION

DAVID E ALBRIGHT

NAME

IH / 1129420 / 1

6367

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
