

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

LICENSE # _____
IH / 1129420 / 1
NAME _____
DAVID E ALBRIGHT
ORDER # _____
6606
DATE OF INSTALLATION _____
LABEL # _____
120081

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT

Order # : 6606	Label # : 120081	Manufacturer: LIVE OAK	Year Model: 2022	Length & Width: 56/60 x 28	Type Longitudinal System: OTI 6	Type Lateral Arm System: OTI 6	New Home: ☒ Used Home: _____	Data Plate Wind Zone: II	Permit #:
Homeowner: STARS AND STRIPES	Address: NW MARBLE WAY	City/State/Zip: LAKE CITY FL 32055	Date Installed:	Installed Wind Zone: II	Note:				



(Check Size of Home)	Single _____	Double X	Triple _____	HUD Label #:	Soil Bearing / PSF:	Torque Probe / in-lbs:
----------------------	--------------	-----------------	--------------	--------------	---------------------	------------------------

Mobile Home Permit Worksheet

Installer: DAVID AIBRIGHT License # 1H-1129420
 Address of home being installed: TBD NW Marble Way Lake City FL
22-2s-16-01721-004
 Manufacturer: Live Oak Length x width: 28x56/60

NOTE: if home is a single wide fill out one half of the blocking plan
 if home is a triple or quad wide sketch in remainder of home
 I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Installer's initials: DA

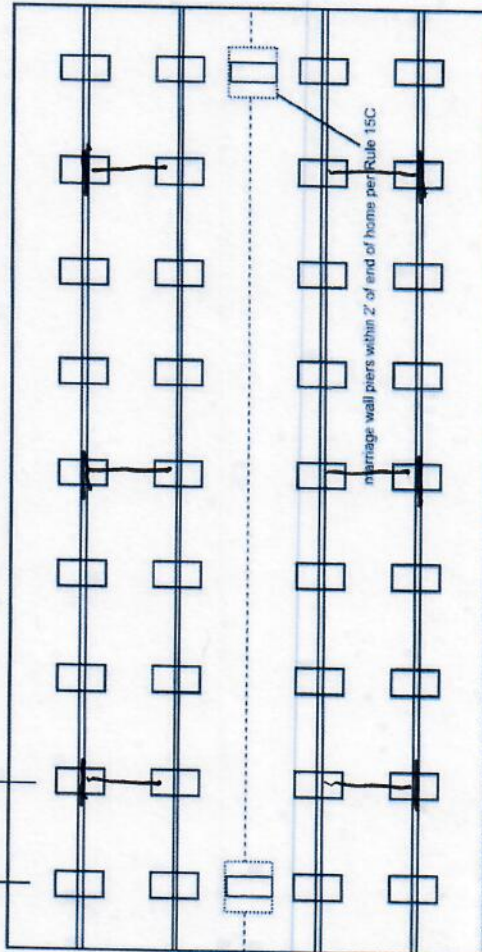

Application Number: _____ Date: _____

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C ☒

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Decal # 120081

Triple/Quad ☐ Serial # LOHGA20037946AB

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3'	3'	4'	5'	6'	7'	8'
1500 psf	4' 6"	4' 6"	6'	7'	8'	8'	8'
2000 psf	6'	6'	8'	8'	8'	8'	8'
2500 psf	7' 6"	7' 6"	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17x25
 Perimeter pier pad size 16x16
 Other pier pad sizes (required by the mfg.) 24x24

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.



List all marriage wall openings greater than 4 foot and their pier pad sizes below.

ANCHORS

Opening FACTORY Pier pad size DIAGRAM

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Number 26
5-3-5-4
 Sidewall Longitudinal Marriage wall Shearwall

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) Manufacturer OLIVER TECHNOLOGIES
 Longitudinal Stabilizing Device w/ Lateral Arms Manufacturer OLIVER TECHNOLOGIES

Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 250 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb. holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

DAVID AUBRIGHT MOBILE HOME SVC

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 64-68

Plumbing

Connect all sewer drains to an existing sewer lap or septic tank. Pg. 70

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 107

Application Number: _____

Date: _____

Site Preparation

Debris and organic material removed ☒
Water drainage: Natural Swale Pad ☒ Other

Fastening multi wide units

Floor: Type Fastener: LAG Length: 6" Spacing: 2'
Walls: Type Fastener: SCREW Length: 4" Spacing: 18"
Roof: Type Fastener: LAG Length: 6" Spacing: 2'
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials DA

Type gasket

Pg. 36

Installed:

Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 119
Siding on units is installed to manufacturer's specifications Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes


Miscellaneous

Skirting to be installed. Yes No ☒
Dryer vent installed outside of skirting. Yes N/A ☒
Range downflow vent installed outside of skirting. Yes
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Date

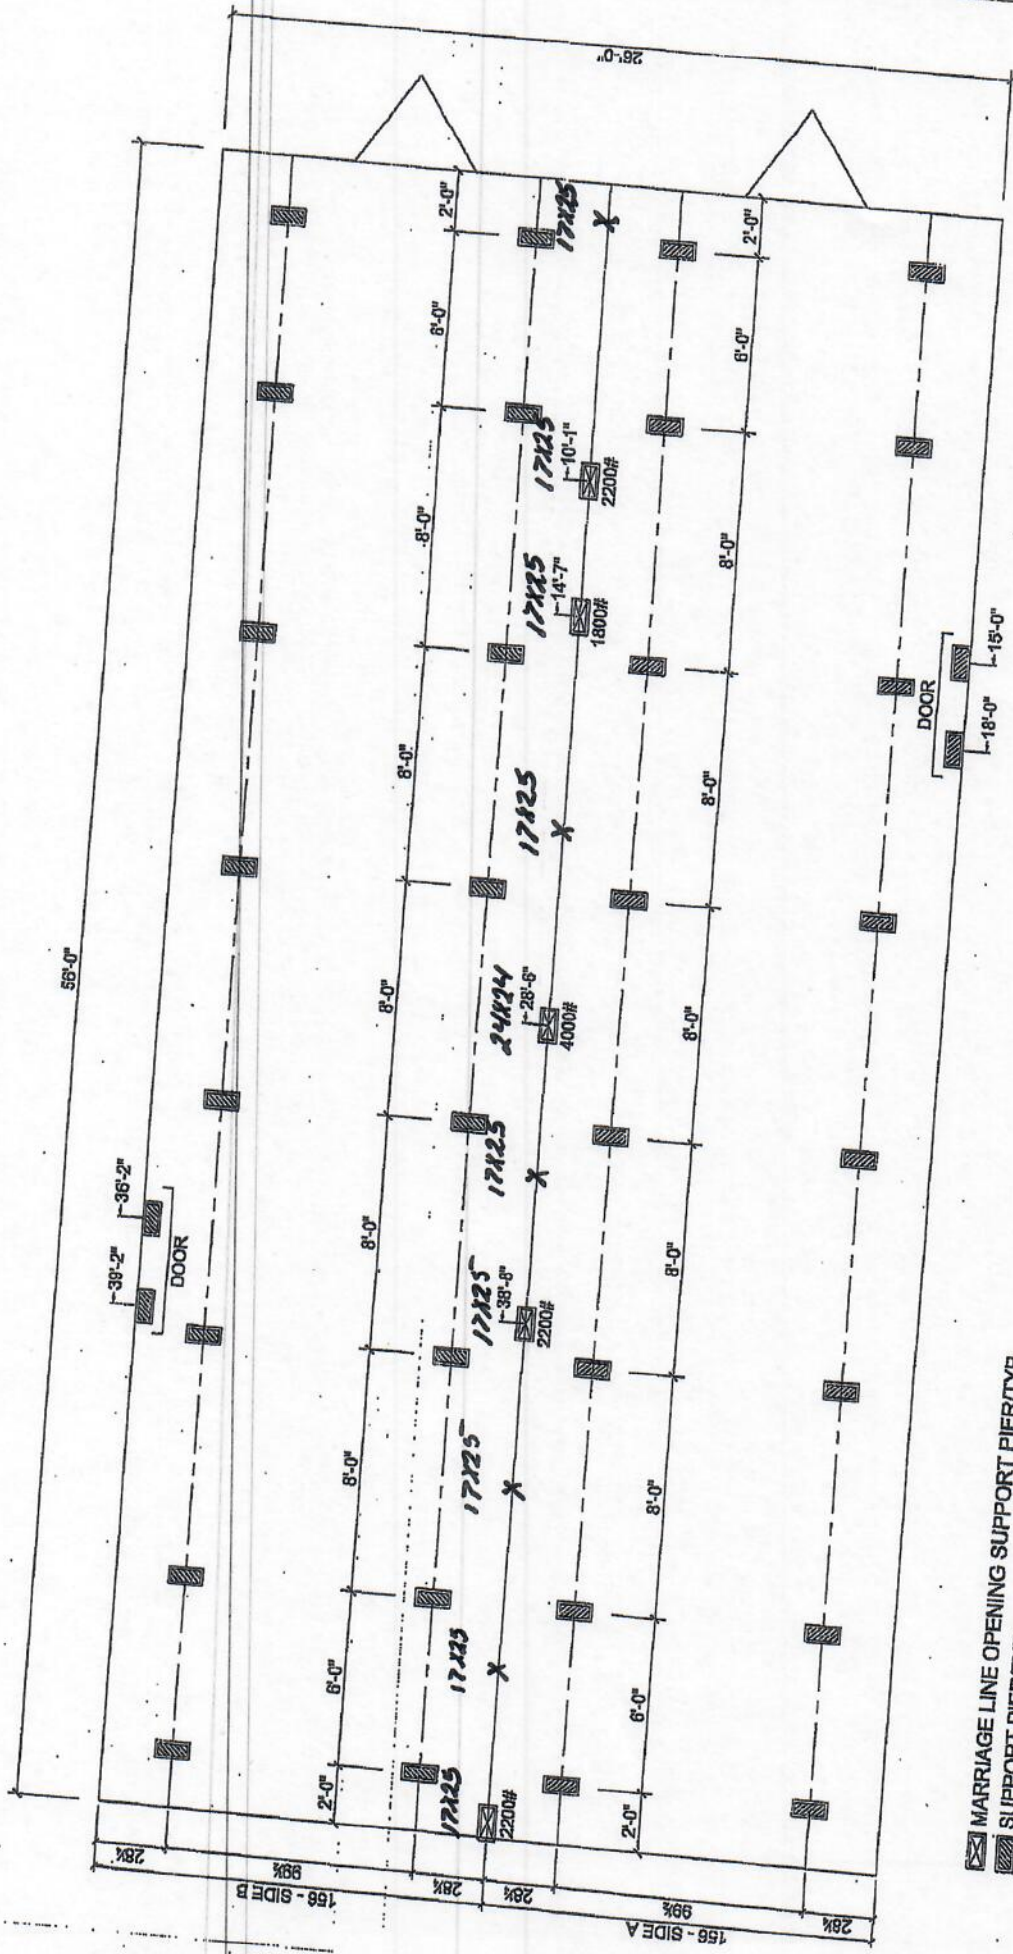

MARRIAGE LINE OPENING SUPPORT PIER/TYP.
 SUPPORT PIER/TYP.

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

REV: 04/18/22

Live Oak Homes
MODEL: L-2563G - 28 X 56
3-BEDROOM / 2-BATH

(99-1/2" I-BEAM SPACING)
L-2563G

This floor plan shows a three-bedroom mobile home with a total width of 59'-0" and a total length of 95'-0". The layout includes:

- Master Bedroom:** 17'-0" x 12'-8", located at the front left.
- Living Room:** 23'-10" x 12'-8", located at the front right.
- Bedroom #2:** 9'-7" x 12'-8", located at the rear right.
- Bedroom #3:** 9'-7" x 12'-8", located at the rear right, adjacent to Bedroom #2.
- Bathrooms:**
 - M. Bath:** Attached to the Master Bedroom.
 - #2 Bath:** Located between the two rear bedrooms.
- Kitchen and Dining Area:** Located in the center, featuring a stove, sink, refrigerator, and optional dishwasher.
- Storage and Utility:** Includes a linen closet (LINEN), a closet (CLO), and a utility area with a washer/dryer space.
- Exterior Features:** The plan shows a side wall with four windows and a set of stairs leading outside. Dimensions for the side wall are 5'-8", 5'-7", 6'-10", 11'-10", 8'-8", 4'-9", and 10'-1".

Room dimensions and labels are as follows:

- MASTER BEDROOM: 17'-0" x 12'-8"
- LIVING ROOM: 23'-10" x 12'-8"
- #2 BEDROOM: 9'-7" x 12'-8"
- #3 BEDROOM: 9'-7" x 12'-8"
- M. BATH
- #2 BATH
- DINING
- KITCHEN: STOVE, SINK, REFRIG, OPT DISH
- WASH DRY
- CLO
- LINEN

Overall dimensions: 59'-0" SIDEWALL, 95'-0" overall length.

- * All room dimensions include closets and square footage figures are approximate.
- * Transom windows are available on optional 9'-0" sidewall houses only.

