



Mobile Home Permit Worksheet

Installer Code Houston License # PH 1133271


Address of home being installed _____

Manufacturer CAVCO Length x width 28x50


NOTE: If home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in

Installer's initials OH

Typical pier spacing



Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

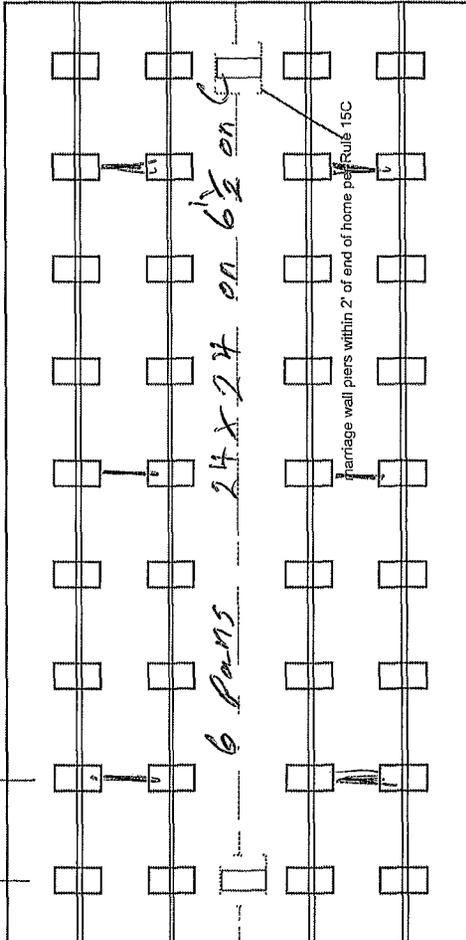

Permit Number: _____ Date: _____

New Home Used Home

Home installed to the Manufacturer's Installation Manual Home is installed in accordance with Rule 15-C

Single wide Wind Zone II Wind Zone III

Double wide Installation Decal # 123576

Triple/Quad Serial # CAV340FL25-244044B

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq ft)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3'	3'	4'	5'	6'	7'	8'
1500 psf	4'6"	4'6"	6'	7'	8'	8'	8'
2000 psf	6'	6'	8'	8'	8'	8'	8'
2500 psf	7'6"	7'6"	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

*interpolated from Rule 15C-1 pier spacing table.

POPULAR PAD SIZES

Pad Size	Sq. In
16 x 16	256
16 x 18	288
18 1/2 x 18 1/2	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

I-beam pier pad size 24x24
Perimeter pier pad size 17x23
Other pier pad sizes (required by the mfg.) _____

Draw the approximate locations of marriage wall openings 4 foot or greater Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below

Opening _____ Pier pad size 24x24

4 ft 5 ft
ANCHORS
FRAME TIES
within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS
Longitudinal Stabilizing Device (LSD)
Manufacturer _____
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer _____

OTHER TIES
Number 2
Sidewall 2
Longitudinal 6
Marriage Wall 5
Shear Wall 4



Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil without testing.

X _____ X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5' anchors without testing _____. A test showing 275 inch pounds or less will require 5' anchors

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5' anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity

Installer's initials DH

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name Dale Houston

Date Tested 12/7/25

ELECTRICAL

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

PLUMBING

Connect all sewer drains to an existing sewer tap or septic tank Pg. _____
Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems Pg. _____

Permit Number: _____ Date: _____

Site Preparation

Debris and organic material removed _____
Water drainage Natural _____ Swale _____ Pad _____ Other _____

Fastening multi wide units

Floor- Type Fastener: lags Length 6" Spacing 18"
 Walls- Type Fastener: 1" Length 1" Spacing 1"
 Roof- Type Fastener: 1" Length: 1" Spacing: 1"

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed I understand a strip of tape will not serve as a gasket.

Installer's initials DH

Type gasket Foam

Installed
 Between Floors _____ Yes
 Between Walls _____ Yes
 Bottom of ridge beam _____ Yes

Weatherproofing


The bottom board will be repaired and/or taped. _____ Yes _____ Pg. _____
 Siding on units is installed to manufacturer's specifications. _____ Yes _____
 Fireplace chimney installed so as not to allow intrusion of rain water. _____ Yes _____

Miscellaneous

Skirting to be installed. _____ Yes _____ No _____ N/A _____
 Dryer vent installed outside of skirting _____ Yes _____ No _____ N/A _____
 Range downflow vent installed outside of skirting. _____ Yes _____ No _____ N/A _____
 Drain lines supported at 4' intervals. _____ Yes _____ No _____ N/A _____
 Electrical crossovers protected. _____ Yes _____ No _____ N/A _____
 Other _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer's Signature Dale Houston Date _____

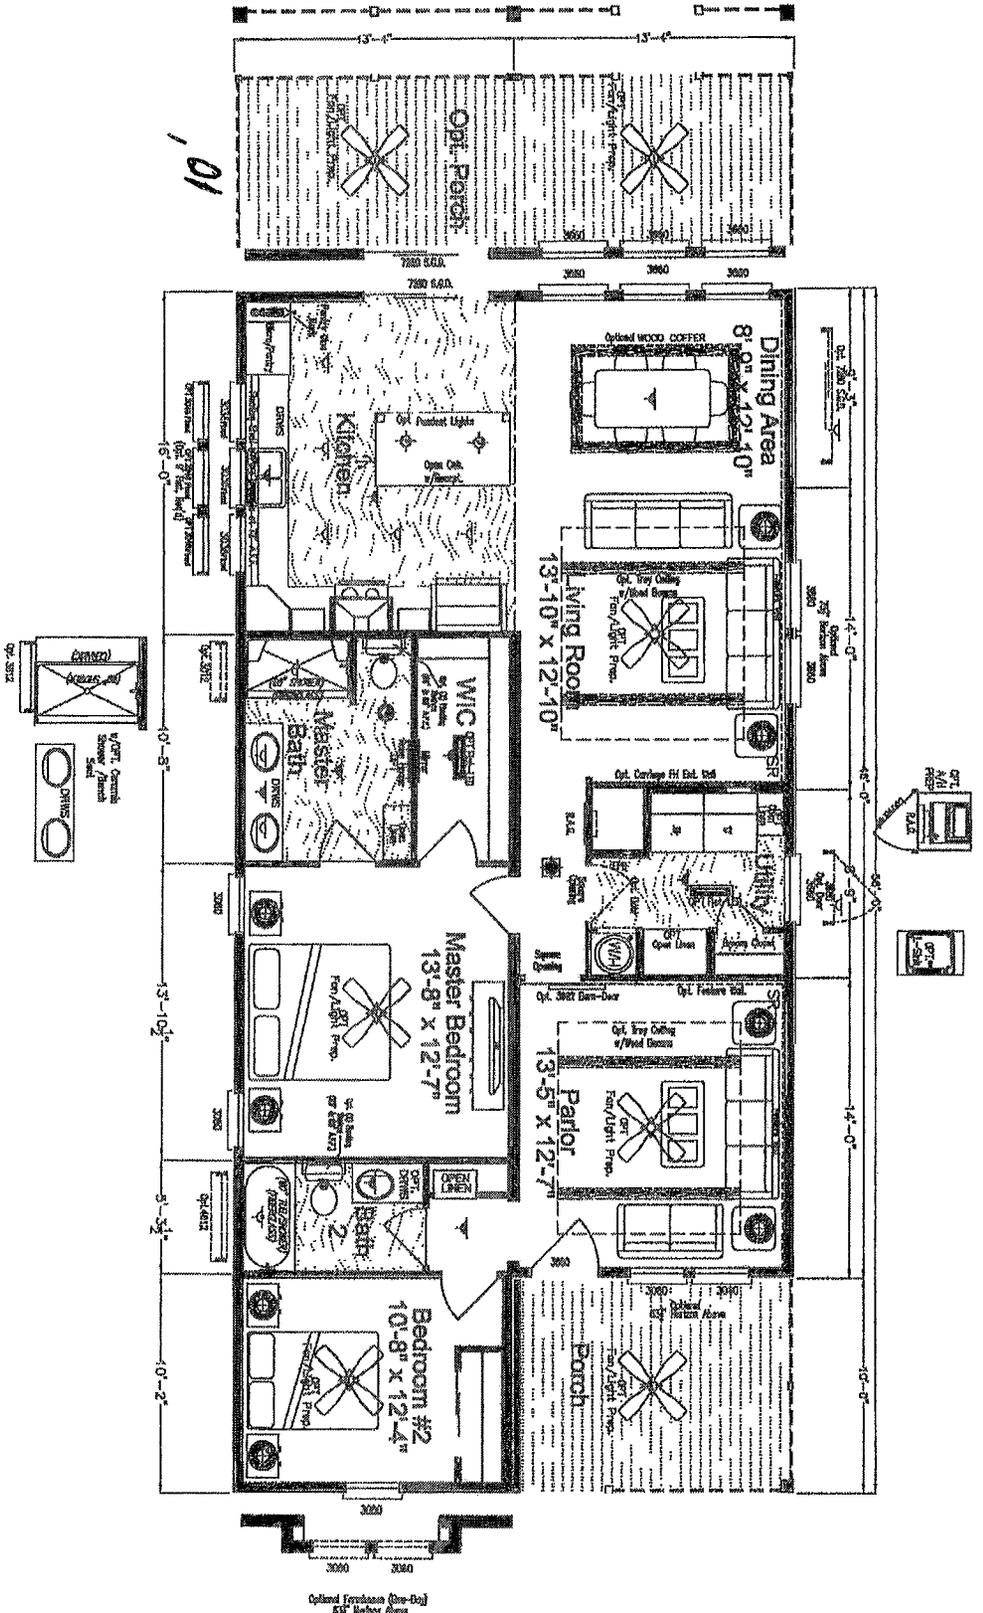

Palm Harbor Homes
Carriage Farmhouse
 Model 340LS28562K
 Approx. 1,363 Sq Ft.

- 26' 8" - 56' Lifestyle Front Porch w/
- 1720 sq. feet of Outdoor Living Area
- Island Kitchen
- Triple Full View Windows in Kitchen
- Bonus Utility Room
- Opt. Full Porch
- Large Master Suite w/ Walk-In Closet
- Open Social Area

Copyright © Palm Harbor Homes, Inc. See respective floor plans for a continuous product updating and improvement process. Dimensions, materials, features, materials, specifications and availability are subject to change without notice or obligation. Please refer to working drawings for actual dimensions, features and floor plans are artist's conceptions only and may vary from the completed home. Square footage calculations and room areas shown are approximate and subject to industry standards.
 Rev 04/28/20

M g.

License Number: IH / 1133271 / 1 Name: DALE HOUSTON

Order #: 6743	Label #: 123576	Manufacturer:	(Check Size of Home)
Homeowner:		Year Model:	Single _____
Address:		Length & Width:	Double _____
City/State/Zip:		Type Longitudinal System:	Triple _____
Phone #:		Type Lateral Arm System:	HUD Label #:
Date Installed:		New Home: _____ Used Home: _____	Soil Bearing / PSF:
Installed Wind Zone:		Data Plate Wind Zone:	Torque Probe / in-lbs
Note:			Permit #

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

123576

LABEL #

DATE OF INSTALLATION

DALE HOUSTON

NAME

IH / 1133271 / 1

6743

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

