

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 150 psi or check here to declare 1000 lb. soil without testing.

150 x 150 x 150

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

150 x 150 x 150

TORQUE PROBE TEST

The results of the torque probe test is 255 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all corners. The points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 400 lb. capacity.

WJH Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name William Price

Date Tested 4/21/23

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 1

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 1

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 1

Site Preparation

Debris and organic material removed Yes
Water drainage Natural Swale Pad X Other Other

Fastening multi wide units

Floor: Type Fastener Length Spacing: 16" / 16"
Walls: Type Fastener Length Spacing: 16" / 16"
Roof: Type Fastener Length Spacing: 16" / 16"

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

WJH Installer's initials

Type gasket Pg. 1
Installed Yes
Between Floors Yes
Between Walls Yes
Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes Yes Pg. 1
Siding on units is installed to manufacturer's specifications. Yes Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes Yes

Miscellaneous

Skirting to be installed. Yes No
Dryer vent installed outside of skirting. Yes N/A
Range downflow vent installed outside of skirting. Yes N/A
Drain lines supported at 4 foot intervals. Yes Yes
Electrical crossovers protected. Yes Yes
Other: Yes

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature William Price

Date 4/21/23

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

Installer: William Price License # 1H-1041936

Address of home being installed

198 NW 6th Ave
Lake City FL 33653


Manufacturer: Loft Length x width 60' x 12'

NOTE: If home is a single wide fill out one half of the blocking plan


If home is a triple or quad wide sketch in remainder of home

Installer's initials WPA

Typical pier spacing



Show locations of longitudinal and lateral systems (use dark lines to show these locations)

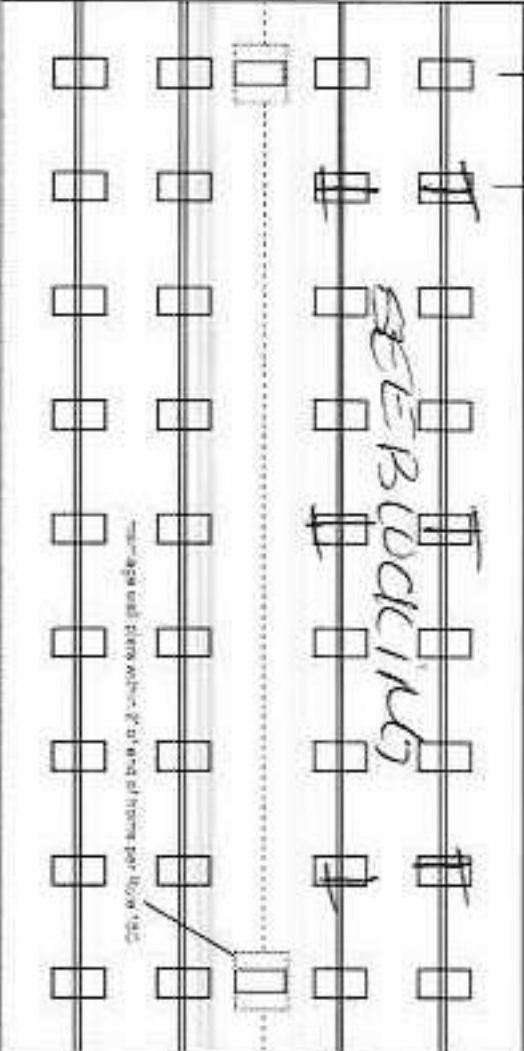

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual

Home is installed in accordance with Rule 15-C ☒

Single wide ☒

Double wide ☐

Triple/Quad ☐

Wind Zone II ☒

Wind Zone III ☐

Installation Decal ☒

Serial # 1041936

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	Footer size (sq ft)	16' x 16'	16' 1/2" x 16'	20' x 20'	22' x 22'	24' x 24'	26' x 26'
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4' 6"	6'	7'	8'	9'	10'	10'
2000 psf	6'	8'	9'	10'	11'	12'	12'
2500 psf	7' 6"	9'	10'	11'	12'	13'	13'
3000 psf	9'	10'	11'	12'	13'	14'	14'
3500 psf	10'	11'	12'	13'	14'	15'	15'

* Interpolated from Rule 15-C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

17x25

Perimeter pier pad size

10x10

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening large Pier pad size 23x31

POPULAR PAD SIZES

Pad Size	Sq ft
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17.5 x 25.5	441
17 1/2 x 25 1/2	448
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft ☐

FRAME TIES

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Sidewall

Longitudinal

Marriage wall

Longitudinal Stabilizing Device w/ Lateral Arms

Shearwall

Over System

Number

4

Byrdon

16480

COLUMBIA
WFFHAC

License Number: IH / 1041936 / 1 Name: WILLIAM R PRICE

Order #: 5453

Label #: 91534

Manufacturer

(Check Size of Home)

Homeowner:

Year Model

Single

Address:

Length & Width:

Double

City/State/Zip:

Type Longitudinal System:

Triple

Phone #:

Type Lateral Arm System:

HUD Label #:

Date Installed:

New Home: _____ Used Home: _____

Soil Bearing / PSF:

Installed Wind Zone:

Data Plate Wind Zone:

Torque Probe / in-lbs:

Note:

Permit #:

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

91534

LABEL #

DATE OF INSTALLATION

WILLIAM R PRICE

NAME

IH / 1041936 / 1

5453

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
NEXT TO HUD LABEL.
PERMANENT INK PEN
MARKER ONLY.
COMPLETE INFORMATION
DATE AND KEEP ON FILE
A MINIMUM OF 2 YEARS.
REQUIRED TO
WHEN
