

CLARK

HORIZON 4-3563C

page 1 of 2

These worksheets must be completed and signed by the installer.
Submit the originals with the packet.

Installer DAVID ALBRIGHT License # IH/ 1129420


811 Address where home is being installed. TBD S.W. OLD NIBLACK AVE
FORT WHITE, FL 32038

Manufacturer LIVE OAK HOMES Length x width 32x56/60

NOTE: If home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

installer's initials _____

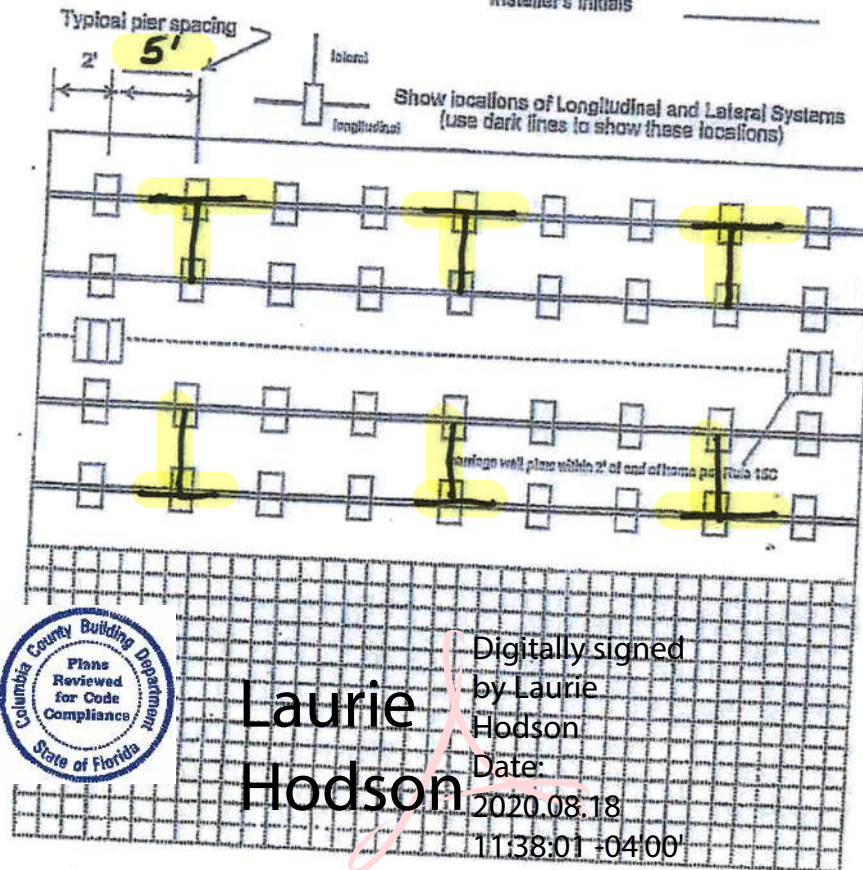

Laurie
Hodson

Digitally signed
by Laurie
Hodson
Date: 2020.08.18
11:38:01 -04:00

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual ☒

Home is installed in accordance with Rule 15-C ☐

Single wide ☐

Wind-Zone II ☒

Wind Zone III ☐

Double wide ☒

Installation Decal #

72902

Triple/Quad ☐

Serial #

LOHGA

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 nsf	3'	4'	5'	6'	7'	8'	8'
1500 nsf	4' 6"	5'	6'	7'	8'	9'	8'
2000 nsf	6'	6'	8'	8'	9'	9'	8'
2500 nsf	7' 6"	8'	8'	8'	9'	9'	8'
3000 nsf	8'	8'	8'	8'	9'	9'	8'
3500 nsf	8'	8'	8'	8'	9'	9'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

17x25

Perimeter pier pad size

16x16

Other pier pad sizes (required by the mfg.)

23x31

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening FACTORY Pier pad size DIAGRAM

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) OTI
Manufacturer _____
Longitudinal Stabilizing Device w/ Lateral Arms OTI
Manufacturer _____

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
16.5 x 16.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft ☒

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Number
Sidewall 24
Longitudinal 6
Marriage wall 7-5-4
Shearwall 2

Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb. soil _____ without testing.

X 1500

X 1500

X 1500

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 1500

X 1500

X 1500

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5' anchors without testing _____. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name DAVID ALBRIGHT MOBILE HOME SVC

Date Tested _____



Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 73-77

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 79-80

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 78-110

Application Number: _____

Date: _____

Site Preparation

Debris and organic material removed X

Water drainage: Natural _____ Swale _____ Pad X _____ Other _____

Fastening multi wide units

Floor: Type Fastener: LAGS Length: 6" Spacing: 2'
Walls: Type Fastener: SCREWS Length: 3" Spacing: 18"
Roof: Type Fastener: LAGS Length: 6" Spacing: 2'

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials DA

Type gasket FACTORY
Pg. 41 _____

Installed:
Between Floors Yes X
Between Walls Yes END WALLS
Bottom of ridgebeam Yes X

Weatherproofing


The bottomboard will be repaired and/or taped. Yes X _____ Pg. 124
Siding on units is installed to manufacturer's specifications. Yes X _____
Fireplace chimney installed so as not to allow intrusion of rain water. Yes X _____

Miscellaneous

Skirting to be installed. Yes _____ No X _____
Dryer vent installed outside of skirting. Yes _____ N/A X _____
Range downflow vent installed outside of skirting. Yes _____ N/A X _____
Drain lines supported at 4 foot intervals. Yes X _____
Electrical crossovers protected. Yes X _____
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature David Albright Date _____

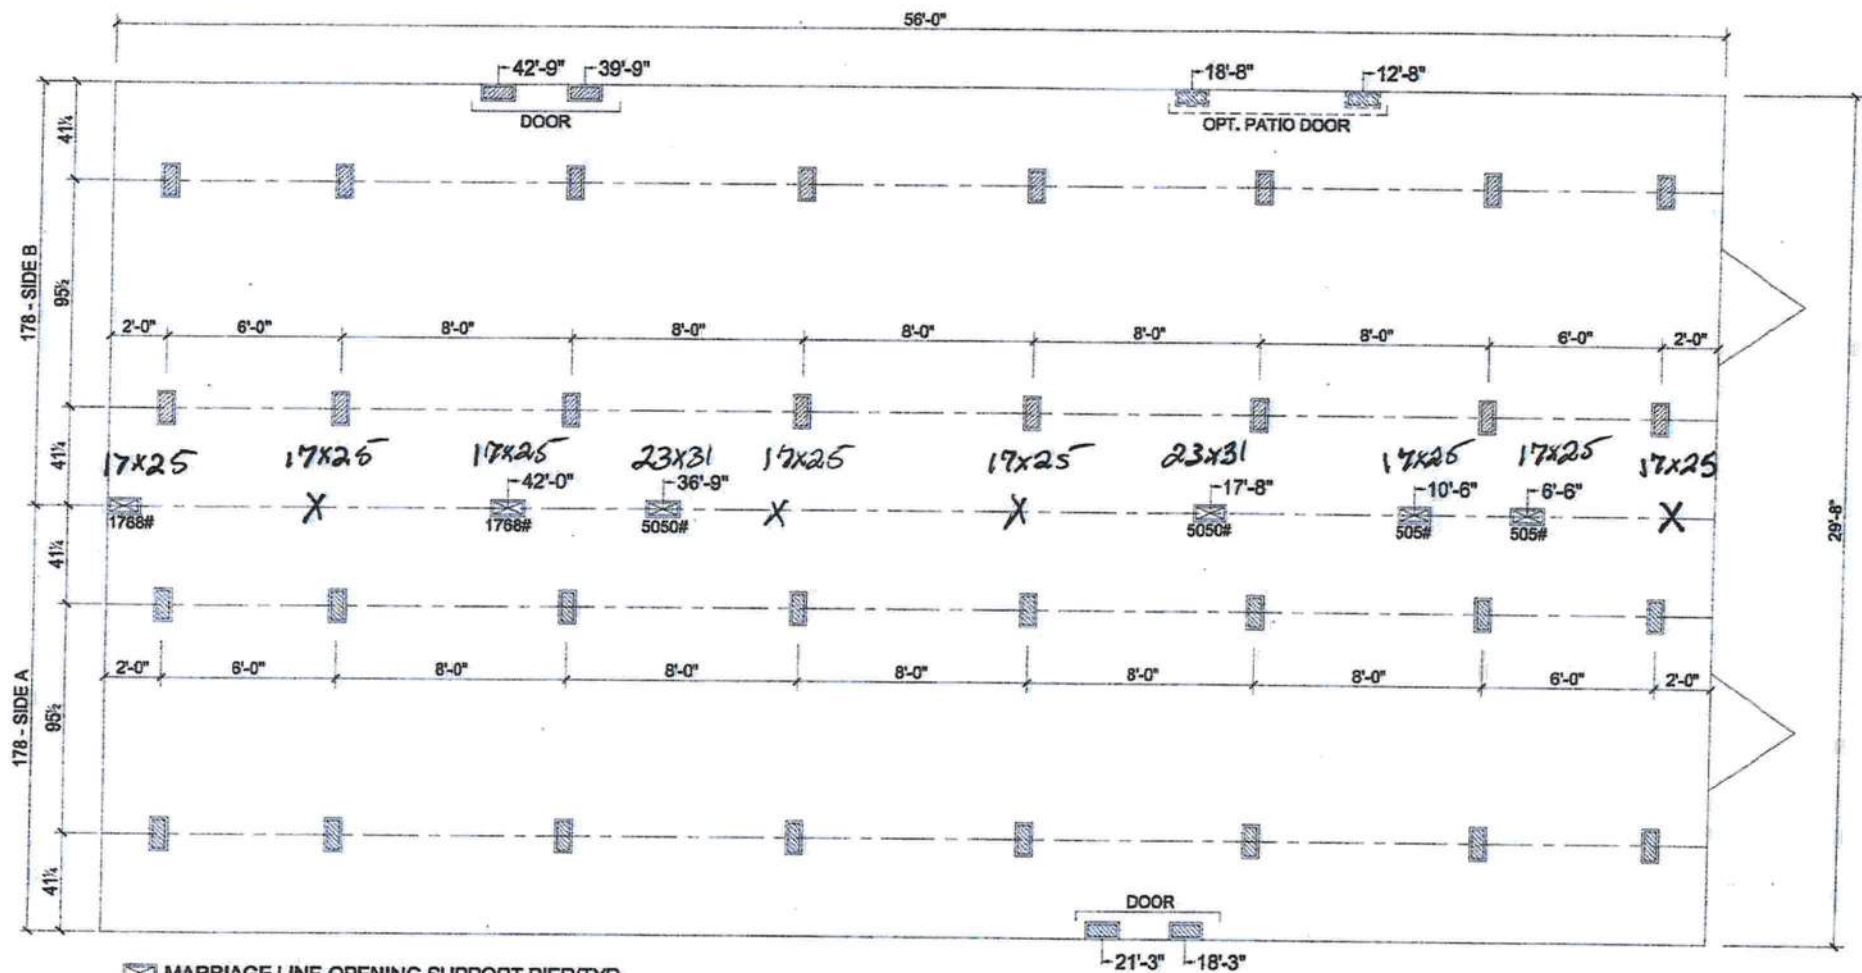

MARRIAGE LINE OPENING SUPPORT PIER/TYP.
 SUPPORT PIER/TYP.
 TIEDOWN LOCATIONS

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND IT'S SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes
MODEL: U-3563E-SIG - 32 X 60
3-BEDROOM / 2-BATH

HORIZON

U-3563E-SIG



License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT		
Order #: 4517	Label #: 72902	Manufacturer: LIVE OAK
Homeowner: CLARK	Year Model:	(Check Size of Home)
Address: S.W. OLD NIBLACK AVE	Length & Width: 60x32	Single _____
City/State/Zip: FORT WORTH FL 32038	Type Longitudinal System: 60TI	Double ☒
Phone #:	Type Lateral Arm System: 60TI	Triple _____
Date Installed:	New Home: ☒ Used Home: _____	HUD Label #:
Installed Wind Zone: II	Data Plate Wind Zone: II	Soil Bearing / PSF:
Note:		Torque Probe / in-lbs:
		Permit #:

**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

72902

LABEL #	DATE OF INSTALLATION
DAVID E ALBRIGHT	
NAME	
IH / 1129420 / 1	4517
LICENSE #	ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS


PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.



HORIZON



FRONT ELEVATION

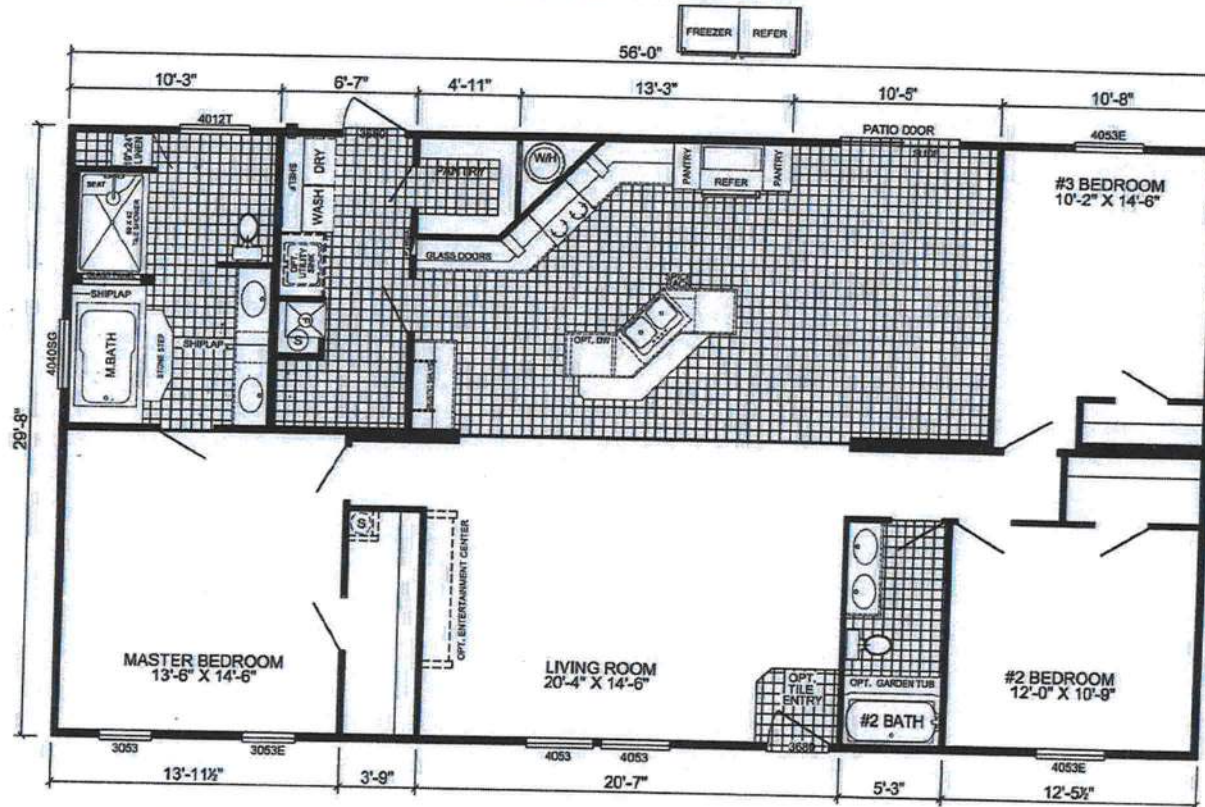

U-3563E-OAK

3-BEDROOM / 2-BATH

32 X 60 - Approx. 1661 Sq. Ft.

Date: 06/04/19

- * All room dimensions include closets and square footage figures are approximate.
- * Transom windows are available on optional 9'-0" sidewall houses only.
- * Live Oak Homes reserves the right to modify product offering at any time.
- * Skirting shown is optional.
- * Small dormer is optional only

OAKS
Signature Series
