


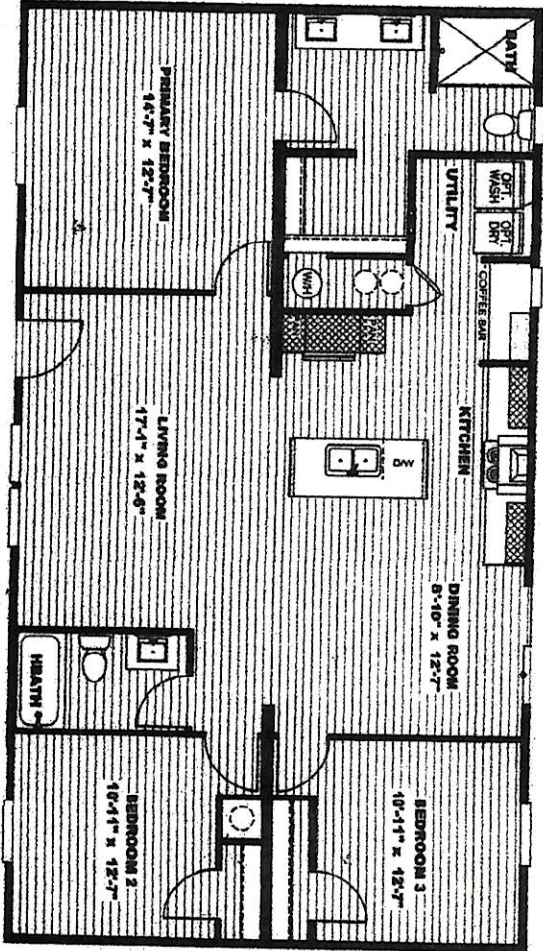


MODEL #CEJ28483AH
DRAWING #CE-MO29-48-3
28'X48' DESOTO

20 lb ROOF LOAD		SCWALL OPENING FT) REQUIRED PERIOD (1.5)					
SCWALL OPENING PERIOD		3	4	5	6	8	10
28 BOX WIDTH		1175	1330	1485	1640	1950	2260

FOR 30 lb & 40 lb ROOF LOAD REFER TO TABLES 7b & 7c IN THE INSTALLATION MANUAL.

20 m Root/Live Load			30 m Root/Live Load			40 m Root/Live Load		
Column Pier #	Distance from Hiltch (ft)	Pier Load (lb)	Column Pier #	Distance from Hiltch (ft)	Pier Load (lb)	Column Pier #	Distance from Hiltch (ft)	Pier Load (lb)
1	12.533	3023	1	12.533	6018	1	12.533	4223
2	29.667	3023	2	29.667	6018	2	29.667	4223

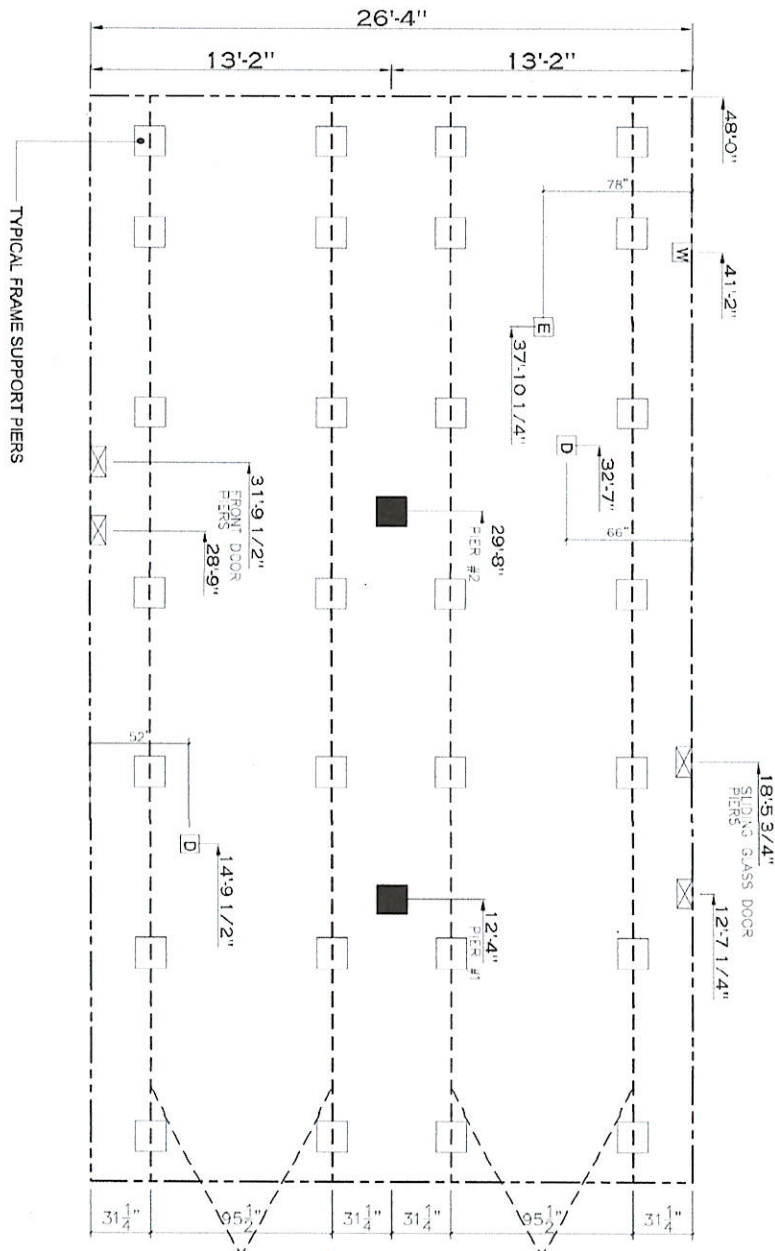

TYPICAL FRAME SUPPORT PIERS

PIER LEGEND

- ☐ * SUPPORT DOES NOT OPERATE
- ☒ ■ * SUPPORT IS AVAILABLE
- ☒ ■ * SUPPORT IS NOT AVAILABLE
- ☒ ■ * SUPPORT IS NOT AVAILABLE
- ☐ ■ * SUPPORT IS NOT AVAILABLE
- ☐ ■ * SUPPORT IS NOT AVAILABLE

• * SUPPORT IS NOT AVAILABLE

• * SUPPORT IS NOT AVAILABLE

SERVICE DROP LEGEND

E	= ELECTRICAL BOX
W	= WATER METER
D	= DRAIN TO JUNCTION BOX
G	= GAS METER

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

Installer: Ernest S Johnson

License # TH1025249

Address of home being installed 180 Diamond Lake Glen High Springs FL 32655

Manufacturer Crafton


Length x width 48' x 28'

NOTE:


if home is a single wide fill out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Installer's initials [Signature]

Typical pier spacing 2'



Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

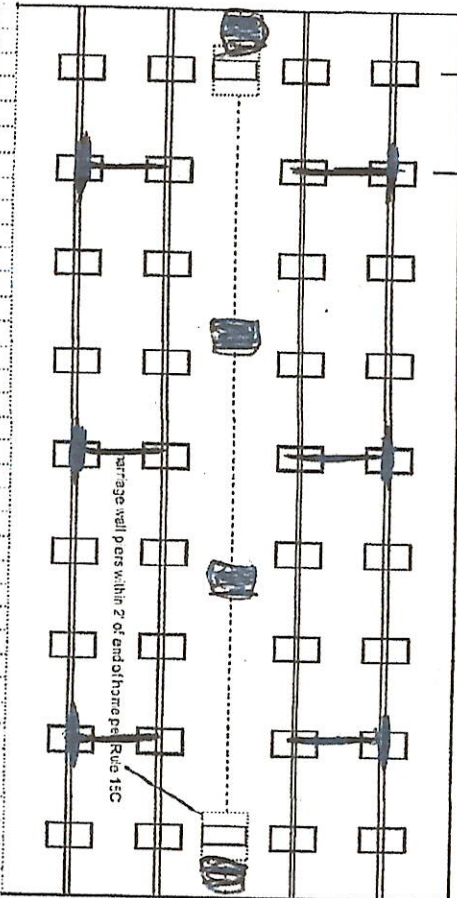

New Home ☒

Used Home ☐

Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C

Single wide ☐

Wind Zone II ☒

Wind Zone III ☐

Double wide ☒

Installation Decal # 83179

Triple/Quad ☐

Serial # 27598

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	16' x 16" (256)	18 1/2" x 18 1/2" (342)	20' x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'6"	6'	7'	8'	9'	10'
2000 psf	6'	8'	9'	10'	11'	12'
2500 psf	7'6"	9'	10'	11'	12'	13'
3000 psf	8'	10'	11'	12'	13'	14'
3500 psf	8'	10'	11'	12'	13'	14'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 23' x 31'
Perimeter pier pad size 16' x 18'
Other pier pad sizes (required by the mfg.) _____

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☐ 5 ft ☐

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer _____
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer Oliver 1101 v

Number _____
Sidewall _____
Longitudinal _____
Marriage wall _____
Shearwall _____

Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil without testing.

x 1000 x 1000 x 1000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1000 x 1000 x 1000

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing _____ A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. 1 unders and 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Ernest Scott Johnson

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Application Number: _____

Date: _____

Site Preparation

Debris and organic material removed _____

Water drainage: Natural _____

Swale _____

Pad ☒

Other _____

Fastening multi wide units

Floor: _____

Type Fastener: 1095

Length: 7

Spacing: 20

Walls: _____

Type Fastener: 1095

Length: 4

Spacing: 20

Roof: _____

Type Fastener: 1095

Length: 7

Spacing: 20

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

Type gasket P-11

Installed: Yes

Between Floors Yes

Between Walls Yes

Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes _____ Pg. _____
Siding on units is installed to manufacturer's specifications. Yes _____
Fireplace chimney installed so as not to allow intrusion of rain water. Yes _____

Miscellaneous

Skirting to be installed. Yes _____ No _____

Dryer vent installed outside of skirting. Yes _____

Range downflow vent installed outside of skirting. Yes _____

Drain lines supported at 4 foot intervals. Yes _____

Electrical crossovers protected. Yes _____

Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Ernest Scott Johnson

Date

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

LABEL # 83179

NAME ERNEST SCOTT JOHNSON

LICENSE # IH / 1025249 / 1

ORDER # 5040

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325 AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF INSTALLATION AND AFFIX LABEL NEXT TO HUD LABEL. USE PERMANENT INK PEN OR MARKER ONLY. COMPLETE INFORMATION ABOVE AND KEEP ON FILE FOR A MINIMUM OF 2 YEARS. YOU ARE REQUIRED TO PROVIDE COPIES WHEN REQUESTED.

License Number: IH / 1025249 / 1 Name: ERNEST SCOTT JOHNSON

Order #: 5040

Label #: 83179

Manufacturer:

Year Model:

Length & Width:

Type Longitudinal System:

Type Lateral Arm System:

New Home: _____ Used Home: _____

Data Plate Wind Zone:

Permit #:

Installed Wind Zone:

Note:

Homeowner:

Address:

City/State/Zip:

Phone #:

Date Installed:

Soil Bearing / PSF:

Torque Probe / in-lbs:

HUD Label #:

Triple _____

Double _____

Single _____

(Check Size of Home)
