

PERMIT WORKSHEET

page 1 of 2

PERMIT NUMBER

Installer Ernest Scott Johnson License # IH-1025249

Installer Mobile Phone # 352-494-8099

Address of home being installed SW VALLEY BLVD

LAKE CITY, FL 32024


Manufacturer LIVLOCK Length x width 64 X 32

NOTE: If home is a single wide fill out one half of the blocking plan.
If home is a triple or quad wide sketch in remainder of home.

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's Initials [Signature]

Typical pier spacing 6.6'

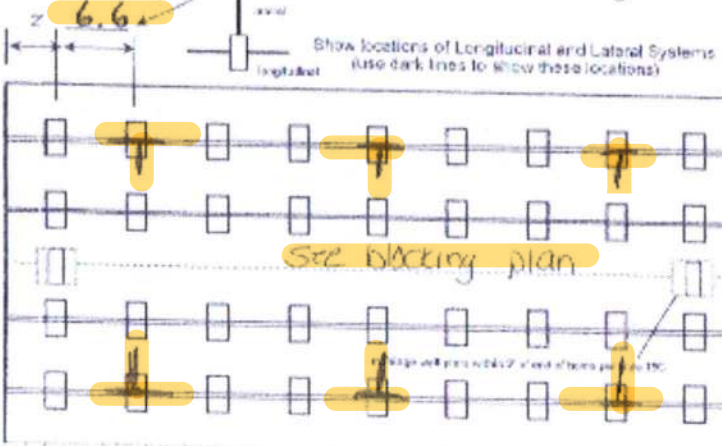

View Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual ☒

Home is installed in accordance with Rule 15-C ☐

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Decal # 88875

Triple/Quad ☐ Serial # LOHGA10022218AB

Roof System: ☒ Typical ☐ Hinged

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq. ft.)	16' x 16' (256)	16 1/2' x 16 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3	4'	5'	5'	7'	8'	8'
1500 psf	4 1/2	6'	7'	8'	9'	10'	10'
2000 psf	6	8'	9'	10'	11'	12'	12'
2500 psf	7 1/2	8'	10'	11'	12'	13'	13'
3000 psf	9	8'	11'	12'	13'	14'	14'
3500 psf	10 1/2	8'	11'	12'	13'	14'	14'

* Interpolated from Rule 15C-1 pier spacing table

PIER PAD SIZES

I-beam pier pad size 23x31

Other pier pad sizes (required by the mfg.): CHRYSLER 1101V-1065

Perimeter pier pad size or 16 x 18

Other pier pad sizes (required by the mfg.):

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening	Pier pad size
<u>17.5 X 25.5</u>	<u>17.5 X 25.5</u>
<u>17.5 X 25.5</u>	<u>17.5 X 25.5</u>
<u>17.5 X 25.5</u>	<u>17.5 X 25.5</u>

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer CHRYSLER 1101V
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer CHRYSLER 1101V

POPULAR PAD SIZES

Pier Size	sq. ft.
16 x 16	256
16 x 18	288
18 x 18	324
18 x 22	396
17 x 22	374
13 1/4 x 28 1/4	348
20 x 20	400
17 3/16 x 25 5/16	441
17 1/2 x 25 1/2	446
24 x 24	576
23 x 26	598

ANCHORS

4 ft ☒ 5 ft ☒

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

	Number
Scowall	26
Longitudinal	0
Marriage wall	10
Shoarwall	2



Anthony Islam

05-06-2022

PERMIT NUMBER

PERMIT WORKSHEET

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psi
or check here to declare 1000 lb. soil _____ without testing.

x 1500

x 1500

x 1500

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 500

x 1500

x 1500

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 8" anchors without testing _____. A test showing 275 inch pounds or less will require 8 foot anchors.

Note: A state approved, safety arm system is being used and 4" anchors are allowed at the sidewall locations. I understand 8" anchors are required at all centerline 16 points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name: Ernest Scott Johnson

Date Tested: Assumed Oliver 11/11/22

4 & 5" Anchors

Electrical

Connect electrical conductors between multi-wire units, but not to the main power source. This includes the bonding wire between multi-wire units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply system. Pg. _____

Site Preparation

Debris and organic material removed ☒
Water drainage: Natural ☒ Swale ☐ Pad ☒ Other _____

Fastening multi-wire units

	Type Fastener	Length	Spacing
Floor	10d	7"	24"
Walls	10d	4"	12"
Roof	10d	3"	24"

For used homes: a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket (weatherstripping) required

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

installer's initials EJ

Type gasket
Pg. 211

Installed:
Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing


The bottom board will be repaired and/or taped. Yes ☒ Pg. _____
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous

Skirting to be installed: Yes ☒ No ☐
Dryer vent installed outside of skirting: Yes ☒ N/A ☐
Range downflow vent installed outside of skirting: Yes ☒ N/A ☐
Drain lines supported at 4 foot intervals: Yes ☒
Electrical crossovers protected: Yes ☒
Other _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature Ernest Scott Johnson Date 5/13/22

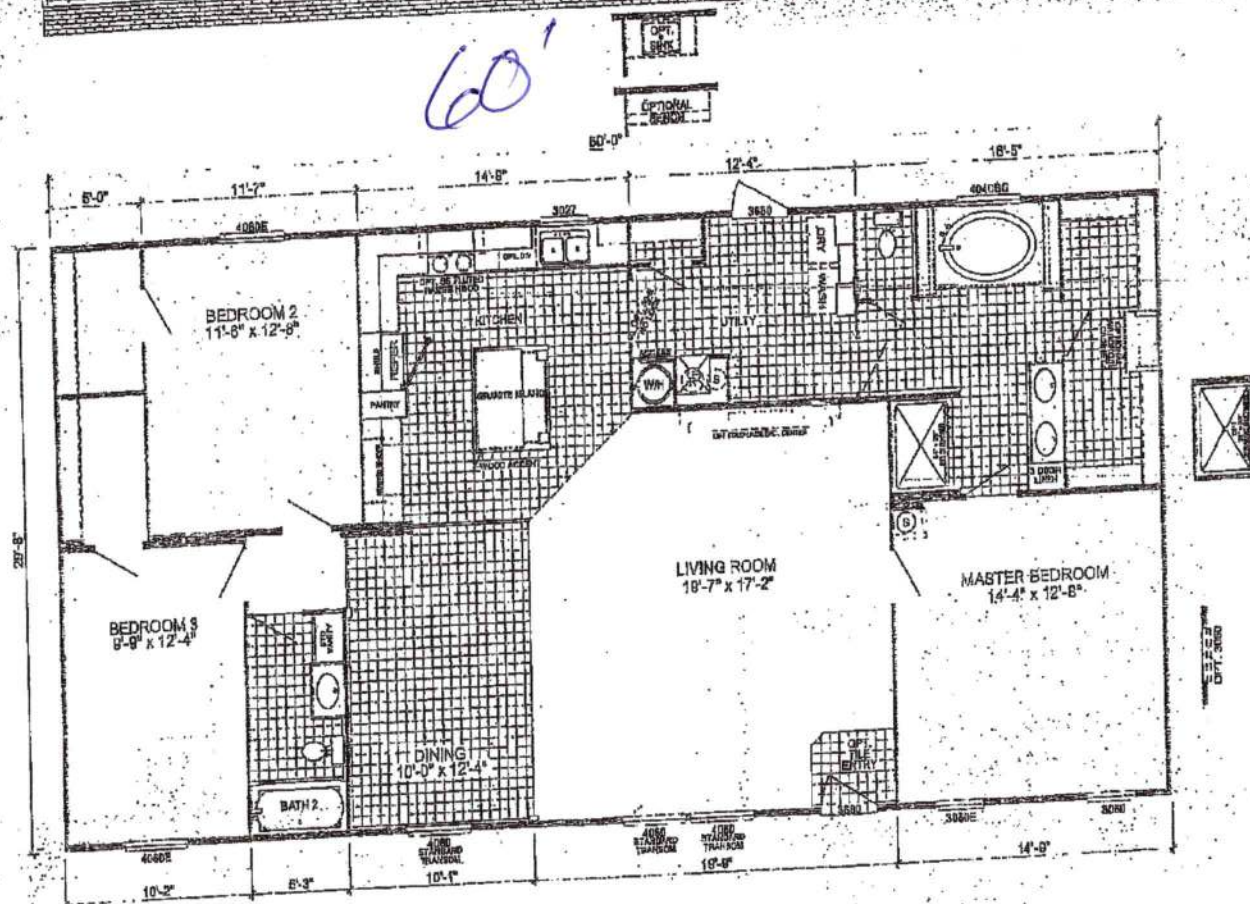

Date: 09/26/18

* All room dimensions include closets and square footage figures are approximate.
* Transom windows are available on optional 8'-0" sidewalk houses only.
* Live Oak Homes reserves the right to modify product offerings at any time.

