CARR

These worksheets must be completed and signed by the installer. Submit the originals with the packet.

DUKE 4-3524D


page 1 of 2

installer DAVID ALBRIGHT License # 1H/ 1129420	New Home Used Home
home is being installed. LAKE CITY, FL 32055 Manufacturer LIVE OAK HOMES Length x width NOTE: If home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home I understand Lateral Arm Systems cannot be used on any home (new or used)	Home installed to the Manufacturer's Installation Mentral Home is installed in accordance with Rule 15-C Single wide
Typical pier spacing Installer's initiels Show locations of Longitudinal and Lateral Systems [Longitudinal (use dark lines to show these locations)	Load Fooler 16" x 16" 18 1/2" x 18 20" x 20" 22" x 22" 24" x 24" 26" x 25" (484)" (578)" (576) 1800 pef 4' 6" 6' 7' 6" 6' 7' 8' 2000 pef 4' 6" 6' 7' 6" 8' 8' 8' 8' 8' 8' 8' 8' 8' 8' 8' 8' 8'
TO THE PARTY OF TH	3000 psf 8' 8' 8' 8' 8' 8' 8' 8
estations wall plans whiteh 2° of and of isoma parties a face	Draw the approximate locations of marriage wall openings 4 fool or greater. Use this symbol to show the piers. List all marriage wall openings greater than 4 foot and their pier pad sizes below.
Plans Reviewed for Code Gampliance Thousan The of Florids Th	Opening Pier pad size 15 32 x 23 4 tt 5 ft CTR 4 /7 x 25 FRAME TIES 3 /7 x 25 within 2' of end of home spaced at 5' 4" oc TIEDOWN COMPONENTS Longitudinal Stabilizing Device (LSD) OT Sidewall Longitudinal Stabilizing Device w/ Lateral Arms Manufacturer Longitudinal Stabilizing Device w/ Lateral Arms Manufacturer Longitudinal Stabilizing Device w/ Lateral Arms Manufacturer Manufacturer OT


Mobile Home Permit Worksheet

	3. Using 500 reading a	D lb. increments, take and round down to th	the lowest at incremen	t.
Г		TORQUE PROBE	TEST	
ancho readin	rs are required	at the sidewall locati at all centerline tie p s and where the mob a 4000 to solding cap l	oints where	the torque test anufacturer may
ALL TES		PERFORMED BY A		
staller Name	DAVID A	LBRIGHT MOE	BILE HON	/IE SVC
te Tested				


	Site Preparation
Debris a	and organic material removed X
Water d	frainage: Natural Swale Pad X Other
	Fastening multi wide units
Floor:	Type Fastener: LAGS Length: 6" Spacing: 2' Type Fastener: SCREWS Length: 3" Spacing: 18"
Walls: Roof:	
NUOI.	Type Fastener: LAGS Length: 6" Spacing: 2' For used homes a min. 30 gauge, 8" wide, galvanized metal strip
	will be centered over the peak of the roof and fastened with galv.
	roofing nails at 2" on center on both sides of the centerline.
	rooming mails at 2. On center on pour sides of the centerline.
	Gasket (weatherproofing requirement)
undere	tand a properly installed gasket is a requirement of all new and used
homes a	and that condensation, mold, meldew and buckled marriage walls are
a result	of a poorly installed or no gasket being installed. I understand a strip
of tape v	vill not serve as a gasket.
•	Installer's initials
n	LA FACTORY
	sket FACTORY Installed:
² g. <u>41</u>	Between Floors Yes X Between Walls Yes END WALLS
	Bottom of ridgebeam Yes X
	bottom of nagebeam res A
	Weatherproofing
Siding or	omboard will be repaired and/or taped. Yes X
Siding or	units is installed to manufacturer's specifications. Yes X
Siding or Fireplace	n units is installed to manufacturer's specifications. Yes X chimney installed so as not to allow intrusion of rain water. Yes X
Siding on Fireplace Skirting to Oryer ven	munits is installed to manufacturer's specifications. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X nt installed outside of skirting. Yes N/A X
Siding or Fireplace Skirting to Pryer ventange do	munits is installed to manufacturer's specifications. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X nt installed outside of skirting. Yes N/A X bownflow vent installed outside of skirting. Yes N/A X
Siding on Fireplace Skirting to Oryer ventange do Orain line	munits is installed to manufacturer's specifications. Yes X chimney installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X it installed outside of skirting. Yes N/A X es supported at 4 foot intervals. Yes X
kirting to ryer ven ange do rain line lectrical	munits is installed to manufacturer's specifications. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X nt installed outside of skirting. Yes N/A X bownflow vent installed outside of skirting. Yes N/A X
kirting to ryer ven ange do rain line lectrical	munits is installed to manufacturer's specifications. Yes X chimney installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X it installed outside of skirting. Yes N/A X es supported at 4 foot intervals. Yes X
kirting to ryer ven ange do rain line lectrical	munits is installed to manufacturer's specifications. Yes X chimney installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X it installed outside of skirting. Yes N/A X es supported at 4 foot intervals. Yes X
Siding on Fireplace Skirting to Oryer ventange do Orain line	munits is installed to manufacturer's specifications. Yes X chimney installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X it installed outside of skirting. Yes N/A X es supported at 4 foot intervals. Yes X
Siding on Fireplace Skirting to Oryer ven tange do train line	munits is installed to manufacturer's specifications. Yes X chimney installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X it installed outside of skirting. Yes N/A X es supported at 4 foot intervals. Yes X
Skirting to Skirting to Oryer ven Range do Irain line Electrical	Miscellaneous Miscellaneous be installed. Yes No _X to installed outside of skirting. Yes N/A _X bownflow vent installed outside of skirting. Yes N/A _X supported at 4 foot intervals. Yes N/A _X crossovers protected. Yes X Iler verifies all information given with this permit workshee
Skirting to Skirting to Oryer ven Range do Irain line Electrical	munits is installed to manufacturer's specifications. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusions. Yes X e chimney installed so as not to allow intrusions. Yes X e chimney installed so as not to allow intrusions. Yes X e chimney installed so as not to allow intrusions. Yes X e chimney installed so as not to allow intrusions. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water. Yes X e chimney installed so as not to allow intrusion of rain water.
Skirting to Skirting to Dryer ver Lange do Train line Electrical Other :	Miscellaneous be installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X to installed outside of skirting. Yes N/A X bwnflow vent installed outside of skirting. Yes N/A X supported at 4 foot intervals. Yes X crossovers protected. Yes X ler verifies all information given with this permit worksheet is accurate and true based on the
Skirting to Skirting to Dryer ver Lange do Train line Electrical Other :	Miscellaneous Miscellaneous be installed. Yes No _X to installed outside of skirting. Yes N/A _X bownflow vent installed outside of skirting. Yes N/A _X supported at 4 foot intervals. Yes N/A _X crossovers protected. Yes X Iler verifies all information given with this permit workshee
Siding on Fireplace Skirting to Proper vertange do Prain line Electrical Other :	Miscellaneous be installed so as not to allow intrusion of rain water. Yes X Miscellaneous be installed. Yes No X to installed outside of skirting. Yes N/A X bwnflow vent installed outside of skirting. Yes N/A X supported at 4 foot intervals. Yes X crossovers protected. Yes X ler verifies all information given with this permit worksheet is accurate and true based on the



EXTERIOR VINYL SHAKER PACKAGE (STD)

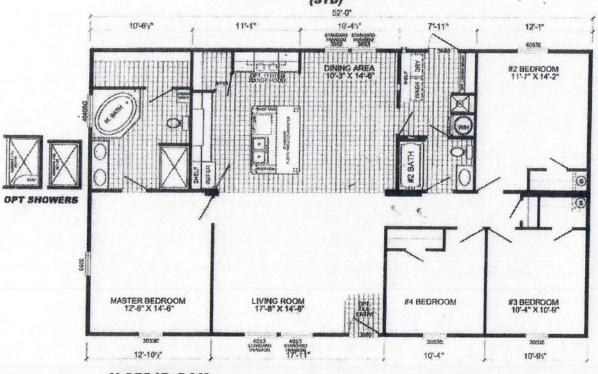





OPTIONAL 3 BEDROOM LAYOUT

U-3524D-OAK 4-BEDROOM / 2-BATH 32 X 56 - Approx. 1525 Sq. Ft.


- All room dimensions include closets and square factage figures are approximate.

 Transom wholevs are available on optional 9°-0° sidesal houses only.

 Lindespining states is epitional.

 Live Oak Homes reserves the right to modify product affeding at any time.



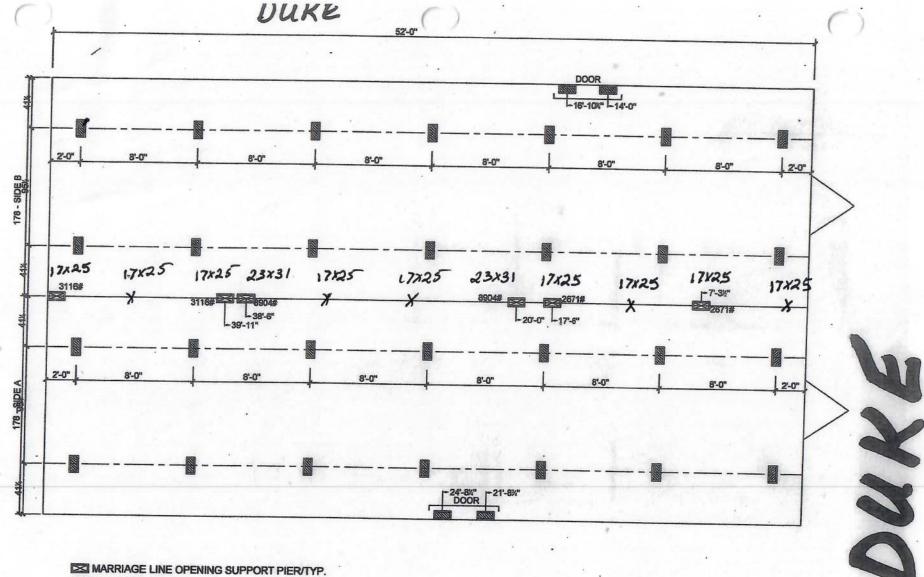

SUPPORT PIER/TYP

8-22-2011

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND IT'S SUPPLEMENTS.
 FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
 FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes MODEL: U3524D - 32 X 52 4-BEDROOM / 2-BATH

- (A) MAIN ELECTRICAL
- G DUCT CROSSOVER
- B ELECTRICAL CROSSOVER
- (H) SEWER DROPS
- © WATER INLET
- (I) RETURN AIR (W/OPT. HEAT PUMP OH DUCT)
- (D) WATER CROSSOVER (IF ANY) (J) SUPPLY AIR (W/OPT. HEAT PUMP OH DUCT)
- E GAS INLET (IF ANY)
- (F) GAS CROSSOVER (IF ANY)

U-3524D

Plans Reviewed for Code Compliance

Pare of Florid

Manufacturer: LIVE ORK	(Check Size of Home	
Year Model: 2021	Single	
Length & Width: 52/56 × 32	Double	
Type Longitudinal System: 6 OTZ	HUD Label #:	
Type Lateral Arm System: 6 07Z	Soil Bearing / PSF:	
New Home: Used Home:	Torque Probe / in-lbs:	
Data Plate Wind Zone:	Permit #:	
	Length & Width: 52/56 × 32 Type Longitudinal System: 6 OTT Type Lateral Arm System: 6 OTT New Home: Used Home:	



STATE OF FLORIDA INSTALLATION CERTIFICATION LABEL 71614

LABEL#

DATE OF INSTALLATION

DAVID E ALBRIGHT

NAME

IH / 1129420 / 1

4444

LICENSE#

ORDER# CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325 AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF INSTALLATION AND AFFIX LABEL NEXT TO HUD LABEL. USE PERMANENT INK PEN OR MARKER ONLY. COMPLETE INFORMATION ABOVE AND KEEP ON FILE FOR A MINIMUM OF 2 YEARS. YOU ARE REQUIRED TO PROVIDE COPIES WHEN REQUESTED.

Freedom Mobile Home Sales, Inc

DATE OF BIRTH BUYER: 07/13/89

466 SW DEPUTY J DAVIS LN, LAKE CITY, FLORIDA 32024 (386) 752-5355 Fax: (386) 752-4757

DRIVER'S LICENSE

BUYER: C600-512-89-753-0 CO-BUYER: C600-424-95-164-0

CO-BUYER: 05/04/95

EMAIL KATIEWEEK@GMAIL.COM

BUYER(S)		LYNNE CARR & JEFFERY		CARR		PHONE 386-339-	7465-HER DATE	10/14/20
ADDRESS	THE RESIDENCE OF THE PROPERTY OF THE COURSE	AYNE PL #201 LAKE CITY F				S	alesperson: MIKE	COX
DELIVERY ADDRESS MAKE & MODEL	TBD NIKITA	PLACE LAKE CITY, FL 3205	55					
LIVE OAK U-3524D					YEAR 2021	BEDROOMS FLOOR SIZE	The state of the s	STOCK NUMBER
SERIAL NUMBER (VIN NUMBER) LOHGA32072058AB		New or Used		COLOR	PROPOSED DELIVERY DATE	32 L 32 W 36	1743 KEY NUMBERS	
LOCATION	R-VALUE	THICKNESS	NEW TYPE OF INSULATION			2405.5		
CEILING	27	9 1/5				BASE P	RICE OF UNIT	\$100,309.00
EXTERIOR	11	3 1/2	ROCKWOOL FIBERGLASS				SUB-TOTAL	6400 200 00
FLOORS	22	7	FIBERGLASS				COUNTY TAX	\$100,309.00
	THIS INSULATION INFORMATION WAS FURNISHED BY THE MANUFACTURER A						SALES TAX 6%	\$50.00
		COMMISSION RULE 16 CRF, SECTIO		2 114			TAG AND TITLE	\$6,018.54
		JIPMENT, LABOR, AND ACC					TAG AND TITLE	\$0.00
Delivered and Set	Up:		LOGOTTIEG	Included				
Trim				Included				
Tied Down:				Included				
Dirt Pad				Included				
land clearing				NO		WELLAS	20 CEDTIC C 050	044 470 00
	sewer within	20 feet of existing facility		Included	1. CASH PU	RCHASE PRICE	20 SEPTIC 6,850	\$11,470.00
	CONTON TOTAL INT	20 lock of existing facility		included	I, CASH FU		00.00	\$117,847.54
						TRADE-IN ALLOWANCE	\$0.00	
Furnished			\$	NO	-	LESS BAL. DUE ON ABOVE	\$0.00	N Section 1
Unfurnished			- Þ	NO		NET ALLOWANCE	\$0.00	
Officialistica	_		_	AGREE	-	CASH DOWN PAYMENT	\$0.00	
Customor rosponsi	blo for any	ecker fees incurred on lot.				0	\$8,000.00	Asia
Customer responsi	ble for any wit	ecker rees incurred on lot.		AGREE			TOTAL CREDITS	\$8,000.00
Wheels & axles del	loted from sale	a price of bassa		100==			JE TO FREEDOM	\$109,847.54
vviieeis & axies dei	leted from sale	e price of nome.		AGREE		LAND PURCHASE PRI		\$12,000.00
Electrical Heature					CLOSING COST FINAN			
Electrical Hookup				Included		-02100	INSURANCE	
						ESTIMATED FINAL	LOAN AMOUNT	\$121,847.54
					Initial:			
					NO VERBAL	AGREEMENTS WILL BE H	IONORED.	
						R AGREES TO PAY U		\$0.00
T		17. (2000)				BUYERS CLOSING CO		
Type of A/C		14 SEER		Included	The U.S	Department of Housing ar	d Urban Developr	ment (HUD)
Type of Skirting		VERTICAL		Included	Manufactured Home Dispute Resolution Program is		n Program is avail	able to resolve
Type of steps		WOOD CODE		Included	disputes among manufacturers, retailers, or installers concerning		erning defects in	
					manufactu	red homes. Many states also	have a concume	r assistance or
					dispute	recolution program For addi	tional information	assistance or
NOTE: WARRANT DESCRIPTION OF TRADE-IN	TY, EXCLUSION	ONS AND LIMITATIONS OF	DAMAGES ON THE REVER		programs as	resolution program. For addi	tional information	about these
DESCRIPTION OF TRADE-IN		N/A	BEDROOMS SIZE		programs se	ee sections titled " Dispute R	esolution Process'	and "additional
MAKE	- X	MODEL	N/A	N/A N/A		HUD Manufactured Home	e Dispute Resoluti	on Program" in
W.W. W. 112					the consu	mer manual required to be p	rovided to the pure	chaser. These
TITLE NO.	SERIAL	C	COLOR		programs are	e not warranty programs and	do not replace the	e manufacturer's
					or any	other person's warranty pro	gram.	
					20000000	, , , , , , , , , , , , , , , , , , , ,	Jr.,	
N/A	N/A							
LIEN HOLDER	IN/A	PHONE NO		AMOUNT	Liquidated Dar	mages are agreed to \$900.00		
N/A		N/A		N/A	171	h price, whichever is greater.	or	
TI	RADE PAYOF	F IS TO BE PAID BY		0	DEEED TO DA	DACDARILES ON THE DELETE		
THIS AGREEMENT CONTAIN	AINS THE ENTIRE	F IS TO BE PAID BY UNDERSTANDING BETWEEN DEALE NTRACT. Dealer and Buyer ce me as if printed above the signatures.	R AND BUYER AN	ND NO OTHER REPR	RESENTATION OR	INDUCEMENT, VERBAL OR WRITTEN	SE SIDE OF THIS CO	NTRACT
are agreed to as part of this	agreement, the sar	ne as if printed above the signatures.	rtify that the add	ditional terms and purchasing	conditions printe	d on Page 2 of this contract are a ibed trailer, manufactured home, or	agreed to as part of the	e contract
and accessories, the insurance	e as described has be	een voluntary, the Buyer's trade-in is free of a	Il claims whatsoever	except as noted.	and above descr	ibod trailer, manufactured nome, or	venicie the optional equ	upment
Eroodom Mobile	Homo Colos							
Freedom Mobile Home Sales, Inc DEALER Not Valid Unless Signed by Steve Smith (Vice Pres)			SIGNED X				BUYER	
James Olymon Dy	Ciliai (vice		SOCIAL	L SECURITY NO.				
DV								
BYAge	ent			SIGNED X				BUYER
Age			SOCIAL	SECURITY NO.				
