
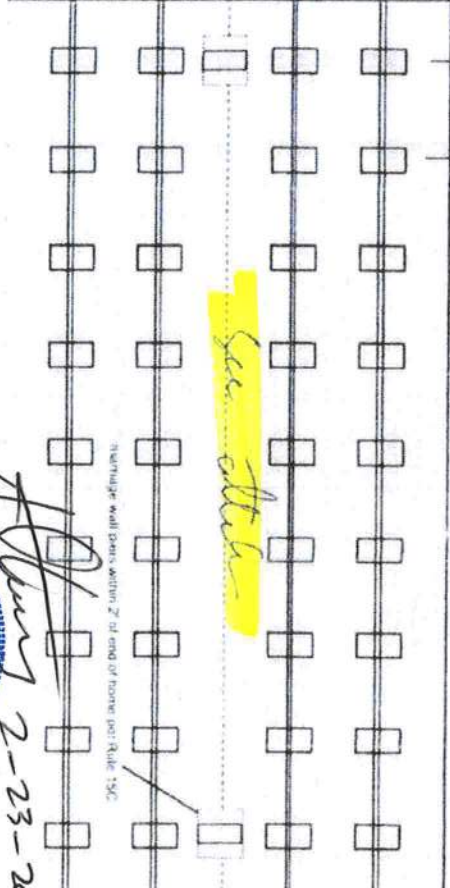


Mobile Home Permit Worksheet

Installer: Michael Lewis License #: 141025316
 Address of home being installed: 1277 Cedar Road
AKA 477, Hwy 32005
 Manufacturer: Live Oak Length x width: 58' x 28'

NOTE: if home is a single wide fill out one half of the blocking plan
 if home is a triple or quad wide sketch in remainder of home
 I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.



Application Number: _____ Date: _____

New Home ☒ Used Home ☐
 Home installed to the Manufacturer's Installation Manual ☒
 Home is installed in accordance with Rule 15-C ☒
 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Decal # 78062
 Triple/Quad ☐ Serial # 10HGA-32072001 A05

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	16' x 16' (256)	18' 1/2" x 18' (324)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'6"	6'	7'	8'	9'	10'
2000 psf	6'	8'	9'	10'	11'	12'
2500 psf	7'6"	9'	10'	11'	12'	13'
3000 psf	8'	10'	11'	12'	13'	14'
3500 psf	8'	10'	11'	12'	13'	14'

interpolated from Rule 15C-1 pier spacing table

PIER PAD SIZES

I-beam pier pad size: 17x75
 Perimeter pier pad size: N/A
 Other pier pad sizes (required by the mfg.): 16x16
D00028

POPULAR PAD SIZES

Pad Size	Sq in
16 x 16	256
16 x 18	288
16.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.
 List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening: _____ Pier pad size: _____

ANCHORS

4 ft ☒ 5 ft ☐

FRAME TIES

within 2' of end of home spaced at 5' 4" oc


TIEDOWN COMPONENTS

OTHER TIES

Longitudinal Stabilizing Device (LSD) _____
 Manufacturer _____
 Longitudinal Stabilizing Device w/ Lateral Arms _____
 Manufacturer _____
 Sidewall _____
 Marriage wall _____
 Shearwall _____

BLOCKING PLAN

Manufacturer Live Oak
Width x length 28' x 55'

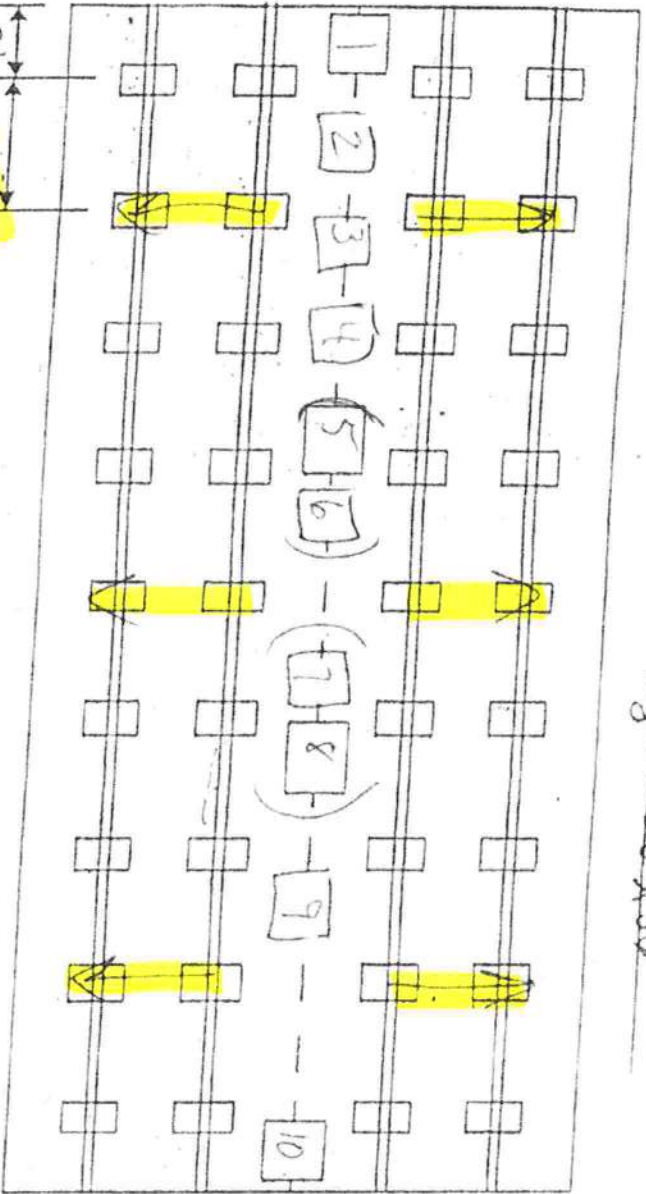

MARRIAGE WALL
Piers & location per floor plan



spaces at
Typical

Pier Spacing based on
for 200PSF Soil

Manual

Soil Bearing Capacity 1500

Probe test / anchor length 10' H

I-beam Pier Pad size 17' x 25'

Marriage Wall Pier Pad Size:

1 16' x 16' 5 24' x 24'

3 17' x 25'

10 17' x 25'

2 16' x 16' 6 16' x 16'

3 16' x 16' 7 24' x 24'

4 16' x 16' 8 16' x 16'

Perimeter Pier Pad Sizes 16' x 16'
10' x 10'

4' x 5' on loads over 3450 #

Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1380 psi or check here to declare 1000 lb. soil without testing

x 1380 x 1380 x 1380

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1380 x 1380 x 1380

TORQUE PROBE TEST

The results of the torque probe test is N/A inch pounds or check here if you are declaring 5" anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

installer's initials bc

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Wendell Davis

Date Tested

1-28-21

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 34

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 34

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 37

Application Number: _____

Date: _____

Site Preparation

Debris and organic material removed ☒ Swale ☒ Pad ☒ Other ☐

Fastening multi wide units

Floor: Type Fastener: LAG Length: 3 1/2" x 5" Spacing: 16" o.c.
Walls: Type Fastener: 5/8" Length: 48" Spacing: 16" o.c.
Roof: Type Fastener: 5/8" Length: 50" Spacing: 24" o.c.
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

installer's initials bc

Type gasket: FCC

Installed ☒
Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 34
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous


Skirting to be installed. Yes ☒ No ☐
Dryer vent installed outside of skirting. Yes ☒ N/A ☐
Range downflow vent installed outside of skirting. Yes ☒ N/A ☐
Drain lines supported at 4 foot intervals. Yes ☒ N/A ☐
Electrical crossovers protected. Yes ☒ N/A ☐
Other ☐

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature Wendell Davis

Date 1-28-21



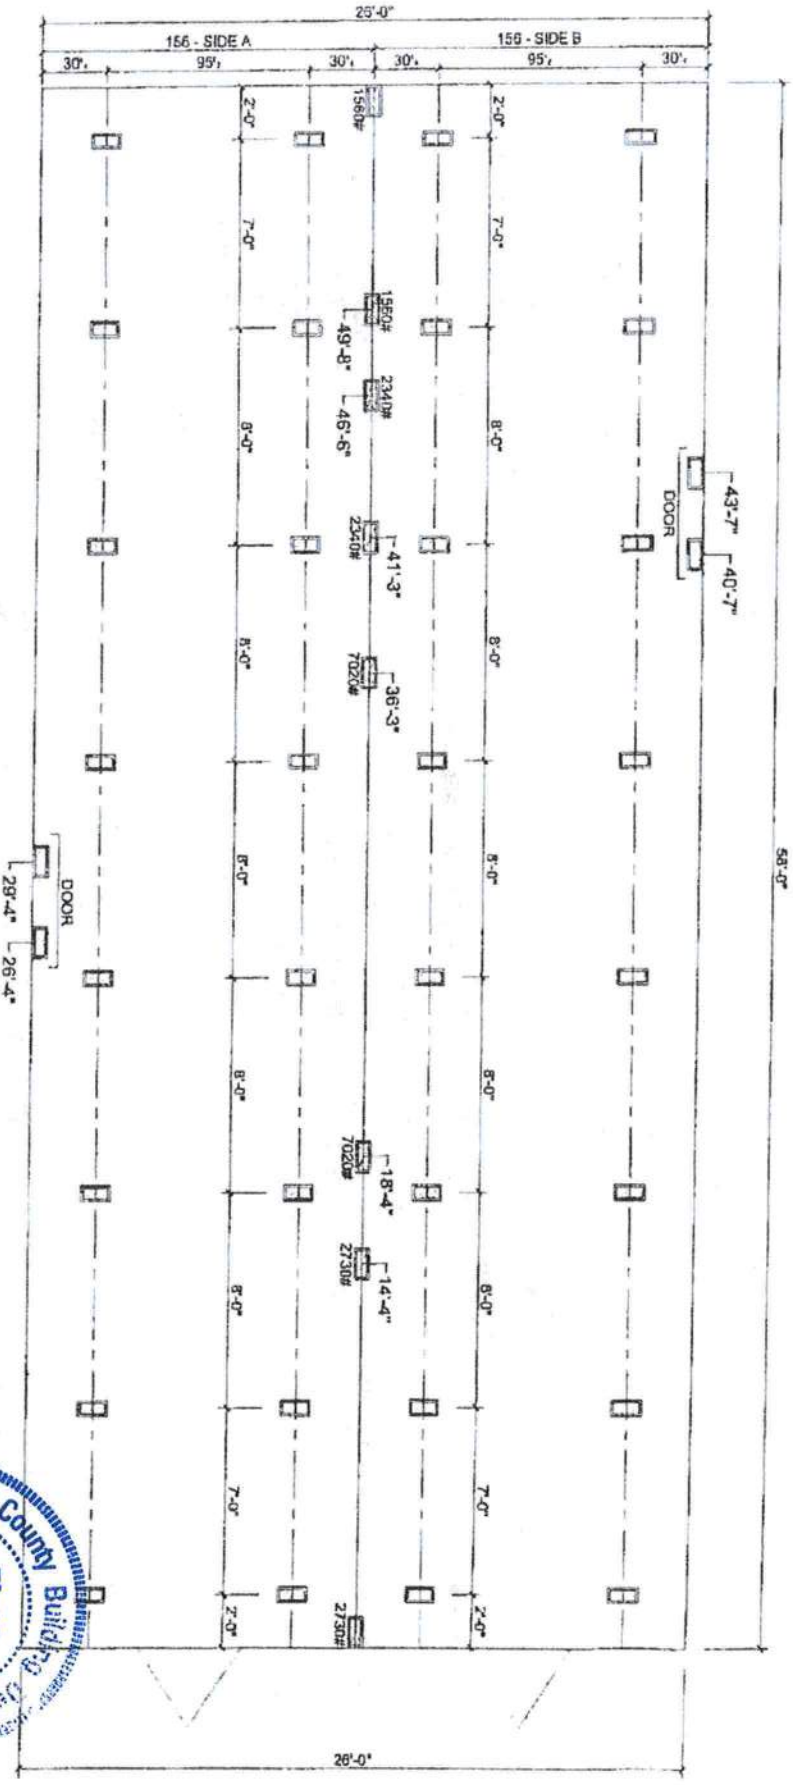

MARRIAGE LINE OPENING SUPPORT PIERTYP.
 SUPPORT PIERTYP

FOUNDATION NOTES:
 - THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
 - FOOTINGS ARE SHOWN FOR EXAMPLE ONLY. QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
 - FOOTINGS ARE REQUIRED AT SUPPORT POSTS. SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes
MODEL: H-2583C-PS - 28 X 60
3-BEDROOM / 2-BATH

Dakota





H-2583C-PS

Chiles Am
Garfield

Proposed

DAKOTA

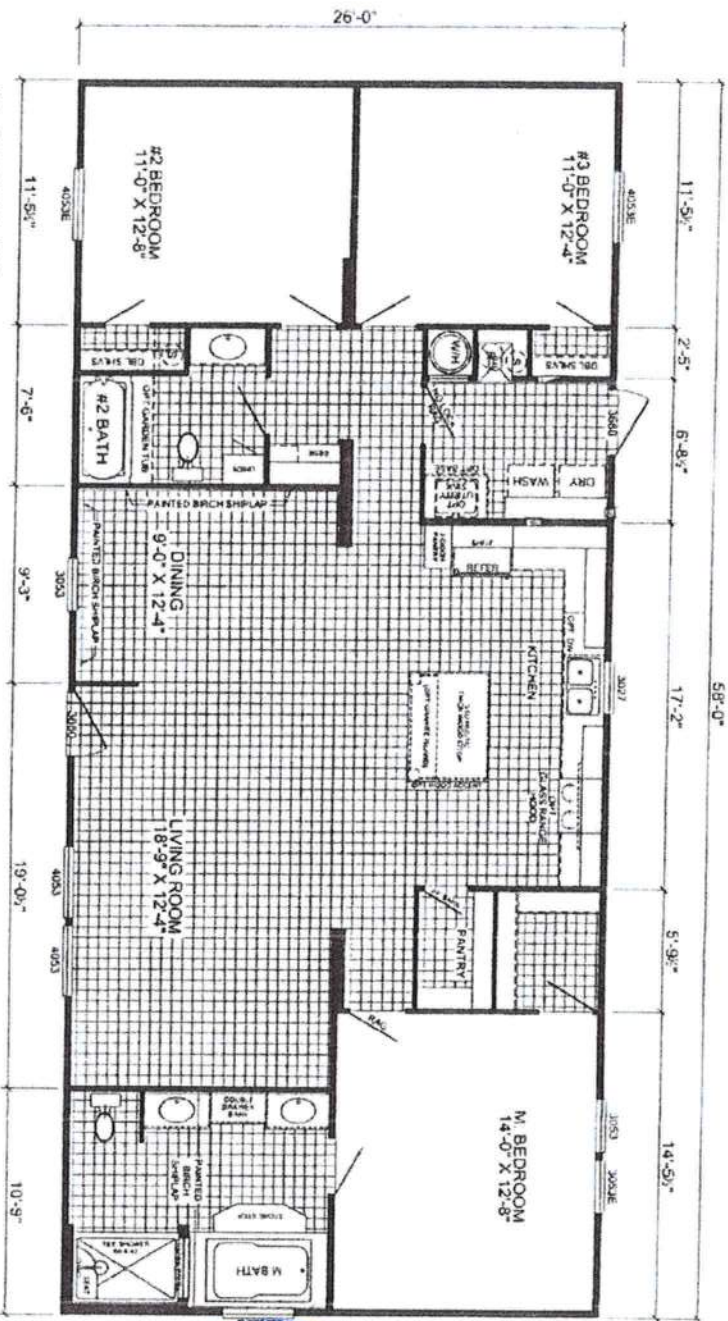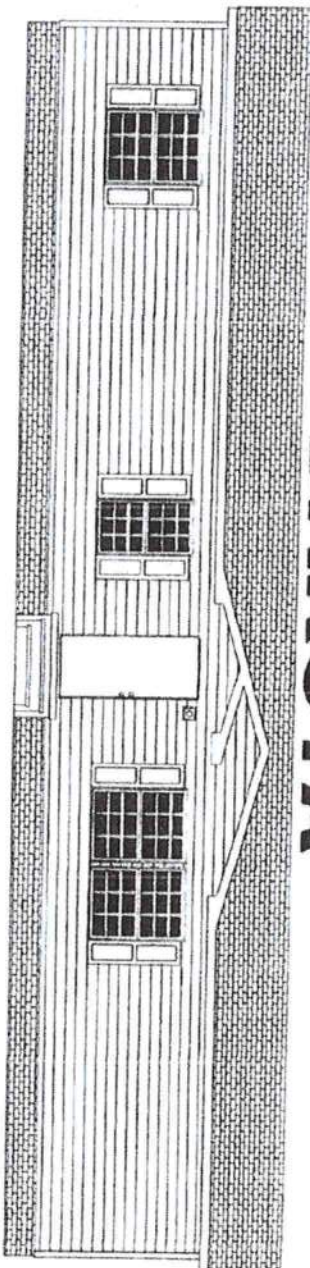

H-2583C-PS
3-BEDROOM / 2-BATH
28 x 62 - Approx. 1508 Sq. Ft.

Date: 04/29/20
* All room dimensions include closets and square footage figures are approximate.
* Live Oak Homes reserves the right to change product offerings at any time.

2/11/21

[Signature]

