


Mobile Home Permit Worksheet

Installer: Rusty L Knowles License # 1H1038219
 Address of home being installed: 1162 SW Al Lemon Ct
Lake City, FL 32024
 Manufacturer: Jacobsen Homes length x width: 32 x 48

NOTE: if home is a single wide fill out one half of the blocking plan
 if home is a triple or quad wide sketch in remainder of home
 I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Installer's initials: RLK

Typical pier spacing

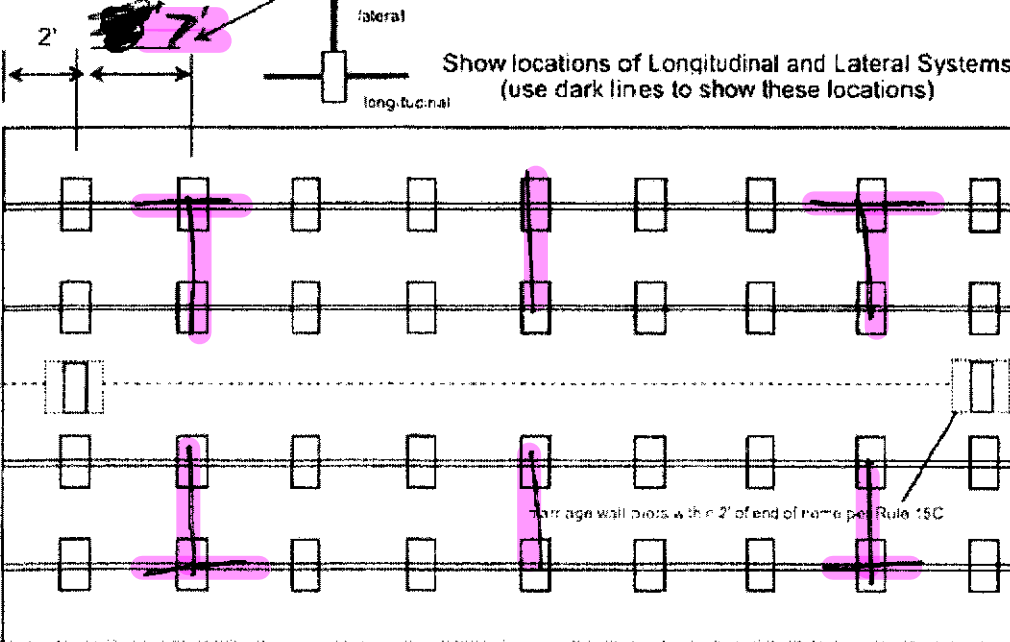

Application Number: _____ Date: _____

New Home ☒ Used Home ☐
 Home installed to the Manufacturer's Installation Manual ☐
 Home is installed in accordance with Rule 15-C ☐
 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Decal # 121715
 Triple/Quad ☐ Serial # ordered

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf		3'	4'	5'	6'	7'	8'
1500 psf		4' 6"	6'	7'	8'	8'	8'
2000 psf		6'	8'	8'	8'	8'	8'
2500 psf		7' 6"	8'	8'	8'	8'	8'
3000 psf		8'	8'	8'	8'	8'	8'
3500 psf		8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size: 24x24
 Perimeter pier pad size: 16x16
 Other pier pad sizes (required by the mfg.): 16x16

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening: 18.5' Pier pad size: 24 x 24

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
 Manufacturer: _____
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer: Oliver Tech

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft ☒

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Sidewall: _____ Number: 18
 Longitudinal: _____
 Marriage wall: 2 min
 Shearwall: 2 min

Mobile Home Permit Worksheet

Application Number: _____ Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb. soil without testing.

x 5 x _____ x _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x _____ x _____ x _____

TORQUE PROBE TEST

The results of the torque probe test is NA/1101V inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

RLK Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Rusty L. Knowles

Date Tested

7/31/25



Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 15C1

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 15C1

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 15C1

Site Preparation

Debris and organic material removed ☒ Pad ☒ Other _____
Water drainage: Natural Swale

Fastening multi wide units

Floor: Type Fastener: Lags Length: 6" Spacing: 20"
Walls: Type Fastener: Screws Length: 4" Spacing: 20"
Roof: Type Fastener: Lags Length: 6" Spacing: 20"
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials RLK

Type gasket Pg. 15C1

Factory

Installed:
Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 15C1
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒



Miscellaneous

Skirting to be installed. Yes ☒ No ☒
Dryer vent installed outside of skirting. Yes ☒ N/A ☒
Range downflow vent installed outside of skirting. Yes ☒ N/A ☒
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Date 7/31/25

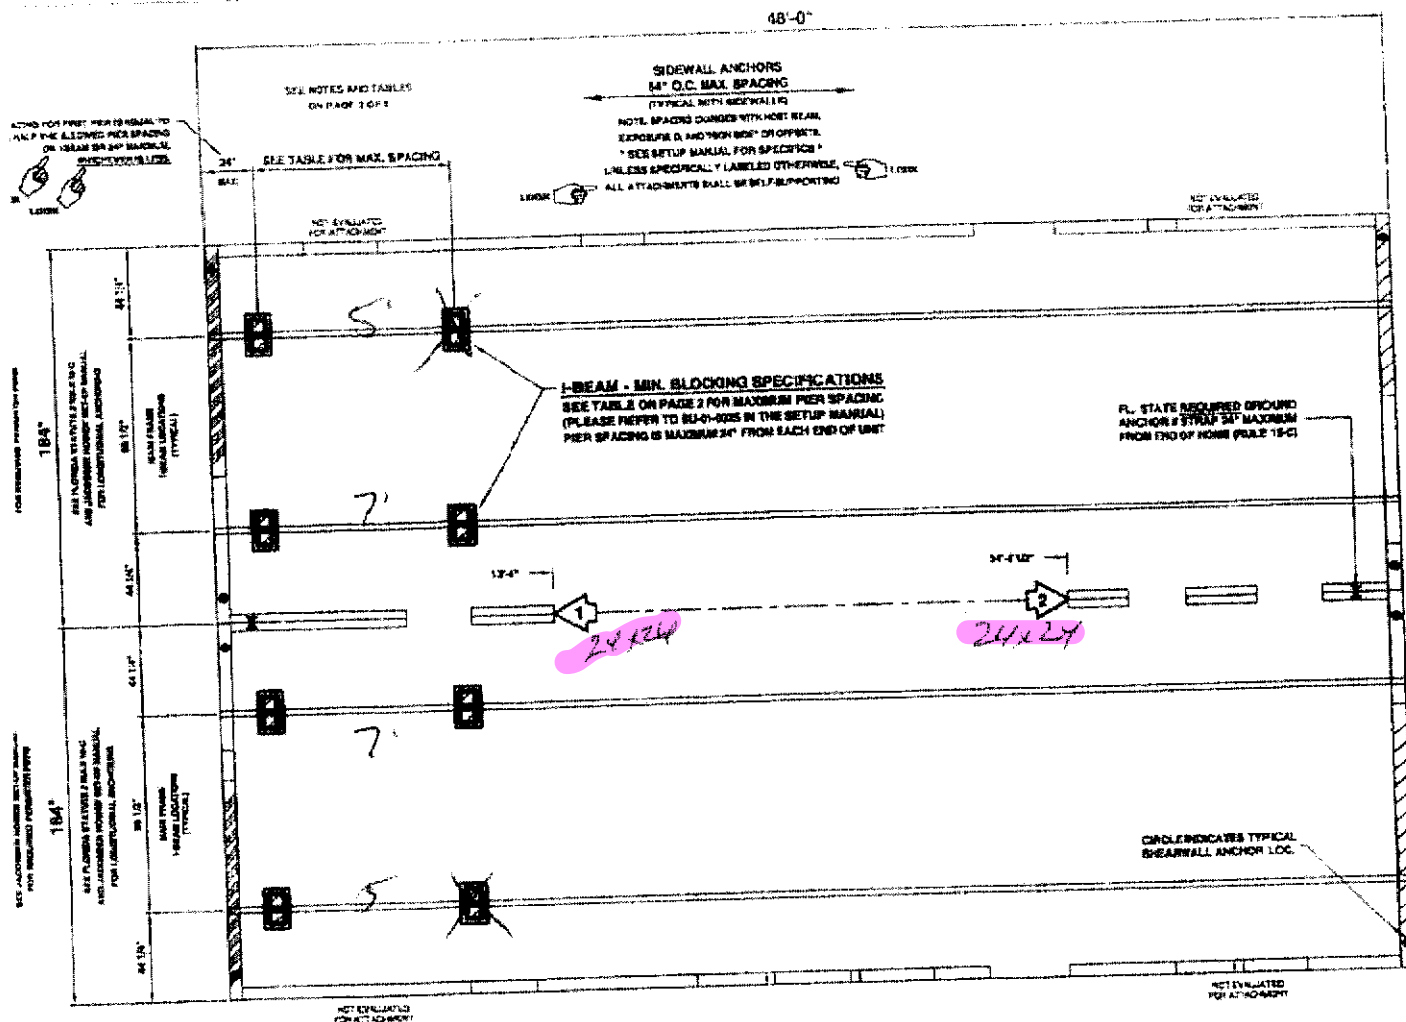


SEE NOTES AND TABLES ON PAGE 2 OF 2

SHEARWALL TIE-DOWN STRAPS ARE NOT INSTALLED AT THE FACTORY. WHEN SHEARWALL IS LOCATED DIRECTLY OVER SOLID I-BEAM HEADERS, SET-UP IS REQUIRED TO INSTALL THE SHEARWALL STRAPS OVER THE I-BEAM HEADERS PER AD-TO-4000 IN THE SET-UP MANUAL. ADDITIONAL STRAPS AND PIER SHALL BE INSTALLED AT BOTH ENDS OF THE BEAMS.



SEE NOTES AND TABLES ON PAGE 1
SEE WARNINGS AND CAUTIONS ON PAGE 2



JACOBSEN HOMES
P.O. BOX 368 // 600 PACKARD CT.
SAFETY HARBOR, FLORIDA 34895

(727) 726-1138
www.jachomes.com

REFER TO SU-01-0020, SU-01-0021, AND/OR OTHER DETAILS IN THE SET-UP MANUAL FOR MAXIMUM HEIGHT
(THIS BLOCKING DIAGRAM IS NOT DESIGNED, NOR IS IT INTENDED, TO BE USED AS A STILT FOUNDATION)

REFER TO SU-01-0005 FOR
ADD'L PIER REQUIREMENTS

REFER TO THE JACOBSEN HOMES SETUP MANUAL AND/OR
ADDENDUM FOR COMPLETE INSTALLATION INSTRUCTIONS

PAGE 1 OF 2

THIS BLOCKING DIAGRAM IS PROVIDED AS A COURTESY ONLY. THE LICENSED SET-UP
CONTRACTOR (INSTALLER) SHALL REVIEW THIS DETAIL AND VERIFY COMPLIANCE. THE
LICENSED INSTALLER IS SOLELY RESPONSIBLE AND/OR LIABLE FOR ALL INSTALLATION

SHEAR
WALLS:
PIERS AND
TIE-DOWNS
REQUIRED
SHEARWALL
CONTRACTOR
VERIFY SET-UP
MANUAL ONLY
PIER OR STRAP
TWO (2) PIER
TWO (2) STRAP
TWO (2) PIER
TWO (2) STRAP

ALL
COLLISION
PIERS AND
TIE-DOWNS
REQUIRED
UNDER 500
COLLISION LOC
TWO (2) PIER
TWO (2) STRAP

IMP - 39119
REPERAL 2
24.0
24.0
11.8 2x8 J
JACOBSEN HOMES
IMP - 44822W - 39119
44822W - 39119
1 19

Order #: 6673	Label #: 121715	Manufacturer:	(Check Size of Home)
Homeowner:	Year Model:	Single	_____
Address:	Length & Width:	Double	_____
		Triple	_____
City/State/Zip:	Type Longitudinal System:	HUD Label #:	
Phone #:	Type Lateral Arm System:	Soil Bearing / PSF:	
Date Installed:	New Home: _____ Used Home: _____	Torque Probe / in-lbs:	
Installed Wind Zone:	Data Plate Wind Zone:	Permit #:	
Note:			

**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

121715

LABEL #	DATE OF INSTALLATION
RUSTY L. KNOWLES	
NAME	
IH / 1038219 / 1	6673
LICENSE #	ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
