
NW IVY GLEN

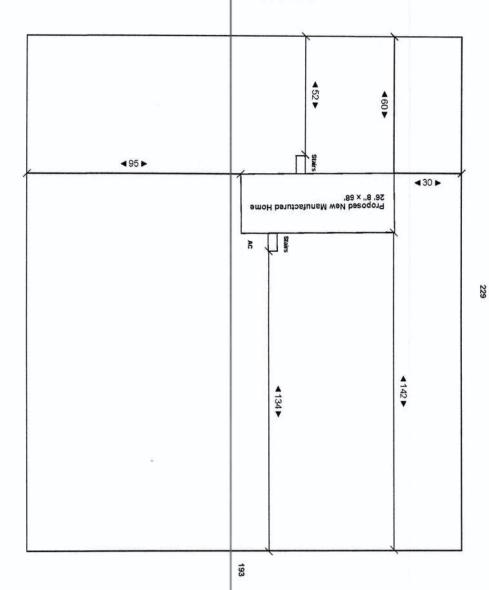

SITE PLAN

OWNER CINERA GROUP LLC

PARCEL 05-3S-17-04843-043


LEGAL (PARTIAL)
Lot 3 Carter Place

4 bedrooms / 2 full bathrooms JOB DESCRIPTION
Installation of a new manufactured home 26' 8" x 68'

FLOOD ZONE
Zone X
CID 120070
Panel #12023C0195D
Published 11/02/2018

FINISHED FLOOR ELEVATION
Finished floor elevation will be 32" above the existing grade

- NOTES
 1. Stairs will be approximately 4' x 8' with a landing at the top and bottom
- 2. AC will be placed on a 4' x 4' pad



	Typical pier spacing Installer's initials ML 2'	Installer: MICHAEL FACUST License # TH/1131539 Address of home TBD NW LVY CIKIN Address of home TBD NW LVY CIKIN Being installed Manufacturer CING MADLE CITY Length x width MOTE: If home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall fles exceed 5 ft 4 in
within 2' of end of home spaced at 5' 4" oc TIEDOWN COMPONENTS Longitudinal Stabilizing Device (LSD) Manufacturer Olyver 1001 V SyStem Sidewall Longitudinal Stabilizing Device w/ Lateral Arms Marriage wall Manufacturer Olyver 1001 V SyStem Shearwall Manufacturer Olyver 1001 V SyStem Shearwall	Load Footer 16" x 16" 18 1/2" x 18 20" x 20" 22" x 24" x 24" 26" x 26" 26" (576) 100" 25" x 26" 26" (576) 100" 25" x 26" 25" 2	e/Q ble le iii

Mobile Home Permit Worksheet

Application Numb
7
Date:

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to or check here to declare 1000 lb. soil withou without testing 1500

x 1500

1500

X)760

POCKET PENETROMETER TESTING METHOD

- Test the perimeter of the home at 6 locations
- 2 Take the reading at the depth of the footer.
- Using 500 lb. increments, take the lowest reading and round down to that increment

x)700

x 1500

x 1500

TORQUE PROBE TEST

showing 275 inch pounds or less will require 5 foot anchors here if you are declaring 5' anchors without testing The results of the torque probe test is 285 inch pounds or check

Note: A state approved lateral arm system is being used and 4 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may anchors are allowed at the sidewall locations. I understand 5 ft requires anchors with 4000 lb holding capacity Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Michael tornes

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between mult-wide units. Pg.

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 5

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 50

Site Preparation

Debris and organic material removed Water drainage: Natural Swale

Pad Other

Fastening multi wide units

Floor. Roof Walls Type Fastener: w) & 1 Length: 3"4 Spacing: 32"

Type Fastener: 1 & 5 Length: 6" Spacing: 26"

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline Type Fastener. vail Length: 11.5 Spacing: 2001

Gasket (weatherproofing requirement)

of tape will not serve as a gasket a result of a poorly installed or no gasket being installed. I understand a strip homes and that condensation, mold, meldew and buckled marriage walls are I understand a properly installed gasket is a requirement of all new and used

Installer's initials

Type gasket 200 KJOHJA 100

Between Walls Yes Between Floors Bottom of ridgebeam nstalled Yes

Weatherproofing

Siding on units is installed to manufacturer's specifications. Yes Fireplace chimney installed so as not to allow intrusion of rain water. The bottomboard will be repaired and/or taped. Yes Yes

Miscellaneous


Range downflow vent installed outside of skirting. Yes Skirting to be installed. Yes Other: Electrical crossovers protected. Yes Drain lines supported at 4 foot intervals. Dryer vent installed outside of skirting. Yes S NA


N/A

Installer verifies all information given with this permit worksheet manufacturer's installation instructions and or Rule 15C-1 & 2 is accurate and true based on the

Installer Signature

Dereil Date /2/2424

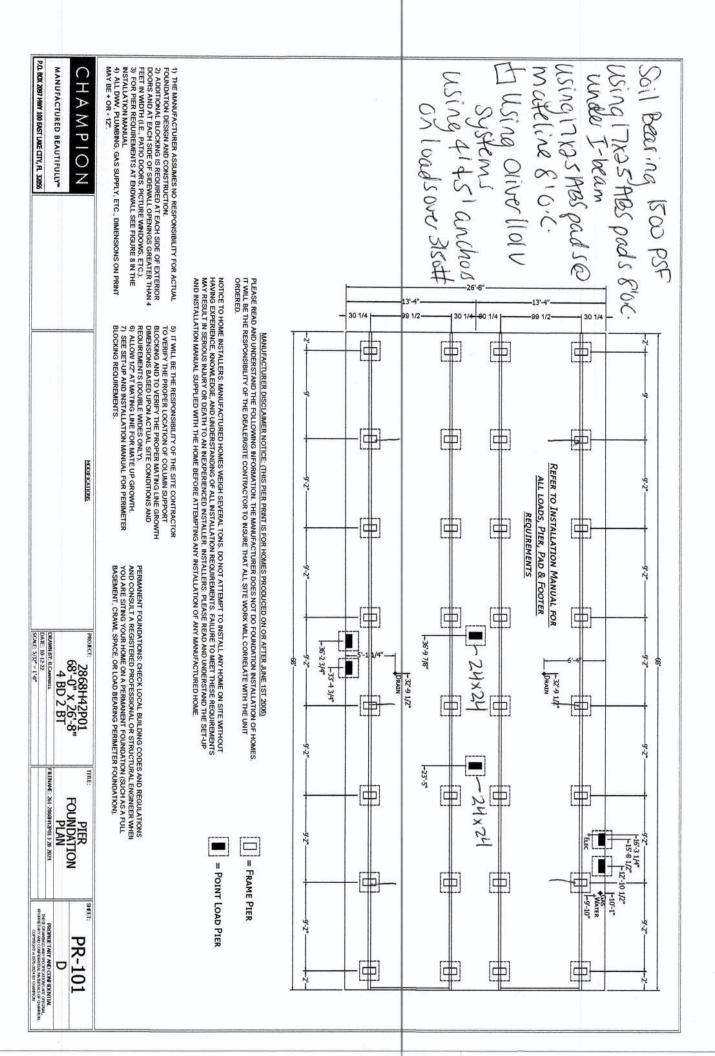

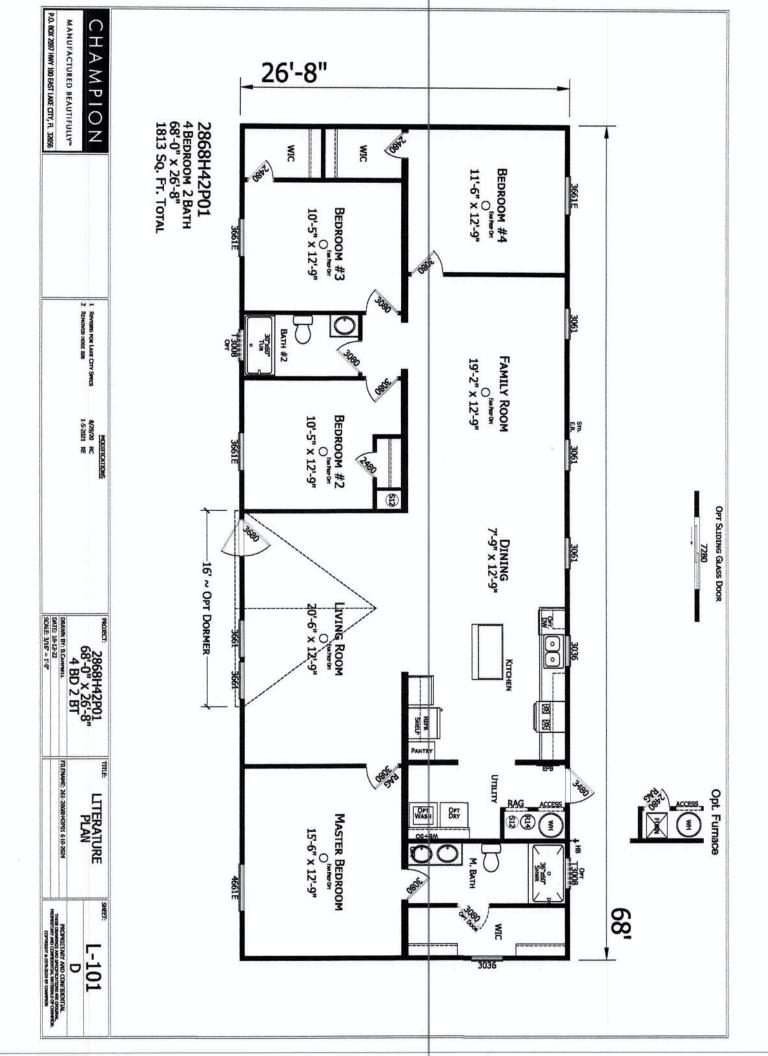

icense Number: IH / 1121:	539/1 Name, Mich	AEL J EARNES I	
Order #: 6476	Label #: 116954	Manufacturer:	(Check Size of Home)
Cinh e	ra Group	Year Model:	Single
Address:		Length & Width:	Double
City/State/Zip:		Type Longitudinal System:	HUD Label #:
Phone #:		Type Lateral Arm System:	Soil Bearing / PSF:
Date Installed:		New Home: Used Home:	Torque Probe / in-lbs:
Installed Wind Zone:		Data Plate Wind Zone:	Permit #:
Note:			

STATE OF FLORIDA INSTALLATION CERTIFICATION LABEL

116954

LABEL#

DATE OF INSTALLATION

MICHAEL J EARNEST

NAME

IH / 1121539 / 1

6476

LICENSE # ORDER #
CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF INSTALLATION AND AFFIX LABEL NEXT TO HUD LABEL. USE PERMANENT INK PEN OR MARKER ONLY. COMPLETE INFORMATION ABOVE AND KEEP ON FILE FOR A MINIMUM OF 2 YEARS. YOU ARE REQUIRED TO PROVIDE COPIES WHEN REQUESTED.
