

Freedom Homes
 Lot 9
 Estates
 Brandon

Cottage Plus U-3463B

page 1 of 2

These worksheets must be completed and signed by the installer.
 Submit the originals with the packet.

Installer **DAVID ALBRIGHT**

License # **IH/ 1129420**

614 Address where home is being installed **192 NW Whitney Glen Lake City FL**

Manufacturer

LIVE OAK HOMES

Length x width

32 x 46 / 50

NOTE:

If home is a single wide fill out one half of the blocking plan
 If home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials

[Signature]

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	19' x 16" (286)	18' 1/2" x 18' (342)	20' x 23" (460)	22' x 22" (484)	24' x 24" (576)	26' x 26" (676)
1500 DSI	4'	4'	5'	5'	7'	8'
2000 DSI	6'	6'	7'	7'	8'	8'
2500 DSI	7'	7'	8'	8'	8'	8'
3000 DSI	8'	8'	8'	8'	8'	8'
3500 DSI	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 150-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size **17 x 25**
 Perimeter pier pad size **16 x 16**
 Other pier pad sizes **23 x 31 PLATE LIDE**
 (required by the mfg.)

POPULAR PAD SIZES

Pad Size	Sq. ft.
16 x 16	256
18 x 18	324
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Operating FACTORY DIAGRAM


Pier pad size **17 x 25**
9' **17 x 25**

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) OTI
 Manufacturer
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer

OTHER TIES

Number **3**
 Longitudinal Marriage Wall Shearwall **5-5.5-4'**
2

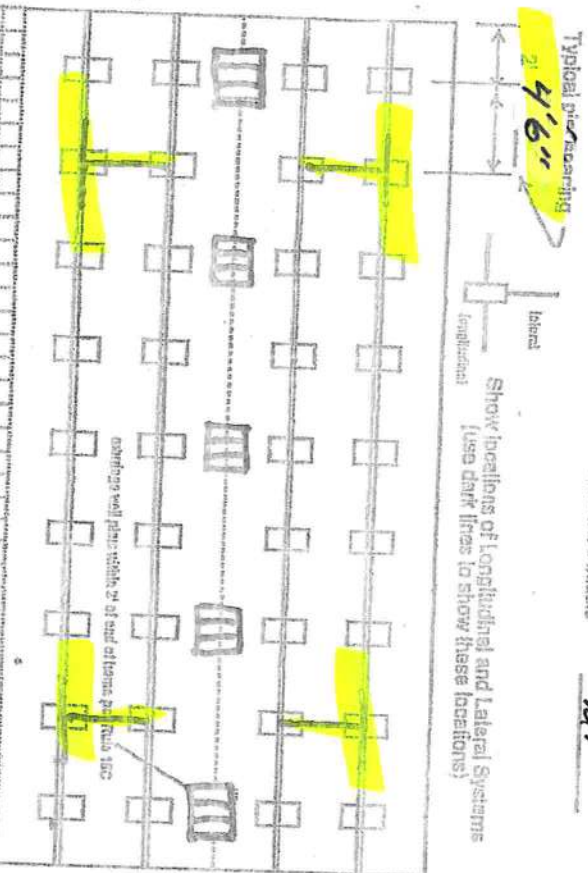

[Signature]
 2-4-22



Mobile Home Permit Worksheet

Application Number: _____

Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. cpi. ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test are _____ inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer requires anchors with 4000 lb. holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name **DAVID ALBRIGHT MOBILE HOME SVC**

Date Tested _____

Electrical

Connect electrical conductions between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 73-77

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 79-80

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 76-110

Site Preparation

Debris and organic material removed ☒ Weather drainage: Natural ☐ Swale ☐ Pad ☒ Other _____

Fastening multi wide units

Floor: Type Fastener: LAGS Length: 6" Spacing: 2' Walls: Type Fastener: SCREWS Length: 3" Spacing: 18" Roof: Type Fastener: LAGS Length: 6" Spacing: 2'

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

(Gasket (weatherproofing requirement))

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials *DAV*

Type gasket **FACTORY** Pg. 41

Installed: Between Floors Yes ☒ Between Walls Yes ☒ Bottom of ridgebeam Yes ☒ END WALLS

Weatherproofing


Skirting to be installed. Yes ☐ No ☒ Skirting installed outside of skirting. Yes ☐ No ☒ N/A ☒ Drain lines supported at 4 foot intervals. Yes ☒ No ☐ N/A ☒ Electrical crossovers protected. Yes ☒ No ☐ Other: _____ Miscellaneous

Sideboard will be repaired and/or taped. Yes ☒ Pg. 124 Sideboard units is installed to manufacturer's specifications. Yes ☒ No ☐ Chimney installed so as not to allow intrusion of rain water. Yes ☒ No ☐ Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature *David Albright* Date _____

COTTAGE PLUS

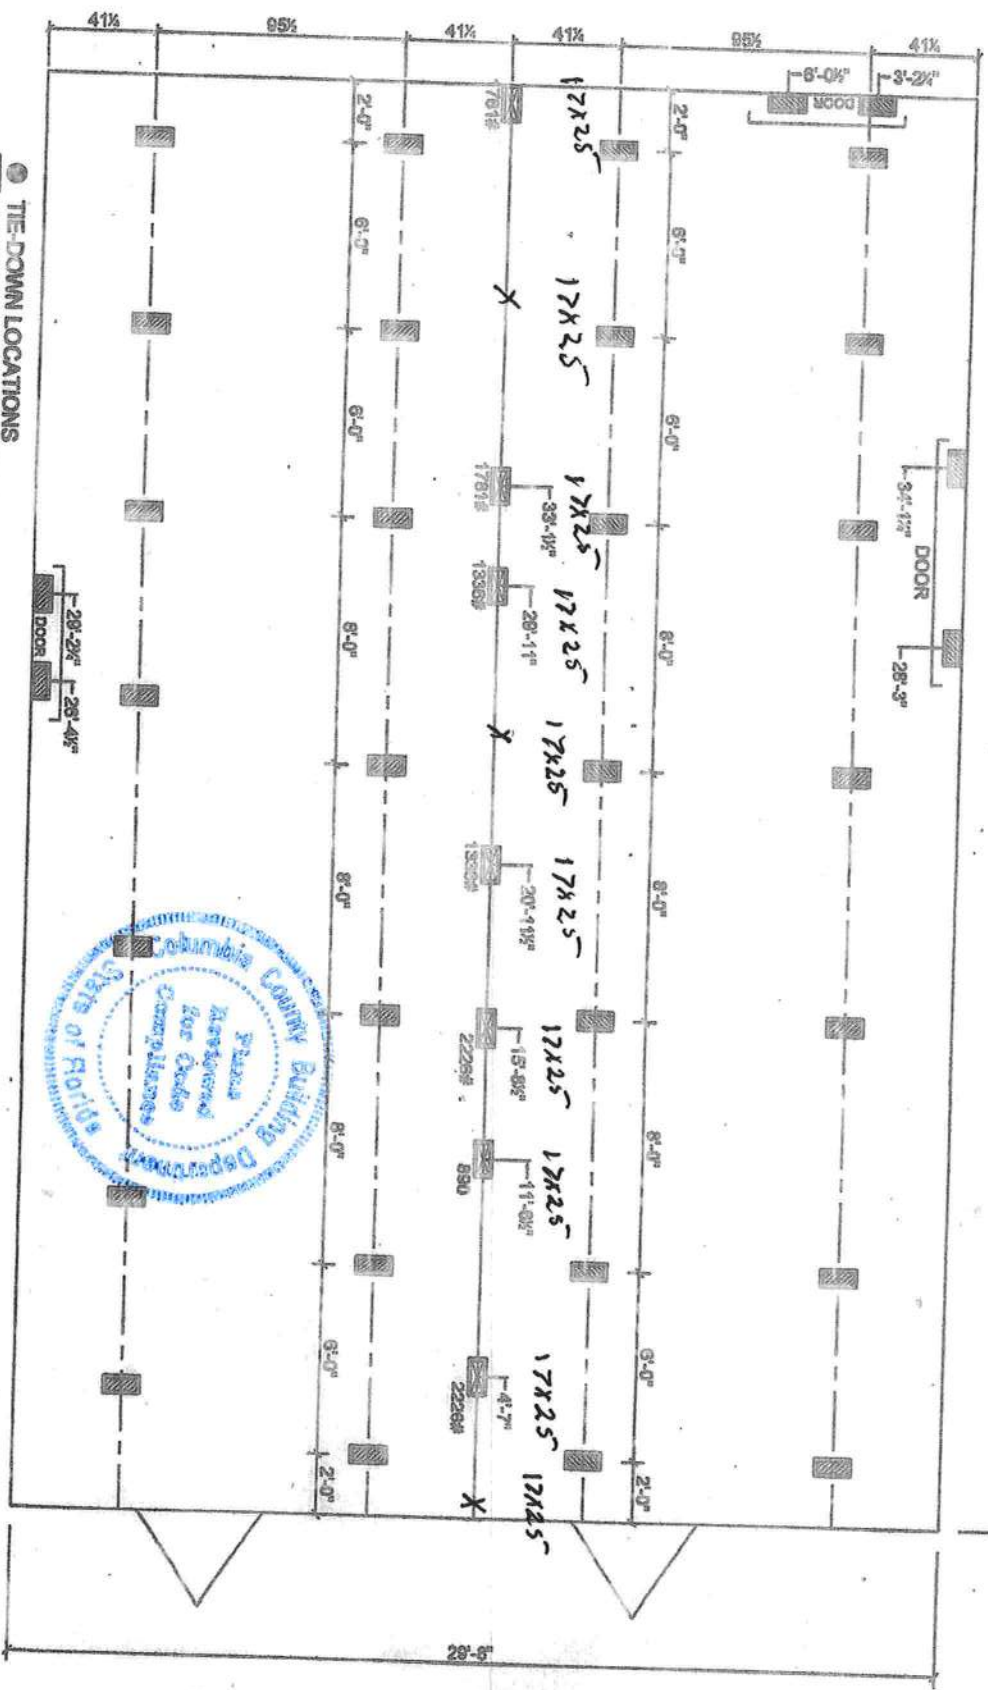

● TIE-DOWN LOCATIONS
 ■ MARRIAGE LINE OPENING SUPPORT PIER/TYP.
 ■ SUPPORT PIER/TYP

2-9-2012

FOUNDATION NOTES:
 - THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
 - FOOTINGS ARE SHOWN FOR EXAMPLE ONLY. QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
 - FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.


U-3463B-SELECT
3-BEDROOM / 2-BATH
32 X 46 - APPROX. 1364 Sq. Ft.
 Date: 6-12-2017

* All room dimensions include closets and square footage figures are approximate.
 * Windows are available in optional 8'-0" or 10'-0" widths only.
 * Available with Linoleum or Shingles around windows.

- (A) MAIN ELECTRICAL
- (B) ELECTRICAL CROSSOVER
- (C) WATER INLET
- (D) WATER/SSEWER ENTRY (ANY)
- (E) GAS INLET (IF ANY)
- (F)
- (G) DUCT CROSSOVER
- (H) SEWER DROPS
- (I) RETURN AIR (W/OPT. HEAT PUMP ON DUCT)
- (J) SUPPLY AIR (W/OPT. HEAT PUMP ON DUCT)

COTTAGE PLUS

COTTAGE PLUS

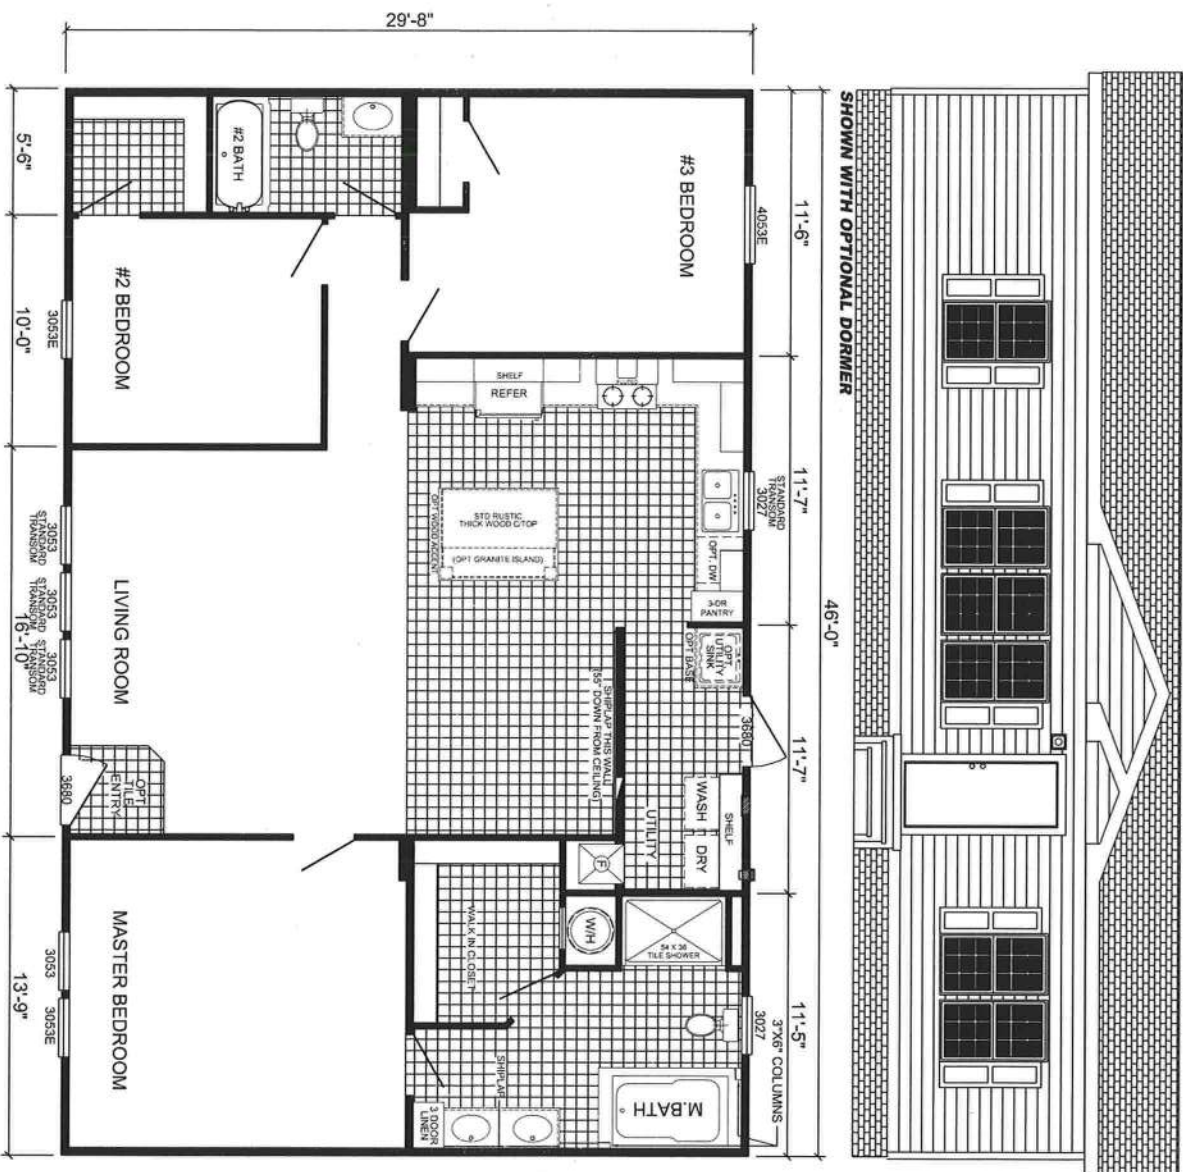

U-3463B-OAK
3-BEDROOM / 2-BATH
32 X 46 - Approx. 1364 Sq. Ft.

Date: 06/11/20

* All room dimensions include closets and square footage figures are approximate.
 * Transom windows are available on optional 9'-0" side wall houses only.
 * Live Oak Homes reserves the right to modify product offering at any time.

Lot #9

Set #
 LOH6A30072642AB



AKS
Signature Series

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT			
Order #: 5175	Label #: 85933	Manufacturer: LIVE OAK	(Check Size of Home)
Homeowner: LOT #9 BRANDAN EST	Year Model: 2022	Single	_____
Address: 192 NW WHITNEY CIRCLE	Length & Width: 46/50 x 32	Double X	_____
City/State/Zip: LAKE CITY FL 32024	Type Longitudinal System: 6 OTI	Triple	_____
Phone #:	Type Lateral Arm System: 6 OTI	HUD Label #:	_____
Date Installed:	New Home: X Used Home: _____	Soil Bearing / PSF:	_____
Installed Wind Zone: II	Data Plate Wind Zone: II	Torque Probe / in-lbs:	_____
Permit #:			
Note:			

**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

85933

LABEL #	DATE OF INSTALLATION
DAVID E ALBRIGHT	

NAME

IH / 1129420 / 1

5175

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
