

Sweet

PERMIT WORKSHEET

page 1 of 2

PERMIT NUMBER

Installer Stephen Weeks License # HT/1025306

Owner Name & Address of home being installed 5614 SW Ichetucknee Ave
Port White FL 32038

Manufacturer Clayton Length x width 28x48

NOTE: If home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home


I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials SW

Typical pier spacing



Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

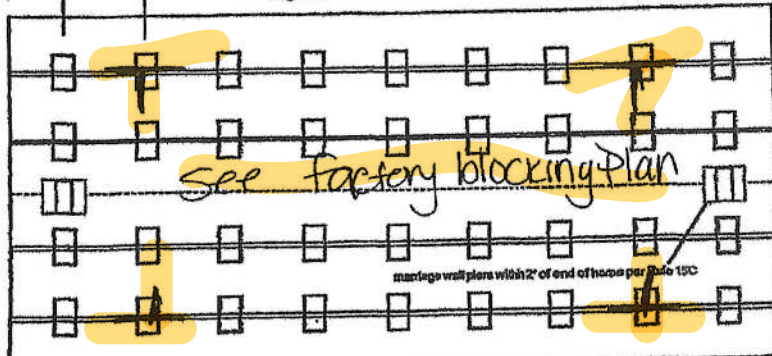

Anthony Nolan

05-19-2023

PERMIT WORKSHEET

New Home ☒ Used Home ☐ Year Model
Home installed to the Manufacturer's Installation Manual ☒
Home is installed in accordance with Rule 15-C ☐
Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
Double wide ☒ Installation Detail # 74430
Triple/Quad ☐ Serial # DES290ga23-13107ab

PIER SPACING TABLE FOR USED HOMES

PIER SPACING TABLE FOR CONCRETE							
Load bearing capacity	Footer size (sq in)	16' x 16' (256)	18 1/2' x 18 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'	
1500 psf	4' 6"	5'	6'	7'	8'	9'	
2000 psf	6'	6'	7'	8'	9'	10'	
2500 psf	7' 6"	8'	8'	9'	10'	11'	
3000 psf	8'	8'	9'	10'	11'	12'	
3500 psf	8'	8'	9'	10'	11'	12'	

* Interpolated from Rule 16C-1 pier spacing table

PIER PAD SIZES

I-beam pier pad size 23x31
Perimeter pier pad size 17.5x25.5

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening See Pier pad size Factory

blocking plan

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer Oliver 1101V
Longitudinal Stabilizing Device w/ lateral Arms
Manufacturer

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 28 1/4	348
20 x 20	400
17 1/2 x 22 1/2	432
17 3/16 x 25 3/16	441
24 x 24	576
28 x 26	676

ANCHORS

4 ft ☒ 5 ft ☒

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Number 24
Sidewall 2
Longitudinal 2
Marriage wall 5
Shearwall 2

page 2 of 2

PERMIT NUMBER _____

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf
or check here to declare 1000 lb. soil without testing.

x1000

x1000

x1000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x1000

x1000

x1000

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. (Understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 _____ capacity.

Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Stephen Weeks
Assumed over 1101V
Uses 4x5 Anchors

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg.

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg.

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg.

Site Preparation

Debris and organic material removed _____
Water drainage: Natural Swale Pad Other

Fastening multi wide units

Floor:	Type Fastener:	1995	Length:	3	Spacing:	20
Walls:	Type Fastener:	1995	Length:	6	Spacing:	20
Roof:	Type Fastener:	1995	Length:	7	Spacing:	20

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials

SW

Type gasket
Pg. R11

Installed:

Between Floors	Yes	✓
Between Walls	Yes	✓
Bottom of ridgebeam	Yes	✓

Weatherproofing

The bottomboard will be repaired and/or replaced. Yes ☒ Pg.
Siding on units to be installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous

Skirting to be installed. Yes ☒ No ☐
Dryer vent installed outside of skirting. Yes ☒ N/A ☐
Range downflow vent installed outside of skirting. Yes ☒ N/A ☐
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other:

Installer verifies all information given with this permit worksheet is accurate and true based on the



Installer Signature

Stephen Weeks 11/15/13

All information on this worksheet must be filled out completely to be accepted.

Jazz backup


SOIL BEARING LOAD 1000LBS
1500LBS=16"x16" ABS FOOTER
1778LBS=16"x16" ABS FOOTER
3000LBS=17.5"x25.5" ABS FOOTER
4800LBS=23.25"x31.25" ABS FOOTER

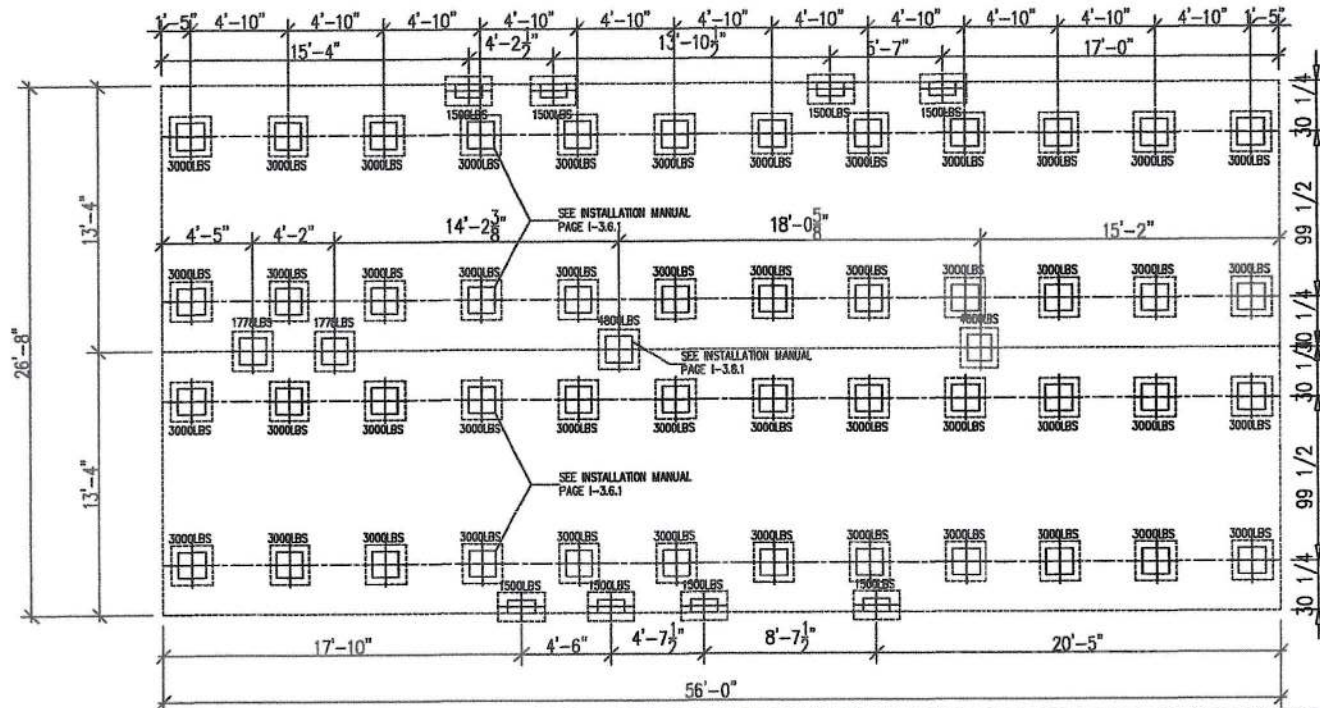

MAXIMUM SPAN BETWEEN PIERS UNDER I-BEAMS (FEET)							MAXIMUM CLEAR SPAN FOR MATING LINE SUPPORTS (FEET)							OVAL PAD SIZES				MAX. LOAD FOR SOIL CAPACITY			
PAD SIZE	PAD AREA (SQ. FT.)	BOX WIDTH (IN.)					PAD SIZE	PAD AREA (SQ. FT.)	BOX WIDTH (IN.)					16" X 18.5"	17.5" X 25.5"	21" X 29"	23.25" X 31.25"	1000 PSF	1500 PSF	2000 PSF	2000 PSF
		SINGLE	WIDE	DOUBLE	WIDE	180			SINGLE	WIDE	DOUBLE	WIDE	180								
16" X 18.5"	2.00	3.30	2.97	3.37	3.05	180	16" X 18.5"	2.00	N/A	N/A	11.43	10.00	8.89	2,000	3,000	4,000	4,000				
17.5" X 25.5"	3.00	4.95	4.45	5.66	4.58	180	17.5" X 25.5"	3.00	N/A	N/A	17.14	15.00	13.33	3,000	4,500	6,000	6,000				
21" X 29"	4.00	6.61	5.93	7.54	6.75	180	21" X 29"	4.00	N/A	N/A	22.86	20.00	17.78	4,000	6,000	8,000	8,000				
23.25" X 31.25"	4.80	7.93	7.12	9.05	8.09	180	23.25" X 31.25"	4.80	N/A	N/A	27.43	24.00	21.33	4,800	7,200	9,388	9,388				
16" X 16"	1.78	2.94	2.64	3.35	3.00	2.71	16" X 16"	1.78	N/A	N/A	10.16	8.89	7.90	1,778	2,667	3,556	3,556				
13" X 16"	2.35	3.88	3.48	4.42	3.96	3.58	13" X 16"	2.35	N/A	N/A	13.41	11.74	10.43	2,347	3,521	4,694	4,694				
18.5" X 18.5"	2.38	3.93	3.53	4.48	4.01	3.63	18.5" X 18.5"	2.38	N/A	N/A	13.58	11.89	10.56	2,377	3,565	4,753	4,753				
20" X 20"	2.78	4.59	4.12	5.24	4.68	4.24	20" X 20"	2.78	N/A	N/A	15.87	13.89	12.36	2,778	4,167	5,556	5,556				
24" X 24"	4.00	6.61	5.93	7.54	6.75	6.10	24" X 24"	4.00	N/A	N/A	22.86	20.00	17.78	4,000	6,000	8,000	8,000				

THIS LETTER SHALL CERTIFY THAT ABS FOUNDATION PADS MANUFACTURED BY OLIVER TECHNOLOGIES, INC. MAY BE USED IN THE LIEU OF POURED CONCRETE FOOTINGS AS A SUPPORT FOR SINGLE & DOUBLE STACKED FOUNDATION PIERS PROVIDED THE FOLLOWING CRITERIA ARE MET:

1. THE ABS PADS MUST BE INSTALLED PER OLIVER TECHNOLOGIES INSTALLATION INSTRUCTIONS.
2. THE PIER LOADS APPLIED TO THE ABS PADS MAY NOT EXCEED THE VALUES NOTED IN THE CHART BELOW.
3. THE ABS PADS MAY BE USED TO SUPPORT A CONTINUOUS FOUNDATION WALL. THE PADS MAY ONLY BE USED FOR INDIVIDUAL FOUNDATION PIERS.
4. ABS PADS MAY BE COMBINED TO COVER A LARGER AREA. IN THIS CASE THE MAX. ALLOWABLE LOADS MAYBE COMBINED AS WELL.
5. IF THE REQUIREMENTS OF DESTINY IND. INSTALLATION MANUAL CONFLICT WITH THE REQUIREMENTS OF THE OLIVER TECHNOLOGIES INSTALLATIONS THE MORE STRINGENT REG. SHALL BE USED.



REVISIONS

DRAWING TITLE: **1000LBS ABSPAD FOUNDATION PLAN**

DRAWING FILE INFORMATION: 28X60 3BR-2B

DRAWN BY: JEREMY RIVERS

PRODUCT	TIMBERLINE	MODEL NO.	DISH11677 290TE28563F
DATE:	7/14/2022	SQ. FT.	1493
SHEET	1-C17	REVISED	-

[illegible]

MODEL: 290TE28563F 3 BR. ~ 2 BA.
28'-0" X 56'-0" ~ 1493 SQ. FT.
