

COLUMBIA COUNTY PERMIT WORKSHEET

These worksheets must be completed and signed by the installer.
Submit the original with the packet.


Installer Debbie Lucas License # EH1025316

911 Address where home is being installed 812 SW LITTLE ROAD
LAKE CITY, FL 32024

Manufacturer SKYLINE Length x width 32x64

NOTE: If frame is a single wide fill out one half of the blocking plan
If frame is a triple or quad write sketch in remainder of home
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Installer's initials DL

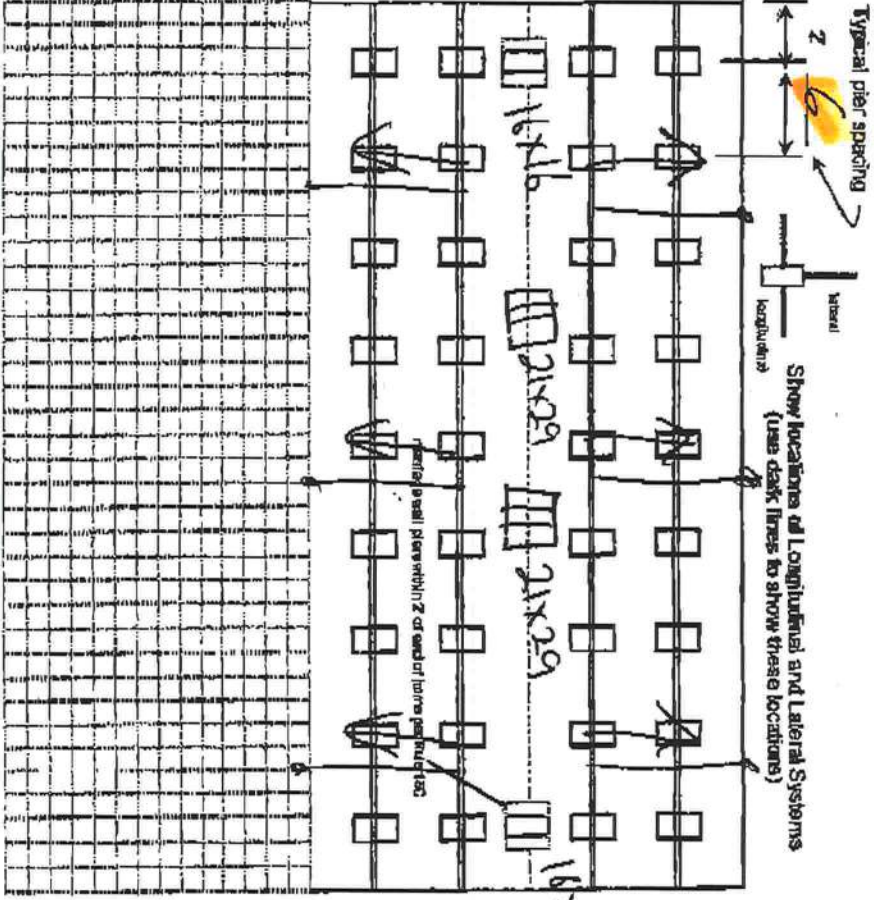

New Home ☒ Used Home ☐
Home installed to the Manufacturer's Installation Manual ☒
Home is installed in accordance with Rule 15-C ☐
Single wide ☐ Wind Zone II ☒
Double wide ☒ Installation Detail # 9117
Triple/Quad ☐ Serial # 0235
(713)

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	Footprint size (2500)	18' 1/2" x 18' (342)	18' 1/2" x 18' (408)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 sq ft	3'	4'	5'	6'	7'	8'	9'
1500 sq ft	4'	5'	6'	7'	8'	9'	10'
2000 sq ft	5'	6'	7'	8'	9'	10'	11'
2500 sq ft	6'	7'	8'	9'	10'	11'	12'
3000 sq ft	7'	8'	9'	10'	11'	12'	13'
3500 sq ft	8'	9'	10'	11'	12'	13'	14'

Interpolated from Rule 15-C-1 pier spacing table.

PIER PAD SIZES

Leaner pier pad size 23x31

Perimeter pier pad size 16x16 Doors

Other pier pad sizes (required by the mfg.) 21x29

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening 15' Pier pad size 21x29

POPULAR PAD SIZES

Pad Size	Sq ft
16 x 16	256
18 x 18	324
20 x 20	400
22 x 22	484
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc ☒

OTHER TIES

Longitudinal Stabilizing Device (LSD) Manufacturer Glenn 11010

Side Wall Longitudinal Marriage wall Shearwall Manufacturer Glenn 11010

Installation Instructions for ABS Pads

For use on all Mobile and Manufactured Homes, including HUD approved Homes and Modular Housing

Patents 5505500 and other patents pending

GENERAL INSTRUCTIONS:

1. All pads are to be installed flat side down, ribbed side up.
2. The ground under the pads should be leveled as smooth as possible with all vegetation removed. Pads to be placed on fully compacted or undisturbed soil, or on below the frost line, or per local jurisdiction.
3. Prior to pad spacing will be determined by the manufacturer's written set-up instructions or any local or state codes.
4. The open cells between the ribs on the upper side of the pads may be filled with soil or sand after installation to prevent any accumulation of stagnant water in the pads.
5. A pocket penetrometer may be used to determine the actual soil bearing value. If soil-testing equipment is not available, use an assumed soil value of 1000 lbs. / square foot.
6. All pad sizes shown are nominal dimensions and may vary up to 1/8".
7. The maximum deflection in a single pad is 5/8" measured from the highest point to the lowest point of the top face. (NOTE: Actual test results were less than 5/8")
8. In frost areas, a 6" deep confined gravel has installed in well drained, non-frost susceptible soil is recommended.
9. Pad loads are the same when using single track or double track blocks.
10. The maximum load at any intermediate soil value may be determined as the average of the next lower and next higher soil value given in the table below.
11. Any configuration (see reverse side) may be used to replace a bearing manufacturer's recommended concrete or wood base pad.
12. If the home manufacturer shows soil densities greater than 3000 lb. when using ABS pads, do not exceed 3000 lb. pad plus spacing per set up manual.

Pad Size		ID No.		Pad Area		1000 PSF Soil		2000 PSF Soil		3000 PSF Soil	
OVAL 16" x 18.5"	1055-23	288 sq. in.	2000 lbs.	4000 lbs.	6000 lbs.	4000 lbs.	6000 lbs.	4000 lbs.	6000 lbs.	4000 lbs.	6000 lbs.
OVAL 17" x 22"	1055-16	360 sq. in.	2500 lbs.	4000 lbs.	6000 lbs.	2500 lbs.	4000 lbs.	3000 lbs.	4500 lbs.	5000 lbs.	7500 lbs.
OVAL 17.5" x 22.5"	1055-21	384 sq. in.	2667 lbs.	4000 lbs.	6000 lbs.	3334 lbs.	5000 lbs.	3334 lbs.	5000 lbs.	3334 lbs.	5000 lbs.
OVAL 17.5" x 25.5"	1055-17	432 sq. in.	3000 lbs.	4000 lbs.	6000 lbs.	3000 lbs.	4000 lbs.	3000 lbs.	4000 lbs.	3000 lbs.	4000 lbs.
OVAL 21" x 29"	1055-22	576 sq. in.	4000 lbs.	4000 lbs.	6000 lbs.	4000 lbs.	6000 lbs.	4000 lbs.	6000 lbs.	4000 lbs.	6000 lbs.
OVAL 23.25" x 31.25"	1035-20	675 sq. in.	4694 lbs.	4000 lbs.	6000 lbs.	4694 lbs.	6000 lbs.	4694 lbs.	6000 lbs.	4694 lbs.	6000 lbs.
Pad Size		ID No.		Pad Area		1000 PSF Soil		2000 PSF Soil		3000 PSF Soil	
16" x 16"	1055-14	256 sq. in.	1780 lbs.	3560 lbs.	5333 lbs.	1780 lbs.	3560 lbs.	1780 lbs.	3560 lbs.	1780 lbs.	3560 lbs.
18.5" x 18.5"	1055-9	342 sq. in.	2375 lbs.	4750 lbs.	7100 lbs.	2375 lbs.	4750 lbs.	2375 lbs.	4750 lbs.	2375 lbs.	4750 lbs.
20" x 20"	1055-7	400 sq. in.	2790 lbs.	5580 lbs.	8250 lbs.	2790 lbs.	5580 lbs.	2790 lbs.	5580 lbs.	2790 lbs.	5580 lbs.
24" x 24"	1055-13	576 sq. in.	4000 lbs.	8000 lbs.	12000 lbs.	4000 lbs.	8000 lbs.	4000 lbs.	8000 lbs.	4000 lbs.	8000 lbs.


* Concrete blocks are required to be double blocked.

13. ALABAMA ONLY: The 16" x 16" ID# 1055-14, 16" x 18.5" ID# 1055-23, 17" x 22" ID# 1055-16, 17.5" x 22.5" ID# 1055-21, 17.5" x 25.5" ID# 1055-17 are the only pads approved in the state of Alabama, and must not have more than 5/8" deflection.
14. TEXAS ONLY: 17.5" x 22.5" ID# 1055-21 and 23.25" x 31.25" ID# 1055-20 may not be installed in the state of Texas.
15. Steel Pads: All pads are tested with steel plates on 1000 PSF soil density unless otherwise noted (#15).
16. Available pads tested on 2000 PSF soil density are: ID# 1055-14, 1055-16, 1055-17, 1055-21, 1055-22, 1055-23, 1055-24.

Example: 16" x 80" section

1000 Lb Paf 2000 Lb Paf

16" x 16" Pad	29"	5' 6"
16" x 18.5" Oval Pad	3' 0"	6' 0"
17" x 22" Oval Pad	3' 9"	7' 6"
17.5" x 22.5" Oval Pad	4' 0"	8' 0"
17.5" x 25.5" Oval Pad	4' 5"	8' 0"
21" x 29" Oval Pad	6' 0"	8' 0"



COLUMBIA COUNTY PERMIT WORKSHEET

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psi or check here to declare 1000 lb. soil ☒ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 8 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing _____ A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewalk locations. I understand 5 ft. anchors are required at all perimeters the points where the torque test readings is 275 or less and where the mobile home manufacturer may require anchors with 4000 to breaking capacity.

Installer's initials _____

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Debbie Cees

Date Tested

11-29-11

Electrical

Connect electrical conductors between multi-wire units, but not to the main power source. This includes the bonding wire between multi-wire units. Pg. 28

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 39

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 39

Site Preparation

Debris and organic material removed ☒ Skids ☒ Pad ☒ Other _____

Water drainage: Natural _____ Swale _____

Fastening multi wire nails

Floor: Type Fastener: 3/8x5 Length: 16g Spacing: 16"
Walls: Type Fastener: 3/8x4 Length: 16x4 Spacing: 16"
Roof: Type Fastener: 3/8x5 Length: 16g Spacing: 16"
For used homes a min. 30 gauge, 6" wide galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherstripping installation)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials DC

Type gasket foam

Installed: Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Pg. 13

Weatherproofing

The bottomboard will be repeated and/or taped. Yes ☒ Pg. 13
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Electronics

Skirting to be installed. Yes ☒ No ☒
Dryer vent installed outside of skirting. Yes ☒ N/A ☒
Range downflow vent installed outside of skirting. Yes ☒ N/A ☒
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature Debbie Cees

Date 11-29-11


11/29/2011 16:16 FAX

07/18/2011 11:06 3957582160

FLORIDA MOBILE MASTERS BUILDING AND ZONING

PAGE 04/11 002/010

OLIVER TECHNOLOGIES, INC.
FLORIDA INSTALLATION INSTRUCTIONS FOR THE
MODEL 1101 "V" SERIES ALL STEEL FOUNDATION SYSTEM
MODEL 1101 "V" (STEPS 1-10)
LONGITUDINAL ONLY: FOLLOW STEPS 1-9
FOR ADDING LATERAL ARM: FOLLOW STEPS 10-15
FOR CONCRETE APPLICATIONS: FOLLOW STEPS 16-19
ENGINEERS STAMP



INSTALLATION OF GROUND PAN

1. SPECIAL CIRCUMSTANCES: If the following conditions occur - STOP! Contact Oliver Technologies at 800-284-7437.
- a) Pier height exceeds 48' b) Length of home exceeds 76' c) Roof eaves exceed 16' d) Sidewall height exceeds 8'
 - e) Location is within 1500 feet of coast
2. Remove weeds and debris in an approximate two foot square to expose firm soil for each ground pan (C).
- SPECIAL NOTE:** The longitudinal "V" brace system serves as a pier under the home and should be loaded as any other pier. It is recommended that after leveling pier, and one-third inch (1/3") before home is lowered completely on to pier, complete steps 4 through 9 below then remove jacks.

INSTALLATION OF LONGITUDINAL "V" BRACE SYSTEM

NOTE: WHEN INSTALLING THE LONGITUDINAL SYSTEM ONLY, A MINIMUM OF 2 SYSTEMS PER FLOOR SECTION IS REQUIRED. SOIL TEST PROBE SHOULD BE USED TO DETERMINE CORRECT TYPE OF ANCHOR PER SOIL CLASSIFICATION. IF PROBE TEST READINGS ARE BETWEEN 176 & 275 A 5 FOOT ANCHOR MUST BE USED. IF PROBE TEST READINGS ARE BETWEEN 276 & 350 A 4 FOOT ANCHOR MAY BE USED. USE GROUND ANCHORS WITH DIAGONAL TIES AND STABILIZER PLATES EVERY 5'4". VERTICAL TIES ARE ALSO REQUIRED ON HOMES SUPPLIED WITH VERTICAL TIE CONNECTION POINTS (PER FLORIDA REG.).

4. Select the correct square tube brace (E) length for set - up (pier) height at support location. (The 18" tube is always used as the bottom part of the longitudinal arm). Note: Either tube can be used by itself, cut and drilled to length as long as a 40 to 45 degree angle is maintained.

PIER HEIGHT (Approx. 45 degrees Max.)
1.25' ADJUSTABLE Tube Length
1.50' ADJUSTABLE Tube Length

24 3/4" to 32 1/4"	32"	18"
32" to 40"	44"	18"
40" to 48"	54"	18"

5. Install (2) of the 1.50" square tubes (E) (18" tube) into the "U" bracket (J), insert carriage bolt and leave nut loose for final adjustment.
6. Place I-beam connector (F) loosely on the bottom flange of the I-beam.
7. Slide the selected 1.25" tube (E) into a 1.50" tube (E) and attach to I-beam connectors (F) and fasten loosely with bolt and nut.
8. Repeat steps 6 through 7 to create the "V" pattern of the square tubes loosely in place. The angle is not to exceed 45 degrees and not below 40 degrees.
9. After all bolts are tightened, secure 1.25" and 1.50" tubes using four (4) 1/4" - 14 x 3/4" self-tapping screws in pre-drilled holes.

INSTALLATION OF LATERAL TELESCOPING TRANSVERSE ARM SYSTEM

THE MODEL 1101 "V" (LONGITUDINAL & LATERAL PROTECTION) ELIMINATES THE NEED FOR MOST STABILIZER PLATES & FRAME TIES. NOTE: THE USE OF THIS SYSTEM REQUIRES VERTICAL TIES SPACED AT 5'4".

10. Install remaining vertical tie-down straps and 4" ground anchors per home manufacturer's instructions. NOTE: Centerline anchors to be sized according to soil torque condition. Any manufacturer's specifications for sidewall anchor loads in excess of 4,000 lbs. require a 5" anchor per Florida Code.
11. NOTE: Each system is required to have a frame tie and stabilizer attached at each lateral arm stabilizing location. This frame tie & stabilizer plate needs to be located within 18" from of center ground pan.

12. Select the correct square tube brace (H) length for set-up lateral transverse at support location. The lengths come in either 60" or 72" lengths. (With the 1.50" tube as the bottom tube, and the 1.25" tube as the inserted tube.)
13. Install the 1.50 transverse brace (H) to the ground pan connector (D) with bolt and nut.
14. Slide 1.25" transverse brace into the 1.50" brace and attach to adjacent I-beam connector (I) with bolt and nut.
15. Secure 1.50" transverse arm to 1.25" transverse arm using four (4) 1/4" - 14 x 3/4" self-tapping screws in pre-drilled holes.

INSTALLATION USING CONCRETE RUNNER / FOOTER

16. A concrete runner, footer or slab may be used in place of the steel ground pan.

- a) The concrete shall be minimum 2500 psi mix
- b) A concrete runner may be either longitudinal or transverse, and must be a minimum of 8" deep with a minimum width of 16 inches longitudinally or 18 inches transverse to allow proper distance between the concrete bolt and the edge of the concrete (see below).
- c) Footers must have minimum surface area of 441 sq. in. (i.e. 21" square), and must be a minimum of 8" deep.
- d) If a full slab is used, the depth must be a 4" minimum at system bracket location, all other specifications must be per local jurisdiction. Special inspection of the system bracket installation is not required. Footers must allow for at least 4" from the concrete bolt to the edge of the concrete.

NOTE: The bottom of all footings, pads, slabs and runners must be per local jurisdiction.

LONGITUDINAL (Model 1101-TC "V")

- 17. When using Part # 1101-W-CRCA (w/sets), simply install the bracket in runner/footer OR When installing in cured concrete use Part # 101-D-CPCA (dryset). The 1101 (dryset) CA bracket is attached to the concrete using (2) 5/8"x3" concrete wedge bolts (Simpson part # S162300H 5/8" X 3" or Powers equivalent). Place the CA bracket in desired location. Mark bolt hole locations, then using a 5/8" diameter masonry bit, drill a hole to a minimum depth of 3". Make sure all dust and concrete is blown out of the holes. Place wedge bolts into drilled holes, then place 1101 (dry set) CA bracket onto wedge bolts and start wedge bolt nuts. Take a hammer and lightly drive the wedge bolts down by hitting the nut (making sure not to hit the top of threads on bolt). The sleeve of concrete wedge bolt needs to be at or below the top of concrete. Complete by tightening nuts.
- LATERAL: (Model 1101 TC "V")
- 18. For wet set (part # 1101-W-TACA) installation simply install the anchor bolt into runner/footer. For dry set installation (part # 1101-D-TACA) mark bolt hole locations, then using a 5/8" diam. masonry bit, drill a hole to a minimum depth of 3". Make sure all dust and concrete is blown out of the hole. Place wedge bolts (Simpson part # S162300H 5/8" X 3" or Powers equivalent) into (D) concrete wedge bolts down by hitting the wedge bolts. The sleeve of concrete wedge bolt needs to be at or below the top of concrete.
- 19. When using part # 1101 CVW (w/sets) or 1101 CVD (dryset), install per steps 17 & 18.

Notes:

1. LENGTH OF HOUSE IS THE ACTUAL BOX SIZE

2. • = STABILIZER PLATE AND FRAME LOCATION (needs to be located within 18 inches of center of ground pan or concrete)


3. □ = LOCATION OF LONGITUDINAL BRACING ONLY

4. ▣ = TRANSVERSE & LONGITUDINAL LOCATIONS


REQUIRED NUMBER AND LOCATION OF MODEL 1101 "V" OR 1101 C "V"

BRACES FOR UP TO 4/12 ROOF PITCH

ALL WIDTHS; AND LENGTHS UP TO 52'

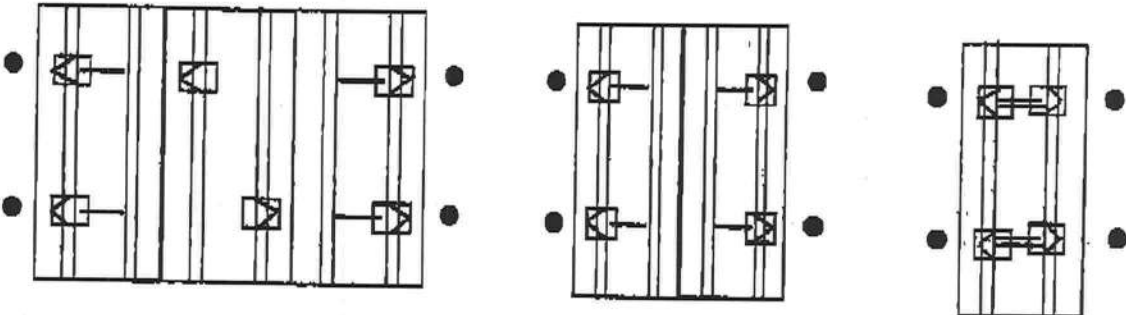


ALL WIDTHS; AND LENGTHS OVER 52' TO 80'

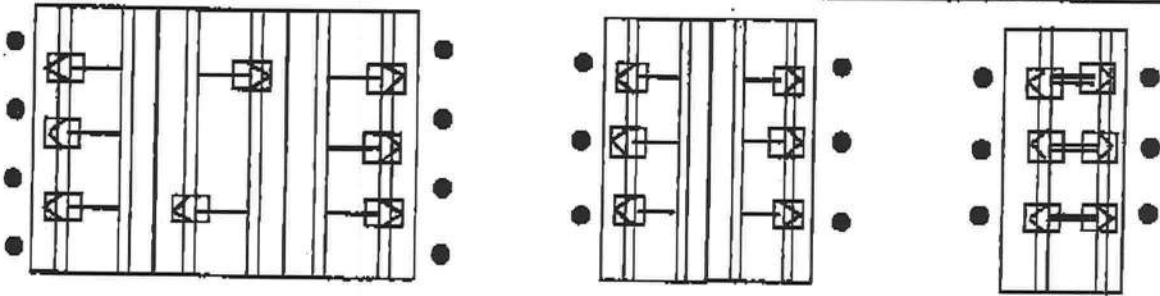



HOMES WITH 5/12 ROOF PITCH REQUIRE PER FLORIDA REGULATIONS

6 systems for home lengths up to 52' and 8 systems for homes over 52' and up to 80'. One stabilizer plate and frame are required at each lateral bracing system.




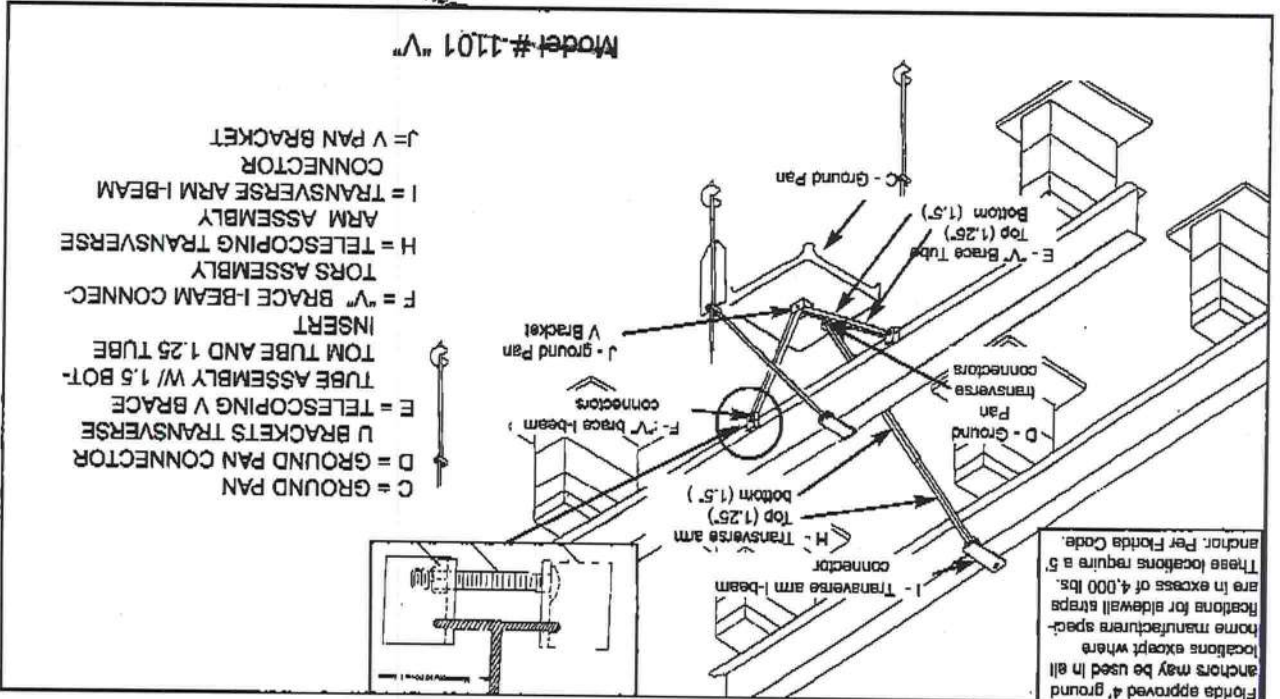

Longitude dry
concrete bracket
part # 1101 D-CPCA
Wet bracket part #
1101 W-CPCA not
shown

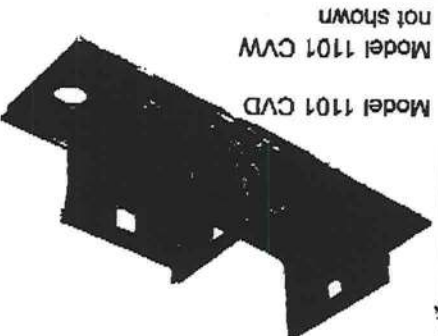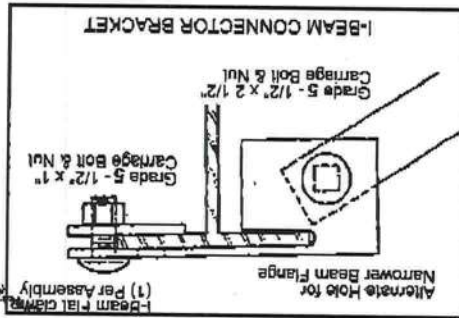

"HADDEN"

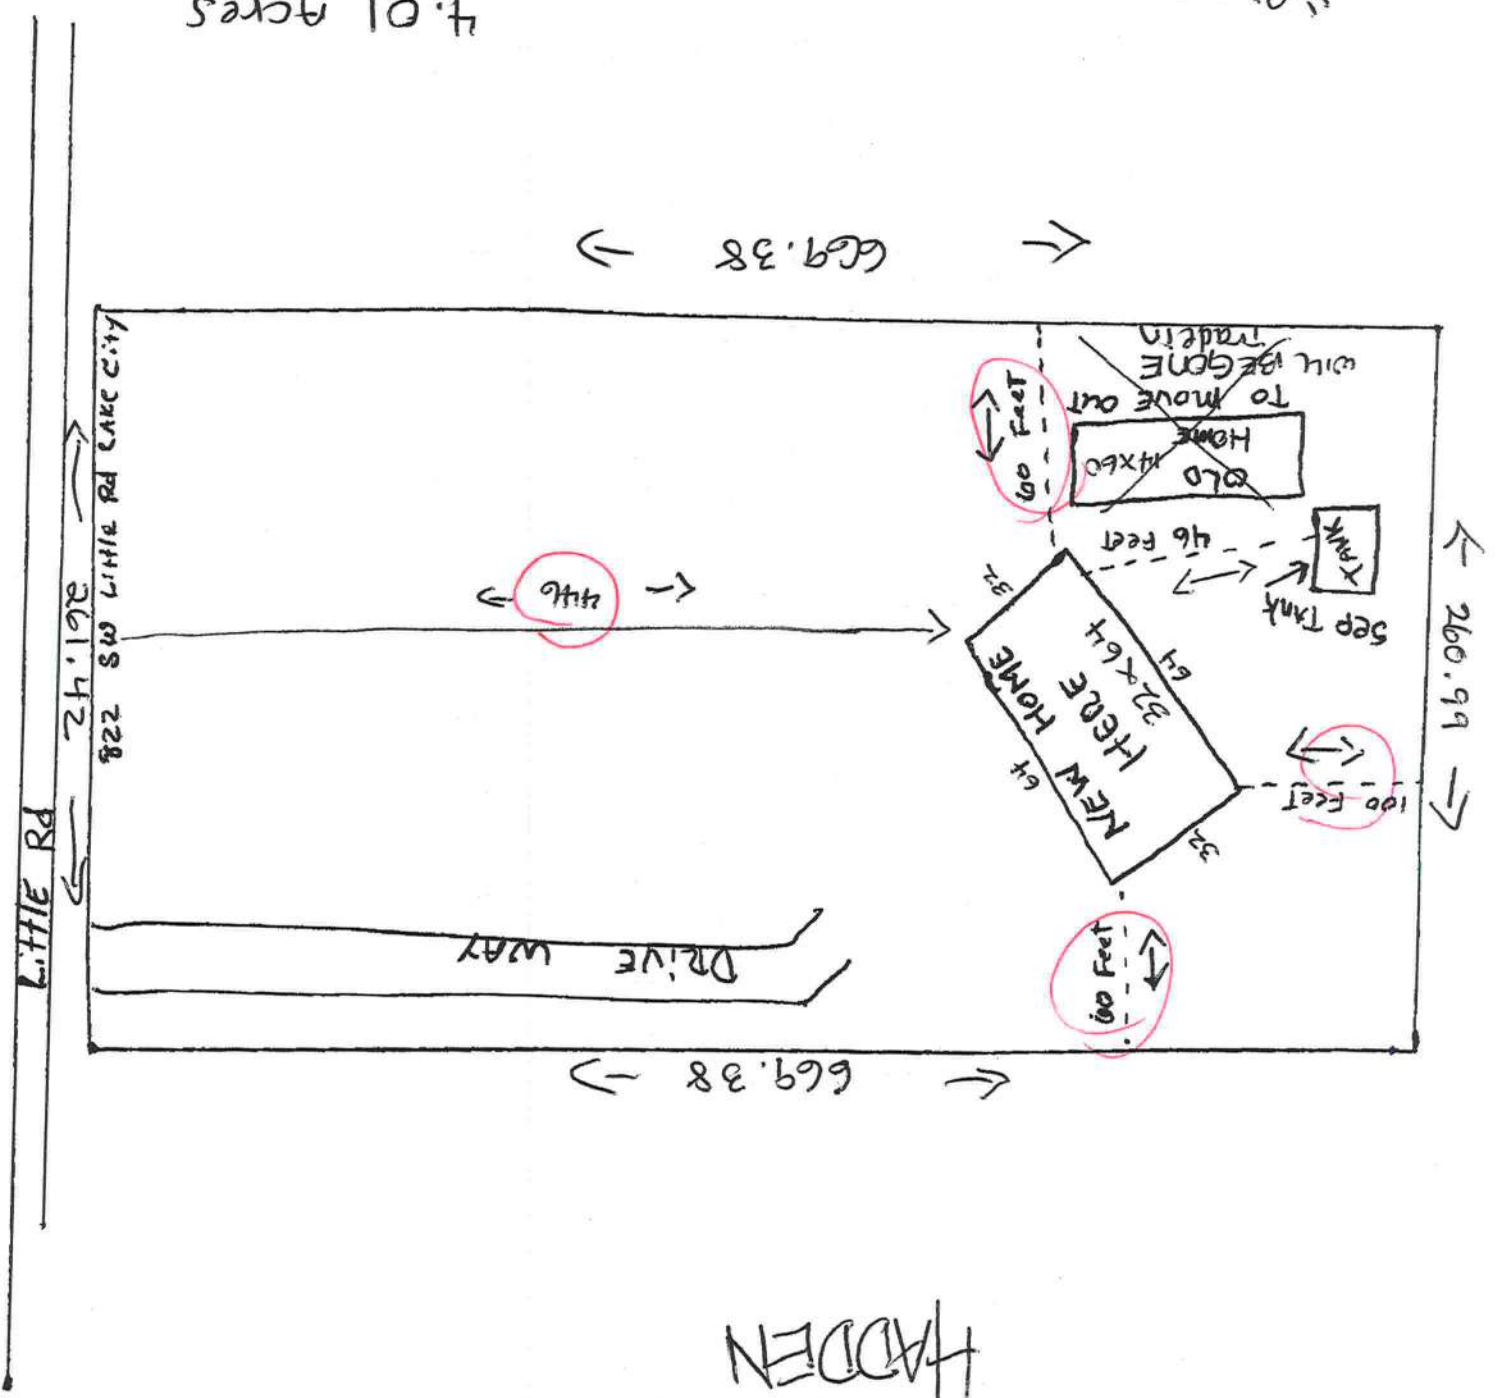

"RIVERS MANOR UNIT 1"
REPLACEMENT HOME
EXISTING DRIVEWAY
EXISTING SEPTIC TANK
4.01 acres

Rec'd
Doc 182

TO STEPHANIE
ROSSI
PROOF
OF LAND
OWNERSHIP

Prepared By and return to:
Deas Bullard Properties
672 East Duval Street
Lake City, Florida 32055

Inst:200712024883 Date:11/6/2007 Time:11:42 AM
Doc Stamp-Deed:182.00
DC,P,DeWitt Cason,Columbia County Page 1 of 1

WARRANTY DEED

This Warranty Deed made this 23rd day of October 2007 by AUDREY S. BULLARD AND JOHN H. DEAS, hereinafter referred to as Grantor to MICHAEL L. HADDEN AND ROSE M. HADDEN, his wife whose post office address is 822 SW Little Rd., Lake City, Florida 32024 hereinafter referred to as the Grantee. Witnesseth: That the grantor, for and in consideration of the sum of \$10.00 and other valuable consideration, confirms unto the grantee, all that certain land situated in Columbia County, Florida. Parcel Identification Number: 01-55-16-03401-106

Lot #6 Rivers Manor Unit 1, a subdivision as recorded in Plat Book 5 Page 139, Public Records of Columbia County, Florida. This Warranty Deed is given subject to the Deed Restrictions recorded in OR Book 682, Page 716, Public Records of Columbia County, Florida and the oil, gas and mineral rights of record, if any.

The above described property is not the homestead property of the Grantors.

N.B: This Warranty Deed is given to fulfill the terms and conditions of that certain Contract For Deed dated December 1, 1993, recorded December 17, 1993 in OR Book 783, page 1766, Public Records of Columbia County, Florida between the above mentioned Grantors and Grantees. The Quit Claim Deed dated August 8, 1995, recorded September 1, 1995, in OR Book 810, page 222, Public Records of Columbia County, Florida Rose M. Hadden, first party to Michael L. Hadden, second party. The Quit Claim Deed dated November 26, 2002, recorded December 31, 2002, in OR Book 971, page 399, Public Records of Columbia County, Florida, Michael L. Hadden, first party to Michael L. Hadden and Rose M. Hadden, his wife second party. Partial Release of Mortgage dated April 6, 2005, recorded April 14, 2005, in OR Book 1043, page 1243, Public Records of Columbia County, Florida.

Together with all the tenements, hereditaments and appurtenances thereto belonging or in anywise appertaining. To Have and to Hold, the same in fee simple forever.

And the grantor hereby covenants with said grantee that the grantor is lawfully seized of said land in fee simple: that the grantor has good right and lawful authority to sell and convey said land: that the grantor hereby warrants the title to said land and will defend the same against the lawful claims of all persons whomsoever, and that said land is free of all encumbrances except as noted above and taxes accruing subsequent to December 31, 2006.

In Witness Whereof, the said grantor has signed and sealed these presents the day and year first above written.

Signed, sealed and delivered in our presence:
Witness: Hollie E. Hanover
Witness: Sue D. Lane

By: Audrey S. Bullard
By: John H. Deas

By: Martha Jo Khachigian, as his duly appointed attorney in fact, pursuant to limited power of attorney dated January 14, 2005

Lot #6 Rivers Manor Unit 1, a subdivision as recorded in Plat Book 5 Page 139, Public Records of Columbia County, Florida.

This Warranty Deed is given subject to the Deed Restrictions recorded in OR Book 682, Page 716, Public Records of Columbia County, Florida and the oil, gas and mineral rights of record, if any.

The above described property is not the homestead property of the Grantors.

N.B.: This Warranty Deed is given to fulfill the terms and conditions of that certain Contract For Deed dated December 1, 1993, recorded December 17, 1993 in OR Book 783, page 1766, Public Records of Columbia County, Florida between the above mentioned Grantors and Grantees.

The Quit Claim Deed dated August 8, 1995, recorded September 1, 1995, in OR Book 810, page 222, Public Records of Columbia County, Florida Rose M. Hadden, first party to Michael L. Hadden, second party.
The Quit Claim Deed dated November 26, 2002, recorded December 31, 2002, in OR Book 971, page 399, Public Records of Columbia County, Florida, Michael L. Hadden, first party to Michael L. Hadden and Rose M. Hadden, his wife second party.
Partial Release of Mortgage dated April 6, 2005, recorded April 14, 2005, in OR Book 1043, page 1243, Public Records of Columbia County, Florida.

Together with all the tenements, hereditaments and appurtenances thereto belonging or in anywise appertaining.

To Have and to Hold, the same in fee simple forever.

And the grantor hereby covenants with said grantee that the grantor is lawfully seized of said land in fee simple: that the grantor has good right and lawful authority to sell and convey said land: that the grantor hereby fully warrants the title to said land and will defend the lawful claims of all persons whomsoever; and that said land is free of all encumbrances except as noted above and taxes accruing subsequent to December 31, 2006.

In Witness Whereof, the said grantor has signed and sealed these presents the day and year first above written.

Signed, sealed and delivered in our presence:

Holly C. Hanover
Witness: Holly C. Hanover
Sue D. Lane
Witness: Sue D. Lane

John H. Deas
By: John H. Deas
Audrey S. Bullard
By: Audrey S. Bullard


Martha Jo Khachigian
By: Martha Jo Khachigian, as his duly appointed attorney in fact, pursuant to limited power of attorney dated January 14, 2005


State of Florida
County of Columbia

I HEREBY CERTIFY that on this day, before me, an officer duly authorized in the State and County last aforesaid to take acknowledgments personally appeared Audrey S. Bullard and Martha Jo Khachigian as attorney in fact for John H. Deas. They are personally known to me and they executed before me the foregoing deed and acknowledged before me that they executed the same.

WITNESSES my hand and official seal in the County and State last aforesaid this 23rd day of Oct. 2007.

Holly C. Hanover
Holly C. Hanover
Notary Public, State of Florida



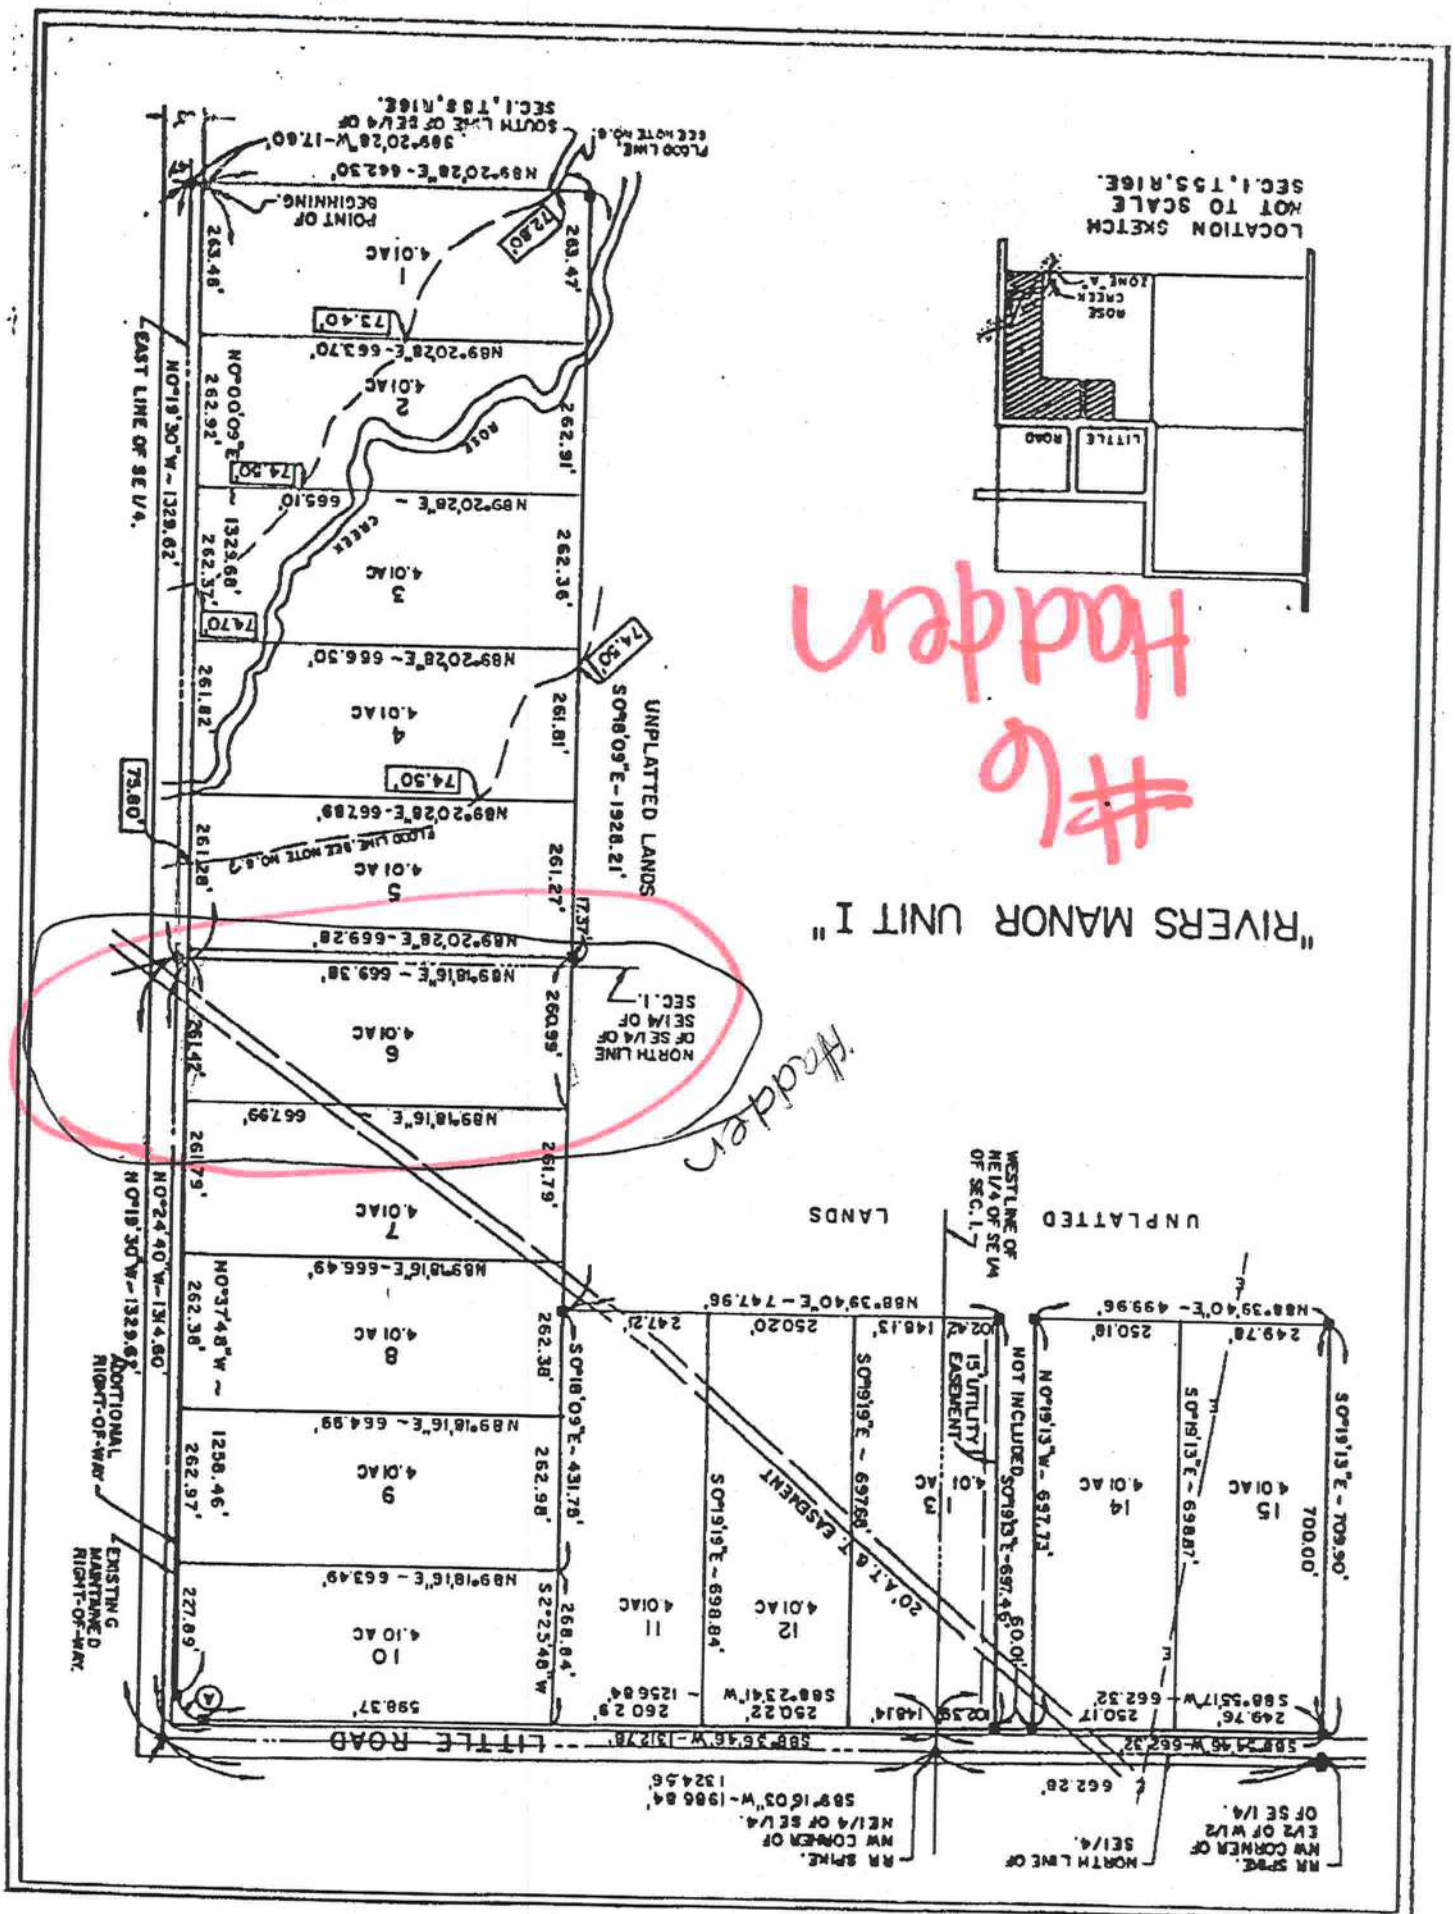

MOBILE HOME INSTALLATION SUBCONTRACTOR VERIFICATION FORM

APPLICATION NUMBER 1111-38 CONTRACTOR Wendell Crews (352) 351-6100

THIS FORM MUST BE SUBMITTED PRIOR TO THE ISSUANCE OF A PERMIT

In Columbia County one permit will cover all trades doing work at the permitted site. It is REQUIRED that we have records of the subcontractors who actually did the trade specific work under the permit. Per Florida Statute 440 and Ordinance 89-6, a contractor shall require all subcontractors to provide evidence of workers' compensation or exemption, general liability insurance and a valid Certificate of Competency license in Columbia County.

Any changes, the permitted contractor is responsible for the corrected form being submitted to this office prior to the start of that subcontractor beginning any work. Violations will result in stop work orders and/or fines.

ELECTRICAL	Print Name: Michael Hadden	Signature: [Signature]	License #: [Blank]	Phone #: [Blank]
MECHANICAL/A/C 568	Print Name: David Hall's Inc.	Signature: [Signature]	License #: 0A60 57424	Phone #: 386-955-9792
PLUMBING/GAS	Print Name: Michael Hadden	Signature: [Signature]	License #: [Blank]	Phone #: 386-9738

Specialty License	License Number	Sub-Contractors Printed Name	Sub-Contractors Signature
MASON			
CONCRETE FINISHER			

F.S. 440.103 Building permits; identification of minimum premium policy.--Every employer shall, as a condition to applying for and receiving a building permit, show proof and certify to the permit issuer that it has secured compensation for its employees under this chapter as provided in ss. 440.10 and 440.38, and shall be presented each time the employer applies for a building permit.

COLUMBIA COUNTY BUILDING DEPARTMENT
135 NE Hernando Ave, Suite B-21, Lake City, FL 32055
Phone: 386-758-1008 Fax: 386-758-2160

MOBILE HOME INSTALLERS AGENT AUTHORIZATION

I, Medell Cruz, give this authority and I do certify that the below

referenced person(s) listed on this form is/are under my direct supervision and control and

is/are authorized to purchase permits, call for inspections and sign on my behalf.

Printed Name of Authorized Person	Signature of Authorized Person	Agents Company Name
Michael Hadden	<u>Michael Hadden</u>	Homeowner

I, the license holder, realize that I am responsible for all permits purchased, and all work done under my license and I am fully responsible for compliance with all Florida Statutes, Codes, and Local Ordinances.

I understand that the State Licensing Board has the power and authority to discipline a license holder for violations committed by him/her or by his/her authorized person(s) through this document and that I have full responsibility for compliance granted by issuance of such permits.

Medell Cruz License Holders Signature (Notarized) License Number TH1025316 Date 11-25-11

NOTARY INFORMATION:


STATE OF: Florida COUNTY OF: Mecklenburg

The above license holder, whose name is Medell Cruz personally appeared before me and he known by me or has produced identification (Type of I.D.) on this 29 day of Nov, 2011

NOTARY SIGNATURE

Medell Cruz

(Seal/Stamp)





STATE OF FLORIDA
DEPARTMENT OF HEALTH
ONSITE SEWAGE TREATMENT AND DISPOSAL
SYSTEM
APPLICATION FOR CONSTRUCTION PERMIT

12-06-11:05:59PM

BLDG/ZONING

:386 758-2187

1 / 2

APPLICATION FOR:
☐ New System
☒ Existing System
☐ Abandonment
☐ Temporary
☐ Holding Tank
☐ Innovative

APPLICANT: Michael L. Hadden

AGENT: Michael Hadden
TELEPHONE: 386-288-9938

MAILING ADDRESS: 882 SW Little Rd Lake City FL 32025

TO BE COMPLETED BY APPLICANT OR APPLICANT'S AUTHORIZED AGENT. SYSTEMS MUST BE CONSTRUCTED BY A PERSON LICENSED PURSUANT TO 489.105(3) (M) OR 489.552, FLORIDA STATUTES. IT IS THE APPLICANT'S RESPONSIBILITY TO PROVIDE DOCUMENTATION OF THE DATE THE LOT WAS CREATED OR PLATTED (MM/DD/YY) IF REQUESTING CONSIDERATION OF STATUTORY GRANDFATHER PROVISIONS.

PROPERTY INFORMATION

LOT: 6 BLOCK: SUBDIVISION: Rivers Manor U-1 PLATTED:

PROPERTY ID #: 01-55-16-03401-106 ZONING: I/M OR EQUIVALENT: [] Y / [] N []

PROPERTY SIZE: 4 ACRES WATER SUPPLY: [X] PRIVATE PUBLIC [] <=2000GPD [] >2000GPD IS SEWER AVAILABLE AS PER 381.0065, FS? [X] N []

DISTANCE TO SEWER: FT

PROPERTY ADDRESS: 882 SW Little Rd Lake City FL 32024

DIRECTIONS TO PROPERTY: Hwy 47 South to Hwy 240 Turn Left go to

Rapier way turn left over to Little Rd turn left 2 Driveway

on left After Creek 822 on oak Tree Driveway on left

BUILDING INFORMATION

[X] RESIDENTIAL [] COMMERCIAL

Unit Type of Establishment No. of Bedrooms Building Area sqft Commercial/Institutional System Design

1 Double wide 3 2000 ORIGINAL ATTACHED

2 32x64

3

4

[] Floor/Equipment Drains [] Other (Specify)

SIGNATURE: Mickey A. Hadden

DATE: 11/29/11

DH 4015, 08/09 (Obsoletes previous editions which may not be used)

Incorporated 64E-6.001, FAC




STATE OF FLORIDA
DEPARTMENT OF HEALTH
APPLICATION FOR ONSITE SEWAGE DISPOSAL SYSTEM CONSTRUCTION PERMIT

Permit Application Number 11-493E

Hadden

PART II - SITE PLAN

Scale: Each block represents 5 feet and 1 inch = 50 feet.

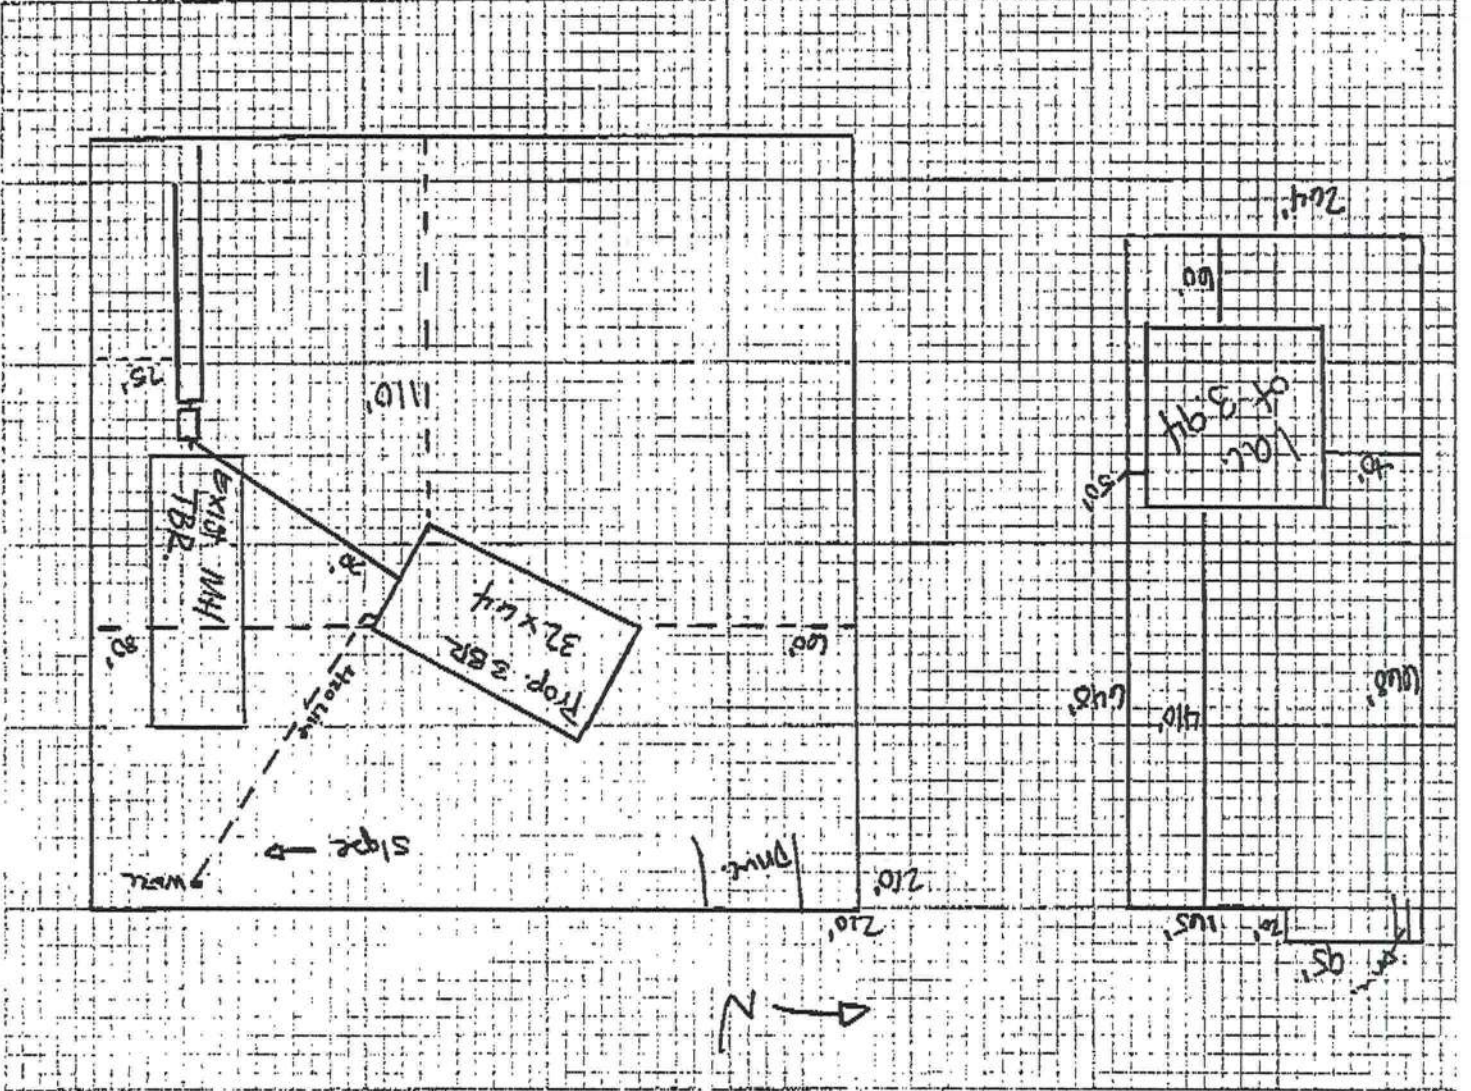

Notes:

Site Plan submitted by: _____

Signature _____

Not Approved _____

Date 12/6/11

Title _____

County Health Department

C. Hadden

Plan Approved ☒ By _____

ALL CHANGES MUST BE APPROVED BY THE COUNTY HEALTH DEPARTMENT

COLUMBIA COUNTY 9-1-1 ADDRESSING

P. O. Box 1787, Lake City, FL 32056-1787
PHONE: (386) 758-1125 * FAX: (386) 758-1365 * Email: ron_croft@columbiacountyfla.com

Addressing Maintenance

To maintain the Countywide Addressing Policy you must make application for a 9-1-1 Address at the time you apply for a building permit. The established standards for assigning and posting numbers to all principal buildings, dwellings, businesses and industries are contained in Columbia County Ordinance 2001-9. The addressing system is to enable Emergency Service Agencies to locate you in an emergency, and to assist the United States Postal Service and the public in the timely and efficient provision of services to residents and businesses of Columbia County.

DATE REQUESTED: 11/30/2011 DATE ISSUED: 12/7/2011

ENHANCED 9-1-1 ADDRESS:

822 SW LITTLE RD

LAKE CITY FL 32024

PROPERTY APPRAISER PARCEL NUMBER:

01-5S-16-03401-106

Remarks:

RE-ISSUE OF EXISTING ADDRESS FOR NEW STRUCTURE ON
PARCEL. OLD STRUCTURE TO BE REMOVED.

Address Issued By: SIGNED: / RONAL N. CROFT
Columbia County 9-1-1 Addressing / GIS Department

NOTICE: THIS ADDRESS WAS ISSUED BASED ON LOCATION
INFORMATION RECEIVED FROM THE REQUESTER. SHOULD
AT A LATER DATE, THE LOCATION INFORMATION BE FOUND
TO BE IN ERROR, THIS ADDRESS IS SUBJECT TO CHANGE.

Columbia County Building Permit

DATE 12/07/2011

APPLICANT MICHAEL HADDEN

ADDRESS 822 SW LITTLE RD

OWNER MICHAEL & ROSIE HADDEN

ADDRESS 822 SW LITTLE ROAD

CONTRACTOR WENDELL CREWS

LOCATION OF PROPERTY 47S, TL ON CR 240, TR PEPPER WAY, TL LITTLE RD, 2ND

DRIVE AFTER CREEK ON LEFT

TYPE DEVELOPMENT MH, UTILITY

ESTIMATED COST OF CONSTRUCTION 0.00

HEATED FLOOR AREA TOTAL AREA

FOUNDATION WALLS ROOF PITCH FLOOR

LAND USE & ZONING A-3

Minimum Set Back Requirements: STREET-FRONT 30.00 REAR 25.00 SIDE 25.00

NO. EX.D.U. 1 FLOOD ZONE X DEVELOPMENT PERMIT NO.

PARCEL ID 01-SS-16-03401-106

SUBDIVISION RIVERS MANOR

LOT 6 BLOCK PHASE UNIT TOTAL ACRES 4.01

Culvert Permit No. IH1025316

Culvert Waiver Contractor's License Number

EXISTING 11-493E BK TC

Driveaway Connection Septic Tank Number LU & Zoning checked by Approved for Issuance New Resident

COMMENTS: FLOOR WILL BE ONE FOOT ABOVE THE ROAD

Check # or Cash 2881

FOR BUILDING & ZONING DEPARTMENT ONLY

Temporary Power

Foundation

Monolithic

(Footer/Slab)

Under slab rough-in plumbing

Slab

Sheathing/Nailing

Framing

Insulation

Electrical rough-in

Rough-in plumbing above slab and below wood floor

Pert. beam (Lintel)

Pool

Heat & Air Duct

C.O. Final

Culvert

Permanent power

Utility Pole

M/H tie downs, blocking, electricity and plumbing

Pump pole

RV

Re-roof

Reconnection

INSPECTORS OFFICE

CLERKS OFFICE

FLOOD DEVELOPMENT FEE \$ FLOOD ZONE FEE \$ 25.00 CULVERT FEE \$ TOTAL FEE 375.00

MISC. FEES \$ 300.00 ZONING CERT. FEE \$ 50.00 FIRE FEE \$ 0.00 WASTE FEE \$

BUILDING PERMIT FEE \$ 0.00 CERTIFICATION FEE \$ 0.00 SURCHARGE FEE \$ 0.00

NOTICE: IN ADDITION TO THE REQUIREMENTS OF THIS PERMIT, THERE MAY BE ADDITIONAL RESTRICTIONS APPLICABLE TO THIS PROPERTY THAT MAY BE FOUND IN THE PUBLIC RECORDS OF THIS COUNTY, AND THERE MAY BE ADDITIONAL PERMITS REQUIRED FROM OTHER GOVERNMENTAL ENTITIES SUCH AS WATER MANAGEMENT DISTRICTS, STATE AGENCIES, OR FEDERAL AGENCIES. "WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY RESULT IN YOUR PAYING TWICE FOR IMPROVEMENTS TO YOUR PROPERTY, IF YOU INTEND TO OBTAIN FINANCING, CONSULT WITH YOUR LENDER OR AN ATTORNEY BEFORE RECORDING YOUR NOTICE OF COMMENCEMENT."

EVERY PERMIT ISSUED SHALL BECOME INVALID UNLESS THE WORK AUTHORIZED BY SUCH PERMIT IS COMMENCED WITHIN 180 DAYS AFTER ITS ISSUANCE, OR IF THE WORK AUTHORIZED BY SUCH PERMIT IS SUSPENDED OR ABANDONED FOR A PERIOD OF 180 DAYS AFTER THE TIME THE WORK IS COMMENCED. A VALID PERMIT RECEIVES AN APPROVED INSPECTION EVERY 180 DAYS. WORK SHALL BE CONSIDERED NOT SUSPENDED, ABANDONED OR INVALID WHEN THE PERMIT HAS RECEIVED AN APPROVED INSPECTION WITHIN 180 DAYS OF THE PREVIOUS INSPECTION. The Issuance of this Permit Does Not Waive Compliance by Permittee with Deed Restrictions.

2881

PERMIT APPLICATION/MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only Date Received: 11/11/11 By: JN Building Official: 7.12.5-11 Zoning Official: 6.12.5-11		Flood Zone: X Development Permit: N/A Land Use Plan Map Category: A-3	
FEMA Map: N/A Elevation: N/A Finished Floor: N/A River: N/A In Floodway: N/A		Site Plan with Setbacks Shown: N/A Recorded Deed or Affidavit from land owner: N/A State Road Access: N/A Well letter: N/A Extending well: N/A	
Impact Fees: EMS Fire: N/A School: N/A TOTAL: N/A Impact Fees Suspended March 2009		Parent Parcel #: N/A F W Comp. letter: N/A STUP-MH: N/A Out County: N/A In County: N/A	

Property ID # 01-55-16-03401-106
 Subdivision: Let #6 RIVERS MANOR UNIT

Used Mobile Home: MH Size: 32x64 Year: 2012
 Applicant: MICHAEL HADDEN Phone # (386) 288-9738
 Address: 822 SW LITTLE RD, LAKE OCH, FL 32024
 Name of Property Owner: MICHAEL HADDEN Phone # same
 811 Address: 822 SW LITTLE RD, LAKE OCH, FL 32024
 Circle the correct power company: (Circle One) - Suwannee Valley Electric - Progress Energy
 Name of Owner of Mobile Home: ROSE + MICHAEL HADDEN Phone # same
 Address: same
 Relationship to Property Owner: owner
 Current Number of Dwellings on Property: 1
 Lot Size: 4.01
 Total Acreage: 4.01

Do you: Have Existing Drive or Private Drive or need Culvert Permit or Culvert Waiver (Circle one)
 (Currently using) (Blue Road Sign) (Putting in a Culvert) (Not existing but do not need a Culvert)
 Is this Mobile Home Replacing an Existing Mobile Home: YES
 Driving Directions to the Property: 47 South to Hwy 940, Turn Left to Paper Way Turn Right to Little Rd, 2nd Avenue of Allen Creek Turn Left
 Name of Licensed Dealer/Installer: Model: Crows Phone # 352-351-600
 4650 Air 35th St Ocala, FL 34479
 License Number: FH1025316
 Installation Decal #: 9117

687
 Spoke to Michael 12/7/11

COLUMBIA COUNTY, FLORIDA

OCCUPANCY

COLUMBIA COUNTY, FLORIDA

Department of Building and Zoning Inspection

This Certificate of Occupancy is issued to the below named permit holder for the building and premises at the below named location, and certifies that the work has been completed in accordance with the Columbia County Building Code.

Parcel Number 01-5S-16-03401-106

Building permit No. 000029804

Use Classification MH, UTILITY

Fire: 0.00

Permit Holder WENDELL CREWS

Waste:

Owner of Building MICHAEL & ROSIE HADDEN

Total: 0.00

Location: 822 SW LITTLE RD, LAKE CITY, FL 32024

Date: 01/20/2012

Steve Lee

Building Inspector



POST IN A CONSPICUOUS PLACE
(Business Places Only)
