



Mobile Home Permit Worksheet

Installer:

William Price

License #

14-1041934

Address of home being installed

243 NW Cornland Ct.

Manufacturer

Little City EL 38035

Length x width


72x28

NOTE:

If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home where the sidewall ties exceed 5 ft 4 in.

Typical pier spacing

2'



Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

Installer's initials

WLP

marriage wall piers within 2' of end of home per Rule 15C

Permit Number:

Date:

New Home

Used Home

Home installed to the Manufacturer's Installation Manual

Home is installed in accordance with Rule 15-C

Single wide

Wind Zone II

Wind Zone III

Double wide

Installation Decal #

41574

Triple/Quad

Serial #

LOH 6A2004114145

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	16' x 16" (256)	18 1/2" x 18 (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'
1600 psf	4'6"	6'	7'	8'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'
2500 psf	7'6"	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'

*Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

17x25

POPULAR PAD SIZES

Pad Size	Sq in
18 x 16	288
16 x 16	256
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/2 x 26 1/2	348
20 x 26	400
17 3/16 x 26 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

I-beam pier pad size

17x25

Perimeter pier pad size

17x25

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

4 ft 24 5 ft 24

LANE 23x21

ANCHORS

FRAME TIES

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer

Longitudinal Stabilizing Device (LSD) Arms

Manufacturer

OTHER TIES

Number

Sidewall

Longitudinal

Marriage Wall

Shear Wall



Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil _____ without testing.

x 1000

x 1000

x 1000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1000

x 1000

x 1000

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing _____. A test showing 275 inch pounds or less will require 5' anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5' anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's Initials

WLF

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER.

Installer Name _____

Date Tested _____

ELECTRICAL

Contact electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 164

PLUMBING

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 78

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 71

Permit Number: _____

Date: _____

Site Preparation

Debris and organic material removed 9/20/10

Water drainage: Natural _____ Swale _____ Pad ✓ Other _____

Fastening multi wide units

Floor- Type Fastener: 1/4" x 4" Length: _____ Spacing: 18"
Walls- Type Fastener: 3/8" x 4" Length: _____ Spacing: 18"
Roof- Type Fastener: 1/2" x 4" Length: _____ Spacing: 18"

For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials

Type gasket: FOAM

Pg. _____

Installed:

Between Floors _____ Yes ✓

Between Walls _____ Yes ✓

Bottom of ridge beam _____ Yes ✓

Weatherproofing

The bottom board will be repaired and/or taped.

Yes ✓ Pg. 124

Siding on units is installed to manufacturer's specifications.

Yes ✓

Fireplace chimney installed so as not to allow intrusion of rain water.

Yes ✓

Miscellaneous

Skirting to be installed.

Yes ✓ No _____ N/A _____

Dryer vent installed outside of skirting.

Yes ✓ No _____ N/A _____

Range downflow vent installed outside of skirting.

Yes ✓ No _____ N/A _____

Drain lines supported at 4' intervals.

Yes ✓ No _____ N/A _____

Other:

Yes ✓ No _____ N/A _____



Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer's Signature

WLF

Date 10/24/25

The COSTMER

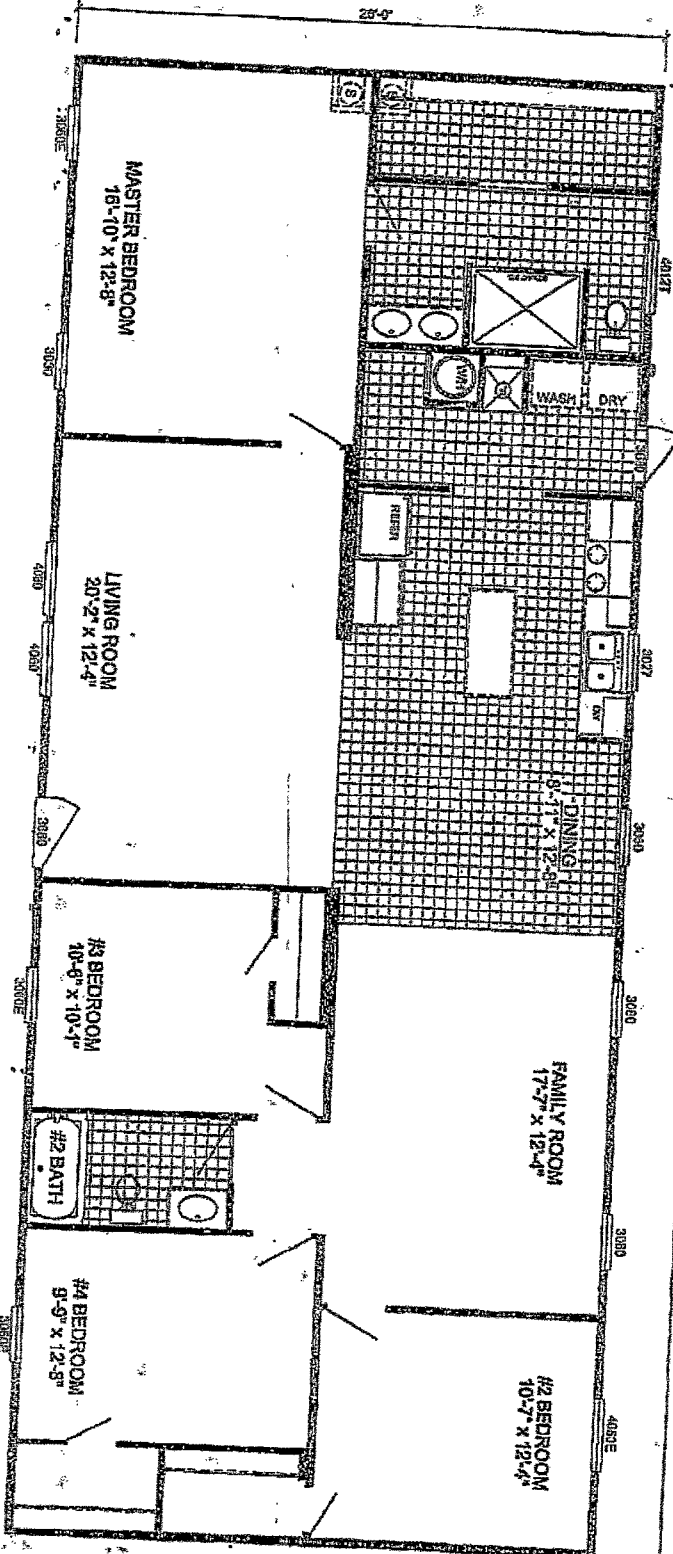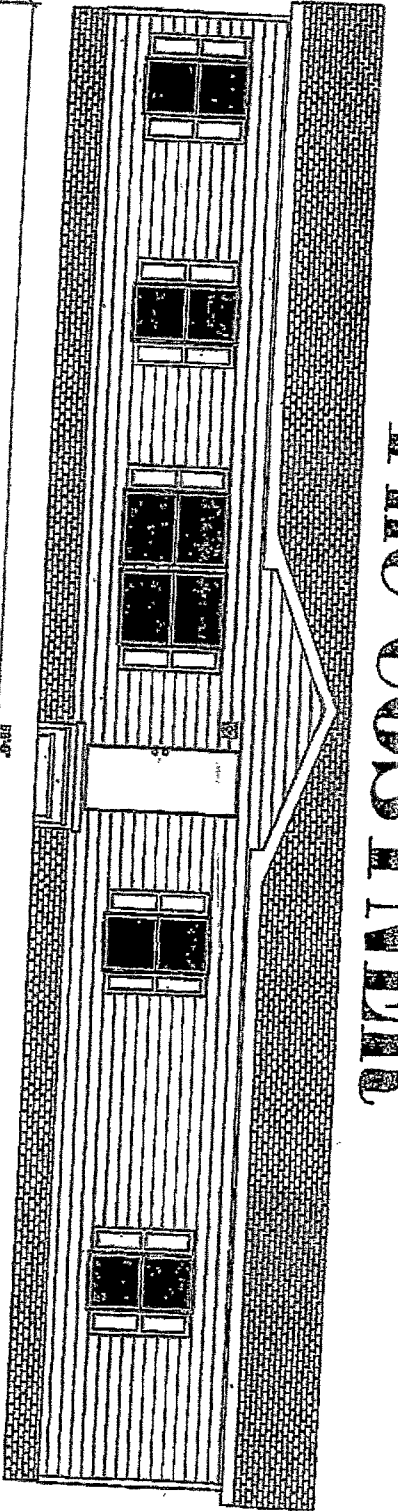

L-2684H - RUNNER SS
4-BEDROOM / 2-BATH
28 x 72 - Approx. 1768 Sq. Ft.
 Date: 05/21/24

*All room dimensions include closets and square footage figures are approximate.
 Live Oak Homes reserves the right to change product offering at any time.

Runner SS

Williams

28X72

Columbia
IWHP

License Number: IH / 1041936 / 1 Name: WILLIAM R PRICE

Order #: 5453

Label #: 91527

Manufacturer:

Homeowner:

Year Model:

Address:

Length & Width:

City/State/Zip:

Type Longitudinal System:

Phone #:

Type Lateral Arm System:

Date Installed:

New Home: _____ Used Home: _____

Installed Wind Zone:

Data Plate Wind Zone:

Note:

(Check Size of Home)

Single _____

Double _____

Triple _____

HUD Label #:

Soil Bearing / PSF:

Torque Probe / in-lbs:

Permit #:

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

91527

LABEL #

DATE OF INSTALLATION

WILLIAM R PRICE

NAME

IH / 1041936 / 1

5453

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
