

COLUMBIA COUNTY PERMIT WORKSHEET

page 1 of 2

These worksheets must be completed and signed by the installer.
Submit the originals with the packet.

Installer RONNIE D. NORRIS License # TH1025145




911 Address where home is being installed. _____

Manufacturer JACOBSEN Length x width 28 X 44

NOTE: if home is a single wide fill out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in _____

Installer's initials RJ

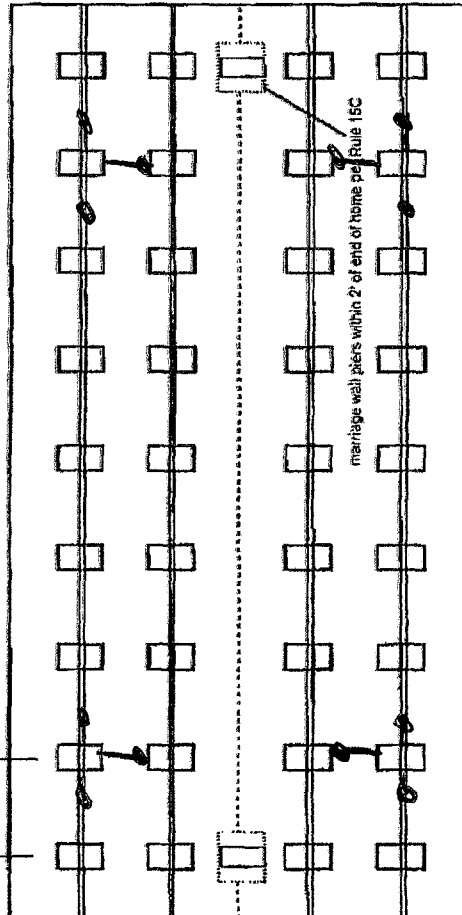

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual ☒

Home is installed in accordance with Rule 15-C ☐

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Decal # 19704

Triple/Quad ☐ Serial # _____

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 dsf	3"	3"	4"	5"	6"	7"	8"
1500 dsf	4"	4"	5"	6"	7"	8"	8"
2000 dsf	6"	6"	8"	8"	8"	8"	8"
2500 dsf	7"	7"	8"	8"	8"	8"	8"
3000 dsf	8"	8"	8"	8"	8"	8"	8"
3500 dsf	8"	8"	8"	8"	8"	8"	8"

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17x25

Perimeter pier pad size 16x16

Other pier pad sizes (required by the mfg.) 17x24

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers

List all marriage wall openings greater than 4 foot and their pier pad sizes below

Opening	Pier pad size
8	17x25
4	16x16
7	16x16

ANCHORS

4 ft 4 5 ft _____

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer _____

Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer _____

OTHER TIES

Sidewall _____
Longitudinal _____
Marriage wall _____
ShearWall _____

Number 22
4
2

COLUMBIA COUNTY PERMIT WORKSHEET

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb. soil without testing

x 1500 x 1500 x 1500

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer
3. Using 500 lb increments, take the lowest reading and round down to that increment.

x 1500 x 1500 x 1500

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5' anchors without testing 60. A test showing 275 inch pounds or less will require 5 foot anchors

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems Pg. _____

Site Preparation

Debris and organic material removed ☒ Swale ☐ Pad ☒ Other ☐

Fastening multi wide units

Floor: Type Fastener: 6x4 Length: 24 Spacing: 24
Walls: Type Fastener: 6x4 Length: 24 Spacing: 24
Roof: Type Fastener: 6x4 Length: 24 Spacing: 24
For used homes a 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv roofing nails at 2" on center on both sides of the centerline

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

Type gasket R
Pg. _____

Installed
Between Floors Yes R
Between Walls Yes R
Bottom of ridgebeam Yes R

Weatherproofing


The bottomboard will be repaired and/or taped. Yes _____ Pg. _____
Siding on units is installed to manufacturer's specifications. Yes _____
Fireplace chimney installed so as not to allow intrusion of rain water. Yes _____

Miscellaneous

Skirting to be installed Yes _____ No _____
Dryer vent installed outside of skirting Yes _____ N/A _____
Range downflow vent installed outside of skirting. Yes _____ N/A _____
Drain lines supported at 4 foot intervals. Yes _____
Electrical crossovers protected. Yes _____
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature Time name Date 1-2-2014



SEE PAPERS AND TABLES ON PAGE 2 OF 2
SEE WARNINGS AND Cautions ON PAGE 2


JACOBSEN HOMES
PO BOX 388, EDDY PARKLAND TX
SAFETY BARRON, FLORIDA 34655


DOJ MEMPHIS

WENT TO SALT-DEER, SALT-DEER, AND OTHER BEHAVIORS IN THE HOT-UP BOILING STEAM TUBS IS NOT ESSENTIAL, MORE IMPORTANT, TO BE A TRAIT CHARACTERISTIC

FILED NUMBER ZONE - 2
FILED NUMBER EXPOSURE CATEGORY - E
31691 - PAGE 1 OF 2

THIS PRODUCT IS DESIGNED TO FUNCTION AS A CONTINUITY SEAL. THE INTERIOR SELF-
CLEANING WALL MEETS THIS REQUIREMENT. AFTER VERIFYING COMPLIANCE, THE INTERIOR
SELF-SEALING FUNCTION IS RESPONSIBLE AND USABLE FOR ALL INSTALLATIONS.

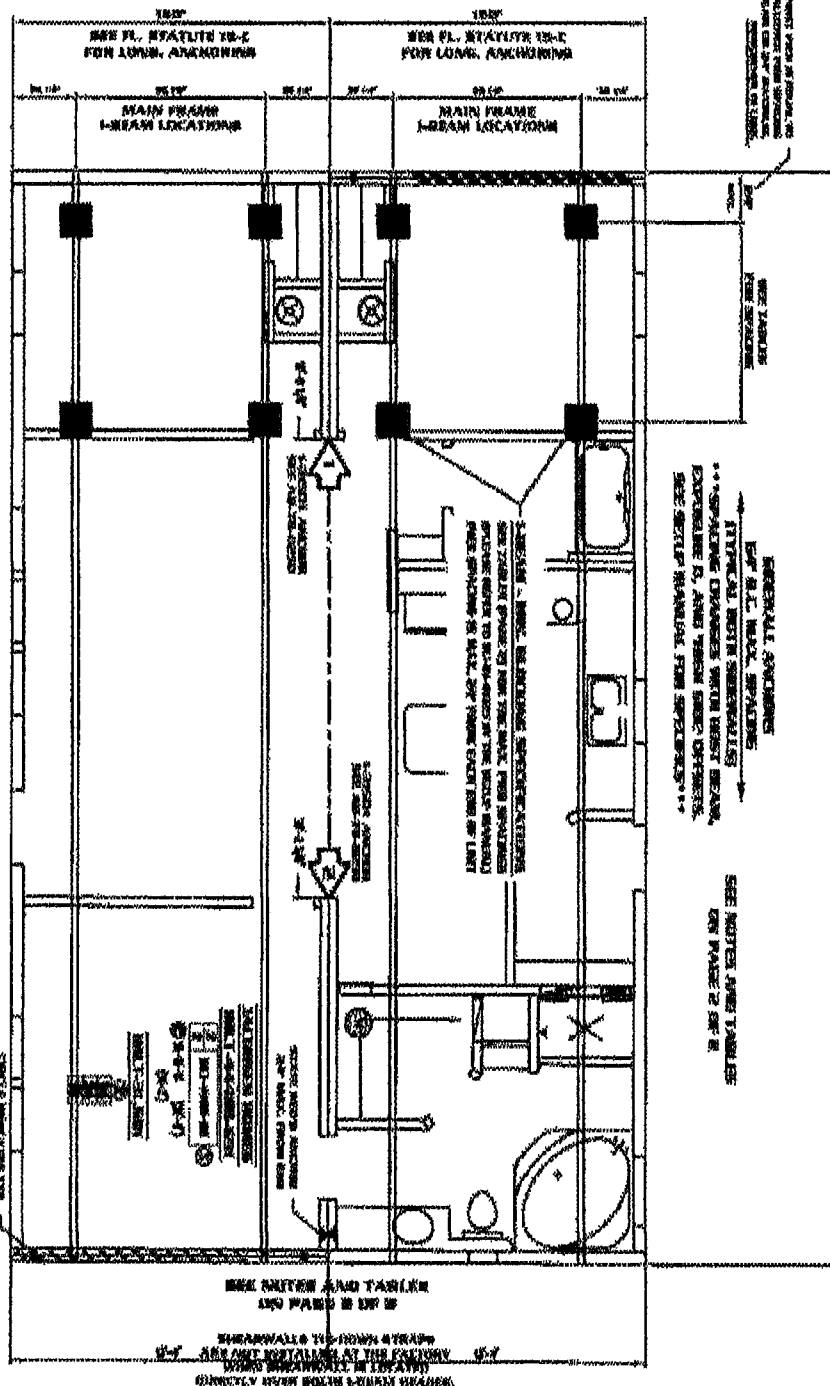



JACOBSEN HOMES

PO BOX 368, 600 PACKARD CT,
SAFETY HARBOR, FLORIDA 34625

(727) 726-1133

www.jacobsenhomes.com

COLLUM INFL. TABLE		COLLUM PAB - MIN. SIZES (sq. in.)									
COL. NO.	SPAN	1000	1500	2000	2500	3000	3500	4000	4500	5000	5500
1	18'-6"	4575	4575	4575	4575	4575	4575	4575	4575	4575	4575
2	18'-6"	4575	4575	4575	4575	4575	4575	4575	4575	4575	4575
3	0'	0	0	0	0	0	0	0	0	0	0
4	0'	0	0	0	0	0	0	0	0	0	0
5	0'	0	0	0	0	0	0	0	0	0	0
6	0'	0	0	0	0	0	0	0	0	0	0
7	0'	0	0	0	0	0	0	0	0	0	0
8	0'	0	0	0	0	0	0	0	0	0	0
9	0'	0	0	0	0	0	0	0	0	0	0
10	0'	0	0	0	0	0	0	0	0	0	0

MINIMUM PIER PAB SIZE (sq. in.)		I-BEAM PIER SPACING									
		1000	1500	2000	2500	3000	3500	4000	4500	5000	5500
A	256 sq. in.	0	0	0	0	0	0	0	0	0	0
B	342.25 sq. in.	0	0	0	0	0	0	0	0	0	0
C	396 sq. in.	0	0	0	0	0	0	0	0	0	0
D	400 sq. in.	0	0	0	0	0	0	0	0	0	0
E	432.875 sq. in.	0	0	0	0	0	0	0	0	0	0
F	576 sq. in.	0	0	0	0	0	0	0	0	0	0
G	676 sq. in.	0	0	0	0	0	0	0	0	0	0

Copyright © 2005, JACOBSEN HOMES, SAFETY HARBOR, FLORIDA. ALL RIGHTS RESERVED.

WARNING:

INSTALLING A MANUFACTURED STRUCTURE/BUILDING CAN BE EXTREMELY DANGEROUS. ONLY QUALIFIED PERSONNEL SHOULD ATTEMPT TO INSTALL A MANUFACTURED STRUCTURE/BUILDING. IMPROPER PROCEDURES AND/OR TECHNIQUES COULD RESULT IN PERSONAL INJURY OR DEATH. IN ADDITION TO THE DANGER TO PERSONNEL, IMPROPER SETTING/INSTALLATION COULD RESULT IN EXTENSIVE/COSTLY DAMAGE TO THE BUILDING/STRUCTURE. NEVER ATTEMPT INSTALLATION IF YOU ARE NOT QUALIFIED AND/OR DO NOT HAVE THE PROPER TOOLS AND/OR EQUIPMENT.

CAUTION:

MANUFACTURED SUBSTRUCTURES CAN WEIGH SEVERAL TONS. IT IS VERY IMPORTANT THAT ALL PERSONNEL, ON THE JOB SITE, BE QUALIFIED AND PROPERLY/IMMEDIATELY TRAINED. A STATE LICENSED SETUP CONTRACTOR IS REQUIRED TO BE RESPONSIBLE FOR ALL SAFETY INITIATIVES, PROGRAMS, POLICES, AND/OR PROCEDURES THAT MAY BE MANDATED BY ORMA AND/OR ANY OTHER LOCAL, STATE, AND/OR FEDERAL CODES AND/OR REQUIREMENTS. THE CONTRACTOR SHALL INSURE/REQUIRE THAT SAFE AND PROPER TECHNIQUES ARE UTILIZED.

NOTES:

1. REFER TO THE MODEL APPROVAL FOR PLAN SPECIFIC INFORMATION.
2. REFER TO THE JACOBSEN HOMES SETUP MANUAL. AND ASSEMBLERS FOR COMPLETE INSTALLATION INSTRUCTIONS. PIERES CAN BE LOCATED ANYWHERE SPACING INCREASED FOR THE SETUP MANUAL.
3. REFER TO SLUG-CORES FOR ADDITIONAL PIER REQUIREMENTS.
4. REFER TO THE APPROVED PLAN FOR THE SPECIFICALLY LOCATIONS AND LOADS.
5. REFER TO THE APPROVED PLAN FOR SPECIFIC LOCATIONS AND TIE-BARS.
6. THE LOCATION SYSTEM OF THE EXTERIOR SIDE OF THE COLLUM. ADDITIONAL PIERES MAY BE REQUIRED ALONG THE MAKING LINE. SEE THE SETUP MANUAL FOR SPECIFICS.
7. ALL 12" WIDE PIERES SYSTEMS REQUIRE PERIMETER AND MOUNTING LINE BENCHMARKING.
8. ALL 24" WIDE PIERES SYSTEMS REQUIRE TRAIL 14" MOUNTING PERIMETER AND MOUNTING LINE BENCHMARKING.
9. ADD BENCHMARK AREA WITH A WIRE BEAM OR A STRUCTURAL ATTACHMENT SMALL BENCH MARK AND ANCHORS SPACED NO FURTHER THAN 48" O.C. BENCHMARKING. THESE WIDE PIERES ARE REQUIRED FOR CLEARER IDENTIFICATION. REFER TO THE JACOBSEN HOMES SETUP MANUAL FOR SPECIFICS REGARDING BENCHMARKING AND SLUG-CORES. WHEN THE ATTACHED STRUCTURE HAS FULFILLED ALL REQUIREMENTS FOR BEING DESIGNED AND CONSTRUCTION TO THE SET SPECIFICATIONS, THESE ADDITIONAL PIERES AND ANCHORS ARE NOT NEEDED.
10. MAX. PIER SPACING OF 14'-0" IS 80". MAX. PIER SPACING OF 17' OR 12' 4-8" IS 100". SEE NOTE 4 FOR PIERES SLUG-CORES THROUGHOUT BENCHMARKING.

MOUNTING LINE PIER SPACING		PERIMETER PIER SPACING									
		1000	1500	2000	2500	3000	3500	4000	4500	5000	5500
A	256 sq. in.	0	0	0	0	0	0	0	0	0	0
B	342.25 sq. in.	0	0	0	0	0	0	0	0	0	0
C	396 sq. in.	0	0	0	0	0	0	0	0	0	0
D	400 sq. in.	0	0	0	0	0	0	0	0	0	0
E	432.875 sq. in.	0	0	0	0	0	0	0	0	0	0
F	576 sq. in.	0	0	0	0	0	0	0	0	0	0
G	676 sq. in.	0	0	0	0	0	0	0	0	0	0

THIS BLOCKING DIAGRAM IS PROVIDED AS A CONVEYANCE ONLY. THE LICENSED SET-UP CONTRACTOR SHALL REVIEW THIS DETAIL AND VERIFY CONFORMANCE. THE LICENSED SET-UP CONTRACTOR IS RESPONSIBLE AND LIABLE FOR ALL INSTALLATION.
