



1

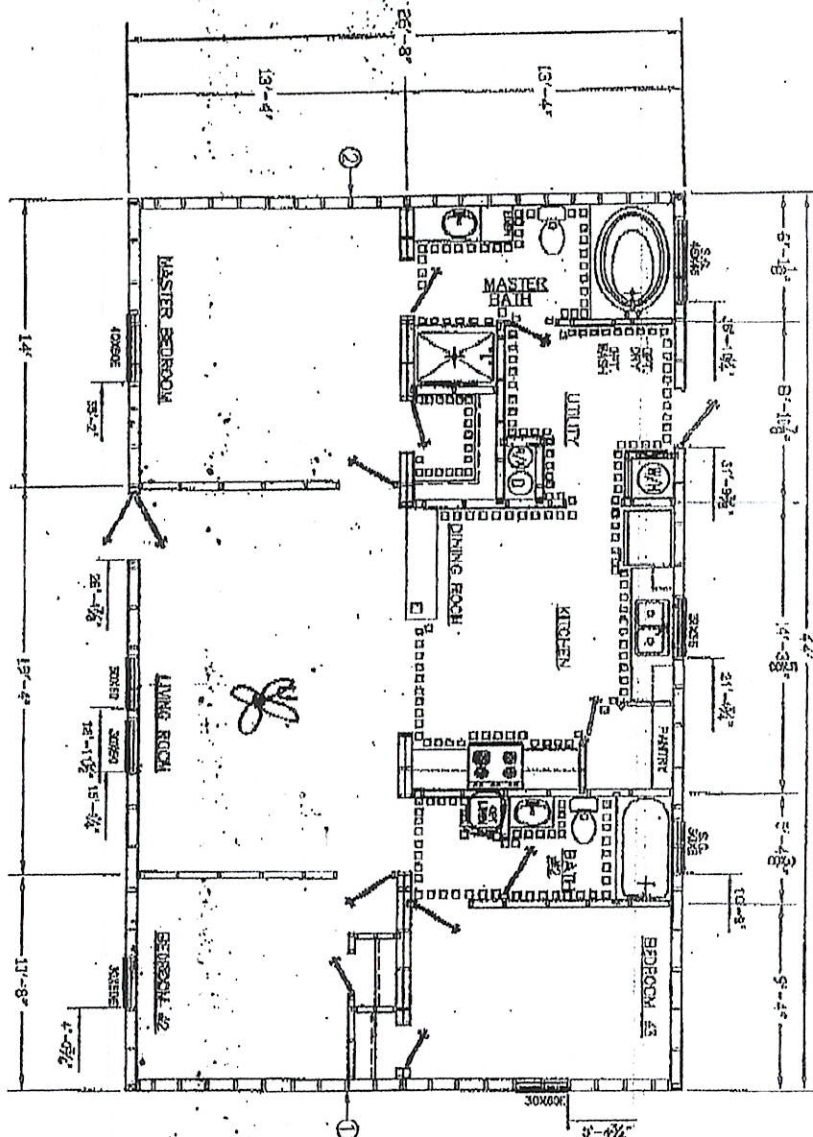

ZONE 1	SW#11	SW#22
ZONE 2	SW#11	SW#22
ZONE 3	SW#11	SW#22

		TownHomes P.O. BOX 1059 LAKE CITY, FLORIDA 32055	
SHOW-TO-LETTER - HIGHLIGHT - QUALITY - DURABLE			
Date:	8-4-14	Penholders	Code# 28030415 C&G W- BATH NO EUBH00
Dt'n:	ROB		
Private:	NEP		
Codes:	1 (15)	C&G ALTH'S N/BTH	
2803 123	2803 2803 2803	2830-215	P&B 8123 SOUT 8123 SOUT

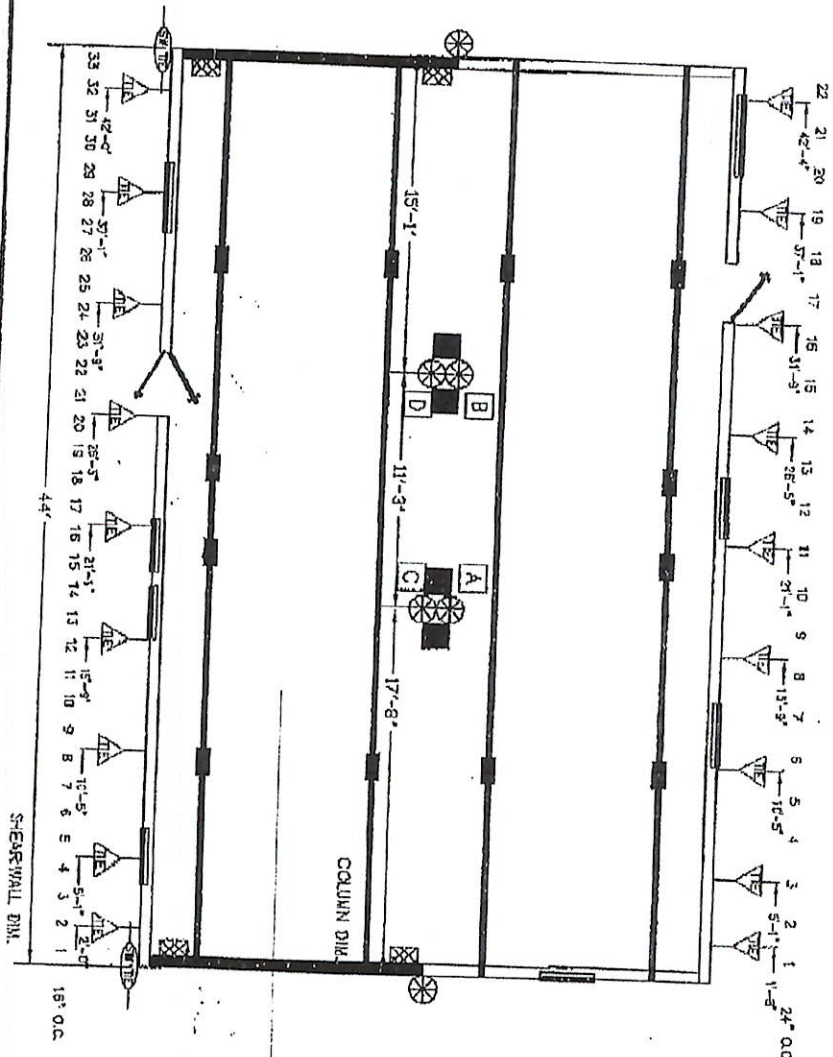

BLOCKING LEGEND:

1) ALL EXTERIOR DOORS, BAY WINDOWS, RECESSED SIDEWALLS AND EXTERIOR WALL OPENINGS 48" OR GREATER WILL REQUIRE BLOCKING ON EACH SIDE.

2) 32" WIDE HOMES REQUIRED TO BE BLOCKED MIN 8'-0" ON CENTER BETWEEN COLUMNS.

- 1-8'x4' BLOCKING
- SEE SOIL BEARING CAPACITY CHARTS FOR SPACING
- COLUMN BLOCKING
- SEE SOIL BEARING CAPACITY CHARTS FOR PAD SIZE
- SHEARWALL BLOCKING
- SHEARWALL FRAME TIE
- CENTER LINE TIES
- VERTICAL TIE
- MAX SPACING 8'-8" CENTER TO CENTER
- LONGITUDINAL TIES



TownHomes
P.O. BOX 1155
LAKE CITY, FLORIDA 32036

Enter: 2-4-14	Revisions:	Date: 28.08.15
City: RCB		
Parent: NEW		
Code: F (15)	2003-215	Phone:
2		BLOCKING PLAN

Mobile Home Permit Worksheet

Application Number: _____

Date: _____


Installer: E. Ernest S. Johnson License # TH-1025249
 Address of home being installed: _____

Manufacturer: Town Home Length x width: 44' x 28'

NOTE: If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home. I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials: [Signature]

Typical pier spacing: 2'
 Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

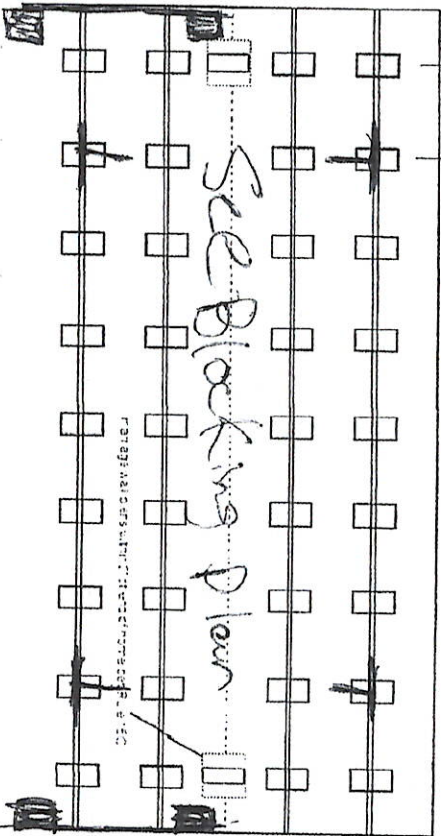

New Home ☒ Used Home ☐
 Home installed to the Manufacturer's Installation Manual ☒
 Home is installed in accordance with Rule 15-C ☒
 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Decal # 80281
 Trailer/Quad ☐ Serial # _____

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sc in)	Footer size (sc in)	16' x 16' (256)	18' 1/2' x 18' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	4'	5'	5'	7'	8'
1500 psf	4'	6'	6'	7'	7'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'	8'
2500 psf	7'	8'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

Interpolated from Rule 15C-1 per spacing table.

PIER PAD SIZES

I-beam pier pad size: 23X31 70c
 Perimeter pier pad size: 11 or 16X18
 Other pier pad sizes (required by the mfg.): _____

POPULAR PAD SIZES

Pad Size	Sq. in
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4' foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4' foot and their pier pad sizes below:

Opening: _____ Pier pad size: _____

See Blocking Plan

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) _____
 Manufacturer _____
 Longitudinal Stabilizing Device w/ Lateral Arms _____
 Manufacturer _____

OTHER TIES

Number _____
 Skewer _____
 Longitudinal _____
 Marriage wall _____
 Shearwall _____

Mobile Home Permit Worksheet

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to soil or check here to declare 1000 b. soil without testing

x 1000 x 1000 x 1000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations
2. Take the reading at the depth of the footar
3. Using 500 lb. increments, take the lowest reading and round down to that increment

x 1000 x 1000 x 1000

TORQUE PROBE TEST

The results of the torque probe test is inch pounds or check here if you are declaring 5' anchors without testing A test: showing 275 inch pounds or less will require 5 foot anchors

Note: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline the points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Ernest S Johnson
Assumed Oliver says 455 foot Anchors

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg

Application Number:

Date:

Site Preparation

Debris and organic material removed Swale ☒ Pad ☐ Other

Fastening multi wide units

Floor: Type Fastener: *1/4"* Length: *7"* Spacing: *24"*
Walls: Type Fastener: *1/4"* Length: *7"* Spacing: *24"*
Roof: Type Fastener: *1/4"* Length: *7"* Spacing: *24"*
For used homes 3 min. 30 gauge, 8 wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that: condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

Type gasket: *211*

Installed: Between Floors Yes
Between Walls Yes
Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes Pg.
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous

Skirting to be installed. Yes No
Dryer vent installed outside of skirting. Yes N/A
Range downflow vent installed outside of skirting. Yes N/A
Drain lines supported at 4 foot intervals. Yes
Electrical crossovers protected. Yes
Other:

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Ernest S Johnson

Date

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

LABEL # 80281

ERNEST SCOTT JOHNSON

NAME IH / 1025249 / 1 4900

LICENSE # ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325 AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

License Number: IH / 1025249 / 1 Name: ERNEST SCOTT JOHNSON

Order #: 4900	Label #: 80281	Manufacturer:	Year Model:	Length & Width:	Type Longitudinal System:	Type Lateral Arm System:	New Home: _____	Used Home: _____	Data Plate Wind Zone:	Permit #:
Homeowner:	Address:	City/State/Zip:	Phone #:	Date Installed:	Installed Wind Zone:	Note:				

(Check Size of Home)	Single	Double	Triple	HUD Label #:	Soil Bearing / PSF:	Torque Probe / in-lbs:
----------------------	--------	--------	--------	--------------	---------------------	------------------------
