

PERMIT NUMBER

PARENT WORKSHEET

Page 2 of 2

POCKET PENETRATOR TEST

The docked per-parameter tests are rounded down to 1500 or effect here to deduct 1000 lb. soil without testing.

5x
x
x

POCKET PNEUMOMETER TESTING METHOD

1. Test the perimeter of the hogue at 6 locations.
2. Take the reading at the depth of the former.
3. Using 500 lb. increments, take the breast reading and round down to that increment.

1

TO MAKE PROBE TEST

The results of the torque probe test is 110.2 inch pounds or check here if you are declaring 5 aircraft without testing. A total showing 275 inch pounds or less will require 5 foot structure.

A state approved lateral entry system is being used and 4 ft. anchors are allowed at the sidewalk locations. 1 unadorned 5 ft anchors are required at all candidate tie points where the torque test resulting is 275 or less and where the middle income manufacturers may require anchors with 4000 lb holding capacity.

Mathematics

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Practical Nutrition

Drink Tested

4/18/25

सिद्धान्तः

Connected electrical conductors between mid-wide units, but not to the main power source. This includes the bonding wire between mid-wide units. Pg. 156

5. TUG-2 Test

Connect all server drives to an existing server I/O or supply back. Pg. 150

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 1561

Sin Proposition

Debris and organic material removed ☒ Yes
Weather-damaged Natural Swale ☐ No
Paved ☒ Yes
Other ☐ No

የጥቅም ስራ ስልጣን

Foot:	Wedge	Length:	20"
Wedge:		Spacing:	1"
Root:		Spacing:	4"
Type Fastener:	bolts	Length:	4 1/2"
Type Fastener:	STYREALS	Length:	3 1/2"
Type Fastener:	STYREALS	Length:	3 1/2"
For used:	Increased 3 mile 30 plates, 8' wide, naturalized in each strip		
	will be cemented over the punk of the root end and fastened with steel		
	rodging nails of 2" on center on both sides of this centerline.		

Check Availability of Services

I understood a properly installed gutter as a requirement of all new and used homes and that condemnation, not, window and buidled marriage was as a result of a poorly installed or no gutter being installed. I understood a strip of tape will not make an a gutter.

Protein Blot's in Toxicity OK

**Two grand
Pg. Factory installed**

15C1

Questioned:	Between Floors	Yes
Between Walls	Yes	✓
Between of adjacent	Yes	✓

Weatherproofing

True bottomboard will be replaced another tapered. Yes ☒ Pg. 15C1
Siding can apply in horizontal to manufacture a specification. Yes ☒
Fireplaces chimney vented so as not to allow intrusion of rain water. Yes ☒

THE POWER OF THE FUTURE


...suiting to use restricted.	Yes ☐	No ☒	N/A ☐
Dryer vent installed outside of skirting.	Yes ☒	N/A ☐	N/A ☐
Range hood/vents vent installed outside of skirting.	Yes ☒	N/A ☐	N/A ☐
Drain lines supported at 4 foot intervals.	Yes ☒	N/A ☐	N/A ☐
Electrical coverovers protected.	Yes ☒	N/A ☐	N/A ☐

Others:

translating vestiges of all information given with this journal's words here
to ascertain and trap based on the
man's effect on a foundation foundation and on the...

1. Introduction

Date 4/18/25

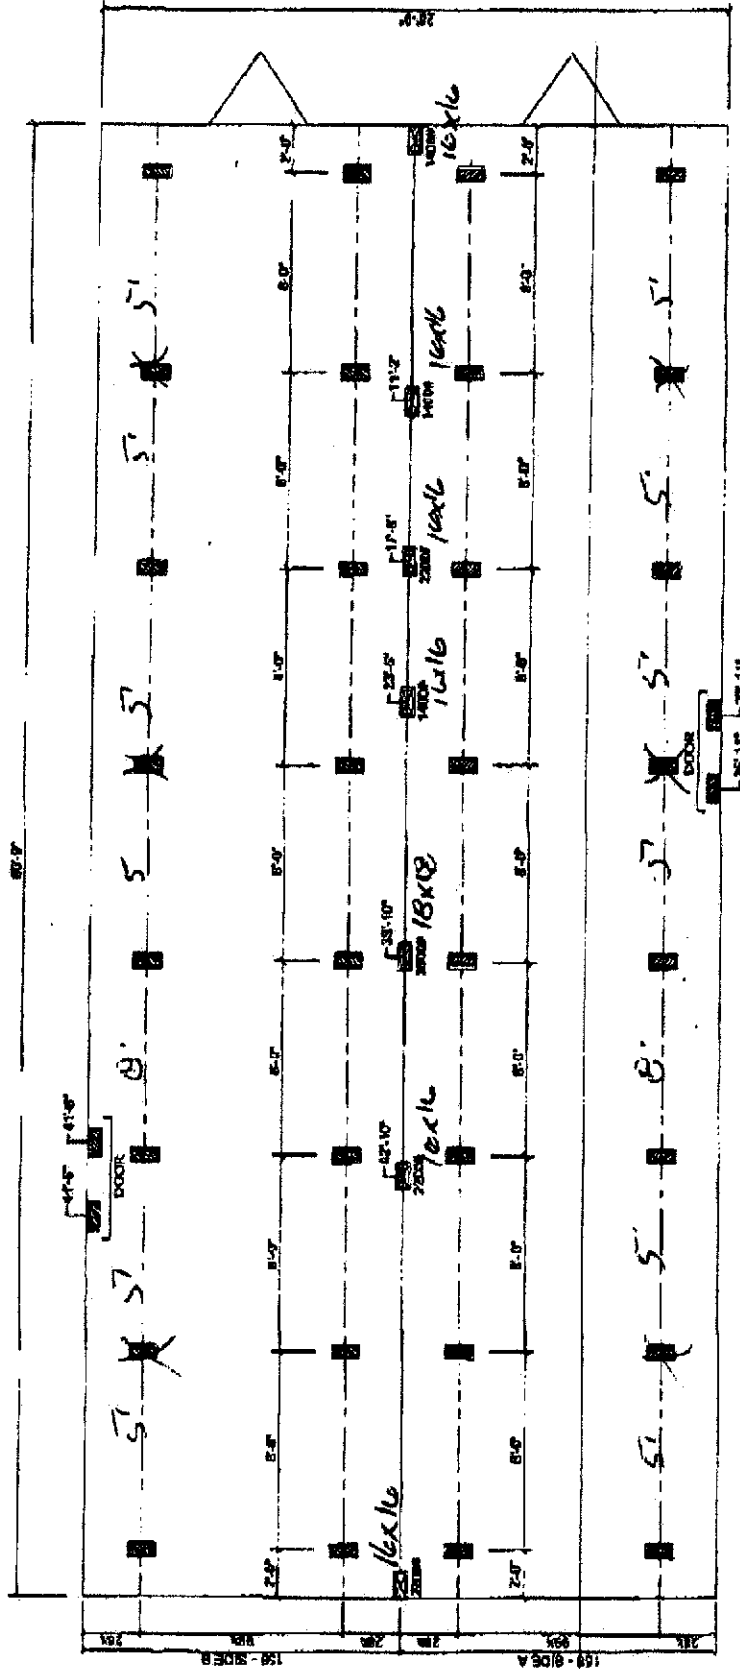

D23 HARRINGE LINE OPENING SUPPORT PIER/TYP.
D28 SUPPORT PIER/TYP

1000023

FOUNDATION NOTES

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY. QUANTITY AND SPACING MAY VARY BASED ON PLOT TYPE, SOIL CONDITIONS, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS. SEE INSTALLATION MANUAL FOR REQUIREMENTS.

Live Oak Homes
MODEL: L-2604F - 28 X 60 (BOX)
4-BEDROOM / 2-BATH

(99-1/2" I-BEAM SPACING)
L-2604F

License Number: 1H / 1038219 / 1 Name: RUSTY L. KNOWLES

Order #: 6566

Label #: 119103

Manufacturer:

Homeowner:

Year Model:

Address:

Length & Width:

City/State/Zip:

Type Longitudinal System:

Phone #:

Type Lateral Arm System:

Date Installed:

New Home: _____ Used Home: _____

Installed Wind Zone:

Data Plate Wind Zone:

Note:

(Check Size of Home)

Single _____

Double _____

Triple _____

HUD Label #:

Soil Bearing / PSF:

Torque Probe / in-lbs:

Permit #:

STATE OF FLORIDA INSTALLATION CERTIFICATION LABEL

119103

LABEL #

DATE OF INSTALLATION

RUSTY L. KNOWLES

NAME

1H / 1038219 / 1

6566

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
