

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT

Order #: 5763	Label #: 98737	Manufacturer: LIVE OAK	Year Model: 2008	Length & Width: 44/48 x 28	Type Longitudinal System: DTI (H)	Type Lateral Arm System: DTI (H)	New Home: ☒ Used Home: ☐	Data Plate Wind Zone: 2	Permit #:
Homeowner:	Address: 391 SW WHITEHILL CIRCLE	City/State/Zip: LAKE CITY FL	Phone #:	Date Installed:	Installed Wind Zone: 2	Note:			
Single	Double ☒	Triple	HUD Label #:	Soil Bearing / PSF:	Torque Probe / in-lbs:				

STATE OF FLORIDA INSTALLATION CERTIFICATION LABEL

98737
LABEL #
DAVID E ALBRIGHT
NAME
IH / 1129420 / 1
5763
ORDER #
LICENSE #
CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS
PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

Mobile Home Permit Worksheet

Installer: DAVID AIBRIGHT License # 1H-1129420
 Address of home being installed 391 SW Whitetail Circle Lake City


Manufacturer Live Oak Length x width 28x44/48

NOTE: If home is a single wide fill out one half of the blocking plan
 If home is a triple or quad wide sketch in remainder of home
 I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Typical pier spacing 2' 4" 6" Installer's Initials MA



Show locations of Longitudinal and Lateral Systems
 (use dark lines to show these locations)

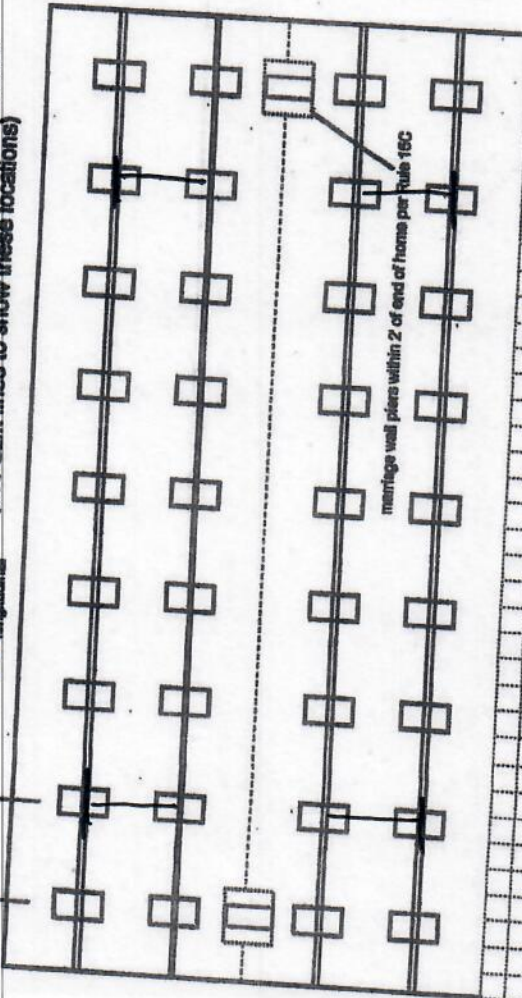

Application Number:

Date:

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Decal # 98737

Tripler/Quad ☐ Serial #

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	4'	4'	5'	6'	7'	8'
1500 psf	4' 6"	6'	6'	7'	8'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'	8'
2500 psf	7' 6"	8'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17x26
 Perimeter pier pad size 16x16
 Other pier pad sizes (required by the mfg.) 34x22 24x24

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

ANCHORS

Opening FACTORY Pier pad size DIAGRAM

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" OC

OTHER TIES

Sidewall 1/8
 Longitudinal 1/4
 Marriage wall 5'-5'-4"
 Shearwall 1

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) 4
 Manufacturer OLIVER TECHNOLOGIES
 Longitudinal Stabilizing Device w/ Lateral Arms 4
 Manufacturer OLIVER TECHNOLOGIES

Mobile Home Permit Worksheet

Dw

Application Number:

Date:

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to or check here to declare 1000 lb. soil ☒ without testing.

X ☐ X ☐ X ☐

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X ☐ X ☐ X ☐

TORQUE PROBE TEST

The results of the torque probe test is 240 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all cantefline locations where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 400 lb. holding capacity.

Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name DAVID AIBRIGHT MOBILE HOME SVC
Date Tested _____

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 64-68

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 70
Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 107

Site Preparation

Debris and organic material removed ☒
Water drainage: Natural Swale Pad ☒ Other

Fastening multi wide units

Floor: Type Fastener: LAG Length: 6" Spacing: 2'
Walls: Type Fastener: LAG Length: 6" Spacing: 18"
Roof: Type Fastener: LAG Length: 6" Spacing: 2'
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the cantefline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials

Type Gasket Pg. 36

Installed:
Between Floors Yes ☒
Between Walls Yes END WALLS
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 119
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes


Miscellaneous

Skirting to be installed. Yes No ☒
Dryer vent installed outside of skirting. Yes
Range downflow vent installed outside of skirting. Yes
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other: N/A ☒

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or rules 15C-1 & 2

Installer Signature David Aibright Date _____

44'-0"

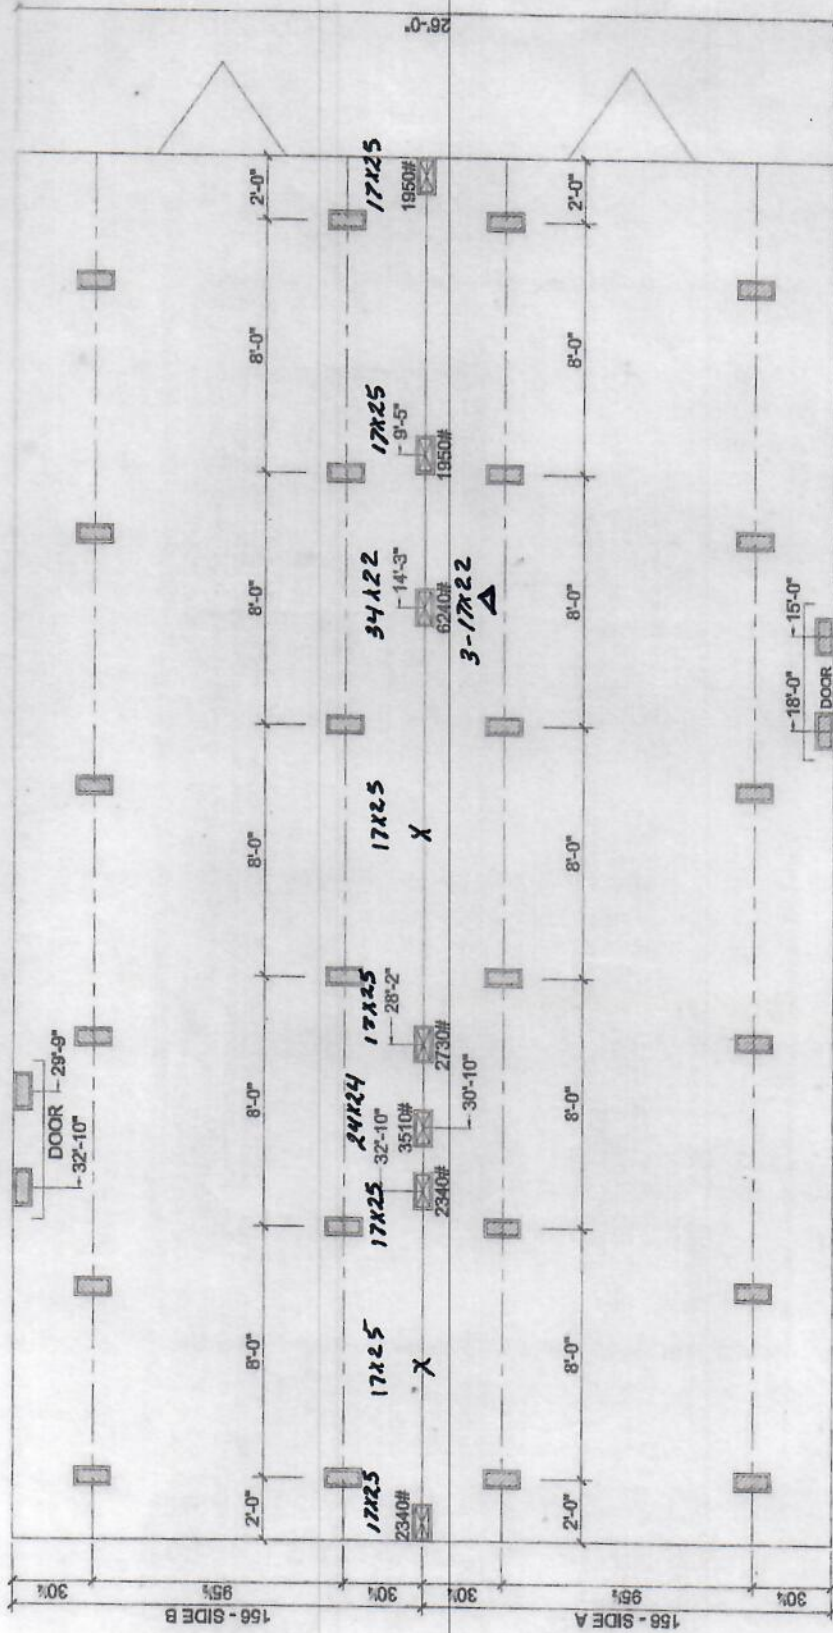

03/11/19

☒ MARRIAGE LINE OPENING SUPPORT PIER/TYP.
☒ SUPPORT PIER/TYP.

FOUNDATION NOTES:



- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

HAMILTON

Live Oak Homes
MODEL: V-2443G - 28 X 44
3-BEDROOM / 2-BATH

V-2443G

HAMILTON

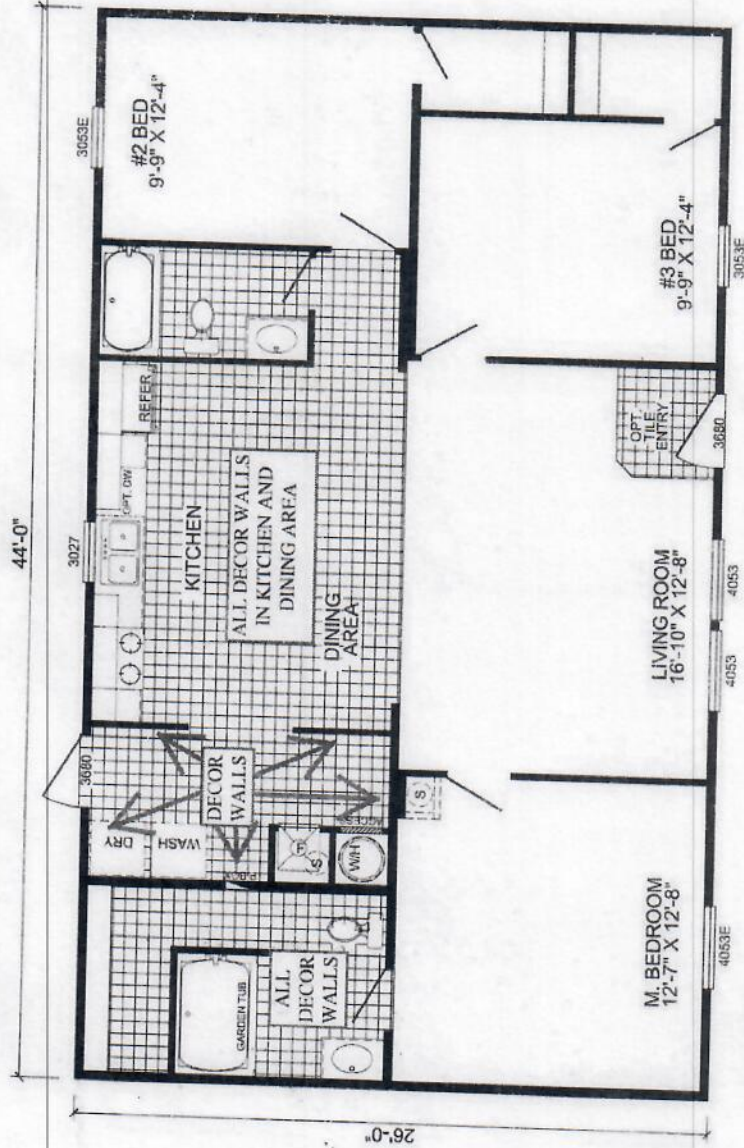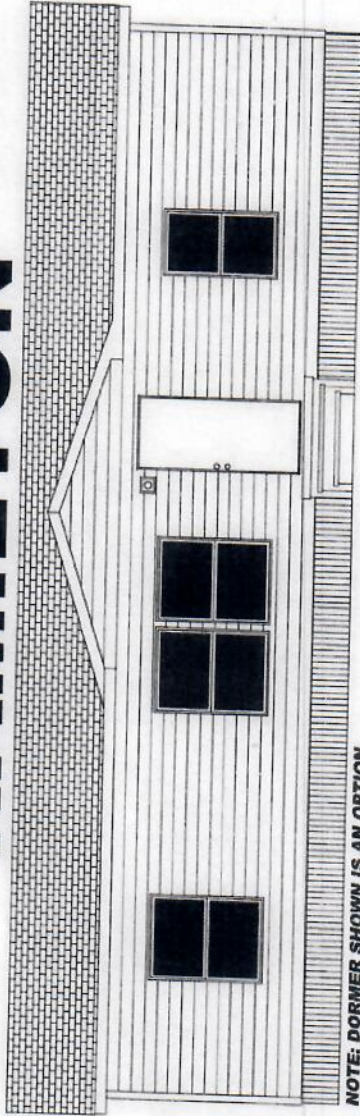

V-2443G
3-BEDROOM / 2-BATH
28 X 48 - Approx. 1144 Sq. Ft.

Date: 02/11/19
 * All room dimensions include closets and square footage figures are approximate.
 * Transom windows are available on optional 9'-0" sidewall houses only.
