

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325 AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

LICENSE # IH / 1129420 / 1 5763

NAME DAVID E ALBRIGHT

LABEL # DATE OF INSTALLATION

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

INSTRUCTIONS
PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT	
Order #: 5763	Label #: 98738
Homeowner: HUDSON	Address: 380 SW MOUNTAIN AVE
City/State/Zip: FT WHITE FL 32024	Phone #: 32024
Date Installed:	Installed Wind Zone: II
Manufacturer: LIVE OAK	Year Model: 2023
Length & Width: 56/60 x 14	Type Longitudinal System: OTI 6
Type Lateral Arm System: OTI 6	New Home: X Used Home:
Torque Probe / in-lbs:	Soil Bearing / PSF:
HUD Label #:	Triple
Double	Single X
(Check Size of Home)	Permit #:

Mobile Home Permit Worksheet



SW

Installer: DAVID ALBRIGHT License # 1H-1129420
 Address of home: 380 SW Montana Ave Ft White 32024
 being installed

Manufacturer: Live Oak Length x width: 14x56/60

NOTE: If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home where the sidewall ties exceed 5 ft 4 in.

Installer's Initials: ALB

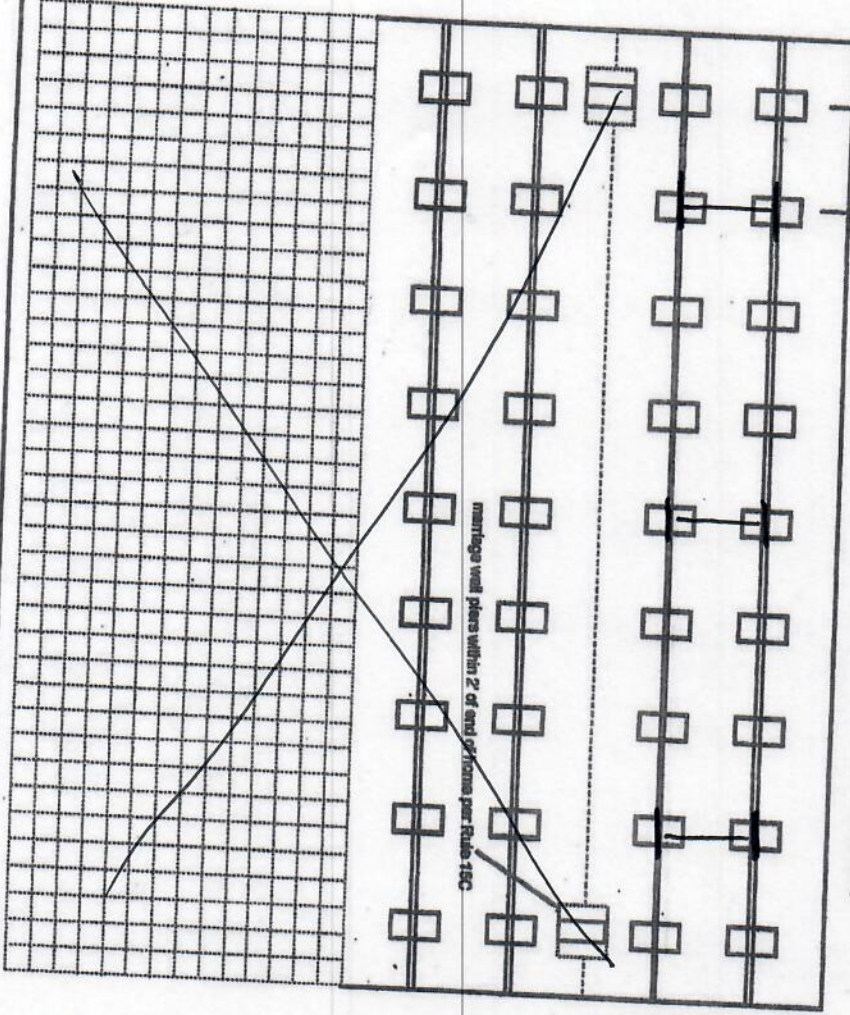

Application Number: _____

Date: _____

New Home ☒ Used Home ☐
 Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C

Single wide ☒ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☐ Installation Decal # _____

Triple/Quad ☐ Serial # _____

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	Footer size (259)	16" x 16"	18 1/2" x 18 1/2"	20" x 20"	22" x 22"	24" x 24"	26" x 26"
1000 psf	3"	4"	5"	6"	7"	8"	8"
1500 psf	4"	5"	6"	7"	8"	8"	8"
2000 psf	5"	6"	7"	8"	8"	8"	8"
2500 psf	6"	7"	8"	8"	8"	8"	8"
3000 psf	7"	8"	8"	8"	8"	8"	8"
3500 psf	8"	8"	8"	8"	8"	8"	8"

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size: 17x25
 Perimeter pier pad size: 16x16
 Other pier pad sizes (required by the mfg.): _____

POPULAR PAD SIZES

Pad Size	Sq in
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening: _____ Pier pad size: _____

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" OC

TIEDOWN COMPONENTS

OTHER TIES

Longitudinal Stabilizing Device (LSD)
 Manufacturer: CLIVER TECHNOLOGIES
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer: CLIVER TECHNOLOGIES

Sidewall Longitudinal Marriage wall Shearwall
 Number: 2.3
6
17

Mobile Home Permit Worksheet

SW

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to or check here to declare 1000 lb. soil ☒ without testing. ☐ psf

X ☐ X ☐ X ☐

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X ☐ X ☐ X ☐

TORQUE PROBE TEST

The results of the torque probe test is 250 inch pounds or check here if you are declaring 5" anchors without testing . A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline the points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

DAVID ALBRIGHT T MOBILE HOME SVC

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg.

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 70

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 107

Application Number:

Date:

Site Preparation

Debris and organic material removed ☒ Pad ☒ Other ☐
Water drainage: Natural ☒ Swale ☐

Fastening multi wide units

Floor: Type Fastener: ☒ Length: ☒ Spacing: ☒
Walls: Type Fastener: ☒ Length: ☒ Spacing: ☒
Roof: Type Fastener: ☒ Length: ☒ Spacing: ☒
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

Type gasket ☒
Pg.

Installed: ☒
Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 119
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous

Skirting to be installed. Yes ☒ No ☒
Dryer vent installed outside of skirting. Yes ☒ N/A ☒
Range downflow vent installed outside of skirting. Yes ☒ N/A ☒
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other: ☐


Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

David Albright T

Date

LIGHTNING

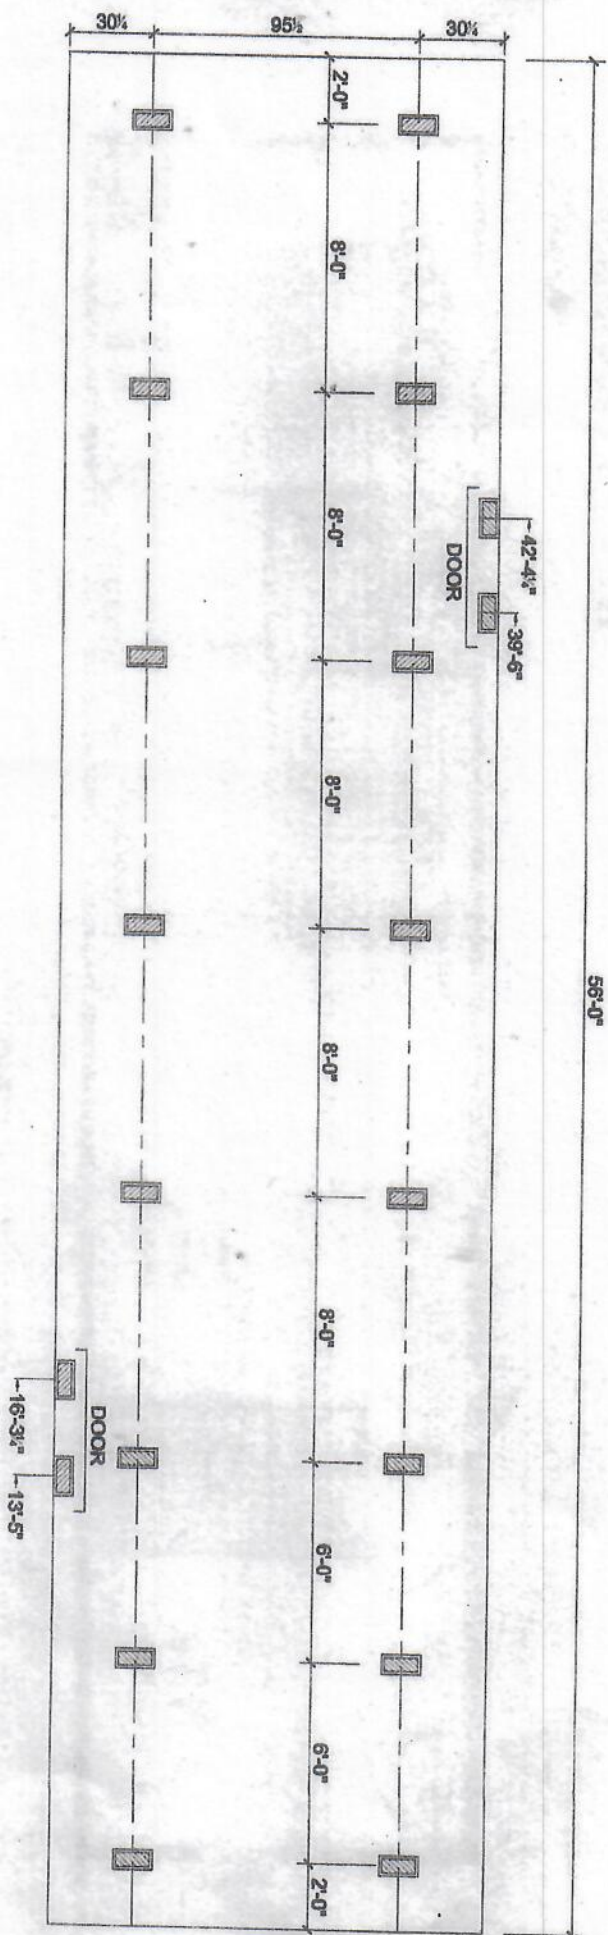

■ SUPPORT PIER/TYP

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.

1-31-2014

Live Oak Homes
MODEL: L-4562A - 14 X 60
2-BEDROOM / 2-BATH

L-4562A



Date: 03/09/23

* All room dimensions include closets and square footage figures are approximate.
* Live Oak Homes reserves the right to change product offering at any time.
