

PERMIT NUMBER

PERMIT WORKSHEET

page 1 of 2

 Installer Randy L. Kunkle License # ZH 1038219
 Installer Mobile Phone # 386.397.0886

Address of home being installed _____

 Manufacturer Line Oak Length x width 28' x 48'

 NOTE: If house is a single wide fill out one half of the blocking plan.
 If house is a triple or quad wide sketch in remainder of home.

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 @ 4 ft.

 Installer's Initials flk

Typical pier spacing

2' 8"

Longitudinal

Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

Marriage wall pier within 2' of end of floor joists 15C


 New Home ☒ Used Home ☐

 Home installed to the Manufacturer's Installation Manual ☒

 Home is installed in accordance with Rule 15-C ☐

 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

 Double wide ☐ Installation Decal # 105534

 Triple/Quad ☐ Serial # actual

 Roof System: Typical ☐ Hinged ☐

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footing size (sq ft)	18' x 18' (252)	18 1/2' x 18 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1600 psf	4' 8"	5'	6'	7'	8'	8'	8'
2000 psf	6'	6'	7'	8'	8'	8'	8'
2500 psf	7' 6"	7'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

 I-beam pier pad size 17.5 x 26.5

 Partner pier pad size not

 Other pier pad sizes (required by the mfg.) 16 x 16

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening _____ Pier pad size _____

TIEDOWN COMPONENTS

 Longitudinal Stabilizing Device (LSD)
 Manufacturer _____
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer _____

POPULAR PAD SIZES

Pad Size	Sq. ft.
18 x 18	258
18 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 28 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 R _____ 5 R _____

FRAME TIES

 within 2' of end of home
 spaced at 8' 4" oc

OTHER TIES

 Sidewall _____ Number _____
 Longitudinal _____
 Marriage wall _____
 Shearwall _____

2.004

FAX No.

2024/OCT/08/TUE 08:53

PERMIT NUMBER

PERMIT WORKSHEET

page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psi or check here to declare 1000 lb. soil without testing.

X 5 X X

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X X X

TORQUE PROBE TEST

The results of the torque probe test is NA N/A inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

RLK Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Rusty K...

Date Tested

10-16-24

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. 1561

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 1561

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 156-1



Site Preparation

Debris and organic material removed ☒
 Water drainage: Natural ☒ Swale ☒ Pad ☒ Other

Fastening multi-wide units

Floor: Type Fastener: Long Length: 6" Spacing: 20"
 Wall: Type Fastener: 5/8" Length: 4" Spacing: 20"
 Roof: Type Fastener: 5/8" Length: 1 1/2" Spacing: 18"
 For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket installation method

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials RLK

Type gasket

Pg. 1561

Installed:

Between Floors Yes ☒Between Walls Yes ☒Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 1561
 Siding on units is installed to manufacturer's specifications. Yes ☒
 Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous

Skinning to be installed. Yes ☒ No ☐
 Dryer vent installed outside of skinning. Yes ☒ N/A ☐
 Range downflow vent installed outside of skinning. Yes ☒ N/A ☐
 Drain lines supported at 4 foot intervals. Yes ☒
 Electrical crossovers protected. Yes ☒
 Other: ☒

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 16C-1 & 2

Installer Signature

Date 10-16-24

License Number: IH / 1038219 / 1 Name: RUSTY L. KNOWLES

Order #: 6147	Label #: 108534	Manufacturer:	(Check Size of Home)
Homeowner:	Year Model:		Single _____
Address:	Length & Width:		Double _____
City/State/Zip:	Type Longitudinal System:		Triple _____
Phone #:	Type Lateral Arm System:		HUD Label #:
Date Installed:	New Home: _____ Used Home: _____		Soil Bearing / PSP:
Installed Wind Zone:	Data Plate Wind Zone:		Torque Probe / in-lbs:
			Permit #:

Note:



**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

108534	
LABEL #	DATE OF INSTALLATION
RUSTY L. KNOWLES	
NAME	
IH / 1038219 / 1	6147
LICENSE #	ORDER #
CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8315 AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.	


INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.

2024/OCT/08/TUE 08:52

PAX No.

P. 002

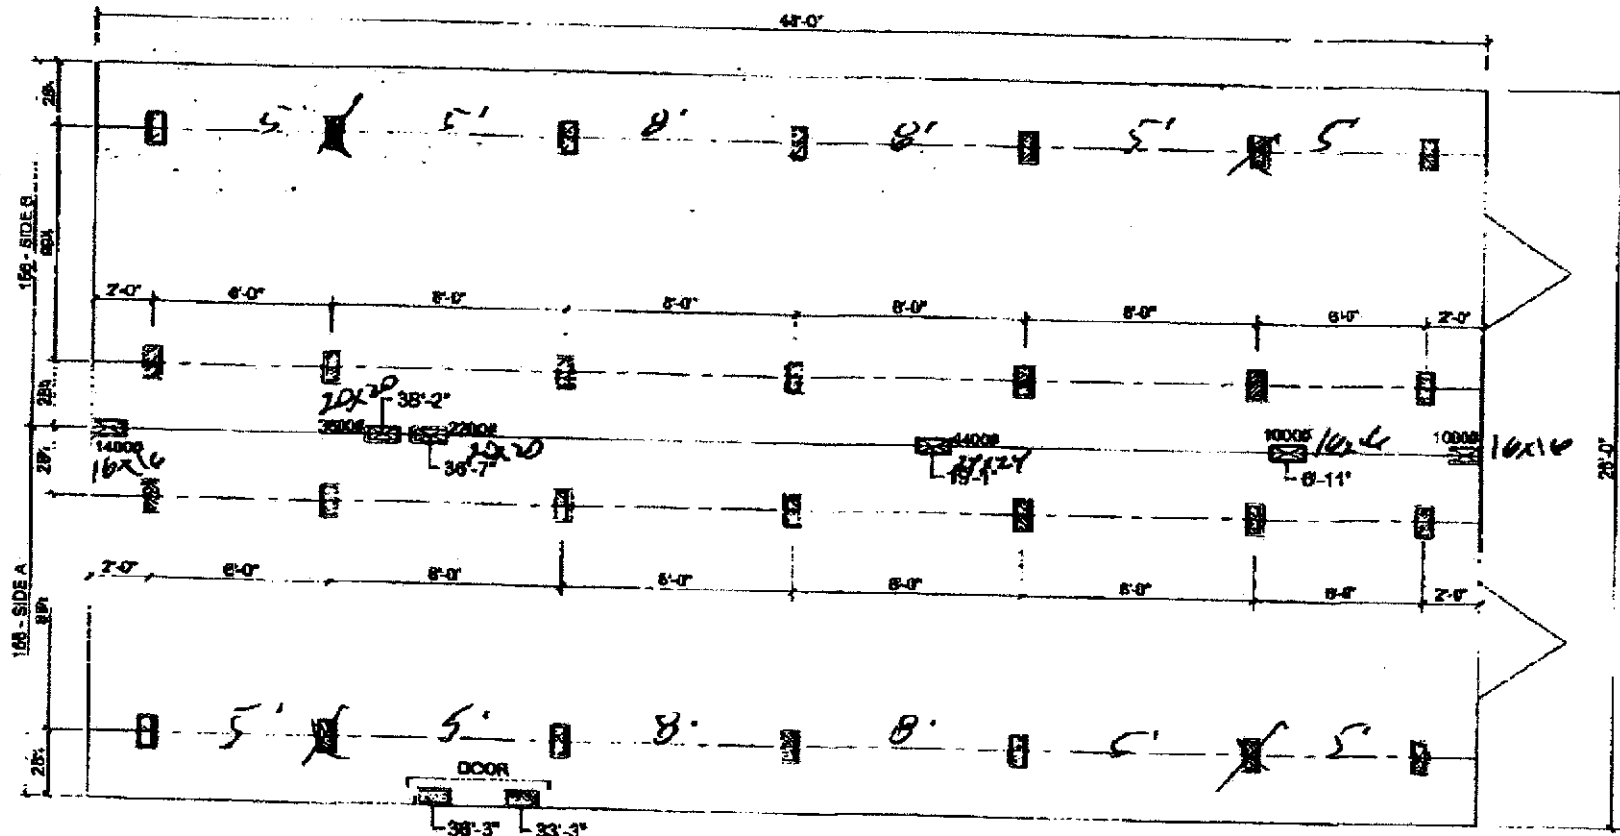

☒ MARRIAGE LINE OPENING SUPPORT PIER/TYP.

☒ SUPPORT PIER/TYP.

FOUNDATION NOTES:

- THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.
- FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAD TYPE, SOIL CONDITION, ETC.
- FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

11/08/22

Live Oak Homes
MODEL: H-2483N-PS - 28 X 48 (BOX)
3-BEDROOM / 2-BATH

(99-1/2" I-BEAM SPACING)

H-2483N-PS
