

2024/OCT/08/TUE 08:52

FAX No.

F.003

PERMIT NUMBER

PERMIT WORKSHEET


page 1 of 2

Installer Andy L. Powell License # ZH1036219  
Address of house 386.397.0884  
being installed

Manufacturer Live Oak Length x width 28' x 48'

NOTE: If house is a single wide fill out one half of the following table.  
If house is a triple or quad wide sketch in remainder of house.  
Understand Lateral Arm Systems cannot be used on any home (new or used)  
where the side walls exceed 5 @ 4 in.

Installer's Initials ALP

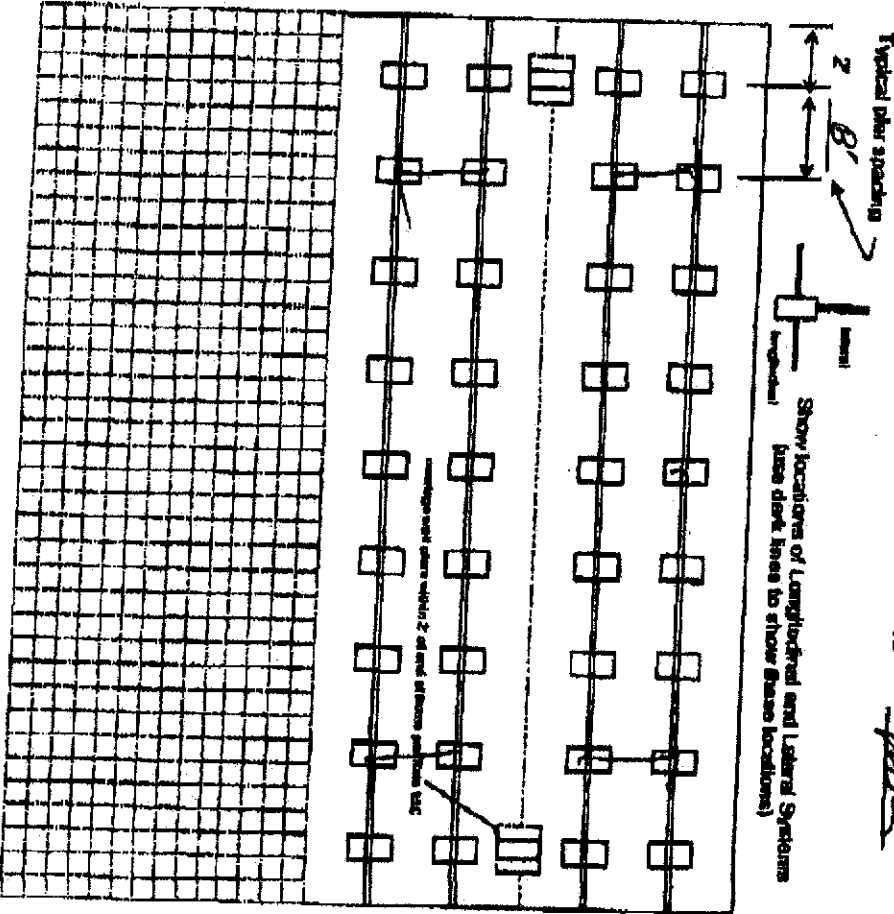

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual  
Home is installed in accordance with Rule 15-C

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☐ Installation Detail # 108534

Triple wide ☐ Serial # Actual

Roof System: Typical ☐ Hinged ☐

PER SPACING TABLE FOR USED HOMES

| Leaf bearing capacity (in lb) | Feeder 16' x 16' (250) | 16 1/2' x 16 1/2' (242) | 20' x 20' (400) | 22' x 22' (444) | 24' x 24' (576) | 26' x 26' (676) |
|-------------------------------|------------------------|-------------------------|-----------------|-----------------|-----------------|-----------------|
| 1000 net                      | 3'                     | 4'                      | 5'              | 6'              | 7'              | 8'              |
| 1600 net                      | 4'                     | 5'                      | 6'              | 7'              | 8'              | 9'              |
| 2000 net                      | 5'                     | 6'                      | 7'              | 8'              | 9'              | 10'             |
| 2500 net                      | 6'                     | 7'                      | 8'              | 9'              | 10'             | 11'             |
| 3000 net                      | 7'                     | 8'                      | 9'              | 10'             | 11'             | 12'             |
| 3500 net                      | 8'                     | 9'                      | 10'             | 11'             | 12'             | 13'             |

PIER PAD SIZES

| 1-beam pier pad size | 2-beam pier pad size | Other pier pad sizes (required by the mfg.) |
|----------------------|----------------------|---------------------------------------------|
| <u>17.5 x 23.5</u>   | <u>24</u>            | <u>flexile</u>                              |

Draw the approximate locations of marriage well openings 4 foot or greater. Use the symbol to show the piers.

List all marriage well openings greater than 4 foot and their pier pad sizes below.

ANCHORS

4 R 5 R

FRAME TIES

within 2' of end of home spaced at 8' 4" OC

OTHER TIES

Longitudinal Stabilizing Device (LSD)  
Manufacturer \_\_\_\_\_  
Longitudinal Stabilizing Device w/ Lateral Arms  
Manufacturer \_\_\_\_\_

Seismic Longitudinal Marriage well Shearwall  
Manufacturer \_\_\_\_\_

2024/OCT/08/TUE 08:53

FAX No.

2.004

## PERMIT NUMBER

## PERMIT WORKSHEET

Page 2 of 2

## POCKET PENETROMETER TEST

This pocket penetrometer scale is rounded down to 1500 psi or check here to determine 1000 lb. soil without testing.

X 15 X 1500 X 1500

## POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X 15 X 1500 X 1500

## TORQUE PEGGEE TEST

The results of the torque peggie test is NA 100 inch pounds or check here if you are determining 5" anchors without testing. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A steel approved lateral arm system is being used and 4 ft. anchors are allowed at the allowed locations. (Understand 5 ft. anchors are required at all cantilevered toe points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.)

ALP Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Kathy Kuehn

Date Tested

10-16-24

## Seachest

Connect electrical conductors between multi-wire units, but not to the main power source. This includes the bonding wire between multi-wire units. Pg. 16C1

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 16C2

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 16C-1

## Site Preparation

Debris and organic material removed ☒   
 Water drainage: Natural ☒ Grade ☒ Pad ☒ Other ☐

## Footings (wall) with units

Four: Long Length: 6' Spacing: 20'   
 Wall: Type Fastener: 5/16" Length: 6" Spacing: 20'   
 Roof: Type Fastener: 5/16" Length: 6" Spacing: 20'   
 For fastener: a min. 30 gauge, 8" wide, galvanized steel strip   
 will be centered over the peak of the roof and fastened with gable   
 roofing nails at 2" on center on both sides of the centerline.

## Ground anchors (no fasteners)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled flooring walls are a result of a poorly installed or no gasket being installed. I understand a slip of tape will not serve as a gasket.

Installer's Initials ALP

Type gasket factory

Pg. 16C1

## Insulation

Between Floors Yes ☒   
 Between Walls Yes ☒   
 Bottom of abdomen Yes ☒

## Weatherproofing

The bottomboard will be required and/or taped. Yes ☒ Pg. 16C1   
 Shading on units is installed to manufacturer's specifications. Yes ☒   
 Flue/vent chimney installed so as not to allow intrusion of rain water. Yes ☒

## Disinfectant

Shading to be installed. Yes ☒ No ☐   
 Dryer vent installed outside of skirting. Yes ☒ N/A ☐   
 Range downflow vent installed outside of skirting. Yes ☒ N/A ☐   
 Drain lines supported at 4 foot intervals. Yes ☒   
 Electrical crossovers protected. Yes ☒   
 Other: ☐

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 16C-1 & 2

Installer Signature

Date 10-16-24

License Number: IH / 1038219 / 1 Name: RUSTY L. KNOWLES

|                      |                                  |               |                        |
|----------------------|----------------------------------|---------------|------------------------|
| Order #: 6147        | Label #: 108534                  | Manufacturer: | (Check Size of Home)   |
| Homeowner:           | Year Model:                      |               | Single _____           |
| Address:             | Length & Width:                  |               | Double _____           |
|                      |                                  |               | Triple _____           |
| City/State/Zip:      | Type Longitudinal System:        |               | HUD Label #:           |
| Phone #:             | Type Lateral Arm System:         |               | Soil Bearing / PSP:    |
| Date Installed:      | New Home: _____ Used Home: _____ |               | Torque Probe / in-lbs: |
| Installed Wind Zone: | Data Plate Wind Zone:            |               | Permit #:              |
| Note:                |                                  |               |                        |

**STATE OF FLORIDA  
INSTALLATION CERTIFICATION LABEL**

108534

LABEL #

DATE OF INSTALLATION

RUSTY L. KNOWLES

NAME

IH / 1038219 / 1

6147

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS  
IN ACCORDANCE WITH FLORIDA STATUTES 320.8248, 320.8325  
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

**INSTRUCTIONS**

PLEASE WRITE DATE OF  
INSTALLATION AND AFFIX  
LABEL NEXT TO HUD LABEL.  
USE PERMANENT INK PEN  
OR MARKER ONLY.  
COMPLETE INFORMATION  
ABOVE AND KEEP ON FILE  
FOR A MINIMUM OF 2 YEARS.  
YOU ARE REQUIRED TO  
PROVIDE COPIES WHEN  
REQUESTED.

**Live Oak Homes**  
**MODEL: H-2483N-PS - 28 X 48 (BOX)**  
**3-BEDROOM / 2-BATH**

**(99-1/2" I-BEAM SPACING)**  
**H-2483N-PS**

**WARRIAGE LINE OPENING SUPPORT PIER/TYP.**  
**SUPPORT PIER/TYP**  
**FOUNDATION NOTES:**  
 - THIS DRAWING IS DESIGNED FOR THE STANDARD WIND ZONE AND IS TO BE USED IN CONJUNCTION WITH THE INSTALLATION MANUAL AND ITS SUPPLEMENTS.  
 - FOOTINGS ARE SHOWN FOR EXAMPLE ONLY QUANTITY AND SPACING MAY VARY BASED ON PAID TYPE, SOIL CONDITION, ETC.  
 - FOOTINGS ARE REQUIRED AT SUPPORT POSTS, SEE INSTALLATION MANUAL FOR REQUIREMENTS.

11/02/22

