


24 23 22 21 20 19 18 17 16 15 14 13 12 11 10 9 8 7 6 5 4 3 2 1 24" O.C.

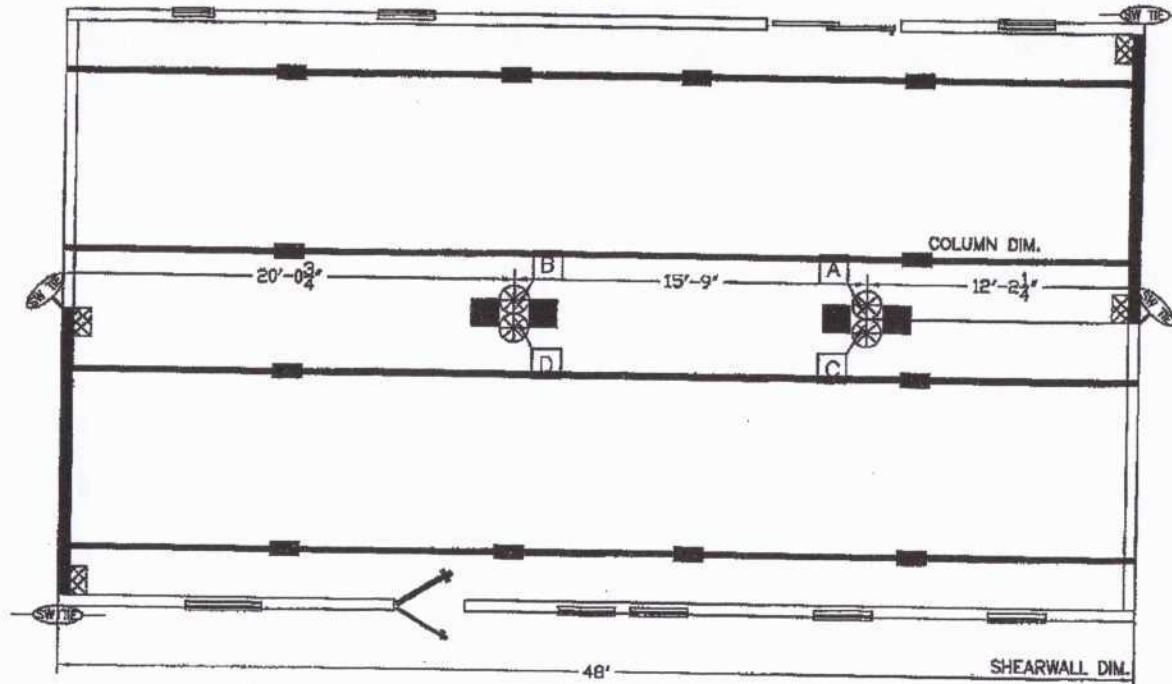

I-BEAM BLOCKING
SEE SOIL BEARING CAPACITY CHARTS FOR SPACING

COLUMN BLOCKING
SEE SOIL BEARING CAPACITY CHARTS FOR PAD SIZE

SHEARWALL BLOCKING

SHEARWALL FRAME TIE

CENTER LINE TIES

VERTICAL TIE
MAX. SPACING 5'-4" CENTER TO CENTER

LONGITUDINAL TIES

FLORIDA

1) ALL EXTERIOR DOORS, BAY WINDOWS, RECESSED SIDEWALLS AND EXTERIOR WALL OPENINGS 48" OR GREATER, WILL REQUIRE BLOCKING ON EACH SIDE.

2) 32' WIDE HOMES REQUIRED TO BE BLOCKED MIN 8'-0" ON CENTER BETWEEN COLUMNS.

TOWNHOMES VISION - ENDURANCE - INTEGRITY - BUILDING YOUR FUTURE		TownHomes P.O. BOX 1059 LAKE CITY, FLORIDA 32056	
Date: 2-24-25	Revisions	Cof:	
Dr's: HLG			
Parent: NEW			
Code: T (25)			
200R 2	Model: 28221-688	Print: FLORIDA BLOCKING PLAN	

License Number: IH / 1025395 / 1 Name: CHRISTOPHER C. OLIN			
Order #: 6879	Label #: 126314	Manufacturer: <u>Town Homes</u>	(Check Size of Home)
Homeowner: <u>Jennifer Terrell</u>		Year Model: <u>2026</u>	Single _____
Address: <u>723 NW Pillsbury dr.</u>		Length & Width: <u>28 x 48</u>	Double ☒ _____
City/State/Zip: <u>Lake City</u>		Type Longitudinal System: _____	Triple _____
Phone #: <u>386-361-0469</u>		Type Lateral Arm System: _____	HUD Label #: _____
Date Installed: <u>0519.26</u>		New Home: ☒ Used Home: _____	Soil Bearing / PSF: _____
Installed Wind Zone: <u>II</u>		Data Plate Wind Zone: _____	Torque Probe / in-lbs: _____
Permit #: _____			
Note: _____			

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

126314

LABEL #

DATE OF INSTALLATION

CHRISTOPHER C. OLIN

NAME

IH / 1025395 / 1

6879

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
